


Sullivan County Jail Additions Preliminary Schedule


ID	Task Mode	Task Name	Duration	Start	Finish
1		Sullivan County Jail	694 days	Mon 2/28/22	Thu 10/24/24
2		Site Work	597 days	Mon 2/28/22	Tue 6/11/24
3		Mobilization / E&S	3 days	Mon 2/28/22	Wed 3/2/22
4		Demolition	8 days	Thu 3/3/22	Mon 3/14/22
5		Mass Grading	10 wks	Tue 3/15/22	Mon 5/23/22
8		Storm	2.5 wks	Tue 3/15/22	Thu 3/31/22
6		Retaining wall 1	8 days	Tue 3/22/22	Thu 3/31/22
10		Sewer	2 wks	Thu 3/24/22	Thu 4/7/22
21		UGE Reloc	4 wks	Thu 3/31/22	Thu 4/28/22
7		Retaining wall 2	12 days	Fri 4/1/22	Mon 4/18/22
11		Fire /Water	8 wks	Thu 4/7/22	Thu 6/2/22
20		Generator Pads	8 days	Thu 4/21/22	Tue 5/3/22
19		Generator Relocation	9 days	Tue 5/10/22	Mon 5/23/22
18		Transformer Relocation	2 days	Wed 5/25/22	Fri 5/27/22
12		UGE New	3 wks	Thu 6/2/22	Thu 6/23/22
9		Finish Grading / Topsoil	3 wks	Fri 4/5/24	Thu 4/25/24
16		Fencing	4 wks	Fri 4/26/24	Thu 5/23/24
17		Site concrete	3 wks	Fri 4/26/24	Thu 5/16/24
15		Paving	8 days	Fri 5/17/24	Tue 5/28/24
14		Site Accessories	2 wks	Fri 5/24/24	Thu 6/6/24
13		Landscaping /Seeding	10 days	Wed 5/29/24	Tue 6/11/24
22		Main Building	588 days	Tue 5/24/22	Thu 8/22/24
24		Micro Piles	11 wks	Tue 5/24/22	Mon 8/8/22
23		Foundations	10 wks	Tue 7/12/22	Mon 9/19/22
25		Masonry to FF	4 wks	Tue 8/16/22	Mon 9/12/22
27		MEP slab RI	7 wks	Tue 8/30/22	Mon 10/17/22
28		Slab Prep & Pour	6 wks	Fri 10/7/22	Thu 11/17/22
30		CMU stairs / misc LB	11 wks	Tue 10/11/22	Mon 12/26/22
32		Structural Steel	16 wks	Fri 11/18/22	Thu 3/9/23
33		Exterior Framing	8 wks	Fri 3/3/23	Thu 4/27/23
34		Slab on Deck	5 wks	Fri 3/10/23	Thu 4/13/23
31		CMU perimeter	7 wks	Fri 3/31/23	Thu 5/18/23
39		Brick	15 wks	Fri 4/7/23	Thu 7/20/23
26		Rod & Hanger Systems	4 wks	Fri 4/14/23	Thu 5/11/23
36		Metal Panels	14 wks	Fri 4/28/23	Thu 8/3/23

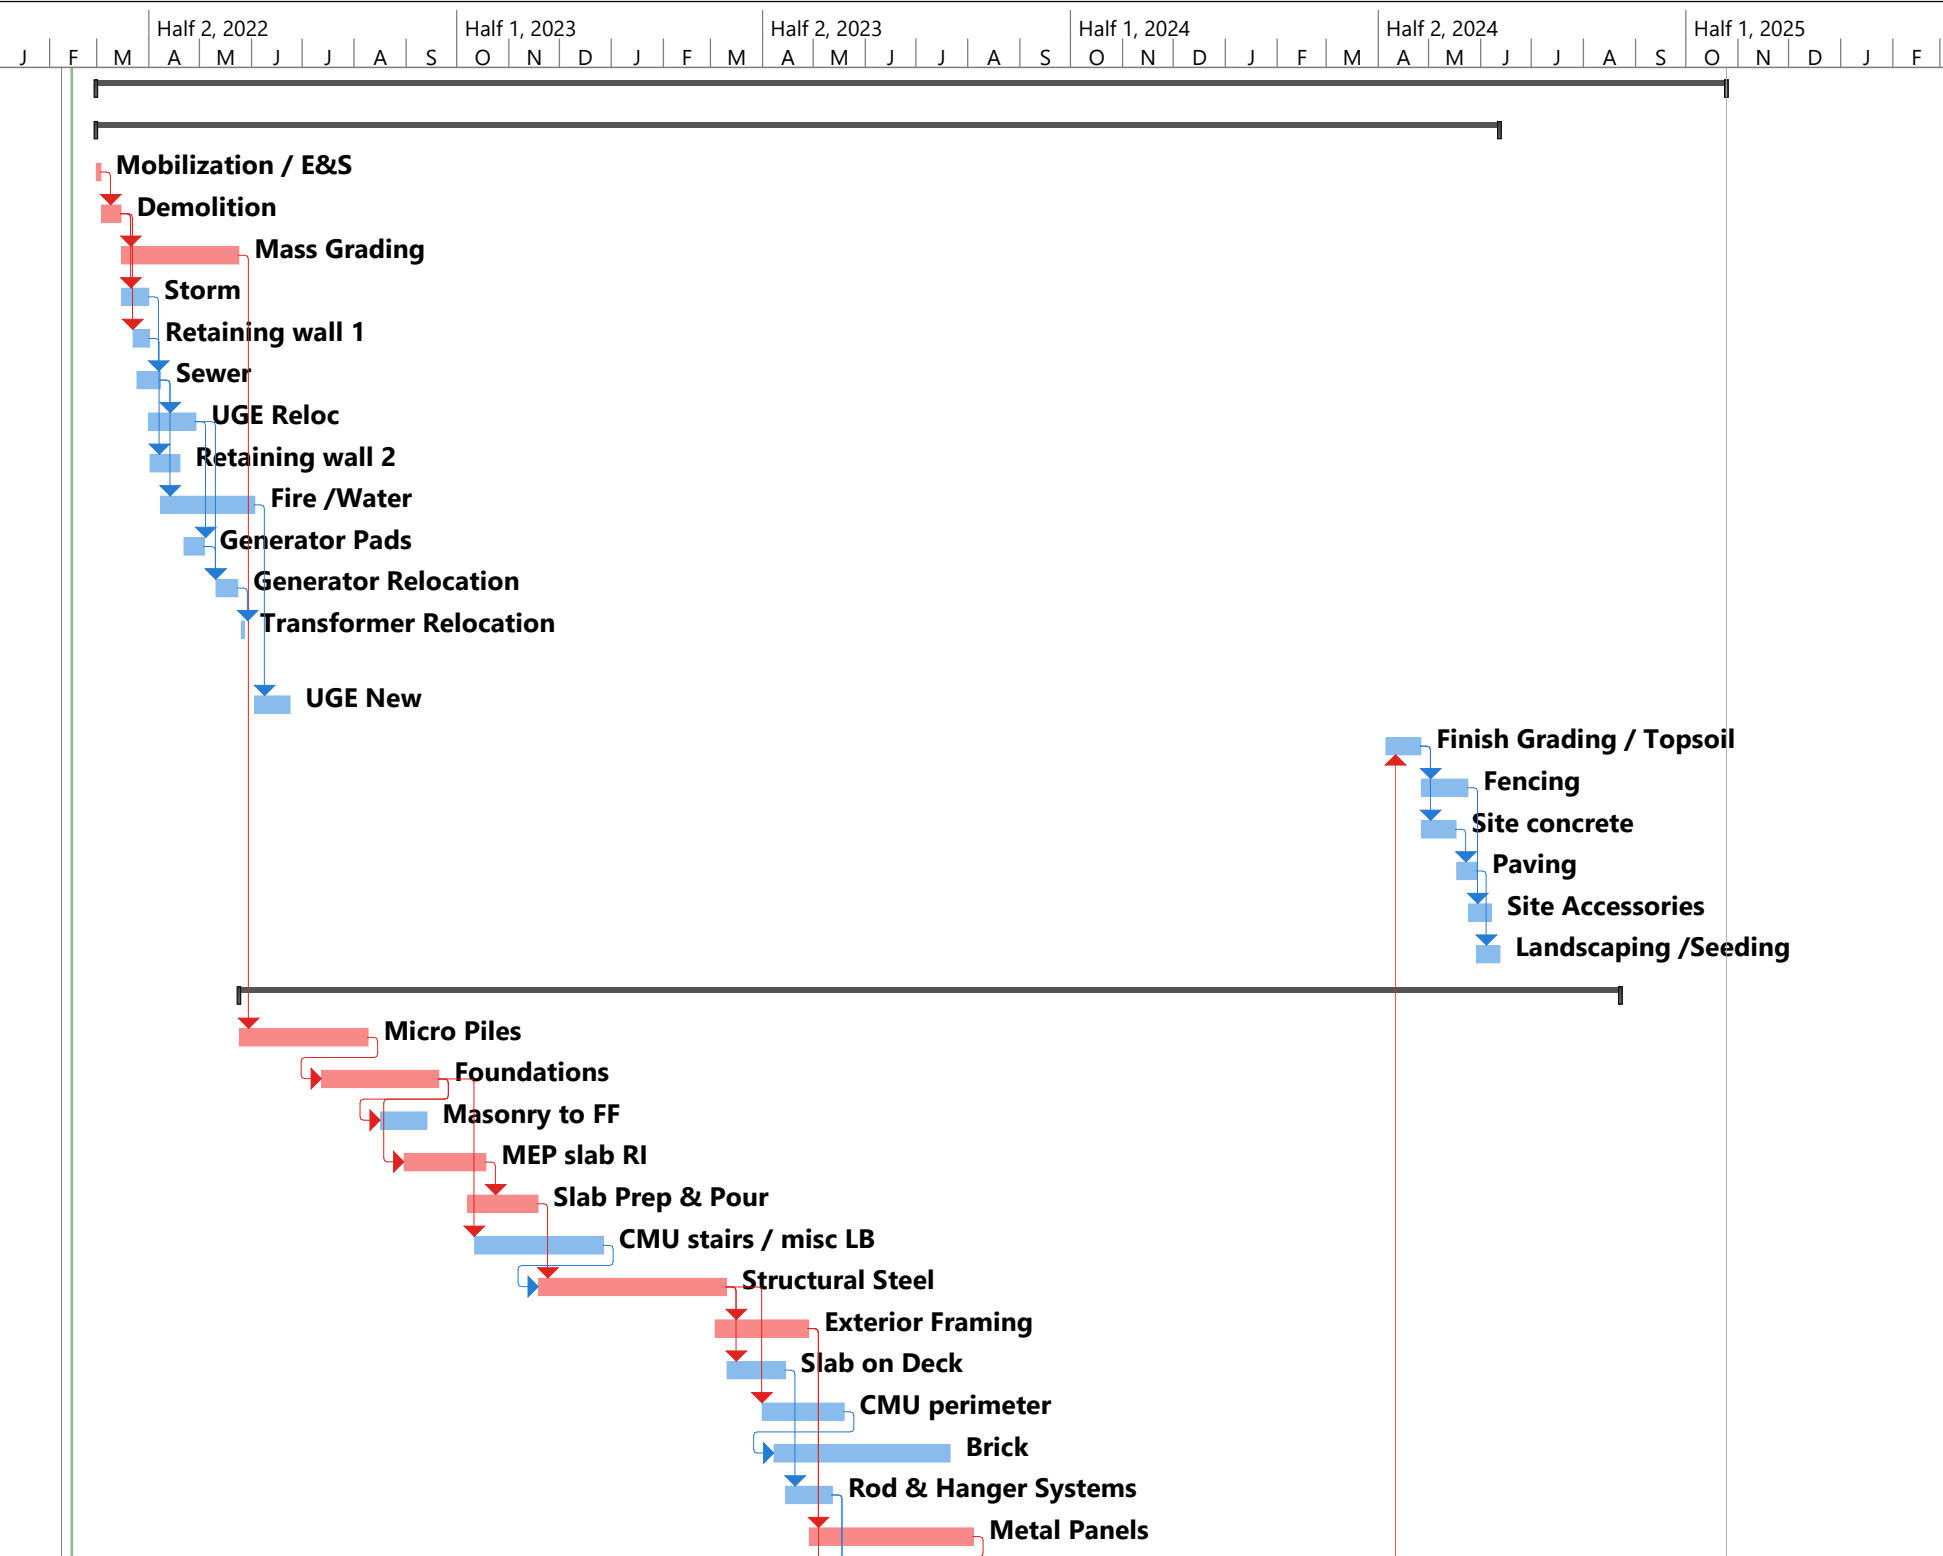

Project: Draft for Testing scope
Date: Mon 2/14/22

Task		Inactive Task		Manual Summary Rollup		External Milestone		Manual Progress	
Split		Inactive Milestone		Manual Summary		Deadline			
Milestone		Inactive Summary		Start-only		Critical			
Summary		Manual Task		Finish-only		Critical Split			
Project Summary		Duration-only		External Tasks		Progress			

Sullivan County Jail Additions Preliminary Schedule

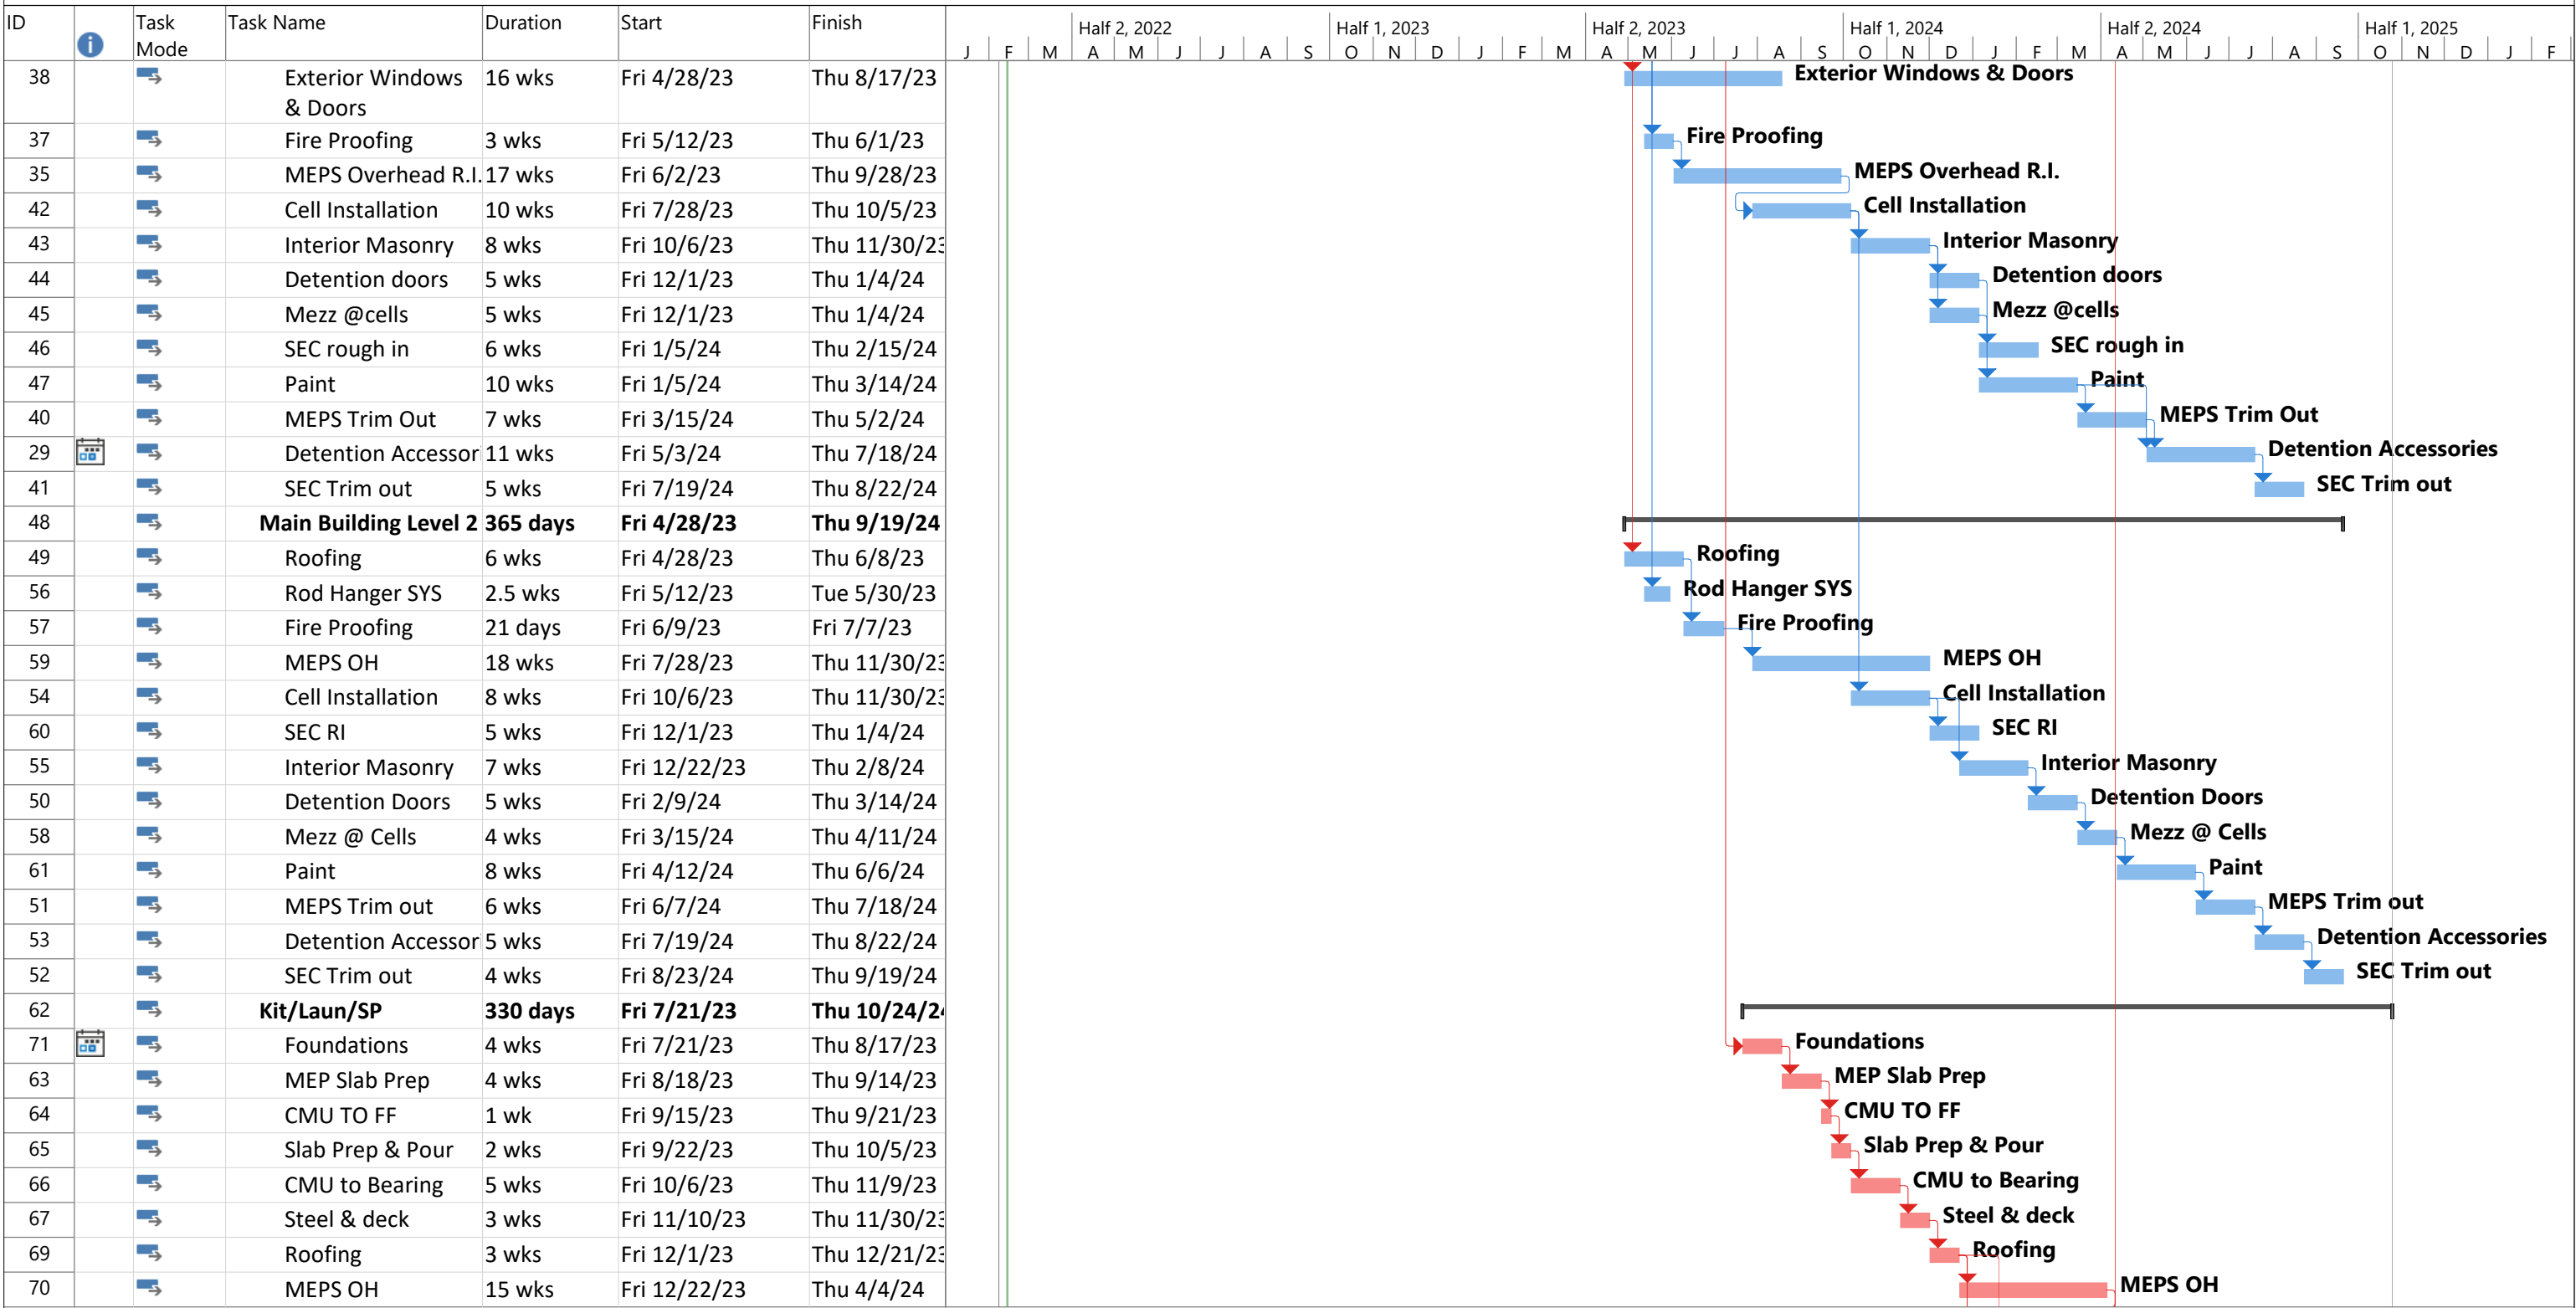

Project: Draft for Testing scope Date: Mon 2/14/22	Task	Inactive Task	Manual Summary Rollup	External Milestone	Manual Progress
	Split	Inactive Milestone	Manual Summary	Deadline	
	Milestone	Inactive Summary	Start-only	Critical	
	Summary	Manual Task	Finish-only	Critical Split	
	Project Summary	Duration-only	External Tasks	Progress	

