

Summer Construction, Inc.

P.O. BOX 30 Santa Paula, CA. 93061
Ph. (805) 933-9364 Fax (805) 525-3000
License # 597494

REQUEST FOR INFORMATION NO. 2

Job Name: San Antonio Parking Lot Improvements, Project 2020-1309

Location: Ojai, CA **Bid Date:** 10/08/2020 @ 2:00 pm

Name of Owner: Ojai Unified School District

Submitted To: Ojai Unified School District

Attention: Adam Dutter **Email:** adutter@ojaiusd.org

DESCRIPTION OF REQUEST

Subject : AC Paving

1. Spec. Section 321216 – Asphalt Concrete Paving Part 2 – Products 2.1 Paragraph B No. 2, lists 2 types of asphalt to be used. a. Base course calls for D1-AR-8000. b. Surface course calls for C2-AR-4000. c. At least two courses shall be laid when the new asphalt is thicker than 4". The top course shall be a surface course a minimum of 2"(inches) thick.

Since our thickest Asphalt on the project is 4" (inches) thick, what type of Asphalt are we to use for the parking lot and the 3" basketball court. Please clarify

Subject : Plan Page C-1.0 Construction Note 15 –Provide Existing 6"-90 degree bend at project end of existing DDC, Install 6" Diameter Tee with F.D.C 6"x 2 ½ " Wye. Provide 2 New Pipe Supports for DDC

1. Is this item apart of this Scope of Work since it was not mentioned at the job walk?

Subject : Plan Page A-1.1 Detail 2 Accessible Walk (See attached Drawing)

1. Keynote 32-03 Provide Accessible Asphalt Walk is shown in the orange outlined area, should it be in the green outlined area since AD-1.1 detail 5 shows concrete pavement in this area? Is it the school intentions to have new Asphalt and Concrete in this area as depicted on the plans?


Subject : Survey **KEYNOTE 32-03 SHOULD POINT TO THE GREEN OUTLINED AREA INSTEAD OF THE CONCRETE.**

1. Per the Architect's answer regarding Survey. They state that verification of construction footprints and elevations to be by contractor's surveyor. So does this mean that we are required to provide survey for this project? If so, will CAD files be available for this project?

REFER TO SPECIFICATION SECTION 017300 EXECUTION 3.2 AND 3.3 FOR REQUIREMENTS. A PROFESSIONAL SURVEYOR IS RECOMMENDED TO AVOID NON-COMPLIANT SLOPES AND REQUIRED REWORK.

Thank you,

Sam Bennett

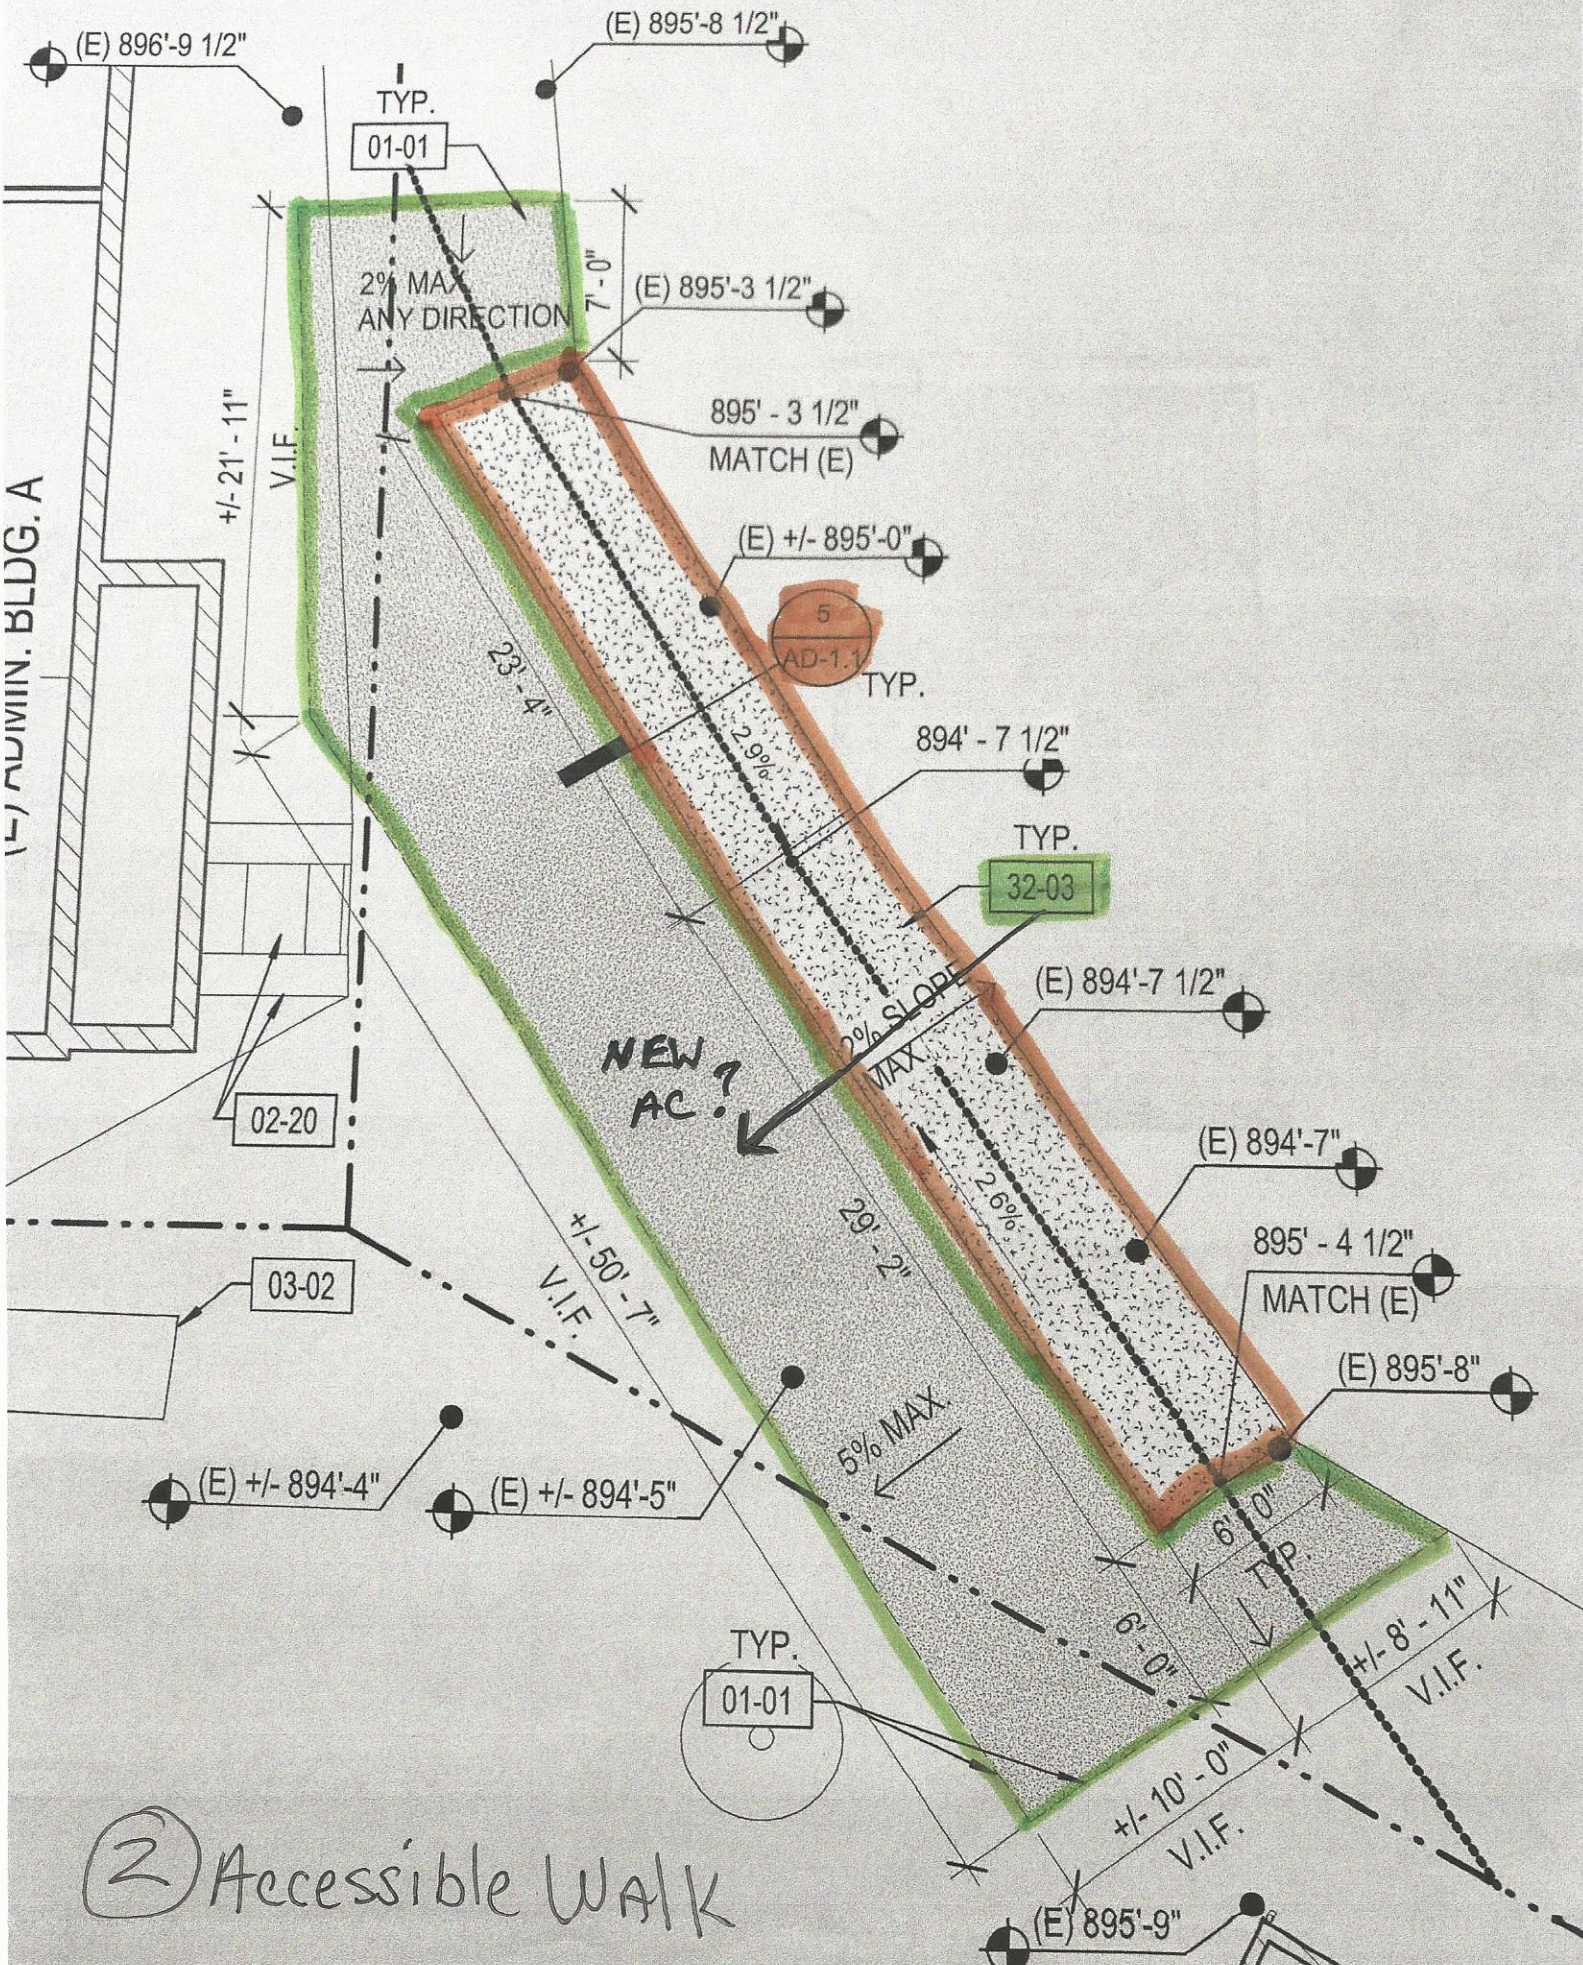

② Accessible Walk
