STONE CONSTRUCTION ENTRANCE



SIDE ELEVATION



* MUST EXTEND FULL WIDTH OF INGRESS AND EGRESS OPERATION

PLAN VIEW



SECTION A–A



SECTION B–B

SOURCE: ADAPTED from 1983 Maryland Standards for Soil erosion and Sediment Control, and Va. DSWC

Plate 3.02-1

GRAVEL CURB INLET SEDIMENT FILTER





SPECIFIC APPLICATION

THIS METHOD OF INLET PROTECTION IS APPLICABLE AT CURB INLETS WHERE PONDING IN FRONT OF THE STRUCTURE IS NOT LIKELY TO CAUSE INCONVENIENCE OR DAMAGE TO ADJACENT STRUCTURES AND UNPROTECTED AREAS.

* GRAVEL SHALL BE VDOT #3, #357 OR 5 COARSE AGGREGATE.

SOURCE: VA. DSWC

PLATE 3.07-6

05/12/2022
date

Qianqian Li, P.E.
ESC Program Administrator
Department of Environmental Sevices
2100 Clarendon Boulevard, Suite 813
Arlington, Virginia 22201

Re: Erosion and Sediment Control Permit Application for:

2751 11TH STREET NORTH ARLINGTON, VA 22201
street address

RPC 18-016-021; RPC 18-016-001
lot, block, section subdivision

LDA 22032
permit number

Dear Mrs. Li:

I hereby certify that I accept the responsibilities of Responsible Land Disturber for the above referenced project. I understand that these responsibilities include:

1. Reviewing the erosion and sedimentation (E&S) plan for the project.
2. Walking the site prior to construction to identify critical areas.
3. Conducting a pre-construction briefing with earth moving and site contractors to present the E&S plan and highlight the presence of critical areas, the limits of clearing and the required E&S controls and tree protection measures to be installed. Call 703-228-0760 to schedule pre-construction meeting.
4. Regularily inspecting the site during construction to ensure that all E&S controls are functioning and are adequate to address erosion and sedimentation. Inspect the site 48 hours after a runoff-generating storm, and provide a copy of the inspection findings to the county.
5. Reporting to the owner the presence inadequate or non functioning E&S controls when they are observed.
6. Ensuring that temporary soil stabilization is applied within 7 days to areas denuded that will remain undisturbed for longer than 14 days. Permanent stabilization shall be applied to areas that are to be left dormant for more than one year.
7. Calling (703) 228-0760 at least 80 hours before demolishing any structure.

I may be reached at 703-228-7598 *telephone number* with questions about this plan or my execution of the duties of Responsible Land Disturber.

Sincerely,

signed

Kathy von Bredow
name printed

#1611
professional registration (type and number)

COIR FILTER LOG

STANDARD SYMBOL
FL-15
15 INCH DIAMETER FILTER LOG.





UNTRENCHED INSTALLATION OR ENTRENCHED INSTALLATION*

*THIS APPLICATION MAY NOT BE USED WITH LOGS SMALLER THAN 12 IN.

ISOMETRIC VIEW



PLAN

CONSTRUCTION SPECIFICATIONS

1. PRIOR TO INSTALLATION, CLEAR ALL OBSTRUCTIONS INCLUDING ROCKS, CLODS, AND DEBRIS GREATER THAN ONE INCH THAT MAY INTERFERE WITH PROPER FUNCTION OF COIR FILTER LOG.
2. FILL LOG NETTING UNIFORMLY WITH COMPOST (IN ACCORDANCE WITH VIRGINIA DEQ MATERIALS SPECIFICATIONS), OR OTHER APPROVED BIODEGRADABLE MATERIAL TO DESIRED LENGTH SUCH THAT LOGS DO NOT DEFORM.
3. INSTALL COIR FILTER LOGS PERPENDICULAR TO THE FLOW DIRECTION AND PARALLEL TO THE SLOPE WITH THE BEGINNING AND END OF THE INSTALLATION POINTING SLIGHTLY UP THE SLOPE CREATING A "J" SHAPE AT EACH END TO PREVENT BYPASS.
4. FOR UNTRENCHED INSTALLATION BLOW OR HAND PLACE MULCH OR COMPOST ON UPHILL SIDE OF THE SLOPE ALONG LOG.
5. STAKE FILTER LOG EVERY 4 FEET OR CLOSER ALONG ENTIRE LENGTH OF LOG OR TRENCH LOG INTO GROUND A MINIMUM OF 4 INCHES AND STAKE LOG EVERY 8 FEET OR CLOSER.
6. USE STAKES WITH A MINIMUM NOMINAL CROSS SECTION OF 2X2 INCH AND OF SUFFICIENT LENGTH TO ATTAIN A MINIMUM OF 12 INCHES INTO THE GROUND AND 3 INCHES PROTRUDING ABOVE LOG.
7. WHEN MORE THAN ONE LOG IS NEEDED, OVERLAP ENDS 12 INCHES MINIMUM AND STAKE.
8. REMOVE SEDIMENT WHEN IT HAS ACCUMULATED TO A DEPTH OF ½ THE EXPOSED HEIGHT OF LOG AND REPLACE MULCH. REPLACE COIR FILTER LOG IF TORN. REINSTALL COIR LOG IF UNDERMINING OR DISLODGING OCCURS. REPLACE CLOGGED COIR LOGS. FOR PERMANENT APPLICATIONS, ESTABLISH AND CONTINUOUSLY MEET REQUIREMENTS FOR ADEQUATE VEGETATIVE ESTABLISHMENT IN ACCORDANCE WITH VIRGINIA VEGETATIVE STABILIZATION.

SAFETY FENCE

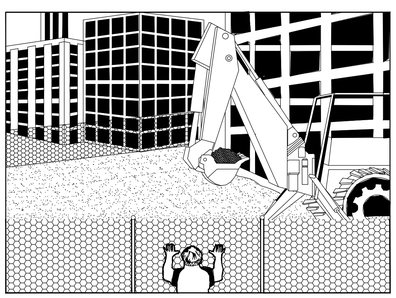

PERSPECTIVE VIEW



PERSPECTIVE VIEW
PLASTIC FENCE



PERSPECTIVE VIEW
METAL FENCE

SOURCE: CONWED PLASTICS
VDOT ROAD AND BRIDGE STANDARDS
VA. DSWC

PLATE. 3.1-1

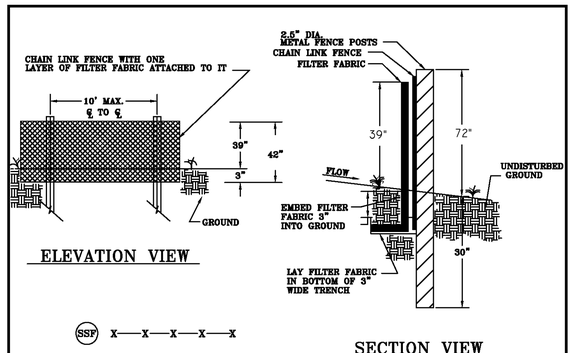

SUPER SILT FENCE
NO SCALE

FENCING

FILTER FABRIC SHALL BE 39" ABOVE GRADE WITH 3" EMBEDDED FOR A TOTAL FABRIC WIDTH OF 42". THE POST SHALL BE 72"ABOVE GRADE WITH 30" PLACED BELOW GRADE (WITHOUT CONCRETE) FOR A TOTAL LENGTH OF 102".

NOTES

1. **Chain link fence shall be fastened securely to fence posts with wire ties.**
2. **Filter fabric shall be fastened securely to chain link fence with ties spaced horizontally 24" at the top and midsection.**
3. **Physical properties of the filter fabric shall conform to the latest edition of THE VIRGINIA EROSION & SEDIMENT CONTROL HANDBOOK.**
4. **When two sections of filter fabric adjoin each other, they shall be overlapped by 6".**
5. **Maintenance shall be performed as needed and material shall be removed when sediment build-up reaches 50% of the height of the super silt fence.**

SILT FENCE DROP INLET PROTECTION



PERSPECTIVE VIEWS



ELEVATION OF STAKE AND FABRIC ORIENTATION



DETAIL A

SPECIFIC APPLICATION

THIS METHOD OF INLET PROTECTION IS APPLICABLE WHERE THE INLET DRAINS A RELATIVELY FLAT AREA (SLOPE NO GREATER THAN 5%) WHERE THE INLET SHEET OR OVERLAND FLOWS (NOT EXCEEDING 1 C.F.S.) ARE TYPICAL. THE METHOD SHALL NOT APPLY TO INLETS RECEIVING CONCENTRATED FLOWS, SUCH AS IN STREET OR HIGHWAY MEDIANS.

SOURCE: N.C. Erosion and Sediment Control Planning and Design Manual, 1988

PLATE 3.07-1

ARLINGTON VIRGINIA

DEPARTMENT OF PARKS AND RECREATION

Park Development Division
2100 Clarendon Boulevard, Suite 414
Arlington, VA 22201
Phone: 703.228.3332
Fax: 703.228.3328

-

Project Name and Location
11th & Danville Public Space Improvements

2751 11th Street North
Arlington, VA 22201

Sheet Title
EROSION AND SEDIMENT CONTROL DETAILS

Approval Date

Design Manager

Revisions Date

Designed: AW
Drawn: AMT
Checked: CMB

Filename: C-08-210330.001 EROSION AND SEDIMENT CONTROL DETAILS
Plotted: 2022-05-12

Scale: AS SHOWN
Date: MAY 12, 2022

Seal

COMMONWEALTH OF VIRGINIA
CHELSEA M. BISHOP
Lic. No. 50030
Chelsea Bishop
MAY 12, 2022

Sheet
C-08

Path: X:\Rockville\21-0330.001 - 11th and Danville\05-CAD\

Filename: C-08-210330.001 Erosion and Sediment Control Details.dwg
