

CONTRACT, LEASE, AGREEMENT CONTROL FORM

Date: 10/20/2022

Contract/Lease Control #: C23-3267-PW

Procurement#: ITB PW 56-22

Contract/Lease Type: AGREEMENT

Award To/Lessee: LAS CONTRACTING CORP

Owner/Lessor: OKALOOSA COUNTY

Effective Date: 10/19/2022

Expiration Date: 240 DAYS FROM NTP

Description of: OLD BETHEL SIDEWALK IMPROVEMENTS

Department: PW

Department Monitor: AUTREY

Monitor's Telephone #: 850-689-5772

Monitor's FAX # or E-mail: JAUTREY@MYOKALOOSA.COM

Closed:

Cc: BCC RECORDS

**PROCUREMENT/CONTRACT/LEASE
INTERNAL COORDINATION SHEET**

Procurement/Contract/Lease Number: <u>TBD 56-22</u>		Tracking Number: <u>493322</u>	
Procurement/Contractor/Lessee Name: <u>LAS Contracting</u>		Grant Funded: YES <input type="checkbox"/> NO <input checked="" type="checkbox"/>	
Purpose: <u>Old Bethel Road Sidewalk Improvements</u>			
Date/Term: <u>240 days from NTP</u>		1. <input checked="" type="checkbox"/> GREATER THAN \$100,000	
Department #: <u>3301</u>		2. <input type="checkbox"/> GREATER THAN \$50,000	
Account #: <u>563001</u>		3. <input type="checkbox"/> \$50,000 OR LESS	
Amount: <u>\$979,24.00</u>			
Department: <u>PW</u>		Dept. Monitor Name: <u>Autry</u>	

Purchasing Review	
Procurement or Contract/Lease requirements are met:	
<u>DeRita Mason</u>	Date: <u>9-19-22</u>
Purchasing Manager or designee	Jeff Hyde, DeRita Mason, Jessica Darr, Amber Hammonds

2CFR Compliance Review (if required)	
Approved as written:	Grant Name: _____
<u>no federal funds</u>	Date: _____
Grants Coordinator	Suzanne Ulloa

Risk Management Review	
Approved as written:	Date: <u>9-19-22</u>
<u>see email attached</u>	
Risk Manager or designee	Kristina LoFria

County Attorney Review	
Approved as written:	Date: <u>9-19-22</u>
<u>see email attached</u>	
County Attorney	Lynn Hoshihara, Kerry Parsons or Designee

Department Funding Review	
Approved as written:	Date: _____

IT Review (if applicable)	
Approved as written:	Date: _____

DeRita Mason

From: Parsons, Kerry <KParsons@ngn-tally.com>
Sent: Monday, September 19, 2022 3:38 PM
To: DeRita Mason
Cc: Lydia Garcia; Lynn Hoshihara
Subject: RE: LAS Contracting Draft Contract 56-22

Hey DeRita:

The agreement is approved for legal purposes.

Kerry A. Parsons, Esq.

**Nabors
Giblin &
Nickerson**
ATTORNEYS AT LAW

1500 Mahan Dr. Ste. 200
Tallahassee, FL 32308
T. (850) 224-4070
Kparsons@ngn-tally.com

The information contained in this e-mail message is intended for the personal and confidential use of the recipient(s) named above. This message and its attachments may be an attorney-client communication and, as such, is privileged and confidential. If the reader of this message is not the intended recipient or an agent responsible for delivering it to the intended recipient, you are hereby notified that you have received this document in error and that any review, dissemination, distribution, or copying of this message is strictly prohibited. If you have received this communication in error, please notify us immediately by telephone or e-mail and delete the original message. Thank you!

From: DeRita Mason <dmason@myokaloosa.com>
Sent: Monday, September 19, 2022 3:35 PM
To: lhoshihara@myokaloosa.com
Cc: Parsons, Kerry <KParsons@ngn-tally.com>; Lydia Garcia <lgarcia@myokaloosa.com>
Subject: LAS Contracting Draft Contract 56-22

Good afternoon,
Please review and approve the attached. The actual contract is word and the attached is the bid and other attachments.

DeRita Mason



DeRita Mason, CPPB, NIGP-CPP
Senior Contracts and Lease Coordinator

DeRita Mason

From: Lydia Garcia
Sent: Monday, September 19, 2022 2:56 PM
To: DeRita Mason; Lynn Hoshihara
Cc: 'Parsons, Kerry'
Subject: RE: LAS Contracting Draft Contract 56-22
Attachments: General Service Insurance Requirements for Contractors 1.3.19 .docx; LAS Contract Draft.docx

Good Afternoon All,

The attached LAS Contracting Corp. contract is approved by Risk Management for insurance purposes contingent upon the General Service Insurance Requirements for Contractors is included in its entirety.



Kind Regards,

L. Garcia
Public Records Request & Contracts Specialist

OKALOOSA COUNTY BCC

Risk Management
Direct: 850.689.4111
Fax: 850.689.5973 |
Email: riskinfo@myokaloosa.com

302 N. Wilson St. Suite 301
Crestview, FL 32539

<https://myokaloosa.com/>

Please note: Due to Florida's very broad public records laws, most written communications to or from county employees regarding county business are public records, available to the public and media upon request. Therefore, this written e-mail communication, including your e-mail address, may be subject to public disclosure.

From: DeRita Mason <dmason@myokaloosa.com>
Sent: Monday, September 19, 2022 2:35 PM
To: Lynn Hoshihara <lhoshihara@myokaloosa.com>
Cc: 'Parsons, Kerry' <KParsons@ngn-tally.com>; Lydia Garcia <lgarcia@myokaloosa.com>
Subject: LAS Contracting Draft Contract 56-22

Good afternoon,
Please review and approve the attached. The actual contract is word and the attached is the bid and other attachments.

DeRita Mason



Board of County Commissioners Purchasing Department

State of Florida

Date: September 9, 2022

OKALOOSA COUNTY PURCHASING DEPARTMENT
NOTICE OF INTENT TO AWARD
ITB PW 56-22

Old Bethel Road Sidewalk Improvements

Okaloosa County would like to thank all businesses, which submitted bids to for Old Bethel Road Sidewalk Improvements (ITB PW 56-22)

After in-depth examination of all responses in accordance with the County's Purchasing Manual, the County announces its intent to award the contract/purchase order to the following:

LAS Contracting Corp
13701 N. Nebraska Ave.
Tampa, FL 33613

This Notice of Intent does NOT constitute the formation of a contract/purchase order between Okaloosa County and the apparent successful bidder/respondent. The County reserves the right to enter into negotiations with the successful bidder/respondent in order to finalize contract terms and conditions. No agreement is entered into between the County and any parties until a contract is approved and fully executed.

Any person/entity desiring to file a procurement protest must meet all the standards and criteria in accordance with Section 31 of the Okaloosa County Purchasing Manual. Failure to file a protest within the time prescribed in Section 31.02 of the Okaloosa County Purchasing Manual, shall constitute a waiver of protest proceedings.

Respectfully,


Jeffrey Hyde
Purchasing Manager



CERTIFICATE OF LIABILITY INSURANCE

DATE (MM/DD/YYYY)

9/21/2022

THIS CERTIFICATE IS ISSUED AS A MATTER OF INFORMATION ONLY AND CONFERS NO RIGHTS UPON THE CERTIFICATE HOLDER. THIS CERTIFICATE DOES NOT AFFIRMATIVELY OR NEGATIVELY AMEND, EXTEND OR ALTER THE COVERAGE AFFORDED BY THE POLICIES BELOW. THIS CERTIFICATE OF INSURANCE DOES NOT CONSTITUTE A CONTRACT BETWEEN THE ISSUING INSURER(S), AUTHORIZED REPRESENTATIVE OR PRODUCER, AND THE CERTIFICATE HOLDER.

IMPORTANT: If the certificate holder is an ADDITIONAL INSURED, the policy(ies) must have ADDITIONAL INSURED provisions or be endorsed. If SUBROGATION IS WAIVED, subject to the terms and conditions of the policy, certain policies may require an endorsement. A statement on this certificate does not confer rights to the certificate holder in lieu of such endorsement(s).

PRODUCER Halifax Insurance 1540 Cornerstone Blvd., Suite 200 Daytona Beach FL 32117	CONTACT NAME: PHONE (A/C, No. Ext): 386-677-4761 FAX (A/C, No): 386-673-5370 E-MAIL ADDRESS: email@HIPFlorida.com
INSURED Las Contracting Corp Jack Gardner PO Box 1275 San Antonio FL 33576-1275	INSURER(S) AFFORDING COVERAGE INSURER A: Auto-Owners Insurance Company INSURER B: Markel American Insurance Company INSURER C: INSURER D: INSURER E: INSURER F:

License#: L100460
LASCONT-01**COVERAGES****CERTIFICATE NUMBER:** 1221908674**REVISION NUMBER:**

THIS IS TO CERTIFY THAT THE POLICIES OF INSURANCE LISTED BELOW HAVE BEEN ISSUED TO THE INSURED NAMED ABOVE FOR THE POLICY PERIOD INDICATED. NOTWITHSTANDING ANY REQUIREMENT, TERM OR CONDITION OF ANY CONTRACT OR OTHER DOCUMENT WITH RESPECT TO WHICH THIS CERTIFICATE MAY BE ISSUED OR MAY PERTAIN, THE INSURANCE AFFORDED BY THE POLICIES DESCRIBED HEREIN IS SUBJECT TO ALL THE TERMS, EXCLUSIONS AND CONDITIONS OF SUCH POLICIES. LIMITS SHOWN MAY HAVE BEEN REDUCED BY PAID CLAIMS.

INSR LTR	TYPE OF INSURANCE	ADDL INSD	SUBR WVD	POLICY NUMBER	POLICY EFF (MM/DD/YYYY)	POLICY EXP (MM/DD/YYYY)	LIMITS
A	<input checked="" type="checkbox"/> COMMERCIAL GENERAL LIABILITY <input type="checkbox"/> CLAIMS-MADE <input checked="" type="checkbox"/> OCCUR GEN'L AGGREGATE LIMIT APPLIES PER: <input checked="" type="checkbox"/> POLICY <input type="checkbox"/> PRO-JECT <input type="checkbox"/> LOC OTHER:			72596968	1/25/2022	1/25/2023	EACH OCCURRENCE \$ 1,000,000 DAMAGE TO RENTED PREMISES (Ea occurrence) \$ 50,000 MED EXP (Any one person) \$ 5,000 PERSONAL & ADV INJURY \$ 1,000,000 GENERAL AGGREGATE \$ 2,000,000 PRODUCTS - COMP/OP AGG \$ 2,000,000 \$
A	AUTOMOBILE LIABILITY <input type="checkbox"/> ANY AUTO <input type="checkbox"/> OWNED AUTOS ONLY <input checked="" type="checkbox"/> SCHEDULED AUTOS <input type="checkbox"/> HIRED AUTOS ONLY <input type="checkbox"/> NON-OWNED AUTOS ONLY			4268766603	12/16/2021	12/16/2022	COMBINED SINGLE LIMIT (Ea accident) \$ 1,000,000 BODILY INJURY (Per person) \$ BODILY INJURY (Per accident) \$ PROPERTY DAMAGE (Per accident) \$ \$
	UMBRELLA LIAB <input type="checkbox"/> OCCUR EXCESS LIAB <input type="checkbox"/> CLAIMS-MADE DED <input type="checkbox"/> RETENTION \$						EACH OCCURRENCE \$ AGGREGATE \$ \$
B	WORKERS COMPENSATION AND EMPLOYERS' LIABILITY ANY PROPRIETOR/PARTNER/EXECUTIVE OFFICER/MEMBER EXCLUDED? (Mandatory in NH) If yes, describe under DESCRIPTION OF OPERATIONS below	Y/N <input type="checkbox"/> N/A		MWC0138081-02	11/12/2021	11/12/2022	<input checked="" type="checkbox"/> PER STATUTE <input type="checkbox"/> OTH-ER E.L. EACH ACCIDENT \$ 1,000,000 E.L. DISEASE - EA EMPLOYEE \$ 1,000,000 E.L. DISEASE - POLICY LIMIT \$ 1,000,000

DESCRIPTION OF OPERATIONS / LOCATIONS / VEHICLES (ACORD 101, Additional Remarks Schedule, may be attached if more space is required)

Job 56-22 Old Bethel Road Sidewalk Improvements
Certificate holder is additional insured with respect to General Liability when required under written contract. General Liability coverage is primary. A 30 day Notice of Cancellation will be provided to the certificate holder except for non-payment.

CERTIFICATE HOLDER**CANCELLATION**Oskaloosa County
5479A Old Bethel Rd.
Crestview FL 32536

SHOULD ANY OF THE ABOVE DESCRIBED POLICIES BE CANCELLED BEFORE THE EXPIRATION DATE THEREOF, NOTICE WILL BE DELIVERED IN ACCORDANCE WITH THE POLICY PROVISIONS.

AUTHORIZED REPRESENTATIVE

THIS AGREEMENT is by and between Okaloosa County, a political subdivision of the State of Florida, by and through its Board of County Commissioners, situated at 1250 N. Eglin Parkway, Shalimar, Florida ("OWNER") and LAS Contracting Corp, a Florida Profit Corporation whose address is 13701 N. Nebraska Ave., Tampa, FL 33613 (address), certified to do business in the state of Florida ("CONTRACTOR").

OWNER and CONTRACTOR hereby agree as follows:

ARTICLE 1 – WORK

- 1.01 CONTRACTOR shall complete all WORK as specified or indicated in the Contract Documents. The WORK is generally described as follows: Old Bethel Road Sidewalk Improvements

ARTICLE 2 – THE PROJECT

2.01 The Project, of which the Work under the Contract Documents is a part, is generally described as follows: Construct the Old Bethel Road Sidewalk Improvements consisting of constructing sidewalk, and other associated work including clearing and grubbing, earthwork, maintenance of traffic, concrete retaining walls, and other improvements. The work is further defined as shown on the Plans and as described by the Contract Documents.

ARTICLE 3 – ENGINEER

- 3.01 The part of the Project that pertains to the WORK has been designed by DRMP (Design Engineer).
3.02 The OWNER has retained the County Engineer ("ENGINEER") to act as OWNER's representative, assume all duties and responsibilities, and have the rights and authority assigned to ENGINEER in the Contract Documents in connection with the completion of the Work in accordance with the Contract Documents.

ARTICLE 4 – CONTRACT TIMES

- 4.01 Time of the Essence
A. All time limits for Milestones, if any, Substantial Completion, and completion and readiness for final payment as stated in the Contract Documents are of the essence of the Contract.
- 4.02 Contract Times: Days
A. The Work will be substantially completed within 180 calendar days after the date when the Contract Times commence to run as provided in Paragraph 4.01 of the General Conditions, and completed and ready for final payment in accordance with Paragraph 15.06 of the General Conditions within 240 calendar days after the date when the Contract Times commence to run.
- 4.03 Liquidated Damages
A. Section 337.18(2) of the Florida Statutes, requires the OWNER adopt regulations for the determination of default and provisions that the Contractor pay liquidated damages (daily charge per calendar day) for any failure of the Contractor to complete the Contract work within the Contract Time.
B. CONTRACTOR and OWNER recognize that time is of the essence as stated in Paragraph 4.01 above and that OWNER will suffer financial and other losses if the Work is not completed and Milestones not achieved within the times specified in Paragraph 4.02 above, plus any extensions thereof

CONTRACT: C23-3267-PW
LAS CONTRACTING CORP
OLD BETHEL SIDEWALK IMPROVEMENTS
EXPIRES: 240 DAYS FROM NTP

allowed in accordance with the Contract. The parties also recognize the delays, expense, and difficulties involved in proving in a legal proceeding the actual loss suffered by OWNER if the Work is not completed on time. Accordingly, instead of requiring any such proof, OWNER and CONTRACTOR agree that as liquidated damages for delay. Contractor specifically acknowledges that the liquidated damages is not a penalty and waives any right to argue such at a later time.

1. Substantial Completion: CONTRACTOR shall pay OWNER \$972.00 for each day that expires after the time (as duly adjusted pursuant to the Contract) specified in Paragraph 4.02.A above for Substantial Completion until the Work is substantially complete.
2. Completion of Remaining Work: After Substantial Completion, if CONTRACTOR shall neglect, refuse, or fail to complete the remaining Work within the Contract Times (as duly adjusted pursuant to the Contract) for completion and readiness for final payment, CONTRACTOR shall pay OWNER \$972.00 for each day that expires after such time until the Work is completed and ready for final payment.
3. Liquidated damages for failing to timely attain Substantial Completion and final completion are not additive and will not be imposed concurrently.

ARTICLE 5 – CONTRACT PRICE

5.01 OWNER shall pay CONTRACTOR for completion of the Work in accordance with the Contract Documents the amounts equal to the sum of the amounts determined pursuant to Paragraph 5.01.A below:

- A. For all Work, at the prices stated in CONTRACTOR's Bid, attached hereto as an exhibit.

As provided in Paragraph 13.03 of the General Conditions, estimated quantities are not guaranteed, and determinations of actual quantities and classifications are to be made by ENGINEER as provided in Paragraph 10.06 of the General Conditions. Unit prices have been computed as provided in Paragraph 13.03 of the General Conditions.

Contract Amount of nine hundred seventy-nine thousand, two hundred fourteen dollars (\$979,214.00).

ARTICLE 6 – PAYMENT PROCEDURES

6.01 Submittal and Processing of Payments

- A. CONTRACTOR shall submit Applications for Payment in accordance with Article 15 of the General Conditions. Applications for Payment will be processed by ENGINEER as provided in the General Conditions.

6.02 Progress Payments; Retainage

- A. OWNER shall make progress payments on account of the Contract Price on the basis of CONTRACTOR's Applications for Payment in accordance with § 218.70-218.79 F.S. (Local Government Prompt Payment Act) during performance of the Work as provided in Paragraph 6.02.A.1 below, provided that such Applications for Payment have been submitted in a timely manner and otherwise meet the requirements of the Contract. All such payments will be measured by the Schedule of Values established in Paragraph 2.03 of the General Conditions (and in the case of Unit Price Work based on the number of units completed) or, in the event there is no Schedule of Values, as provided elsewhere in the Contract.
 1. Progress payments will be made in an amount equal to the percentage indicated below but, in each case, less the aggregate of payments previously made and less such amounts as OWNER may withhold, including but not limited to liquidated damages, in accordance with the Contract:
 - a. 95 percent of Work completed (with the balance being retainage)

- b. 95 percent of cost of materials and equipment not incorporated in the Work (with the balance being retainage).

6.03 Final Payment

- A. Upon final completion and acceptance of the Work in accordance with Paragraph 15.06 of the General Conditions, OWNER shall pay the remainder of the Contract Price as recommended by ENGINEER as provided in said Paragraph 15.06.

ARTICLE 7 – INTEREST

7.01 All amounts not paid when due shall bear interest at the rate of 1% percent per month in accordance with § 218.735 F.S. (Local Government Prompt Payment Act).

ARTICLE 8 – CONTRACTOR’S REPRESENTATIONS

8.01 In order to induce OWNER to enter into this Contract, CONTRACTOR makes the following representations:

- A. CONTRACTOR has examined and carefully studied the Contract Documents, and any data and reference items identified in the Contract Documents.
- B. CONTRACTOR has visited the Site, conducted a thorough, alert visual examination of the Site and adjacent areas, and become familiar with and is satisfied as to the general, local, and Site conditions that may affect cost, progress, and performance of the Work.
- C. CONTRACTOR is familiar with and is satisfied as to all Federal, State and Local Laws and Regulations that may affect cost, progress, and performance of the Work.
- D. CONTRACTOR has carefully studied all, if any: (1) reports of explorations and tests of subsurface conditions at or adjacent to the Site and all drawings of physical conditions relating to existing surface or subsurface structures at the Site that have been identified in the Supplementary Conditions, especially with respect to Technical Data in such reports and drawings, and (2) reports and drawings relating to Hazardous Environmental Conditions, if any, at or adjacent to the Site that have been identified in the Supplementary Conditions, especially with respect to Technical Data in such reports and drawings.
- E. CONTRACTOR has considered the information known to CONTRACTOR itself; information commonly known to CONTRACTORS doing business in the locality of the Site; information and observations obtained from visits to the Site; the Contract Documents; and the Site-related reports, if any, and drawings identified in the Contract Documents, with respect to the effect of such information, observations, and documents on (1) the cost, progress, and performance of the Work; (2) the means, methods, techniques, sequences, and procedures of construction to be employed by CONTRACTOR; and (3) CONTRACTOR’s safety precautions and programs.
- F. Based on the information and observations referred to in the preceding paragraph, CONTRACTOR agrees that no further examinations, investigations, explorations, tests, studies, or data are necessary for the performance of the Work at the Contract Price, within the Contract Times, and in accordance with the other terms and conditions of the Contract.
- G. CONTRACTOR is aware of the general nature of work to be performed by OWNER and others at the Site that relates to the Work as indicated in the Contract Documents.
- H. CONTRACTOR has given ENGINEER written notice of all conflicts, errors, ambiguities, or discrepancies that CONTRACTOR has discovered in the Contract Documents, and the written resolution thereof by ENGINEER is acceptable to CONTRACTOR.
- I. The Contract Documents are generally sufficient to indicate and convey understanding of all terms and conditions for performance and furnishing of the Work.
- J. CONTRACTOR’s entry into this Contract constitutes an incontrovertible representation by CONTRACTOR that without exception all prices in the Agreement are premised upon performing and furnishing the Work required by the Contract Documents.

ARTICLE 9 – CONTRACT DOCUMENTS**9.01 Contents**

- A. The Contract Documents consist of the following:
 - 1. Bid Form with Attachments (pages 00410-1 to 00410-20, inclusive).
 - 2. This Agreement (pages 00520-1 to 00520-11, inclusive).
 - 3. General Service Insurance Requirements for Contractors.
 - 4. Performance bond (pages 00610-1 to 00610-3, inclusive).
 - 5. Payment bond (pages 00620-1 to 00620-3, inclusive).
 - 6. EJCDC General Conditions (pages 00700-1 to 00700-62, inclusive).
 - 7. Supplementary Conditions (pages 00800-1 to 00800-9, inclusive).
 - 8. Summary of Work (page 01010-1, inclusive).
 - 9. Project Coordination (pages 01040-1 to 01040-3, inclusive).
 - 10. Warranties and Manuals (page 01350-1, inclusive).
 - 11. Temporary Facilities (pages 01500-1 to 01500-4, inclusive).
 - 12. Project Closeout (pages 01700-1 to 01700-3, inclusive).
 - 13. Record Documents (pages 01750-1 to 01750-3, inclusive).
 - 14. Drawings consisting of 52 sheets with each sheet bearing the following general title: Old Bethel Road Sidewalk Design, (incorporated by reference). Technical specifications are included as part of the drawing package.
 - 15. Addenda (numbers 1 to 2, inclusive).
 - 16. The following which may be delivered or issued on or after the Effective Date of the Contract and are not attached hereto:
 - a. Notice to Proceed.
 - b. Work Change Directives.
 - c. Contractor's Application for Payment
 - d. Change Orders.
 - e. Field Orders.
- B. The documents listed in Paragraph 9.01.A are attached to this Agreement (except as expressly noted otherwise above).
- C. There are no Contract Documents other than those listed above in this Article 9.
- D. The Contract Documents may only be amended, modified, or supplemented as provided in the General Conditions.

ARTICLE 10 – MISCELLANEOUS**10.01 Terms**

- A. Terms used in this Agreement will have the meanings stated in the General Conditions and the Supplementary Conditions.

10.02 Assignment of Contract

- A. Unless expressly agreed to elsewhere in the Contract, no assignment by a party hereto of any rights under or interests in the Contract will be binding on another party hereto without the written consent of the party sought to be bound; and, specifically but without limitation, money that may become due and money that is due may not be assigned without such consent (except to the extent that the effect of this restriction may be limited by law), and unless specifically stated to the contrary in any written consent to an assignment, no assignment will release or discharge the assignor from any duty or responsibility under the Contract Documents.

10.03 Successors and Assigns

- A. OWNER and CONTRACTOR each binds itself, its successors, assigns, and legal representatives to the other party hereto, its successors, assigns, and legal representatives in respect to all covenants, agreements, and obligations contained in the Contract Documents.

10.04 Severability

- A. Any provision or part of the Contract Documents held to be void or unenforceable under any Law or Regulation shall be deemed stricken, and all remaining provisions shall continue to be valid and binding upon OWNER and CONTRACTOR, who agree that the Contract Documents shall be reformed to replace such stricken provision or part thereof with a valid and enforceable provision that comes as close as possible to expressing the intention of the stricken provision.

10.05 CONTRACTOR's Certifications

- A. CONTRACTOR certifies that it has not engaged in corrupt, fraudulent, collusive, or coercive practices in competing for or in executing the Contract. For the purposes of this Paragraph 10.05:
 - 1. "corrupt practice" means the offering, giving, receiving, or soliciting of any thing of value likely to influence the action of a public official in the bidding process or in the Contract execution;
 - 2. "fraudulent practice" means an intentional misrepresentation of facts made (a) to influence the bidding process or the execution of the Contract to the detriment of OWNER, (b) to establish Bid or Contract prices at artificial non-competitive levels, or (c) to deprive OWNER of the benefits of free and open competition;
 - 3. "collusive practice" means a scheme or arrangement between two or more Bidders, with or without the knowledge of OWNER, a purpose of which is to establish Bid prices at artificial, non-competitive levels; and
 - 4. "coercive practice" means harming or threatening to harm, directly or indirectly, persons or their property to influence their participation in the bidding process or affect the execution of the Contract.

10.06 Independent CONTRACTORS

- A. CONTRACTOR enters into the Contract as, and shall continue to be, an independent CONTRACTOR. All services shall be performed only by CONTRACTOR and CONTRACTOR's employees. Under no circumstances shall CONTRACTOR or any of CONTRACTOR's employees look to the OWNER as his/her employer, or as partner, agent or principal. Neither CONTRACTOR, nor any of CONTRACTOR's employees, shall be entitled to any benefits accorded to the OWNER's employees, including without limitation worker's compensation, disability insurance, vacation or sick pay. CONTRACTOR shall be responsible for providing, at CONTRACTOR's expense, and in CONTRACTOR's name, unemployment, disability, worker's compensation and other insurance as well as licenses and permits usual and necessary for conducting the services to be provided under this Contract.

10.07 Audit Provision

- A. The OWNER and/or its designee shall have the right from time to time at its sole expense to audit the compliance by the CONTRACTOR with the terms, conditions, obligations, limitations, restrictions and requirements of this Agreement and such right shall extend for a period of three (3) years after termination of this Agreement.
- B. Pursuant to section 20.055(5), Florida Statutes, the OWNER, its contractors and subcontractors have a duty to cooperate with the inspector general in any investigation, audit, inspection, review, or hearing. By entering into the Agreement, the CONTRACTOR understands and agrees to comply with this requirement and will incorporate in all subcontracts the obligation to comply with section 20.055(5), Florida Statutes.

10.08 Public Records

- A. CONTRACTOR shall adhere to the Public Records law of Florida.
- B. Specifically, CONTRACTOR must:
 - 1. Keep and maintain public records require by the OWNER to perform the service.
 - 2. Upon request from the OWNER's custodian of public records, provide the OWNER with a copy of the requested records or allow the records to be inspected or copied within a reasonable time at a cost that does not exceed the cost provided in chapter 119 Florida Statutes or as otherwise provided by law.

3. Ensure that public records that are exempt or confidential and exempt from public records disclosure requirements are not disclosed except as authorized by law for the duration of the Agreement term and following completion of the Agreement if the CONTRACTOR does not transfer the records to the OWNER.
4. Upon completion of the Agreement, transfer, at no cost, to the OWNER all public records in possession of the CONTRACTOR or keep and maintain public records required by the OWNER to perform the service. If the CONTRACTOR transfers all public records to the OWNER upon completion of the Contract, the CONTRACTOR shall destroy any duplicate public records that are exempt or confidential and exempt from public records disclosure requirements. If the CONTRACTOR keeps and maintains public records upon completion of the Contract, the CONTRACTOR shall meet all applicable requirements for retaining the public records. All records stored electronically must be provided to the OWNER, upon the request from the OWNER's custodian of public records, in a format that is compatible with the information technology system of the OWNER.

c. IF THE CONTRACTOR HAS QUESTIONS REGARDING THE APPLICATION OF CHAPTER 119, FLORIDA STATUTES, TO THE CONTRACTOR'S DUTY TO PROVIDE PUBLIC RECORDS RELATING TO THIS CONTRACT, CONTACT THE CUSTODIAN OF PUBLIC RECORDS AT OKALOOSA COUNTY RISK MANAGEMENT DEPARTMENT 302 N. WILSON ST., CRESTVIEW, FL 32536 PHONE (850) 689-5977 riskinfo@myokaloosa.com.

10.09 Third Party Beneficiaries

- A. It is specifically agreed between the parties executing this Agreement that it is not intended by any of the provisions of any part of the Agreement to create in the public or any member thereof, a third-party beneficiary under this Agreement, or to authorize anyone not a part to this Agreement to maintain a suit for personal injuries or property damage pursuant to the terms or provision of this Agreement.

10.10 Other Provisions

- A. OWNER stipulates that if the General Conditions that are made a part of this Contract are based on EJCDC® C-700, Standard General Conditions for the Construction Contract, published by the ENGINEERS Joint Contract Documents Committee®, and if OWNER is the party that has furnished said General Conditions, then OWNER has plainly shown all modifications to the standard wording of such published document to the CONTRACTOR, through a process such as highlighting or "track changes" (redline/strikeout), or in the Supplementary Conditions.
- B. The individual signing this Agreement on behalf of CONTRACTOR represents and warrants that he or she is duly authorized and has legal capacity to execute and deliver this Agreement. The CONTRACTOR represents and warrants to the OWNER that the execution and delivery of the Agreement and the performance of CONTRACTOR's obligations hereunder have been duly authorized and that the Agreement is a valid and legal agreement binding on the CONTRACTOR and enforceable in accordance with its terms.
- C. The waiver by a party of any breach or default in performance shall not be deemed to constitute a waiver of any other or succeeding breach or default. The failure of the OWNER to enforce any of the provisions hereof shall not be construed to be a waiver of the right of the OWNER thereafter to enforce such provisions.
- D. All notices required by this Agreement shall be in writing to the representatives listed below:

AUTHORIZED REPRESENTATIVES:

OWNER:

Chairman – Board of County CommissionersAddress1250 N. Eglin ParkwayShalimar, FL 32579Phone850-651-7105

CONTRACTOR:

LAS Contracting Corp.Address13701 N. Nebraska Ave.Tampa, FL 33613Phone813-240-1069

10.11 Equal Opportunity Employment

A. During the performance of this CONTRACT, the contractor agrees as follows:

1. The contractor will not discriminate against any employee or applicant for employment because of race, color, religion, sex, or national origin. The contractor will take affirmative action to ensure that applicants are employed, and that employees are treated during employment without regard to their race, color, religion, sex, or national origin. Such action shall include, but not be limited to the following: employment, upgrading, demotion, or transfer; recruitment or recruitment advertising; layoff or termination; rates of pay or other forms of compensation; and selection for training, including apprenticeship. The contractor agrees to post in conspicuous places, available to employees and applicants for employment, notices to be provided setting forth the provisions of this nondiscrimination clause.
2. The contractor will, in all solicitations or advertisements for employees placed by or on behalf of the contractor, state that all qualified applicants will receive considerations for employment without regard to race, color, religion, sex, or national origin.
3. The contractor will send to each labor union or representative of workers with which he has a collective bargaining agreement or other contract or understanding, a notice to be provided advising the said labor union or workers' representatives of the contractor's commitments under this section, and shall post copies of the notice in conspicuous places available to employees and applicants for employment.
4. The contractor will comply with all provisions of Executive Order 11246 of September 24, 1965, and of the rules, regulations, and relevant orders of the Secretary of Labor.
5. The contractor will furnish all information and reports required by Executive Order 11246 of September 24, 1965, and by rules, regulations, and orders of the Secretary of Labor, or pursuant thereto, and will permit access to his books, records, and accounts by the administering agency and the Secretary of Labor for purposes of investigation to ascertain compliance with such rules, regulations, and orders.
6. In the event of the contractor's noncompliance with the nondiscrimination clauses of this contract or with any of the said rules, regulations, or orders, this contract may be canceled, terminated, or suspended in whole or in part and the contractor may be declared ineligible for further Government contracts or federally assisted construction contracts in accordance with procedures authorized in Executive Order 11246 of September 24, 1965, and such other sanctions may be imposed and remedies invoked as provided in Executive Order 11246 of September 24, 1965, or by rule, regulation, or order of the Secretary of Labor, or as otherwise provided by law.
7. The contractor will include the portion of the sentence immediately preceding paragraph (1) and the provisions of paragraphs (1) through (7) in every subcontract or purchase order unless exempted by rules, regulations, or orders of the Secretary of Labor issued pursuant to section 204 of Executive Order 11246 of September 24, 1965, so that such provisions will be binding upon each subcontractor or vendor. The contractor will take such action with respect to any subcontract or purchase order as the administering agency may direct as a means of enforcing

such provisions, including sanctions for noncompliance: provided, however, that in the event a contractor becomes involved in, or is threatened with, litigation with a subcontractor or vendor as a result of such direction by the administering agency the contractor may request the United States to enter into such litigation to protect the interests of the United States.

10.12 Federal Fair Labor Standards Act (Federal Minimum Wage)

- A. All contracts and subcontracts that result from this solicitation incorporate by reference the provisions of 29 CFR part 201, the Federal Fair Labor Standards Act (FLSA), with the same force and effect as if given in full text. The FLSA sets minimum wage, overtime pay, recordkeeping, and child labor standards for full and part time workers.
- B. The CONTRACTOR has full responsibility to monitor compliance to the referenced statute or regulation. The CONTRACTOR must address any claims or disputes that arise from this requirement directly with the U.S. Department of Labor – Wage and Hour Division.

10.13 Occupational Safety and Health Act of 1970

- A. All contracts and subcontracts that result from this solicitation incorporate by reference the requirements of 29 CFR Part 1910 with the same force and effect as if given in full text. CONTRACTOR must provide a work environment that is free from recognized hazards that may cause death or serious physical harm to the employee. The CONTRACTOR retains full responsibility to monitor its compliance and their subcontractor's compliance with the applicable requirements of the Occupational Safety and Health Act of 1970 (20 CFR Part 1910). CONTRACTOR must address any claims or disputes that pertain to a referenced requirement directly with the U.S. Department of Labor – Occupational Safety and Health Administration.

10.14 E-Verify

- A. Enrollment and verification requirements.
 - 1. If the CONTRACTOR is not enrolled as a Federal Contractor in E-Verify at time of contract award, the CONTRACTOR shall-
 - a. Enroll. Enroll as a Federal Contractor in the E-Verify Program within thirty (30) calendar days of Contract award;
 - b. Verify all new employees. Within ninety (90) calendar days of enrollment in the E-Verify program, begin to use E-Verify to initiate verification of employment eligibility of all new hires of the CONTRACTOR, who are working in the United States, whether or not assigned to the Contract, within three (3) business days after the date of hire (but see paragraph (3.) of this section); and,
 - c. Verify employees assigned to the Contract. For each employee assigned to the Contract, initiate verification within ninety (90) calendar days after date of enrollment or within thirty (30) calendar days of the employee's assignment to the Contract, whichever date is later (but see paragraph (4.) of this section.)
 - 2. If the CONTRACTOR is enrolled as a Federal Contractor in E-Verify at time of Contract award, the CONTRACTOR shall use E-Verify to initiate verification of employment eligibility of
 - a. All new employees.
 - 1) Enrolled ninety (90) calendar days or more. The CONTRACTOR shall initiate verification of all new hires of the CONTRACTOR, who are working in the United States, whether or not assigned to the Contract, within three (3) business days after the date of hire (but see paragraph (3.) of this section); or
 - 2) Enrolled less than ninety (90) calendar days. Within ninety (90) calendar days after enrollment as a Federal Contractor in E-Verify, the CONTRACTOR shall initiate verification of all new hires of the CONTRACTOR, who are working in the United States, whether or not assigned to the contract, within three (3) business days after the date of hire (but see paragraph (3.) of this section); or
 - b. Employees assigned to the Contract. For each employee assigned to the Contract, the CONTRACTOR shall initiate verification within ninety (90) calendar days after date of

Contract award or within thirty (30) days after assignment to the Contract, whichever date is later (but see paragraph (4.) of this section.)

3. If the CONTRACTOR is an institution of higher education (as defined at 20 U.S.C. 1001(a)); a State of local government or the government of a Federally recognized Indian tribe, or a surety performing under a takeover agreement entered into with a Federal agency pursuant to a performance bond, the CONTRACTOR may choose to verify only employees assigned to the Contract, whether existing employees or new hires. The CONTRACTOR shall follow the applicable verification requirements of (1.) or (2.), respectively, except that any requirement for verification of new employees applies only to new employees assigned to the Contract.
4. Option to verify employment eligibility of all employees. The CONTRACTOR may elect to verify all existing employees hired after November 6, 1986 (after November 27, 2009, in the Commonwealth of the Northern Mariana Islands), rather than just those employees assigned to the Contract. The CONTRACTOR shall initiate verification for each existing employee working in the United States who was hired after November 6, 1986 (after November 27, 2009, in the Commonwealth of the Northern Mariana Islands), within one hundred eighty (180) calendar days of-
 - a. Enrollment in the E-Verify program; or
 - b. Notification to E-Verify Operations of the CONTRACTOR's decision to exercise this option, using the Contract information provided in the E-Verify program Memorandum of Understanding (MOU)
5. The CONTRACTOR shall comply, for the period of performance of this Contract, with the requirements of the E-Verify program MOU.
 - a. The Department of Homeland Security (DHS) or the Social Security Administration (SSA) may terminate the CONTRACTOR's MOU and deny access to the E-Verify system in accordance with the terms of the MOU. In such case, the CONTRACTOR, will be referred to a suspension or debarment official.
 - b. During the period between termination of the MOU and a decision by the suspension or debarment official whether to suspend or debar, the CONTRACTOR is excused from its obligations under paragraph (b) of this clause. If the suspension or debarment official determines not to suspend or debar the CONTRACTOR, then the CONTRACTOR must reenroll in E-Verify.
 - c. Web site. Information on registration for and use of the E-Verify program can be obtained via the Internet at the Department of Homeland Security Web site: <http://www.dhs.gov/E-Verify>.
 - d. Individuals previously verified. The CONTRACTOR is not required by this clause to perform additional employment verification using E-Verify for any employee-
 - 1) Whose employment eligibility was previously verified by the CONTRACTOR through the E-Verify program;
 - 2) Who has been granted and holds an active U.S. Government security clearance for access to confidential, secret, or top-secret information in accordance with the National Industrial Security Program Operating Manual; or
 - 3) Who has undergone a completed background investigation and been issued credentials pursuant to Homeland Security Presidential Directive (HSPD)-12. Policy for a Common Identification Standard for Federal Employees and Contractors.
6. Subcontracts. The CONTRACTOR shall include the requirements of this clause, including this paragraph (appropriately modified for identification of the parties in each subcontract) that-
 - a. Is for
 - 1) Commercial and noncommercial services (except for commercial services that are part of the purchase of a COTS item (or an item that would be a COTS item, but for

minor modifications), performed by the COTS provider, and are normally provided for that COTS item); or


- 2) Construction;
- b. Has a value of more than \$3,500; and
- c. Includes work performed in the United States.

IN WITNESS WHEREOF, OWNER and CONTRACTOR have signed this Agreement.


This Agreement will be effective on October 18, 2022 (which is the Effective Date of the Contract).


OWNER:

BOARD OF COUNTY COMMISSIONERS
OKALOOSA COUNTY, FLORIDA


Mel Ponder, Chairman



Attest: 
JD Peacock II, Clerk of Courts



Address for giving notices:

1250 N. Eglin Parkway

Shalimar, FL 32579

CONTRACTOR:

LAS Contracting Corp

By: 

Title: President
(If CONTRACTOR is a corporation, a partnership, or a joint venture, attach evidence of authority to sign.)

Attest: 

Title: V.P.

Address for giving notices:

13701 N. Nebraska Ave.

Tampa, FL 33613

License No.: 59-3674850-0001

END OF DOCUMENT 00520 –AGREEMENT BETWEEN OWNER &
CONTRACTOR FOR CONSTRUCTION
CONTRACT

GENERAL SERVICES INSURANCE REQUIREMENTS

CONTRACTORS INSURANCE

1. The Contractor shall not commence any work in connection with this Agreement until obtaining all required insurance and the certificate of insurance has been approved by the Okaloosa County Risk Manager or designee.
2. All insurance policies shall be with insurers authorized to do business in the State of Florida and having a minimum rating of A, Class X in the Best Key Rating Guide published by A.M. Best & Co. Inc.
3. All insurance shall include the interest of all entities named and their respective officials, employees & volunteers of each and all other interests as may be reasonably required by Okaloosa County. The coverage afforded the Additional Insured under this policy shall be primary insurance. If the Additional Insured have other insurance that is applicable to the loss, such other insurance shall be on an excess or contingent basis. The amount of the company's liability under this policy shall not be reduced by the existence of such other insurance.
4. Where applicable the County shall be shown as an Additional Insured with a waiver of subrogation on the Certificate of Insurance.
5. The County shall retain the right to reject all insurance policies that do not meet the requirement of this Agreement. Further, the County reserves the right to change these insurance requirements with 60-day prior written notice to the Contractor.
6. The County reserves the right at any time to require the Contractor to provide copies of any insurance policies to document the insurance coverage specified in this Agreement.
7. Any subsidiaries used shall also be required to obtain and maintain the same insurance requirements as are being required herein of the Contractor.
8. Any exclusions or provisions in the insurance maintained by the Contractor that excludes coverage for work contemplated in this agreement shall be deemed unacceptable and shall be considered a breach of contract.

WORKERS' COMPENSATION INSURANCE

1. The Contractor shall secure and maintain during the life of this Agreement Workers' Compensation insurance for all of his employees employed for the project or any site connected with the work, including supervision, administration or management of this

project and in case any work is sublet, with the approval of the County, the Contractor shall require the Subcontractor similarly to provide Workers' Compensation insurance for all employees employed at the site of the project, and such evidence of insurance shall be furnished to the County not less than ten (10) days prior to the commencement of any and all sub-contractual Agreements which have been approved by the County.

2. Contractor must be in compliance with all applicable State and Federal workers' compensation laws, including the U.S. Longshore Harbor Workers' Act or Jones Act, if applicable.
3. No class of employee, including the Contractor himself, shall be excluded from the Workers' Compensation insurance coverage. The Workers' Compensation insurance shall also include Employer's Liability coverage.
4. A Waiver of Subrogation is required to be shown on all Workers Compensation Certificates of Insurance.

BUSINESS AUTOMOBILE LIABILITY

Coverage must be afforded for all Owned, Hired, Scheduled, and Non-Owned vehicles for Bodily Injury and Property Damage in an amount not less than \$1,000,000 (One Million Dollars) combined single limit each accident. If the contractor does not own vehicles, the contractor shall maintain coverage for Hired & Non-Owned Auto Liability, which may be satisfied by way of endorsement to the Commercial General Liability policy or separate Business Auto Policy. Contractor must maintain this insurance coverage throughout the life of this Agreement.

COMMERCIAL GENERAL LIABILITY INSURANCE

1. The Contractor shall carry Commercial General Liability insurance against all claims for Bodily Injury, Property Damage and Personal and Advertising Injury caused by the Contractor.
2. Commercial General Liability coverage shall include the following:
 - 1.) Premises & Operations Liability
 - 2.) Bodily Injury and Property Damage Liability
 - 3.) Independent Contractors Liability
 - 4.) Contractual Liability
 - 5.) Products and Completed Operations Liability
3. Contractor shall agree to keep in continuous force Commercial General Liability coverage for the length of the contract.

INSURANCE LIMITS OF LIABILITY

The insurance required shall be written for not less than the following, or greater if required by law and shall include Employer's liability with limits as prescribed in this contract:

LIMIT

- | | | |
|----|---------------------------------|--|
| 1. | Workers' Compensation | |
| | 1.) State | Statutory |
| | 2.) Employer's Liability | \$500,000 each accident |
| 2. | Business Automobile | \$1,000,000 each accident
(A combined single limit) |
| 3. | Commercial General Liability | \$1,000,000 each occurrence
Bodily Injury & Property
Damage
\$1,000,000 each occurrence
Products and completed
operations |
| 4. | Personal and Advertising Injury | \$1,000,000 each occurrence |

NOTICE OF CLAIMS OR LITIGATION

The Contractor agrees to report any incident or claim that results from performance of this Agreement. The County representative shall receive written notice in the form of a detailed written report describing the incident or claim within ten (10) days of the Contractor's knowledge. In the event such incident or claim involves injury and/or property damage to a third party, verbal notification shall be given the same day the Contractor becomes aware of the incident or claim followed by a written detailed report within ten (10) days of verbal notification.

INDEMNIFICATION & HOLD HARMLESS

To the fullest extent permitted by law, Contractor shall indemnify and hold harmless the County, its officers and employees from liabilities, damages, losses, and costs including but not limited to reasonable attorney fees, to the extent caused by the negligence, recklessness, or wrongful conduct of the Contractor and/or other persons employed or utilized by the Contractor in the performance of this contract.

CERTIFICATE OF INSURANCE

1. Certificates of insurance indicating the job site and evidencing all required coverage must be submitted not less than 10 days prior to the commencement of any of the work. The certificate holder(s) shall be as follows: Okaloosa County, 5479A Old Bethel Road, Crestview, Florida, 32536.

2. The contractor shall provide a Certificate of Insurance to the County with a thirty (30) day prior written notice of cancellation; ten (10) days' prior written notice if cancellation is for nonpayment of premium.
3. In the event that the insurer is unable to accommodate the cancellation notice requirement, it shall be the responsibility of the contractor to provide the proper notice. Such notification shall be in writing by registered mail, return receipt requested, and addressed to the Okaloosa County Purchasing Department at 5479-A Old Bethel Road, Crestview, FL 32536.
4. In the event the contract term goes beyond the expiration date of the insurance policy, the contractor shall provide the County with an updated Certificate of insurance no later than ten (10) days prior to the expiration of the insurance currently in effect. The County reserves the right to suspend the contract until this requirement is met.
5. The certificate shall indicate if coverage is provided under a claims-made or occurrence form. If any coverage is provided on a claims-made form, the certificate will show a retroactive date, which should be the same date of the initial contract or prior.
6. All certificates shall be subject to Okaloosa County's approval of adequacy of protection.
7. All deductibles or self-insured retentions (SIRs), whether approved by Okaloosa County or not, shall be the Contractor's full responsibility.
8. In no way will the entities listed as Additional Insured be responsible for, pay for, be damaged by, or limited to coverage required by this schedule due to the existence of a deductible or SIR.

GENERAL TERMS

Any type of insurance or increase of limits of liability not described above which, the Contractor required for its own protection or on account of statute shall be its own responsibility and at its own expense.

Any exclusions or provisions in the insurance maintained by the contractor that excludes coverage for work contemplated in this contract shall be deemed unacceptable and shall be considered a breach of contract.


The carrying of the insurance described shall in no way be interpreted as relieving the Contractor of any responsibility under this contract.

Should the Contractor engage a subcontractor or sub-subcontractor, the same conditions will apply under this Agreement to each subcontractor and sub-subcontractor.

The Contractor hereby waives all rights of subrogation against Okaloosa County and its employees under all the foregoing policies of insurance.

EXCESS/UMBRELLA INSURANCE

The Contractor shall have the right to meet the liability insurance requirements with the purchase of an EXCESS/UMBRELLA insurance policy. In all instances, the combination of primary and EXCESS/UMBRELLA liability coverage must equal or exceed the minimum liability insurance limits stated in this Agreement. An Excess liability policy must be submitted indicating which policy it applies to.



INVITATION TO BID (ITB) & RESPONDENT'S ACKNOWLEDGEMENT

ITB TITLE:
Old Bethel Road Sidewalk Improvements

ITB NUMBER:
ITB PW 56-22

ISSUE DATE: July 25, 2022

LAST DAY FOR QUESTIONS: August 19, 2022 3:00 P.M. est

ITB OPENING DATE & TIME: August 31, 2022 3:00 P.M. est

NOTE: BIDS RECEIVED AFTER THE BID OPENING DATE & TIME WILL NOT BE CONSIDERED.

Okaloosa County, Florida solicits your company to submit a bid on the above referenced goods or services. All terms, specifications and conditions set forth in this ITB are incorporated into your response. A bid will not be accepted unless all conditions have been met. All bids must have an authorized signature in the space provided below. All bids must be submitted electronically by the time and date listed above. Bids may not be withdrawn for a period of ninety (90) days after the bid opening unless otherwise specified.

RESPONDENT ACKNOWLEDGEMENT FORM BELOW MUST BE COMPLETED, SIGNED, AND RETURNED AS PART OF YOUR BID. BIDS WILL NOT BE ACCEPTED WITHOUT THIS FORM, SIGNED BY AN AUTHORIZED AGENT OF THE RESPONDENT.

COMPANY NAME LAS CONTRACTING CORP

MAILING ADDRESS 13701 N. NEBRASKA AVE 102

CITY, STATE, ZIP Tampa, FL. 33613

FEDERAL EMPLOYER'S IDENTIFICATION NUMBER (FEIN): 59-3674850

TELEPHONE NUMBER: 813-240-1069 EXT: N/A FAX: N/A

EMAIL: LASCONTRACTING@AOL.COM

I CERTIFY THAT THIS BID IS MADE WITHOUT PRIOR UNDERSTANDING, AGREEMENT, OR CONNECTION WITH ANY OTHER RESPONDENT SUBMITTING A BID FOR THE SAME MATERIALS, SUPPLIES, EQUIPMENT OR SERVICES, AND IS IN ALL RESPECTS FAIR AND WITHOUT COLLUSION OR FRAUD. I AGREE TO ABIDE BY ALL TERMS AND CONDITIONS OF THIS BID AND CERTIFY THAT I AM AUTHORIZED TO SIGN THIS BID FOR THE RESPONDENT.

AUTHORIZED SIGNATURE: [Signature] TYPED OR PRINTED JACK GARDNER

NAME

TITLE: PRESIDENT DATE: 8-29-22

ADVERTISEMENT FOR BIDS

**OKALOOSA BOARD OF COUNTY COMMISSIONERS
CRESTVIEW, FLORIDA
ITB PW 56-22 Old Bethel Road Sidewalk Improvements**

Notice is hereby given that Sealed Bids for the construction of the Old Bethel Road Sidewalk Improvements ITB PW 56-22 will be received by Board of County Commissioners of Okaloosa County at the Okaloosa County Purchasing Department until 03:00 PM local time on August 31, 2022, at which time the Bids received will be publicly opened and read. No bids will be received after the designated time. The project consists of constructing sidewalk along Old Bethel Rd going west from Davidson Middle School and other associated work including clearing and grubbing, earthwork, maintenance of traffic, concrete retaining walls, and other improvements. The work is further defined as shown on the Plans and as described by the Contract Documents.

Bids will be received for a single prime Contract. Bids shall be on a unit price basis as indicated in the Bid Form. All terms, specifications and conditions set forth in this ITB are incorporated into your response. A bid will not be accepted unless all conditions have been met.

Bid security shall be furnished in accordance with the Instructions to Bidders.

Interested respondents desiring consideration shall submit their response online at Vendor Registry through the link provided below:

<https://vrapp.vendorregistry.com/Bids/View/BidsList?BuyerId=21d474a1-e536-4f4d-9f2c-77c3b1e3c683>

The Okaloosa BCC reserves the right to award the bid to the lowest responsive, responsible Bidder and to waive any irregularity or technicality in bids received. Okaloosa County shall be the sole judge of the bid and the resulting negotiated agreement that is in its best interest and its decision shall be final. Bids may not be withdrawn for a period of sixty (60) days after the bid opening unless otherwise specified.

**OKALOOSA COUNTY
BOARD OF COUNTY COMMISSIONERS**

Jeffrey Hyde, Purchasing Manager

Date

Okaloosa County
Board of County Commissioners
Mel Ponder, Chairman

END OF DOCUMENT 00020 - ADVERTISEMENT FOR BIDS

TABLE OF CONTENTS	Page
Instructions to Bidders	00100-01 thru 00100-15
Bid Form with Attachments	00410-01 thru 00410-17
Bid Bond	00430-01 thru 00430-02
Agreement Between Owner and Contractor for Construction Contract	00520-01 thru 00520-11
Performance Bond	00610-01 thru 00610-03
Payment Bond	00620-01 thru 00620-03
General Conditions	00700-01 thru 00700-62
Supplementary Conditions	00800-01 thru 00800-10
Summary of Work	01010-1
Project Coordination	01040-01 thru 01040-03
Warranties and Manuals	01350-1
Temporary Facilities	01500-01 thru 01500-03
Project Close-out	01700-01 thru 01700-03
Record Documents	01750-01 thru 01750-03

Drawings - Consisting of 52 sheets with each sheet bearing the following general title: Old Bethel Rd Sidewalk Improvements; technical specifications referenced in drawings

DOCUMENT 00100 – INSTRUCTIONS TO BIDDERS
--

ARTICLE 1 – DEFINED TERMS

Terms used in these Instructions to BIDDERS will have the meanings indicated in the General Conditions and Supplementary Conditions. Additional terms used in these Instructions to Bidders have the meanings indicated below which are applicable to both the singular and plural thereof.

- 1.01 Issuing Office – The office from which the Bidding Documents are to be issued and where the bidding procedures are to be administered; the Okaloosa County Purchasing Department, 5479A Old Bethel Road, Crestview, FL 32536.
- 1.02 BIDDER – The individual or entity who submits a Bid directly to OWNER.
- 1.03 Successful BIDDER – The lowest, responsible BIDDER submitting a responsive bid to whom OWNER (on the basis of OWNER's evaluation as hereinafter provided) makes an award.
- 1.04 OWNER – Okaloosa County, a political subdivision of the State of Florida, by and through its Board of County Commissioners.
- 1.05 Vendor Registry – An entity providing service to the OWNER by making available an internet presence and platform for the dissemination of OWNER's solicitations and procurement documents including the receipt of responses to an Invitation of Bid, Invitation to Quote, Invitation to Negotiate, and Request for Proposal. Bidders will be required to register with Vendor Registry (www.vendorregistry.com) prior to use. There is no charge or fee to BIDDERS for the use of Vendor Registry.

ARTICLE 2 – COPIES OF BIDDING DOCUMENTS

- 2.01 Complete sets of the Bidding Documents in electronic format are available over the internet from Vendor Registry (www.vendorregistry.com).
- 2.02 Complete sets of Bidding Documents must be used in preparing Bids; neither OWNER nor ENGINEER assume any responsibility for errors or misinterpretations resulting from the use of incomplete sets of Bidding Documents.
- 2.03 OWNER and ENGINEER, in making copies of Bidding Documents available on the above terms, do so only for the purpose of obtaining Bids for the Work and do not authorize or confer a license or grant for any other use.

ARTICLE 3 – CONE OF SILENCE CLAUSE

- 3.01 The Okaloosa County Board of County Commissioners has established a solicitation silence policy (Cone of Silence Clause) that prohibits oral and written communication regarding all formal solicitations for goods and services (Invitation to Bid, Request for Proposals, Invitation to Quote, Invitation to Negotiate, and Request for Qualifications) issued by the Board through the County Purchasing Department. The period commences from the time of advertisement until CONTRACT award. Each BIDDER shall review and sign the enclosed form indicating that the BIDDER agrees to abide by the County's "Cone of Silence Clause" and understands that a violation of this policy shall result in disqualification of their bid.

ARTICLE 4 – QUALIFICATIONS OF BIDDERS

- 4.01 A person or affiliate who has been placed on the convicted vendor list following a conviction for a public entity crime may not submit a bid on a contract to provide any goods or services to a public entity, may

not submit a bid on a contract with a public entity for the construction or repair of a public building or public work, may not submit bids on leases of real property to the public entity, may not be awarded or perform work as contractor, supplier, subcontractor, or consultant under a contract with any public entity, and may not transact business with any public entity in excess of the threshold amount provided in Section 287.017, Florida Statutes, for CATEGORY TWO for the period of 36 months from the date of being placed on the convicted vendor list.

- 4.02 An entity or affiliate who has been placed on the discriminatory vendor list may not submit a bid on a contract to provide goods or services to a public entity, may not submit a bid on a contract with a public entity for the construction or repair of a public building or public work, may not submit bids on leases of real property to a public entity, may not award or perform work as a contractor, supplier, subcontractor, or consultant under contract with any public entity, and may not transact business with any public entity.
- 4.03 Florida Statutes 607.1501 requires that all vendors who wish to do business in the State of Florida be licensed to do business through the Department of State of Florida and be in good standing with the State of Florida. As such, to do business with Okaloosa County a vendor must provide a Certificate of Good Standing with their bid/proposal package to the County. For more information on doing business in the State of Florida, please refer to the Florida Department of State. The website to register is <https://dos.myflorida.com/sunbiz/manage-business/certification/>.
- 4.04 To demonstrate qualifications to perform the Work, each BIDDER must be prepared to submit within five days of OWNER's request written evidence such as financial data, previous experience, present commitments and other such data as may be called for below. The successful low BIDDER will be required to acquire a county business license before the contract will be awarded.

ARTICLE 5 – PRE-BID CONFERENCE

- 5.01 Deleted

ARTICLE 6 – SITE AND OTHER AREAS; EXISTING SITE CONDITIONS; EXAMINATION OF SITE; OWNER'S SAFETY PROGRAM; OTHER WORK

6.01 Site and Other Areas

- A. The Site is identified in the Bidding Documents. By definition, the Site includes rights-of-way, easements, and other lands furnished by Owner for the use of the Contractor. Any additional lands required for temporary construction facilities, construction equipment, or storage of materials and equipment, and any access needed for such additional lands, are to be obtained and paid for by Contractor.

6.02 Existing Site Conditions

- A. Subsurface and Physical Conditions; Hazardous Environmental Conditions
1. The Supplemental Conditions Identify:
 - a. those reports known to Owner of explorations and test of subsurface conditions at or adjacent to the site.
 - b. those drawings known to Owner of physical conditions relating to existing surface or subsurface structures at the Site (except Underground Facilities)
 - c. reports and drawings known to Owner relating to Hazardous Environmental Conditions that have been identified at or adjacent to the Site.
 - d. Technical Data contained in such reports and drawings.
 2. Owner will make copies of reports and drawings referenced above available to any Bidder on request. These reports and drawings are not part of the Contract Documents, but the

Technical Data contained therein upon whose accuracy Bidder is entitled to rely as provided in the General Conditions, has been identified and established in the Supplementary Conditions. Bidder is responsible for any interpretations or conclusion Bidder draws from any Technical Data or any other data, interpretations, opinions, or information contained in such reports or shown or indicated in such drawings.

3. If the Supplementary Conditions do not identify Technical Data, the default definition of Technical Data set forth in Article 1 of the General Conditions will apply.

Underground Facilities: Information and data shown or indicated in the Bidding Documents with respect to existing Underground Facilities at or adjacent or contiguous to the Site are set forth in the Contract Documents and are based upon information and data furnished to OWNER and ENGINEER by owners of such Underground Facilities, including OWNER, or others.

- B. Adequacy of Data: Provisions concerning responsibilities for the adequacy of data furnished to prospective Bidders with respect to subsurface conditions, other physical conditions, and Underground Facilities, and possible changes in the Bidding Documents due to differing or unanticipated subsurface or physical conditions appear in Paragraphs 5.03, 5.04, and 5.05 of the General Conditions. Provisions concerning responsibilities for the adequacy of data furnished to prospective Bidders with respect to a Hazardous Environmental Condition at the Site, if any, and possible changes in the Contract Documents due to any Hazardous Environmental Condition uncovered or revealed at the Site which was not shown or indicated in the Drawings or Specifications or identified in the Contract Documents to be within the scope of the Work, appear in Paragraph 5.06 of the General Conditions.

6.03 Site Visit and Testing by Bidders

- A. Bidder shall conduct the required Site visit during normal working hours, and shall not disturb any ongoing operations at the Site.
- B. Bidder is not required to conduct any subsurface testing, or exhaustive investigations of Site conditions.
- C. On request, and to the extent Owner has control over the Site, and schedule permitting, the Owner will provide Bidder access to the Site to conduct such additional examinations, investigations, explorations, test, and studies as Bidder deems necessary for preparing and submitting a successful Bid. Owner will not have any obligation to grant such access if doing so is not practical because of existing operations, security or safety concerns, or restraints on Owner's authority regarding the Site.
- D. Bidder shall comply with all applicable Laws and Regulations regarding excavation and location of utilities, obtain all permits, and comply with all terms and conditions established by Owner or by property owners or other entities controlling the Site with respect to schedule, access, existing operations, security, liability insurance, and applicable safety programs.
- E. Bidder shall fill all holes and clean up and restore the Site to its former condition upon completion of such explorations, investigations, tests, and studies.

6.04 Owner's Safety Program

- A. Site visits and work at the Site may be governed by an Owner safety program. As the General Conditions indicate, if an Owner safety program exists, it will be noted in the Supplementary Conditions.
- B. Provisions concerning responsibilities for the adequacy of data furnished to prospective BIDDERS with respect to subsurface conditions, other physical conditions and Underground Facilities, and possible changes in the Bidding Documents due to differing or unanticipated conditions appear in Paragraphs 5.03, 5.04 and 5.05 of the General Conditions. Provisions concerning responsibilities for the adequacy of data furnished to prospective BIDDERS with respect to a Hazardous Environmental Condition at the Site, if any, and possible changes in the Contract Documents due to any Hazardous Environmental Condition uncovered or revealed at the Site which was not shown

or indicated in the Drawings or Specifications or identified in the Contract Documents to be within the scope of the Work, appear in Paragraph 5.06 of the General Conditions.

6.05 Other Work at the Site

- A. Reference is made to Article 8 of the Supplementary Conditions for the identification of the general nature of other work of which Owner is aware (if any) that is to be performed at the Site by Owner or others (such as utilities and other prime contractors) and relates to the Work contemplated by these Bidding Documents. If Owner is party to a written contract for such other work, then on request, Owner will provide to each Bidder access to examine such contracts (other than portions thereof related to price and other confidential matters), if any.

ARTICLE 7 – BIDDER’S REPRESENTATIONS

7.01 It is the responsibility of each BIDDER before submitting a Bid to:

- A. examine and carefully study the Bidding Documents, including any Addenda and any data and reference items identified in the Bidding Documents;
- B. visit the Site, conduct a thorough, alert visual examination of the Site and adjacent areas, and become familiar with and satisfy itself as to the general, local, and Site conditions that may affect cost, progress, and performance of the Work;
- C. become familiar with and satisfy itself as to all Laws and Regulations that may affect cost, progress, and performance of the Work;
- D. carefully study all: (1) reports of explorations and tests of subsurface conditions at or adjacent to the Site and all drawings of physical conditions relating to existing surface or subsurface structures at the Site that have been identified in the Supplementary Conditions, especially with respect to Technical Data in such reports and drawings, and (2) reports and drawings relating to Hazardous Environmental Conditions, if any, at or adjacent to the Site that have been identified in the Supplementary Conditions, especially with respect to Technical Data in such reports and drawings;
- E. consider the information known to Bidder itself; information commonly known to contractors doing business in the locality of the Site; information and observations obtained from visits to the Site; the Bidding Documents; and the Site-related reports and drawings identified in the Bidding Documents, with respect to the effect of such information, observations, and documents on (1) the cost, progress, and performance of the Work; (2) the means, methods, techniques, sequences, and procedures of construction to be employed by Bidder; and (3) Bidder’s safety precautions and programs;
- F. agree, based on the information and observations referred to in the preceding paragraph, that at the time of submitting its Bid no further examinations, investigations, explorations, tests, studies, or data are necessary for the determination of its Bid for performance of the Work at the price bid and within the times required, and in accordance with the other terms and conditions of the Bidding Documents;
- G. become aware of the general nature of the work to be performed by OWNER and others at the Site that relates to the Work as indicated in the Bidding Documents;
- H. promptly give Engineer via the Purchasing Office written notice of all conflicts, errors, ambiguities, or discrepancies that Bidder discovers in the Bidding Documents and confirm that the written resolution thereof by Engineer is acceptable to Bidder;
- I. determine that the Bidding Documents are generally sufficient to indicate and convey understanding of all terms and conditions for the performance and furnishing of the Work;
- J. review with his insurance agent/carrier the insurance requirements for this work and has obtained a quotation for additional policies or policy modifications or policy endorsements required to meet

the requirements for this work. Article 6 of the General Conditions, as may be modified by the Supplementary Conditions, sets forth OWNER's requirements as to performance and payment bonds and insurance; and

- K. agree that the submission of a Bid will constitute an incontrovertible representation by Bidder that Bidder has complied with every requirement of this Article 7, that without exception the Bid and all prices in the Bid are premised upon performing and furnishing the Work required by the Bidding Documents.

ARTICLE 8 – INTERPRETATIONS AND ADDENDA

- 8.01 All questions about the meaning or intent of the Bidding Documents are to be submitted to Purchasing via the Vendor Registry portal for this solicitation. The deadline for questions will be 3:00 PM local time on August 19, 2022. Questions submitted after the deadline may or may not be answered. Interpretations or clarifications considered necessary by Purchasing in response to such questions will be issued by Addenda and uploaded to the Vendor Registry portal for this solicitation. Only questions answered by Addenda will be binding. **Oral and other interpretations or clarifications will be without legal effect.**
- 8.02 Addenda may be issued to clarify, correct or change the Bidding Documents.
- 8.03 Bidders shall acknowledge receipt of all Addenda by completing the acknowledgement form included with the Bid Form.

ARTICLE 9 – BID SECURITY

- 9.01 A Bid must be accompanied by Bid security made payable to OWNER in an amount of 5% of BIDDER's maximum Bid price and in the form of a cashier's check or a Bid Bond on the form attached issued by a surety meeting the requirements of Paragraphs 6.01 and 6.02 of the General Conditions.
- 9.02 For Bids submitted electronically, a copy of the Bid security shall be uploaded with their bid. The original Bid security shall be delivered to the Issuing Office (c/o DeRita Mason, Okaloosa County Purchasing Department, 5479A Old Bethel Road, Crestview, FL 32536) within 48 hours from the days from the date set forth to receive bids. Failure to deliver the Bid security within the five- business day window may cause the Bid to be declared non-responsive.
- 9.03 The Bid security of the apparent Successful BIDDER will be retained until OWNER awards the contract to such BIDDER, and such BIDDER has executed the Contract Documents, furnished the required contract security, and met the other conditions of the Notice of Award, whereupon the Bid security will be released. If the Successful BIDDER fails to execute and deliver the Contract Documents and furnish the required contract security within 10 days after the Notice of Award, OWNER may consider BIDDER to be in default, annul the Notice of Award and the Bid security of that BIDDER will be forfeited.
- 9.04 The Bid security of other BIDDERS whom OWNER believes to have a reasonable chance of receiving the award may be retained by OWNER until the earlier of ten (10) days after the effective date of the Agreement or sixty (60) days after the bid opening whereupon Bid security furnished by such BIDDERS will be released.
- 9.05 Bid security of other BIDDERS that OWNER believes do not have a reasonable chance of receiving the award will be released within ten days after the Bid opening.

ARTICLE 10 – CONTRACT TIMES

- 10.01 The number of days within which, or the dates by which, the Work is to be substantially completed and ready for final payment, are set forth in the Agreement.

ARTICLE 11 – LIQUIDATED DAMAGES

- 11.01 Provisions for liquidated damages, if any, for failure to timely attain a Milestone, Substantial Completion, or completion of the Work in readiness for final payment, are set forth in the Agreement.

ARTICLE 12 – SUBSTITUTE AND “OR-EQUAL” ITEMS

- 12.01 The Contract for the Work, if awarded, will be on the basis of materials and equipment specified or described in the Bidding Documents without consideration of possible substitute or “or-equal” items. In cases in which the Contract allows the Contractor to request that Engineer authorize the use of a substitute or “or-equal” item of material or equipment, application for such acceptance may not be made to and will not be considered by Engineer until after the Effective Date of the Contract.
- 12.02 All prices that Bidder sets forth in its Bid shall be based on the presumption that the Contractor will furnish the materials and equipment specified or described in the Bidding Documents, as supplemented by Addenda. Any assumptions regarding the possibility of post-Bid approvals or “or-equal” or substitution requests are made at Bidder’s sole risk.

ARTICLE 13 – SUBCONTRACTORS, SUPPLIERS, AND OTHERS

- 13.01 If OWNER requests the identity of certain Subcontractors, Suppliers, individuals or entities to be submitted to OWNER in advance of the Effective Date of the Agreement as provided for in Paragraph 7.06 of the General Conditions, the apparent Successful BIDDER, and any other BIDDER so requested, shall within seven (7) days after receipt of a written request from the OWNER or the ENGINEER, submit to OWNER a list of all such Subcontractors, Suppliers, individuals, or entities proposed for those portions of the Work for which such identification is required. Such list shall be accompanied by experience statement with pertinent information regarding similar projects and other evidence of qualification for each such Subcontractor, Supplier, individual or entity if requested by OWNER. If OWNER or ENGINEER, after due investigation, has reasonable objection to any proposed Subcontractor, Supplier, individual, or entity, OWNER may, before the Notice of Award is given, request apparent Successful BIDDER to submit a substitute, in which case apparent Successful BIDDER shall submit an acceptable substitute, BIDDER’s Bid price will be increased (or decreased) by the difference in cost occasioned by such substitution, and OWNER may consider such price adjustment in evaluating Bids and making the Contract award.
- 13.02 If apparent Successful BIDDER declines to make any such substitution, OWNER may award the Contract to the next lowest BIDDER that proposes to use acceptable Subcontractors, Suppliers, individuals or entities. Declining to make requested substitutions will not constitute grounds for forfeiture of the Bid security of any BIDDER. Any Subcontractor, Supplier, individual, or entity so listed and against which OWNER or ENGINEER makes no written objection prior to the giving of the Notice of Award will be deemed acceptable to OWNER and ENGINEER subject to subsequent revocation of such acceptance after the Effective Date of the Agreement as provided in Paragraph 7.06 of the General Conditions.
- 13.03 CONTRACTOR shall not be required to employ any Subcontractor, Supplier, individual or entity against who CONTRACTOR has reasonable objection.

ARTICLE 14 – PREPARATION OF BID

- 14.01 The Bid Form is included with the Bidding Documents
- 14.02 All blanks on the Bid Form shall be completed in ink or type written and the Bid Form signed in ink. A Bid price shall be indicated for each section, Bid item, alternate, adjustment unit price item, and unit price item listed therein, or the words “No Bid”, “No Change”, or “Not Applicable” entered. Bids having

erasures or corrections must be initialed in ink by the BIDDER. If a correction is necessary, draw a single line through the entered figure and enter the corrected figure above it and initial the correction. Any illegible entries, pencil bids or corrections not initialed may not be accepted.

- 14.03 A Bid by a corporation shall be executed in the corporate name by the president or a vice-president or other corporate officer who has legal authority to sign. The corporate seal shall be affixed and attested by the secretary or an assistant secretary. The corporate address and state of incorporation shall be shown below the signature.
- 14.04 A Bid by a partnership shall be executed in the partnership name and signed by a partner (whose title must appear under the signature). The official address of the partnership shall be shown below the signature.
- 14.05 A Bid by a limited liability company shall be executed in the name of the firm by a member and accompanied by evidence of authority to sign. The state of formation of the firm and the official address of the firm must be shown below the signature.
- 14.06 A Bid by an individual shall show the BIDDER's name and official address.
- 14.07 A Bid by a joint venture shall be executed by each joint venturer in the manner indicated on the Bid Form. The official address of the joint venture must be shown below the signature.
- 14.08 All names shall be typed or printed in ink below the signatures.
- 14.09 The Bid shall contain an acknowledgment of receipt of all Addenda, the numbers of which shall be filled in on Attachment "A" with Section 00410 "Bid Form with Attachments".
- 14.10 The address and telephone number for communications regarding the Bid shall be shown.
- 14.11 If the BIDDER is an out-of-state corporation, the Bid shall contain evidence of BIDDER's authority and qualification to do business as an out-of-state corporation in the State of Florida. BIDDER's state contractor license number for the State of Florida shall also be shown on the Bid Form. Contractor shall be licensed in accordance with the requirements of Chapter 489 of the Florida Statutes.

ARTICLE 15 – BASIS OF BID

15.01 Unit Price

- A. BIDDERS shall submit a Bid on a unit price basis for each item of Work listed in the Bid Schedule.
- B. The total of all estimated prices will be determined as the sum of the products of the estimated quantity of each item and the unit price Bid for the item. The final quantities and Contract Price will be determined in accordance with Paragraph 13.03 of the General Conditions.
- C. Discrepancies between the multiplication of units of Work and unit prices will be resolved in favor of the unit prices. Discrepancies between the indicated sum of any column of figures and the correct sum thereof will be resolved in favor of the correct sum. Discrepancies between words and figures will be resolved in favor of the words.

ARTICLE 16 – SUBMITTAL OF BID

- 16.01 A bid with all required forms shall be submitted electronically via the Vendor Registry portal no later than the date and time prescribed on the Advertisement or Notice to Respondents. Copies of required bid bond/certified check shall also be submitted electronically using the portal. The response submitted should be one (1) completed document, unless otherwise specified within the document. The original bonds/certified check shall be delivered to the Issuing Office (Attn: Mrs. DeRita Mason) no later than four (4) business days from the date the bids are due.

ARTICLE 17 – MODIFICATION AND WITHDRAWAL OF BID

- 17.01 A Bid may be modified or withdrawn by an appropriate document duly executed in the manner that a Bid must be executed and delivered to the place where Bids are to be submitted prior to the date and time for the opening of Bids.
- 17.02 Once bids are open, the bid submittal may not be withdrawn for sixty (60) days, unless within 24 hours after Bids are opened the BIDDER files a duly signed written notice with OWNER and promptly thereafter demonstrates to the reasonable satisfaction of OWNER that there was a material and substantial mistake in the preparation of its Bid, that BIDDER may withdraw its Bid, and the Bid security will be returned. Thereafter, if the Work is rebid, that BIDDER will be disqualified from (1) further bidding on the Work, and (2) doing any work on the Contract, either as a subcontractor or any other capacity.

ARTICLE 18 – OPENING OF BIDS

- 18.01 Bid opening shall be public, on the date and time specified on the Bid form. It is the BIDDER's responsibility to assure that their bid is submitted electronically via Vendor Registry by the bid opening time.
- 18.02 Bids will be opened at the time and place indicated in the advertisement or invitation to Bid and, unless obviously non-responsive, read aloud publicly. A tabulation of the amounts of Bids will be made available to BIDDERS after the opening of Bids.

ARTICLE 19 – BIDS TO REMAIN SUBJECT TO ACCEPTANCE

- 19.01 All Bids will remain subject to acceptance for the period of ninety (90) days after the day of the bid opening, but the OWNER may, in its sole discretion, release any Bid and return the Bid security prior to the end of this period.

ARTICLE 20 – EVALUATION OF BIDS & AWARD OF CONTRACT

- 20.01 Right to Waive and Reject:
- A. The County, in its absolute discretion, may reject any Bid or a BIDDER that has failed, in the opinion of the County, to complete or perform and Okaloosa County contracted project in a timely fashion or has failed in any other way, in the opinion of the Board, to perform a prior contract in a satisfactory manner, and has directed the Okaloosa County Purchasing Director to emphasize this condition to potential proposers.
 - B. There is no obligation on the part of the County to award the Bid to the lowest BIDDER, and the County reserves the right to award the Bid to the BIDDER submitting the lowest most responsible and responsive Bid with a resulting negotiated Agreement which is most advantageous and in the best interest of Okaloosa County and to reject any and all Bids or to waive any irregularity or technicality in Bids received. Okaloosa County shall be the sole judge of the Bid and the resulting negotiated Agreement that is in the best interest and its decision shall be final.
 - C. The Board of County Commissioners reserves the right to waive any informalities or reject any and all Bids, in whole or part, to utilize any applicable state contracts in lieu of or in addition to this Bid and to accept the Bid that in its judgement will best serve the interest of the County.
 - D. The Board of County Commissioners specifically reserves the right to reject any conditional Bids and will normally reject those which made it impossible to determine the true amount of the Bid. Each item must be Bid separately, and no attempt is to be made to tie any item or items to any other item or items.

- E. In the case of Federal and/or Florida State funded procurements, prior to awarding this contract, the top respondents will be required to submit to a soft credit pull for purposes of the County's Risk Assessment consideration; objections by any respondent will disqualify them from consideration. Bad credit indicating you are a high risk may impact your application. ORGANIZATION OR BANKRUPTCY PROCEEDINGS – Qualifications will not be considered from respondents who are currently involved in official financial reorganization or bankruptcy proceedings.

20.02 Disqualification of BIDDERS:

Any of the following reasons may be considered as sufficient for the disqualification of a BIDDER and the rejection of his Bid or Bids:

- A. More than one Bid for the same work from an individual, firm or corporation under the same or different name.
- B. Evidence that the BIDDER has a financial interest in the firm of another BIDDER for the same work.
- C. Evidence of collusion among BIDDERS. Participants in such collusion will receive no recognition as BIDDERS for any future work of the County until such participant shall have reinstated as a qualified BIDDER.
- D. Uncompleted work which in the judgement of the County might hinder or prevent the prompt completion of additional work if awarded.
- E. Failure to pay or satisfactorily settle all bills due for labor and material on former contracts in force at the time of advertisement for Bids.
- F. Default under previous contract.
- G. The Board of County Commissioners, in its absolute discretion, may reject any Bid or a BIDDER that has failed, in the opinion of the Board, to complete or perform and Okaloosa County contracted project in a timely fashion or has failed in any other way, in the opinion of the Board, to perform a prior contract in a satisfactory manner, and has directed the Okaloosa County Purchasing Director to emphasize this condition to potential proposers.
- H. Listing of the BIDDER by any Local, State or Federal Government on its barred/suspended vendor list.
- I. Bids will not be considered from BIDDERS who are currently involved in official financial reorganization or bankruptcy proceedings.

ARTICLE 21 – SIGNING OF AGREEMENT

21.01 When OWNER issues a Notice of Award to the Successful BIDDER, it shall be accompanied by the required number of unsigned counterparts of the Agreement with the other Contract Documents, which are identified in the Agreement as attached thereto. Within 15 days thereafter, Successful BIDDER shall sign and deliver the required number of counterparts of the Agreement and attached documents to OWNER. Within ten days thereafter, OWNER shall deliver one fully signed counterpart to Successful BIDDER with a complete set of the Drawings with appropriate identification.

ARTICLE 22 – CONFLICT OF INTEREST

22.01 The award hereunder is subject to the provision of Chapter 112, Florida Statutes. All BIDDERS must disclose with their bid proposal the name of any officer, director or agent who is also a public officer or an employee of the Okaloosa County Board of County Commissioners, or any of its agencies. Further, all BIDDERS must disclose with their bid proposal the name of any County officer or employee who owns, directly or indirectly an interest of five percent (5%) or more in the firm or any of its branches.

22.02 The Contractor, prior to or at the time of submission of the bid proposal, must file a statement with the

Clerk of Circuit Court of Okaloosa County, or other designated official in the case of another OWNER, if he is an officer or employee of the County, disclosing his or spouse's or child's interest and the nature of the intended business.

ARTICLE 23 – RECYCLED CONTENT INFORMATION

23.01 In support of the Florida Waste Management Law, BIDDERS are encouraged to supply with their bid any information available regarding recycled material content in the projects bid. The County is particularly interested in the type of recycled material used (such as paper, plastic, glass, metal, etc.) and the percentage of recycled material contained in the product. The County also requests information regarding any known or potential material content in the product that may be extracted and recycled after the product has served its intended purpose.

ARTICLE 24 – IDENTICAL TIE PROPOSALS

24.01 In cases of identical procurement responses, the award shall be determined either by lot or on the basis of factors deemed to serve the best interest of the County. In the case of the latter, there must be adequate documentation to support such a decision.

ARTICLE 25 – DRUG-FREE WORKPLACE PROGRAM

25.01 Bids will only be received from BIDDERS who can certify to having in place a drug-free workplace program. To have a Drug-Free Workplace program, a business shall, at a minimum, meet the requirements of Florida Statutes, Section 287.087.

ARTICLE 26 – INDEMNIFICATION AND HOLD HARMLESS

- 26.01 Each BIDDER must submit with his bid an executed sworn certification that he will comply with the Hold Harmless in accordance with the provisions of Florida Statutes, Section 725.06.
- 26.02 BIDDER shall indemnify hold harmless the OWNER and the design Engineer, its officers and employees from liabilities, damages, losses, and costs including but not limited to reasonable attorney fees, to the extent caused by the negligence, recklessness, or intentionally wrongful conduct of the BIDDER and other persons employed or utilized by the BIDDER in the performance of these services.

ARTICLE 27 – PROTECTION OF RESIDENT WORKERS

- 27.01 The Okaloosa County Board of County Commissioners actively supports the Immigration & Nationality Act (INA) which includes provisions addressing employment eligibility, employment verification, and nondiscrimination. Under the INA, employers may hire only persons who may legally work in the United States, (i.e., citizens and nationals of the U.S.) and aliens authorized to work in the U.S. the employer must verify the identity and employment eligibility of anyone to be hired, which includes completing the Employment Eligibility Verification. The contractor shall establish appropriate procedures and controls so no services or products under the contract documents will be performed or manufactured by any worker who is not legally eligible to perform such services or employment.
- 27.02 Okaloosa County reserves the right to request documentation showing compliance with the requirement.
- 27.03 BIDDERS doing construction business with Okaloosa County are required to use the Federal Government Department of Homeland Security's website and use the E-Verify Employment Eligibility Verifications System to confirm eligibility of all new and existing employees hired by the CONTRACTOR during the term of the Contract and shall expressly require subcontractors performing work or

providing services pursuant to the Contract to likewise utilize the E-Verify system during the Contract term.

ARTICLE 28 – NON-COLLUSION STATEMENT

28.01 BIDDER certifies, using the form provided in the Bid Form, that it has entered into no Agreement to commit a fraudulent, deceitful, unlawful or wrongful act, or any act which may result in an unfair advantage over other BIDDERS. See Florida Statutes 838.22.

ARTICLE 29 – REVIEW OF PROCUREMENT DOCUMENTS

29.01 Per Florida Statutes 119.071(1)(b)2. sealed bids, proposals, or replies received by an agency pursuant to a competitive solicitation are exempt from s. 119.07(1) (Inspection and copying of public records) and s. 24(a), Art. I of the State Constitution until such time as the agency provides notice of an intended decision or until 30 days after opening the bids, proposals, or final replies, whichever is earlier.

ARTICLE 30 – COMPLIANCE WITH FLORIDA STATUTE 119.071

30.01 The BIDDER shall comply with all the provisions of section 119.071, Florida Statutes relating to the public records which requires, among other things, that the BIDDER: (a) Keep and maintain public records; (b) Provide the public with access to public records on the same terms and conditions that the public agency would provide the records; (c) Ensure that public records that are exempt or confidential and exempt from public records disclosure requirements are not disclosed except as authorized by law; and (d) Meet all requirements for retaining public records and transfer, at no cost, to the public agency all public records in possession of the BIDDER upon termination of the contract.

ARTICLE 31 – HIERARCHY OF CONTRACT DOCUMENTS

In the event of conflicts, inconsistencies, discrepancies or ambiguities between the Contract Document arise, unless otherwise provided, the controlling instrument shall be determined by the descending order of the Contract Documents as follows:

1. Modifications issued after the execution of the Agreement
2. Agreement between Owner & Contractor for Construction Contract
3. Addenda issued after the Bid Specifications were advertised to potential Bidders
4. Supplementary Conditions
5. EJCDC General Conditions, 2013 Edition
6. Technical Specifications
7. Construction Drawings
8. Computed dimensions govern over scaled dimensions

ARTICLE 32 – APPLICABLE LAWS & REGULATIONS

32.01 All applicable Federal and State laws, County and municipal ordinances, orders, rules and regulations of all authorities having jurisdiction over the project shall apply to the bid throughout, and they will be deemed to be included in the contract the same as though they were written in full therein.

ARTICLE 33 – SYSTEM FOR AWARD MANAGEMENT (SAM)

- 33.01 The BIDDER shall ensure registration with the Federal Government’s System for Award Management (SAM) database prior to award, during performance and through final payment of the CONTRACT. All mandatory information must be entered to include the Core, Assertions, Representations and Certifications, and Points of Contact sections.
- 33.02 Information on registration for and use of the SAM database can be obtained via the internet at the U.S. General Services Administration site: <https://www.sam.gov/>. Processing time for new registration normally takes 48 hours, BIDDER should apply for registration immediately upon receipt of this ITB.
- 33.03 If the BIDDER does not register in the SAM database in a timely manner, the OWNER may proceed to award to the next otherwise successful registered BIDDER.
- 33.04 The BIDDER is required to provide their SAM information as part of **Article 10 - Bid Submittal** in Section 00410 “Bid Form with Attachments” and is made a part of the Bid Package.
- 33.05 See this Section, Exhibit A, “System for Award Management (Oct 2016)” for additional information.

ARTICLE 34 – OTHER STATEMENTS, FORMS AND DOCUMENTATION

- 34.01 The following forms and certifications are found in Section 00410, Bid Form with Attachments, and shall be submitted with the BID:
 - A. Addendum Acknowledgement (See Section 00410, Attachment A)
 - B. Cone of Silence (See Section 00410, Attachment B)
 - C. Conflict of Interest Disclosure (See Section 00410, Attachment C)
 - D. Recycled Content (See Section 00410, Attachment D)
 - E. Indemnification and Hold Harmless (See Section 00410, Attachment E)
 - F. Drug Free Workplace Program Certification (See Section 00410, Attachment F)
 - G. Federal E-Verify Compliance Certification (See Section 00410, Attachment G)
 - H. Anti-Collusion Statement (See Section 00410, Attachment H)
 - I. Certification Regarding Lobbying (See Section 00410, Attachment I)
 - J. List of References (See Section 00410, Attachment J)
 - K. Vendors on Scrutinized Companies Lists (See Section 00410, Attachment K)
 - L. Certification Regarding Debarment and Suspension (See Section 00410, Attachment L)
 - M. Federal Grant Terms (See Section 00410, Attachment M)

Exhibit A**SYSTEM FOR AWARD MANAGEMENT (OCT 2016)**

(a) Definitions. As used in this provision.

“Electronic Funds Transfer (EFT) indicator” means a four-character suffix to the unique entity identifier. The suffix is assigned at the discretion of the commercial, nonprofit, or Government entity to establish additional System for Award Management records for identifying alternative EFT accounts (see subpart 32.11) for the same entity.

“Registered in the System for Award Management (SAM) database” means that—

(1) The Offeror has entered all mandatory information, including the unique entity identifier and the EFT indicator, if applicable, the Commercial and Government Entity (CAGE) code, as well as data required by the Federal Funding Accountability and Transparency Act of 2006 (see subpart 4.14) into the SAM database;

(2) The offeror has completed the Core, Assertions, and Representations and Certifications, and Points of Contact sections of the registration in the SAM database;

(3) The Government has validated all mandatory data fields, to include validation of the Taxpayer Identification Number (TIN) with the Internal Revenue Service (IRS). The offeror will be required to provide consent for TIN validation to the Government as a part of the SAM registration process; and

(4) The Government has marked the record “Active”.

“Unique entity identifier” means a number or other identifier used to identify a specific commercial, nonprofit, or Government entity. See www.sam.gov for the designated entity for establishing unique entity identifiers.

(b) (1) By submission of an offer, the offeror acknowledges the requirement that a prospective awardee shall be registered in the SAM database prior to award, during performance, and through final payment of any contract, basic agreement, basic ordering agreement, or blanket purchasing agreement resulting from this solicitation.

(2) The Offeror shall enter, in the block with its name and address on the cover page of its offer, the annotation “Unique Entity Identifier” followed by the unique entity identifier that

identifies the Offeror's name and address exactly as stated in the offer. The Offeror also shall enter its EFT indicator, if applicable. The unique entity identifier will be used by the Contracting Officer to verify that the Offeror is registered in the SAM database.

- (c) If the Offeror does not have a unique entity identifier, it should contact the entity designated at www.sam.gov for establishment of the unique entity identifier directly to obtain one. The Offeror should be prepared to provide the following information:
- (1) Company legal business name.
 - (2) Tradestyle, doing business, or other name by which your entity is commonly recognized.
 - (3) Company Physical Street Address, City, State, and Zip Code.
 - (4) Company Mailing Address, City, State and Zip Code (if separate from physical).
 - (5) Company telephone number.
 - (6) Date the company was started.
 - (7) Number of employees at your location.
 - (8) Chief executive officer/key manager.
 - (9) Line of business (industry).
 - (10) Company Headquarters name and address (reporting relationship within your entity).
- (d) If the Offeror does not become registered in the SAM database in the time prescribed by the Contracting Officer, the Contracting Officer will proceed to award to the next otherwise successful registered Offeror.
- (e) Processing time, which normally takes 48 hours, should be taken into consideration when registering. Offerors who are not registered should consider applying for registration immediately upon receipt of this solicitation.
- (f) Offerors may obtain information on registration at <https://www.acquisition.gov>.

Offerors SAM information:

Entity Name: LAS CONTRACTING CORP

Entity Address: 13701 N. NEWMARKET AVE¹⁰² TAMPA, FL 33613

SAM.GOV UNIQUE ENTITY IDENTIFIER: _____

CAGE Code: 858J2

DOCUMENT 00410 – BID FORM WITH ATTACHMENTS
--

ARTICLE 1 – BID RECIPIENT

- 1.01 This Bid is submitted to: Okaloosa County, a political subdivision of the State of Florida.
- 1.02 The undersigned BIDDER proposes and agrees, if this Bid is accepted, to enter into an Agreement with OWNER in the form included in the Bidding Documents to perform all Work as specified or indicated in the Bidding Documents for the prices and within the times indicated in this Bid and in accordance with the other terms and conditions of the Bidding Documents.

ARTICLE 2 – BIDDER'S ACKNOWLEDGEMENTS

- 2.01 BIDDER accepts all of the terms and conditions of the Instructions to BIDDERS, including without limitation those dealing with the disposition of Bid security. This Bid will remain subject to acceptance for 60 days after the Bid opening, or for such longer period of time that BIDDER may agree to in writing upon request of OWNER.

ARTICLE 3 – BIDDER'S REPRESENTATIONS

- 3.01 In submitting this Bid, BIDDER represents that:
 - A. BIDDER has examined and carefully studied the Bidding Documents, and any data and reference items identified in the Bidding Documents, and hereby acknowledges receipt of the Addenda as defined in Attachment "A".
 - B. BIDDER has visited the Site, conducted a thorough, alert visual examination of the Site and adjacent areas, and become familiar with and satisfied itself as to the general, local, and Site conditions that may affect cost, progress, and performance of the Work.
 - C. BIDDER is familiar with and has satisfied itself as to all Laws and Regulations that may affect cost, progress, and performance of the Work.
 - D. BIDDER has carefully studied all: (1) reports, if any, of explorations and tests of subsurface conditions at or adjacent to the Site and all drawings of physical conditions relating to existing surface or subsurface structures at the Site that have been identified in the Supplementary Conditions, especially with respect to Technical Data in such reports and drawings, and (2) reports and drawings relating to Hazardous Environmental Conditions, if any, at or adjacent to the Site that have been identified in the Supplementary Conditions, especially with respect to Technical Data in such reports and drawings.
 - E. BIDDER has considered the information known to BIDDER itself; information commonly known to contractors doing business in the locality of the Site; information and observations obtained from visits to the Site; the Bidding Documents; and any Site-related reports and drawings identified in the Bidding Documents, with respect to the effect of such information, observations, and documents on (1) the cost, progress, and performance of the Work; (2) the means, methods, techniques, sequences, and procedures of construction to be employed by BIDDER; and (3) BIDDER's safety precautions and programs.
 - F. BIDDER agrees, based on the information and observations referred to in the preceding paragraph, that no further examinations, investigations, explorations, tests, studies, or data are necessary for the determination of this Bid for performance of the Work at the price bid and within the times required, and in accordance with the other terms and conditions of the Bidding Documents.
 - G. BIDDER is aware of the general nature of work to be performed by OWNER and others at the Site that relates to the Work as indicated in the Bidding Documents.

- H. BIDDER has given Engineer written notice of all conflicts, errors, ambiguities, or discrepancies that BIDDER has discovered in the Bidding Documents, and confirms that the written resolution thereof by Engineer is acceptable to BIDDER.
- I. The Bidding Documents are generally sufficient to indicate and convey understanding of all terms and conditions for the performance and furnishing of the Work.
- J. The submission of this Bid constitutes an incontrovertible representation by BIDDER that BIDDER has complied with every requirement of this Article, and that without exception the Bid and all prices in the Bid are premised upon performing and furnishing the Work required by the Bidding Documents.

ARTICLE 4 – BIDDER’S CERTIFICATION

4.01 BIDDER certifies that:

- A. This Bid is genuine and not made in the interest of or on behalf of any undisclosed individual or entity and is not submitted in conformity with any collusive agreement or rules of any group, association, organization, or corporation;
- B. BIDDER has not directly or indirectly induced or solicited any other BIDDER to submit a false or sham Bid;
- C. BIDDER has not solicited or induced any individual or entity to refrain from bidding; and
- D. BIDDER has not engaged in corrupt, fraudulent, collusive, or coercive practices in competing for the Contract. For the purposes of this Paragraph 4.01.D:
 - 1. “corrupt practice” means the offering, giving, receiving, or soliciting of anything of value likely to influence the action of a public official in the bidding process;
 - 2. “fraudulent practice” means an intentional misrepresentation of facts made (a) to influence the bidding process to the detriment of OWNER, (b) to establish bid prices at artificial non-competitive levels, or (c) to deprive OWNER of the benefits of free and open competition;
 - 3. “collusive practice” means a scheme or arrangement between two or more BIDDERS, with or without the knowledge of OWNER, a purpose of which is to establish bid prices at artificial, non-competitive levels; and
 - 4. “coercive practice” means harming or threatening to harm, directly or indirectly, persons or their property to influence their participation in the bidding process or affect the execution of the Contract.

ARTICLE 5 – BASIS OF BID

- 5.01 BIDDER acknowledges that (1) each Bid Unit Price includes an amount considered by BIDDER to be adequate to cover CONTRACTOR’s overhead and profit for each separately identified item, and (2) estimated quantities are not guaranteed, and are solely for the purpose of comparison of Bids, and final payment for all unit price Bid items will be based on actual quantities, determined as provided in the Contract Documents. Unit Prices have been computed in accordance with Paragraph 13.03B of the General Conditions.
- 5.02 BIDDER will complete the Work in accordance with the Contract Documents for the following price(s):

Okaloosa County
Old Bethel Road Sidewalk Improvements

DATE: 6/9/2022

ITEM NO.	FDOT PAY ITEM NO.	DESCRIPTION	EST. QTY.	UNIT	UNIT PRICE	CONTRACT PRICE
1	101-1	MOBILIZATION (15%)	1	LS	45 000	45 000
2	102-1	MAINTENANCE OF TRAFFIC (2.5%)	1	LS	45 000	45 000
3	104-10-3	SEDIMENT BARRIER	285	LF	10	2850
4	110-1-1	CLEARING AND GRUBBING (includes tree removal and concrete/asphalt removal)	1.80	AC	20 000	32 000
5	120-1	REGULAR EXCAVATION (CAD QUANTITY)	116	CY	50	5800
6	120-6	EMBANKMENT (CAD QUANTITY)	935	CY	80	74 800
7	400-1-11	CONCRETE CLASS NS, GRAVITY WALL INDEX 400-011	135	CY	1300	175 500
8	515-2311	PEDESTRIAN/ BICYCLE RAILING, ALUMINUM ONLY, 42" TYPE 1	816	LF	129	105 264
9	425-1541	INLETS, DT BOT, TYPE D, <10'	4	EA	4500	18 000
10	430-174-118	PIPE CULVERT, OPT MATL, 18" S/CD	38	LF	100	3800
11	430-175-224	PIPE CULVERT, OPTIONAL MATERIAL, OTHER SHAPE-ELIP/ARCH, 24"S/CD	304	LF	120	36 480
12	425-2-41	MANHOLES, P-7, <10'	2	EA	3900	7800
13	430-982-125	MITERED END SECT. OPTIONAL, RD, 18" SD	4	EA	1400	5600
14	430-984-629	MITERED END SECT. OPTIONAL - ELLIPTICAL / ARCH, 24" SD	1	EA	1900	1900
15	522-1	CONCRETE SIDEWALKS AND DRIVEWAYS, 4" THICK	3,419	SY	74	253 006
16	522-2	CONCRETE SIDEWALKS AND DRIVEWAYS, 6" THICK	101	SY	89	8989
17	520-1-10	CONC. CURB AND GUTTER TYPE F MOD. (18")	115	LF	45	5175
18	334-1-12	SUPERPAVE ASPHALTIC CONCRETE, TRAFFIC B (TYPE SP-9.5 and SP-12.5)	41	TN	900	36 900
19	527-2	DETECTABLE WARNINGS	325	SF	38	12 350
20	570-1-2	PERFORMANCE TURF (SODDING) (CENTIPEDE)	3,810	SY	8	30 480
21	630-2-11	CONDUIT, FURNISH & INSTALL, OPEN TRENCH	117	LF	25	2925
22	635-2-11	PULL & SPLICE BOX, F&I, 13" x 24" COVER SIZE	4	EA	500	2000
23	700-1-11	SINGLE POST SIGN, F&I GROUND MOUNT, UP TO 12 SF	8	EA	600	4800
24	700-1-12	SINGLE POST SIGN, F&I GROUND MOUNT, 12-20 SF	2	EA	1000	2000
25	700-1-60	SINGLE POST SIGN, REMOVE	8	EA	300	2400
26	711-11-123	THERMO. STAND, WHITE, 12" SOLID	920	LF	12	11040
27	711-11-125	THERMO. STAND, WHITE, 24" SOLID	145	LF	15	2175
28	700-12-12	SIGN BEACON, F&I GROUND MOUNT- AC POWERED, TWO BEACONS	2	EA	8000	16 000
29	711-14125	THERMOPLASTIC, PREFORMED, WHITE, SOLID, 24" FOR CROSSWALK	140	LF	25	3500
30	711-17-11	THERMOPLASTIC, REMOVE EXISTING THERMOPLASTIC PAVEMENT MARKINGS- SURFACE TO R	167	SF	15	2505
31	550 10440	FENCING, WOOD FENCE, 7.1-8.0'	163	LF	45	7335
32	0550 10222	FENCING, TYPE B, 5.1-8.0, W/ VINYL COATING	214	LF	60	12 840
33	0110 7 1	MAILBOX, F & I	10	EA	300	3000
TOTAL						979,214.00

ARTICLE 6 – TIME OF COMPLETION

- 6.01 BIDDER agrees that the Work will be substantially complete within 180 calendar days after the date when the Contract Times commence to run as provided in Paragraph 4.01 of the General Conditions, and will be completed and ready for final payment in accordance with Paragraph 15.06 of the General Conditions within 240 calendar days after the date when the Contract Times commence to run.
- 6.02 BIDDER accepts the provisions of the Agreement as to liquidated damages.

ARTICLE 7 – ATTACHMENTS TO THIS BID

- 7.01 The following documents are submitted with and made a condition of this Bid:
- A. Required Bid security as discussed in Article 7 of the Instructions to BIDDERS;
 - B. Evidence of authority to do business in the state of the Project; or a written covenant to obtain such license within the time for acceptance of Bids;
 - C. Contractor's License Number or Evidence of BIDDER's ability to obtain a State Contractor's License and a covenant by BIDDER to obtain said license within the time for acceptance of Bids;
 - D. Attachments
 - A. Addendum Acknowledgement (See Section 00410, Attachment A)
 - B. Cone of Silence (See Section 00410, Attachment B)
 - C. Conflict of Interest Disclosure (See Section 00410, Attachment C)
 - D. Recycled Content (See Section 00410, Attachment D)
 - E. Indemnification and Hold Harmless (See Section 00410, Attachment E)
 - F. Drug Free Workplace Program Certification (See Section 410 Attachment F)
 - G. Federal E-Verify Compliance Certification (See Section 00410, Attachment G)
 - H. Anti-Collusion Statement (See Section 00410, Attachment H)
 - I. DELETED
 - J. List of References (See Section 00410, Attachment J)
 - K. Vendors on Scrutinized Companies Lists (See Section 00410, Attachment K)
 - L. Certification Regarding Debarment and Suspension (See Section 00410, Attachment L)
 - M. Federal Grant Terms
 - E. Defined Terms
- 7.02 The terms used in this Bid with initial capital letters have the meanings stated in the Instructions to BIDDERS, the General Conditions, and the Supplementary Conditions.

ARTICLE 8 – GRANT DIRECTIVES

- 8.01 Contractor Purchased Equipment for State or Local Ownership
- A. The Contractor shall not purchase any equipment for state or local ownership.
- 8.02 Local / State Hiring Preference
- A. No local / state hiring preferences shall be used.
- 8.03 Public Agencies in Competition with the Private Sector
- A. No public agency shall be permitted to bid in competition or to enter into subcontract with private contractors.
- 8.04 Publicly Owned Equipment
- A. Publicly owned equipment shall not compete with privately owned equipment on this contract.

ARTICLE 9 – BID SUBMITTAL

Bidder: Indicate correct name of bidding entity:

LAS CONTRACTING CORP

By:

Signature:




Printed name:

JACK GARDNER

(If BIDDER is a corporation, a limited liability company, a partnership, or a joint venture, attach evidence of authority to sign.)

Attest:

Signature:



Printed name:

Mark A. TESTA

Title:

V.P.

Submittal Date:

8-29-22

Address for giving notices:

13701 N. NEBRASKA AVE¹⁰²

Tampa, FL. 33613

Telephone Number:

813-240-1069

Fax Number:

N/A

Contact Name:

Mark / Jack

Contact Phone Number:

813-240-1069

Contact Email Address:

LASCONTRACTING@AOL.COM

Federal ID or SS Number:

59-3674850

Bidder's License No.:

DUNS Number:

CAGE Code:

DOCUMENT 00410 – ADDENDUM ACKNOWLEDGEMENT – ATTACHMENT “A”

Acknowledgement is hereby made of the following addenda (identified by number) received since issuance of solicitation:

ADDENDUM NUMBER	DATE
#1	8-19-22

NOTE: Prior to submitting the response to this solicitation, it is the responsibility of the BIDDER to confirm if any addenda have been issued. If such addenda have been issued, acknowledge receipt by noting number(s) and date(s) above.

DOCUMENT 00410 – CONE OF SILENCE CLAUSE – ATTACHMENT "B"


The Board of County Commissioners has established a solicitation silence policy (**Cone of Silence**) that prohibits oral and written communication regarding all formal solicitations for goods and services (ITB, RFP, ITQ, ITN, and RFQ) or other competitive solicitation between the bidder (or its agents or representatives) or other entity with the potential for a financial interest in the award (or their respective agents or representatives) regarding such competitive solicitation, and any County Commissioner or County employee, selection committee member or other persons authorized to act on behalf of the Board including the County's Architect, Engineer or their subconsultants, or anyone designated to provide a recommendation to award a particular contract, other than the Purchasing Department Staff.

The period commences from the time of advertisement until contract award.

Any information thought to affect the committee or staff recommendation submitted after bids are due, should be directed to the Purchasing Manager or an appointed representative. It shall be the Purchasing Manager's decision whether to consider this information in the decision process.

Any violation of this policy shall be grounds to disqualify the bidder from consideration during the selection process.

All bidders must agree to comply with this policy by signing the following statement and including it with their submittal.

I, , representing LAS CONTRACTING CORP
Signature Company Name

On this 29 day of Aug, 20 22 hereby agree to abide by the County's "Cone of Silence Clause" and understand violation of this policy shall result in disqualification of my proposal/submittal.

DOCUMENT 00410 – CONFLICT OF INTEREST DISCLOSURE – ATTACHMENT "C"

For purposes of determining any possible conflict of interest, all BIDDERS, must disclose if any Okaloosa Board of County commissioner, employee(s), elected official(s) or if any of its agencies is also an owner, corporate officer, agency, employee, etc., of their business.

Indicate either "YES" (a county employee, elected official or agency is also associated with your business) or "NO". If yes, give person(s) name(s) and position(s) with your business.

YES: _____ NO: ✓

NAME

POSITION

NONE

Date

8-24-22

By (Signature)



Firm Name

LAS CONTRACTING CORP

By (Printed)

JACK GARDNER

Address

13701 N. NEBRASKA AVE¹⁰²

Title

PRESIDENT

Address

Tampa, FL. 33613

Email

LASCONTRACTING@AOL.COM

Office Number

813-240-1069

Cell Number

386-527-9113

DOCUMENT 00410 – RECYCLED CONTENT – ATTACHMENT "D"

1. Material: CONCRETEIs the above material: Virgin ☒ Recycled ☐ If recycled, what percentage %

Describe: _____

Is the material packaged/shipped in packaging containing recycled content? Yes ☐ No ☐

If yes, specify packaging: _____

Is the material recyclable after it has reached the end of its intended use? Yes ☐ No ☐

If yes, explain: _____

2. Material: _____

Is the above material: Virgin ☐ Recycled ☐ If recycled, what percentage %

Describe: _____

Is the material packaged/shipped in packaging containing recycled content? Yes ☐ No ☐

If yes, specify packaging: _____

Is the material recyclable after it has reached the end of its intended use? Yes ☐ No ☐

If yes, explain: _____

3. Material: _____

Is the above material: Virgin ☐ Recycled ☐ If recycled, what percentage %

Describe: _____

Is the material packaged/shipped in packaging containing recycled content? Yes ☐ No ☐

If yes, specify packaging: _____

Is the material recyclable after it has reached the end of its intended use? Yes ☐ No ☐

If yes, explain: _____

DOCUMENT 00410 – INDEMNIFICATION AND HOLD HARMLESS – ATTACHMENT "E"

To the fullest extent permitted by law, CONTRACTOR shall indemnify and hold harmless the OWNER, The Design Engineer and the officers and employees of each from liabilities, damages, losses and costs including but not limited to reasonable attorney fees, to the extent caused by the negligence, recklessness or intentional wrongful conduct of the CONTRACTOR and other persons employed or utilized by the CONTRACTOR in the performance of this Agreement.

Date 8-29-22By (Signature) Firm Name LAS CONTRACTING CORPBy (Printed) JACK GARONEAddress 13701 N. NEARNS AVE¹⁰²Title PRESIDENTAddress TAMPA, FL. 33613Email LASCONTRACTING@AOL.COMOffice Number 813-240-1069

Cell Number _____

Fax Number N/AAfter-Hour Number(s) SAME

DOCUMENT 00410 – DRUG-FREE WORKPLACE PROGRAM CERTIFICATION – ATTACHMENT “F”

THE BELOW SIGNED BIDDER CERTIFIES that it has implemented a drug-free workplace program. In order to have a drug free workplace program, a business shall:

1. Publish a statement notifying employees that the unlawful manufacture, distribution, dispensing, possession, or use of a controlled substance is prohibited in the workplace and specifying the actions that will be taken against employees for violations of such prohibition.
2. Inform employees about the dangers of drug abuse in the workplace, the business's policy of maintaining a drug-free workplace, any available drug counseling, rehabilitation and employee assistance programs, and the penalties that may be imposed upon employees for drug abuse violations.
3. Give each employee engaged in providing the commodities or contractual services that are under quote a copy of the statement specified in subsection 1.
4. In the statement specified in subsection 1, notify the employees that, as a condition of working on the commodities or contractual services that are under quote, the employee will abide by the terms of the statement and will notify the employer of any conviction of, or plea of guilty or nolo contendere to, any violation of Chapter 893, Florida Statutes, or of any controlled substance law of the United States or any state, for a violation occurring in the workplace no later than five (5) days after such conviction.
5. Impose a sanction on, or require the satisfactory participation in, drug abuse assistance or rehabilitation program if such is available in employee's community, by any employee who is convicted.
6. Make a good faith effort to continue to maintain a drug-free workplace through implementation of this section.

As the person authorized to sign this statement, I certify that this firm complies fully with the above requirements.

Date

8-29-22

By (Signature)



Firm Name

LAS CONTRACTING CORP

By (Printed)

Jack Gammal

Address

13701 N. NEARNS AVE¹⁰²

Title

PRESIDENT

Address

TAMPA, FL. 33613

Email

LASCONTRACTING@AOL.COM

Office Number

813-240-1069

Cell Number

DOCUMENT 00410 – FEDERAL E-VERIFY COMPLIANCE CERTIFICATION – ATTACHMENT "G"

In accordance with Okaloosa County Policy and Executive Order Number 11-116 from the office of the Governor of the State of Florida, BIDDER hereby certifies that the U.S. Department of Homeland Security's E-Verify system will be used to verify the employment eligibility of all new employees hired by the BIDDER during the contract term, and shall expressly require any subcontractors performing work or providing services pursuant to the contract to likewise utilize the U.S. Department of Homeland Security's E-Verify system to verify the employment of all new employees hired by the subcontractor during the contract term; and shall provide documentation of such verification to the COUNTY upon request.

As the person authorized to sign this statement, I certify that this company complies/will comply fully with the above requirements.

Date 8-29-22

Firm Name LAS CONTRACTING Corp

Address 13701 N. NEBRASKA AVE 102

Address Tampa, FL 33613

Office Number 813-240-1069

By (Signature) 

By (Printed) JACK GUEVARA

Title PRESIDENT

Email LASCONTRACTING@AOL.COM

Cell Number SAME

DOCUMENT 00410 – ANTI-COLLUSION STATEMENT – ATTACHMENT “H”

The below signed BIDDER has not divulged to, discussed or compared his bid with other BIDDERS and has not colluded with any other BIDDER or parties to bid whatever. (Note: No premiums, rebates or gratuities permitted either with, prior to, or after any delivery of materials.) Any such violation will result in the cancellation and/or return of material (as applicable) and the removal from bid list(s).


Date 8-29-22By (Signature) Firm Name LAS CONTRACTING CORPBy (Printed) JACK GAROVERAddress 13701 N. NEBRASKA AVE 102Title PRESIDENTAddress TAMPA, FL. 33613Email LASCONTRACTING@AOL.COMOffice Number 813-240-1069Cell Number SAME

1. _____ Company Name <u>FOOT</u> <u>DISTRICT 3</u> Address _____ _____ City, State, Zip	_____ Contact Person <u>Meshele Engles</u> <u>850-981-2734</u> Telephone Number _____ <u>meshele.engles@dot.state.fl.us</u> Email _____
2. _____ Company Name <u>FOOT</u> <u>DISTRICT 2</u> Address _____ _____ City, State, Zip	_____ Contact Person <u>Tommie Hines</u> <u>352-816-5484</u> Telephone Number _____ <u>Tommie.Hines@dot.state.fl.us</u> Email _____
3. _____ Company Name <u>City of Callaway</u> _____ Address _____ _____ City, State, Zip	_____ Contact Person <u>EDDIE - City Manager</u> <u>501-605-2752</u> Telephone Number _____ _____ Email _____

DOCUMENT 00410 – VENDORS ON SCRUTINIZED COMPANIES LISTS – ATTACHMENT "K"

By executing this Certificate LAS CONTRACTING Corp, the bid proposer, certifies that it is not: (1) listed on the Scrutinized Companies that Boycott Israel List, created pursuant to section 215.4725, Florida Statutes, (2) engaged in a boycott of Israel, (3) listed on the Scrutinized Companies with Activities in Sudan List or the Scrutinized Companies with Activities in the Iran Petroleum Energy Sector List, created pursuant to section 215.473, Florida Statutes, or (4) engaged in business operations in Cuba or Syria. Pursuant to section 287.135(5), Florida Statutes, the County may disqualify the bid proper immediately or immediately terminate any agreement entered into for cause if the bid proposer is found to have submitted a false certification as to the above or if the Contractor is placed on the Scrutinized Companies that Boycott Israel List, is engaged in a boycott of Israel, has been placed on the Scrutinized Companies with Activities in Sudan List or the Scrutinized Companies with Activities in the Iran Petroleum Energy Sector List, or has been engaged in business operations in Cuba or Syria, during the term of the Agreement. If the County determines that the bid proposer has submitted a false certification, the County will provide written notice to the bid proposer. Unless the bid proposer demonstrates in writing, within 90 calendar days of receipt of the notice, that the County's determination of false certification was made in error, the County shall bring a civil action against the bid proposer. If the County's determination is upheld, a civil penalty shall apply, and the bid proposer will be ineligible to bid on any Agreement with a Florida agency or local governmental entity for three years after the date of County's determination of false certification by bid proposer.

As the person authorized to sign this statement, I certify that this firm complies fully with the above requirements.

DATE: 8-29-22 SIGNATURE: 
COMPANY: LAS CONTRACTING Corp NAME: JACK GRANER
(Typed or Printed)
ADDRESS: 13701 N. NIMBLE AVE¹⁰² TITLE: PRESIDENT
TAMPA, FL. 33613
E-MAIL: LASCONTRACTING@AOL.COM
PHONE NO.: 813-240-1069

DOCUMENT 00410 – DEBARMENT & SUSPENSION – ATTACHMENT “L”

GOVERNMENT DEBARMENT & SUSPENSION**Instructions**

1. By signing and submitting this form, the prospective lower tier participant is providing the certification set out in accordance with these instructions.
2. The certification in this clause is a material representation of fact upon which reliance was placed when this transaction was entered into. If it is later determined that the prospective lower tier participant knowingly rendered an erroneous certification, in addition to other remedies available to the Federal Government, the department or agency with which this transaction originated may pursue available remedies, including suspension or debarment.
3. The prospective lower tier participant shall provide immediate written notice to the person(s) to which this response is submitted if at any time the prospective lower tier participant learns that its certification was erroneous when submitted or has become erroneous by reason of changed circumstances.
4. The terms "covered transaction," "debarred," "suspended," "ineligible," "lower tier covered transaction," "participant," "person," "primary covered transaction," "principal," "proposal," and "voluntarily excluded," as used in this clause, have the meanings set out in the Definitions and Coverage sections of the rules implementing Executive Orders 12549, at Subpart C of OMB 2 C.F.R. Part 180 and 3000.332. You may contact the department or agency to which this response is being submitted for assistance in obtaining a copy of those regulations.
5. The prospective lower tier participant agrees by submitting this form that, should the proposed covered transaction be entered into, it shall not knowingly enter into any lower tier covered transaction with a person who is debarred, suspended, declared ineligible, or voluntarily excluded from participation in this covered transaction, unless authorized by the department or agency with which this transaction originated.
6. The prospective lower tier participant further agrees by submitting this form that it will include this clause titled "Certification Regarding Debarment, Suspension, Ineligibility and Voluntary Exclusion - Lower Tier Covered Transactions," without modification, in all lower tier covered transactions and in all solicitations for lower tier covered transactions.
7. A participant in a covered transaction may rely upon a certification of a prospective participant in a lower tier covered transaction that is not debarred, suspended, ineligible, or voluntarily excluded from the covered transaction, unless it knows that the certification is erroneous. A participant may decide the method and frequency by which it determines the eligibility of its principals. Each participant may, but is not required to, check the System for Award Management (SAM) database.
8. Nothing contained in the foregoing shall be construed to require establishment of a system of records in order to render in good faith the certification required by this clause. The knowledge and information of a participant is not required to exceed that which is normally possessed by a prudent person in the ordinary course of business dealings.

9. Except for transactions authorized under paragraph (5) of these instructions, if a participant in a covered transaction knowingly enters into a lower tier covered transaction with a person who is suspended, debarred, ineligible, or voluntarily excluded from participation in this transaction, in addition to other remedies available to the Federal Government, the department or agency with which this transaction originated may pursue available remedies, including suspension and/or debarment.

**Certification Regarding Debarment, Suspension,
Ineligibility and Voluntary Exclusion
Lower Tier Covered Transactions**

The following statement is made in accordance with the Privacy Act of 1974 (5 U.S.C. § 552(a), as amended). This certification is required by the regulations implementing Executive Orders 12549, Debarment and Suspension, and OMB 2 C.F.R. Part 180, Participants' responsibilities. The regulations were amended and published on August 31, 2005, in 70 Fed. Reg. 51865-51880.

1. The prospective lower tier participant certifies, by submission of this response, that neither it nor its principals is presently debarred, suspended, proposed for debarment, declared ineligible, or voluntarily excluded from participation in this transaction by any Federal or State department or agency;
2. Where the prospective lower tier participant is unable to certify to any of the statements in this certification, such prospective participant shall attach an explanation to this response.

LAS CONTRACTING CORP

Printed Name and Title of Authorized Representative

JACK GRADNER - PRESIDENT

Signature



Date

8-29-22

END OF DOCUMENT 00410 – BID FORM WITH ATTACHMENTS

This Exhibit is hereby incorporated by reference into the main *Procurement*.

FEDERAL PROVISION RELATED TO GRANT FUNDS THAT MAY BE USED TO FUND THE SERVICES AND GOODS UNDER THIS SOLICITATION

This *solicitation* is or may become fully or partially Federally Grant funded. To the extent applicable, in accordance with Federal law, respondents shall comply with the clauses as enumerated below. *Proposer* shall adhere to all grant conditions as set forth in the requirements of grant which have been provided to [*Proposer/Contractor/Consultant*], along with any and all other applicable Federal Laws. Including, but not limited to, those set forth below, as well as those listed below, which are incorporated herein by reference:

- a. 2 CFR. 25.110
- b. 2 CFR Part 170 (including Appendix A), 180, 200 (including Appendixes), and 3000
- c. Executive Orders 12549 and 12689
- d. 41 CFR s. 60-1(a) and (d)
- e. Consolidated Appropriations Act, 2021, Public Law 116-260 related to salary limitations

These cited regulations are hereby incorporated and made part of this *Solicitation* as if fully set forth herein. As stated above, this list is not all inclusive, any other requirement of law applicable in accordance with the Federal, State or grant requirements are also applicable and hereby incorporated into this *Solicitation*. If *Proposer* cannot adhere to or objects to any of the applicable federal requirements, *Proposer's* proposal may be deemed by the County as unresponsive. The provisions in this exhibit are supplemental and in addition to all other provisions within the *Procurement*. In the event of any conflict between the terms and conditions of this Exhibit and the terms and conditions of the remainder of the *Procurement* the conflicting terms and conditions of this Exhibit shall prevail. However, in the event of any conflict between the terms and conditions of this Exhibit and the terms and conditions of any federal grant funding document provided specific to the funds being used to contract services or goods under this *Procurement* the conflicting terms and conditions of that document shall prevail.

Drug Free Workplace Requirements (Drug-Free Workplace Act of 1988 (41 U.S.C. § 701 et seq.), 2 CFR § 182):

Applicability: As required in the Drug-free workplace requirements in accordance with Drug Free Workplace Act of 1988 (Pub L 100-690, Title V, Subtitle D). Requirement: to the extent applicable, *proposer* must comply with Federal Drug Free workplace requirements as Drug Free Workplace Act of 1988.

Conflict of Interest (2 CFR § 200.112): Applicability: Any federal grant funded Contract or Contract that may receive federal grant funds. Requirement: The *proposer* must disclose in writing any potential conflict of interest to the County or pass-through entity in accordance with applicable Federal policy. Further, the County is required to maintain conflict of interest policies as it relates to procured contracts. In accordance with the Okaloosa County Purchasing Manual section 41.05(8), a conflict of interest exists when and of the following occur: i. Because of other activities, relationships, or contracts, a *proposer* is unable, or potentially unable, to render impartial assistance or advice; ii. A *proposer's* objectivity in performing the contract work is or might be otherwise impaired; or iii. The *proposer* has an unfair competitive advantage.

Mandatory Disclosures (31 U.S.C. §§ 3799 – 3733): Applicability: All Contracts using federal grants funds, or which may use federal grant funds. Requirement: *proposer* acknowledges that 31 U.S.C. Chapter 38 (Administrative Remedies for False Claims and Statements) applies to the *proposer's* actions pertaining to this *solicitation*. The contractor must disclose in writing all violations of Federal criminal law involving fraud, bribery, or gratuity violations potentially affecting the Federal award.

Utilization of Minority and Women Firms (M/WBE) (2 CFR § 200.321): Applicability: All federally grant funded Contracts or Contracts which may use federal grant funds. Requirement: The *proposer* must take all necessary affirmative steps to

assure that minority businesses, women's business enterprises, and labor surplus area firms are used when possible, in accordance with 2CFR 200.321. If subcontracts are to be let, prime *proposer* will require compliance by all sub-contractors. Prior to contract award, the *proposer* shall document efforts to utilize M/WBE firms including what firms were solicited as suppliers and/or subcontractors as applicable and submit this information with their bid submittal. Information regarding certified M/WBE firms can be obtained from:

Florida Department of Management Services (Office of Supplier Diversity)
Florida Department of Transportation
Minority Business Development Center in most large cities and
Local Government M/DBE programs in many large counties and cities

Equal Employment Opportunity (As per 2 CFR Part 200, Appendix II(C); 41 CFR § 61-1.4; 41 CFR § 61-4.3; Executive Order 11246 as amended by Executive Order 11375): Applicability: except as otherwise provided under 41 CFR Part 60, applies to all contracts that meet the definition of "federally assisted construction contract" in 41 CFR Part 60-1.3. Requirement: During the performance of this Contract, the *proposer* agrees as follows: (1) The *Proposer* will not discriminate against any employee or applicant for employment because of race, color, religion, sex, or national origin. The *Proposer* will take affirmative action to ensure that applicants are employed, and that employees are treated during employment, without regard to their race, color, religion, sex, sexual orientation, gender identify, or national origin. Such action shall include, but not be limited to, the following: employment, upgrading, demotion, or transfer; recruitment or recruitment advertising; layoff, or termination; rates of pay or other forms of compensation; and selection for training, including apprenticeship. The [Proposer/Contractor/Consultant] agrees to post in conspicuous places, available to employees and applicants for employment, notices to be provided setting forth the provisions of this nondiscrimination clause; (2) The *Proposer* will, in all solicitations or advertisements for employees placed by or on behalf of the *Proposer*, state that all qualified applicants will receive considerations for employment without regard to race, color, religion, sex, or national origin; (3) The *Proposer* will send to each labor union or representative of workers with which it has a collective bargaining Contract or other contract or understanding, a notice to be provided advising the said labor union or workers' representatives of the *Proposer's* commitments under this section and shall post copies of the notice in conspicuous places available to employees and applicants for employment; (4) The *Proposer* will comply with all provisions of Executive Order 11246 of September 24, 1965, and of the rules, regulations, and relevant orders of the Secretary of Labor; (5) The *Proposer* will furnish all information and reports required by Executive Order 11246 of September 24, 1965, and by rules, regulations, and orders of the Secretary of Labor, or pursuant thereto, and will permit access to his books, records, and accounts by the administering agency and the Secretary of Labor for purposes of investigation to ascertain compliance with such rules, regulations, and orders.; (6) In the event of the *Proposer's* noncompliance with the nondiscrimination clauses of this contract or with any of the said rules, regulations, or orders, this contract may be canceled, terminated, or suspended in whole or in part and the [Proposer/Contractor/Consultant] may be declared ineligible for further Government contracts or federally assisted construction contracts in accordance with procedures authorized in Executive Order 11246 of September 24, 1965, and such other sanctions may be imposed and remedies invoked as provided in Executive Order 11246 of September 24, 1965, or by rule, regulation, or order of the Secretary of Labor, or as otherwise provided by law.; (7) *Proposer* will include the portion of the sentence immediately preceding paragraph (1) and the provisions of paragraphs (1) through (7) in every subcontract or purchase order unless exempted by rules, regulations, or orders of the Secretary of Labor issued pursuant to section 204 of Executive Order 11246 of September 24, 1965, so that such provisions will be binding upon each subcontractor or vendor. The *Proposer* will take such action with respect to any subcontract or purchase order as the administering agency may direct as a means of enforcing such provisions, including sanctions for noncompliance: Provided, however, that in the event a *Proposer* becomes involved in, or is threatened with, litigation with a subcontractor or vendor as a result of such direction by the administering agency the *Proposer* may request the United States to enter into such litigation to protect the interests of the United States.

Additional notice and requirement for federally assisted contracts or subcontracts in excess of \$10,000.00:

NOTICE OF REQUIREMENT FOR AFFIRMATIVE ACTION TO ENSURE EQUAL EMPLOYMENT OPPORTUNITY (EXECUTIVE ORDER 11246).

THE OFFEROR'S OR BIDDER'S ATTENTION IS CALLED TO THE "EQUAL OPPORTUNITY CLAUSE" AND THE "STANDARD FEDERAL EQUAL EMPLOYMENT SPECIFICATIONS" SET FORTH HEREIN. THE GOALS AND TIMETABLES FOR MINORITY AND FEMALE PARTICIPATION, EXPRESSED IN PERCENTAGE TERMS FOR THE CONTRACTOR'S AGGREGATE WORKFORCE IN EACH TRADE ON ALL CONSTRUCTION WORK IN THE COVERED AREA, ARE AS FOLLOWS:

TIME-TABLES	GOALS FOR MINORITY PARTICIPATION FOR EACH TRADE	GOALS FOR FEMALE PARTICIPATION IN EACH TRADE
	INSERT GOALS FOR EACH YEAR <i>T.B.D.</i>	INSERT GOALS FOR EACH YEAR. <i>T.B.D.</i>

THESE GOALS ARE APPLICABLE TO ALL THE CONTRACTOR'S CONSTRUCTION WORK (WHETHER OR NOT IT IS FEDERAL OR FEDERALLY ASSISTED) PERFORMED IN THE COVERED AREA. IF THE CONTRACTOR PERFORMS CONSTRUCTION WORK IN A GEOGRAPHICAL AREA LOCATED OUTSIDE OF THE COVERED AREA, IT SHALL APPLY THE GOALS ESTABLISHED FOR SUCH GEOGRAPHICAL AREA WHERE THE WORK IS ACTUALLY PERFORMED. WITH REGARD TO THIS SECOND AREA, THE CONTRACTOR ALSO IS SUBJECT TO THE GOALS FOR BOTH ITS FEDERALLY INVOLVED AND NONFEDERALLY INVOLVED CONSTRUCTION. THE CONTRACTOR'S COMPLIANCE WITH THE EXECUTIVE ORDER AND THE REGULATIONS IN 41 CFR PART 60-4 SHALL BE BASED ON ITS IMPLEMENTATION OF THE EQUAL OPPORTUNITY CLAUSE, SPECIFIC AFFIRMATIVE ACTION OBLIGATIONS REQUIRED BY THE SPECIFICATIONS SET FORTH IN 41 CFR 60-4.3(A), AND ITS EFFORTS TO MEET THE GOALS. THE HOURS OF MINORITY AND FEMALE EMPLOYMENT AND TRAINING MUST BE SUBSTANTIALLY UNIFORM THROUGHOUT THE LENGTH OF THE CONTRACT, AND IN EACH TRADE, AND THE CONTRACTOR SHALL MAKE A GOOD FAITH EFFORT TO EMPLOY MINORITIES AND WOMEN EVENLY ON EACH OF ITS PROJECTS. THE TRANSFER OF MINORITY OR FEMALE EMPLOYEES OR TRAINEES FROM CONTRACTOR TO CONTRACTOR OR FROM PROJECT TO PROJECT FOR THE SOLE PURPOSE OF MEETING THE CONTRACTOR'S GOALS SHALL BE A VIOLATION OF THE CONTRACT, THE EXECUTIVE ORDER AND THE REGULATIONS IN 41 CFR PART 60-4. COMPLIANCE WITH THE GOALS WILL BE MEASURED AGAINST THE TOTAL WORK HOURS PERFORMED.

THE CONTRACTOR SHALL PROVIDE WRITTEN NOTIFICATION TO THE DIRECTOR OF THE OFFICE OF FEDERAL CONTRACT COMPLIANCE PROGRAMS WITHIN 10 WORKING DAYS OF AWARD OF ANY CONSTRUCTION SUBCONTRACT IN EXCESS OF \$10,000 AT ANY TIER FOR CONSTRUCTION WORK UNDER THE CONTRACT RESULTING FROM THIS SOLICITATION. THE NOTIFICATION SHALL LIST THE NAME, ADDRESS AND TELEPHONE NUMBER OF THE SUBCONTRACTOR; EMPLOYER IDENTIFICATION NUMBER OF THE SUBCONTRACTOR; ESTIMATED DOLLAR AMOUNT OF THE SUBCONTRACT; ESTIMATED STARTING AND COMPLETION DATES OF THE SUBCONTRACT; AND THE GEOGRAPHICAL AREA IN WHICH THE SUBCONTRACT IS TO BE PERFORMED.

AS USED IN THIS NOTICE, AND IN THE CONTRACT RESULTING FROM THIS SOLICITATION, THE "COVERED AREA" IS (INSERT DESCRIPTION OF THE GEOGRAPHICAL AREAS WHERE THE CONTRACT IS TO BE PERFORMED GIVING THE STATE, COUNTY AND CITY, IF ANY).

Davis-Bacon Act (40 U.S.C. §§ 3141-3144 and 3146-3148, as supplemented by 29 CFR Part 5): Applicability: When required by Federal Program legislation, grant funding, and all prime construction contracts in excess of \$2,000 awarded by non-Federal entities, including Okaloosa County. Requirement: If applicable to this *solicitation*, the *proposer* agrees to comply with all provisions of the Davis Bacon Act as amended (40 U.S.C. 3141-3148). *proposer* are required to pay wages to laborers and mechanics at a rate not less than the prevailing wages specified in a wage determination made by the Secretary of Labor. In addition, contractors must be required to pay wages not less than once a week. If the grant award contains Davis Bacon provisions, the County will place a copy of the current prevailing wage determination issued by the Department of Labor in the solicitation document. The decision to award a contract shall be conditioned upon the acceptance of the wage determination.

Copeland Anti Kick Back Act (40 U.S.C. § 3145 as supplemented by 29 CFR Part 3): Applicability: When required by Federal Program legislation, grant funding, and all prime construction contracts in excess of \$2,000 awarded by non-Federal entities, including Okaloosa County. Requirement: If applicable to this *Solicitation*, *proposer* shall comply with all the requirements of 18 U.S.C. § 874, 40 U.S.C. § 3145, 29 CFR Part 3 which are incorporated by reference to this *solicitation*. *Proposer* are prohibited from inducing by any means any person employed in the construction, completion or repair of public work to give up any part of the compensation to which he or she is otherwise entitled.

Contract Work Hours and Safety Standards Act (40 U.S.C. 3701-3708 as supplemented by 29 CFR Part 5): Applicability: All contracts awarded in excess of \$100,000 that involve the employment of mechanics or laborers. Requirement: All

contracts awarded in excess of \$100,000 that involve the employment of mechanics or laborers must be in compliance with 40 U.S.C. 3702 and 3704, as supplemented by Department of Labor regulations (29 CFR Part 5). Under 40 U.S.C. 3702 of the Act, each contractor is required to compute the wages of every mechanic and laborer on the basis of a standard work week of 40 hours. Work in excess of the standard work week is permissible provided that the worker is compensated at a rate of not less than one and a half times the basic rate of pay for all hours worked in excess of 40 hours in the work week. The requirements of 40 U.S.C. 3704 are applicable to construction work and provide that no laborer or mechanic must be required to work in surroundings or under working conditions which are unsanitary, hazardous or dangerous. These requirements do not apply to the purchases of supplies or materials or articles ordinarily available on the open market, or contracts for transportation or transmission of intelligence.

Clean Air Act (42 U.S.C. 7401–7671q.) and the Federal Water Pollution Control Act (33 U.S.C. 1251–1387, as amended):

Applicability: Contracts and subgrants of amounts in excess of \$150,000.00. Requirement: *proposer* agrees to comply with all applicable standards, orders or regulations issued pursuant to the Clean Air Act (42 U.S.C. 7401–7671q) and the Federal Water Pollution Control Act as amended (33 U.S.C. 1251–1387). Violations must be reported to the Federal awarding agency and the Regional Office of the Environmental Protection Agency (EPA).

Debarment and Suspension (2 CFR part 180, Executive Orders 12549 and 12689): Applicability: All contracts with federal grant funding or possibility of federal grant funds being used. Requirement: *proposer* certifies that it and its principals, if applicable, are not presently debarred or suspended by any Federal department or agency from participating in this transaction. *proposer* now agrees to verify, to the extent applicable that for each lower tier subcontractor that exceeds \$25,000 as a “covered transaction” under the Services to be provided is not presently disbarred or otherwise disqualified from participating in the federally assisted services. The *proposer* agrees to accomplish this verification by: (1) Checking the System for Award Management at website: <http://www.sam.gov>; (2) Collecting a certification statement similar to the Certification of Offeror /Bidder Regarding Debarment, herein; (3) Inserting a clause or condition in the covered transaction with the lower tier contract.

Byrd Anti-Lobbying Amendment (31 U.S.C. 1352): Applicability: Applicable to any individual/entity that applies or bids/procures an award in excess of \$100,000. Requirement: *proposer* must file the required certification, attached to the procurement. Each tier certifies to the tier above that it will not and has not used Federal appropriated funds to pay any person or organization for influencing or attempting to influence an officer or employee of any agency, a member of Congress, officer or employee of Congress, or an employee of a member of Congress in connection with obtaining any Federal contract, grant or any other award covered by 31 U.S.C. 1352. Each tier must also disclose any lobbying with non-Federal funds that takes place in connection with obtaining any Federal award. Such disclosures are forwarded from tier to tier up to the non-Federal award. The contractor shall certify compliance.

Rights to Inventions Made Under a Contract or Agreement (37 CFR Part 401): Applicability: If the Federal award meets the definition of “funding agreement” under 37 CFR § 401.2 additional Standard patent rights clauses in accordance with 37 CFR § 401.14 shall apply. Requirement: Please contact the County for further information related to the applicable standard patent rights clauses.

Procurement of Recovered Materials (2 CFR 200.323 and 40 CFR Part 247): Applicability: All contractors of Okaloosa County when federal funds may be or are being used under the Contract. Requirement: *proposer* must comply with section 6002 of the Solid Waste Disposal Act, as amended by the Resource Conservation and Recovery Act. The requirements of Section 6002 include procuring only items designated in guidelines of the Environmental Protection Agency (EPA) at 40 CFR part 247 that contain the highest percentage of recovered materials practicable, consistent with maintaining a satisfactory level of competition, where the purchase price of the item exceeds \$10,000 or the value of the quantity acquired during the preceding fiscal year exceeded \$10,000; procuring solid waste management services in a manner that maximizes energy and resource recovery; and establishing an affirmative procurement program for procurement of recovered materials identified in the EPA guidelines.

Access to Records and Reports: Applicability: All Contracts that received or may receive federal grant funding.

Requirement: *Proposer* will make available to the County's granting agency, the granting agency's Office of Inspector General, the Government Accountability Office, the Comptroller General of the United States, Okaloosa County, Okaloosa County Clerk of Court's Inspector General, or any of their duly authorized representatives any books, documents, papers or other records, including electronic records, of the contractor that are pertinent to the County's grant award, in order to make audits, investigations, examinations, excerpts, transcripts, and copies of such documents. The right also includes timely and reasonable access to the contractor's personnel during normal business hours for the purpose of interview and discussion related to such documents. This right of access shall continue as long as records are retained.

Record Retention (2 CFR § 200.33): Applicability: All Contracts that received or may receive federal grant funding. Requirement: *proposer* will retain of all required records pertinent to this contract for a period of three years, beginning on a date as described in 2 C.F.R. §200.333 and retained in compliance with 2 C.F.R. §200.333.

Federal Changes: *proposer* shall comply with all applicable Federal agency regulations, policies, procedures and directives, including without limitation those listed directly or by reference, as they may be amended or promulgated from time to time during the term of *any awarded contract*.

Termination for Default (Breach or Cause): Applicability: All Contracts that may receive federal funds or that are federally funded above the micro-purchase amount. Requirement: If Contractor does not deliver supplies in accordance with the contract delivery schedule, or, if the contract is for services, the Contractor fails to perform in the manner called for in the contract, or if the Contractor fails to comply with any other provisions of the contract, the County may terminate the contract for default. Termination shall be effected by serving a notice of termination on the contractor setting forth the manner in which the Contractor is in default. The contractor will only be paid the contract price for supplies delivered and accepted, or services performed in accordance with the manner of performance set forth in the contract.

Termination for Convenience: Applicability: All Contracts that may receive federal funds or that are federally funded above the micro-purchase amount. Requirement: *Any Awarded Contract* may be terminated by Okaloosa County in whole or in part at any time, upon ten (10) days written notice. If the Contract is terminated before performance is completed, the *Contractor* shall be paid only for that work satisfactorily performed for which costs can be substantiated.

Safeguarding Personal Identifiable Information (2 CFR § 200.82): Applicability: All Contracts receiving, or which may receive federal grant funding. Requirement: *proposer* will take reasonable measures to safeguard protected personally identifiable information and other information designated as sensitive by the awarding agency or is considered sensitive consistent with applicable Federal, state and/or local laws regarding privacy and obligations of confidentiality.

Prohibition On Utilization Of Cost Plus A Percentage Of Cost Contracts (2 CFR Part 200): Applicability: All Contracts receiving or which may receive federal grant funding. Requirement: The County will not award contracts containing Federal funding on a cost-plus percentage of cost basis.

Energy Policy and Conservation Act (43 U.S.C. § 6201 and 2 CFR Part 200 Appendix II (H)): Applicability: For any contracts except micro-purchases (\$3000 or less, except for construction contracts over \$2000). Requirement: *proposer* shall comply with mandatory standards and policies relating to energy efficiency, stating in the state energy conservation plan issued in compliance with the Energy Policy and Conservation act. (Pub. L. 94-163, 89 Stat. 871) [53 FR 8078, 8087, Mar. 11, 1988, as amended at 60 FR 19639, 19645, Apr. 19, 1995].

Trafficking Victims Protection Act (2 CFR Part 175): Applicability: All federally grant funded contracts or contracts which may become federally grant funded. Requirement: *Propose* will comply with the requirements of Section 106(g) of the Trafficking Victims Protection Act (TVPA) of 2000, as amended (22 U.S.C. 7104) which prohibits *Proposer* from (1) engaging in severe forms of trafficking in persons during the period of time that *resulting contract* is in effect; (2) procuring a commercial sex act during the period of time that [*this Contract/resulting contract*] is in effect; or (3) using forced labor in the performance of the contracted services under a *resulting contract*. A *resulting contract* may be unilaterally terminated immediately by County for *Proposer's* violating this provision, without penalty.

Domestic Preference For Procurements (2 CFR § 200.322): Applicability: All Contracts using federal grant funds or which may use federal grant funds. Requirement: As appropriate and to the extent consistent with law, to the greatest extent practicable when using federal funds for the services provided in *a resulting contract*, shall provide a preference for the purchase, acquisition, or use of goods and products or materials produced in the United States.

Buy America (Build America, Buy America Act (Public Law 117-58, 29 U.S.C. § 50101, Executive Order 14005): Applicability: Applies to purchases of iron, steel, manufactured products and construction materials permanently incorporated into infrastructure projects, where federal grant funding agency requires it or if the grant funds which may come from any federal agency, but most commonly: the U.S. Environmental Protection Agency (EPA), the U.S. Federal Transit Administration (FTA), the US Federal Highway Administration (FHWA), the U.S. Federal Railroad Administration (FRA), Amtrack and the U.S. Federal Aviation Administration (FAA). Requirement: All iron, steel, manufactured products and construction materials used under a federally grant funded project must be produced in the United States. Additional requirements may apply depending on the Federal Granting Agency provisions, please check with Okaloosa County for further details. Proposers shall be required to submit a completed Buy America Certificate with this procurement, an incomplete certificate may deem the proposers submittal non-responsive.

Prohibition On Certain Telecommunications And Video Surveillance Services Or Equipment (2 CFR § 200.216): Applicability: All Contracts using federal grant funds or which may use federal grant funds. Requirement: *Proposer* and any subcontractors are prohibited to obligate or spend grant funds to: (1) procure or obtain, (2) extend or renew a contract to procure or obtain; or (3) enter into a contract to procure or obtain equipment, services, or systems that use covered telecommunications equipment or services as a substantial or essential component of any system, or as critical technology as part of any system. As described in Pub. L. 115-232, section 889, covered telecommunications equipment is telecommunications equipment produced by Huawei Technologies Company or ZTE Corporation (or any subsidiary or affiliate of such entities). i. For the purpose of public safety, security of government facilities, physical security surveillance of critical infrastructure, and other national security purposes, video surveillance and telecommunications equipment produced by Hytera Communications Corporation, Hangzhou Hikvision Digital Technology Company, or Dahua Technology Company (or any subsidiary or affiliate of such entities). ii. Telecommunications or video surveillance services provided by such entities or using such equipment. iii. Telecommunications or video surveillance equipment or services produced or provided by an entity that the Secretary of Defense, in consultation with the Director of the National Intelligence or the Director of the Federal Bureau of Investigation, reasonably believes to be an entity owned or controlled by, or otherwise, connected to the government of a covered foreign country.

Enhanced Whistleblower Protections (41 U.S.C. § 4712): Applicability: National Defense Authorization Act of 2013 extending whistleblower protections to *Proposer* employees may apply to the Federal grant award dollars involved with *a resulting contract*. Requirement: See 42 U.S. Code § 4712 for further requirements. Requirement: An employee of *Proposer* and/or its subcontractors may not be discharged, demoted, or otherwise discriminated against as a reprisal for disclosing to a person or body described in 42 U.S.C. § 4712(a)(2) information that the employee reasonably believes is evidence of gross mismanagement of a Federal contract or grant, a gross waste of Federal funds, an abuse of authority relating to a Federal contract or grant, a substantial and specific danger to public health or safety, or a violation of law, rule, or regulation related to a Federal contract (including the competition for or negotiation of a contract) or grant.

Federal Funding Accountability and Transparency Act (FFATA) (2 CFR § 200.300; 2 CFR Part 170): Applicability: All Contracts that may receive federal grant funding or are funded with federal grant funding. Requirement: In accordance with FFATA, the *Proposer* shall, upon request, provide Okaloosa County the names and total compensation of the five most highly compensated officers of the entity, if the entity in the preceding fiscal year received 80 percent or more of its annual gross revenues in federal awards, received \$25,000,000 or more in annual gross revenues from federal awards, and if the public does not have access to information about the compensation of the senior executives of the entity through periodic reports filed under section 13(a) or 15(d) of the Securities Exchange Act of 1934 or section 6104 of the Internal Revenue Code of 1986.

Federal Awardee Performance and Integrity Information System (FAPIS) (The Duncan Hunter National Defense Authorization Act of 2009 (Public Law 110-417 and 2 CFR Part 200 Appendix XII)): Applicability: All Contracts that may receive federal grant funding or are funded with federal grant funding. Requirement: The *Proposer* shall update the information in the Federal Awardee Performance and Integrity Information System (FAPIS) on a semi-annual basis, throughout the life of this contract, by posting the required information in the System for Award Management via <https://www.sam.gov>.

Never Contract With The Enemy (2 CFR Part 183): Applicability: only to grant and cooperative agreements in excess of \$50,000 performed outside of the United States, Including U.S. territories and are in support of a contingency operation in which members of the Armed Forces are actively engaged in hostilities. Requirement: *proposer* must exercise due diligence to ensure that none of the funds, including supplies and services, received are provided directly or indirectly (including through subawards or contracts) to a person or entity who is actively opposing the United States or coalition forces involved in a contingency operation in which members of the Armed Forces are actively engaged in hostilities, which must be completed through 2 CFR 180.300 prior to issuing a subcontract.

Federal Agency Seals, Logos and Flags: Applicability: All Contracts that may receive federal grant funding or are funded with federal grant funding. Requirement: The *proposer* shall not use any Federal Agency seal(s), logos, crests, or reproductions of flags or likenesses of any federal agency officials without specific federal agency pre-approval.

No Obligation by Federal Government: Applicability: All Contracts that may receive federal grant funding or are funded with federal grant funding. Requirement: The Federal Government is not a party to this contract and is not subject to any obligations or liabilities to the non-Federal entity, contractor, or any other party pertaining to any matter resulting from a resulting contract.

The PRESIDENT on behalf of LAS CONTRACTING CORP the *proposer* is authorized to sign below and confirm the *proposer* is fully able to comply with these requirements, federal terms and conditions and has made inquiries and further examination of the law and requirements as is necessary to comply.

DDATE: 8-29-22

SIGNATURE: 

COMPANY: LAS CONTRACTING CORP

NNAME: JACK CHAVIRA

ADDRESS: 13701 N. NEBRASKA AVE 102
TAMPA, FL. 33613

TTITLE: PRESIDENT

E-MAIL: LASCONTRACTING@AOL.COM

PHONE NO.: 813-240-1069

Buy America Certificates

If steel, iron, or manufactured products (as defined in 49 CFR §§ 661.3 and 661.5 of this part) are being procured, the appropriate certificate as set forth below shall be completed and submitted by each bidder or offeror in accordance with the requirement contained in 49 CFR § 661.13(b) of this part.

Certificate of Compliance with Buy America Requirements

The bidder or offeror hereby certifies that it will comply with the requirements of 49 U.S.C. 5323(j)(1), and the applicable regulations in 49 CFR part 661.

DATE: 8-29-22SIGNATURE: WHEN AND WHERE
POSSIBLECOMPANY: LAS CONTRACTING CorpNAME: Jack CoanTITLE: PRESIDENT**Certificate of Non-Compliance with Buy America Requirements**

The bidder or offeror hereby certifies that it cannot comply with the requirements of 49 U.S.C. 5323(j), but it may qualify for an exception to the requirement pursuant to 49 U.S.C. 5323(j)(2), as amended, and the applicable regulations in 49 CFR 661.7.

DATE: _____

SIGNATURE: _____

COMPANY: _____

NAME: _____

TITLE: _____

DOCUMENT 00430 – BID BOND

Any singular reference to Bidder, Surety, Owner or other party shall be considered plural where applicable.

BIDDER (Name and Address):

LAS Contracting Corp.

13701 N. Nebraska Avenue, #102

Tampa, FL 33613

SURETY (Name, and Address of Principal Place of Business):

Merchants Bonding Company

6700 Westown Parkway

West Des Moines, IA 50266

OWNER (Name and Address):

Okaloosa Board of County Commissioners

1250 N. Eglin Parkway

Shalimar, FL 32579

BID

Bid Due Date:

August 31, 2022

Description (Project Name— Include Location):

Old Bethel Road Sidewalk Improvements, ITB PW 56-22

BOND

Bond Number:

N/A

Date:

August 22, 2022

Penal sum: Five Percent of the Amount Bid

5%

(Words)

(Figures)

Surety and Bidder, intending to be legally bound hereby, subject to the terms set forth below, do each cause this Bid Bond to be duly executed by an authorized officer, agent, or representative.

BIDDER

LAS Contracting Corp. (seal)

Contractor's Name and Corporate Seal

By:

Signature

Print Name

Title

Attest:

Signature

Title

SURETY

Merchants Bonding Company (seal)

Surety's Name and Corporate Seal

By:

Signature (attach power of attorney)

Tyler D DeBord

Print Name

Attorney-In-Fact

Title

Attest:

Signature

Ashley Tyree, Account Manager

Title

Note: Addresses are to be used for giving any required notice.

Provide execution by additional parties, such as joint venturers, if necessary.

1. Bidder and Surety, jointly and severally, bind themselves, their heirs, executors, administrators, successors, and assigns to pay to Owner upon default of Bidder the penal sum set forth on the face of this Bond. Payment of the penal sum is the extent of Bidder's and Surety's liability. Recovery of such penal sum under the terms of this Bond shall be Owner's sole and exclusive remedy upon default of Bidder.
2. Default of Bidder shall occur upon the failure of Bidder to deliver within the time required by the Bidding Documents (or any extension thereof agreed to in writing by Owner) the executed Agreement required by the Bidding Documents and any performance and payment bonds required by the Bidding Documents.
3. This obligation shall be null and void if:
 - 3.1 Owner accepts Bidder's Bid and Bidder delivers within the time required by the Bidding Documents (or any extension thereof agreed to in writing by Owner) the executed Agreement required by the Bidding Documents and any performance and payment bonds required by the Bidding Documents, or
 - 3.2 All Bids are rejected by Owner, or
 - 3.3 Owner fails to issue a Notice of Award to Bidder within the time specified in the Bidding Documents (or any extension thereof agreed to in writing by Bidder and, if applicable, consented to by Surety when required by Paragraph 5 hereof).
4. Payment under this Bond will be due and payable upon default of Bidder and within 30 calendar days after receipt by Bidder and Surety of written notice of default from Owner, which notice will be given with reasonable promptness, identifying this Bond and the Project and including a statement of the amount due.
5. Surety waives notice of any and all defenses based on or arising out of any time extension to issue Notice of Award agreed to in writing by Owner and Bidder, provided that the total time for issuing Notice of Award including extensions shall not in the aggregate exceed 120 days from the Bid due date without Surety's written consent.
6. No suit or action shall be commenced under this Bond prior to 30 calendar days after the notice of default required in Paragraph 4 above is received by Bidder and Surety and in no case later than one year after the Bid due date.
7. Any suit or action under this Bond shall be commenced only in a court of competent jurisdiction located in the state in which the Project is located.
8. Notices required hereunder shall be in writing and sent to Bidder and Surety at their respective addresses shown on the face of this Bond. Such notices may be sent by personal delivery, commercial courier, or by United States Registered or Certified Mail, return receipt requested, postage pre-paid, and shall be deemed to be effective upon receipt by the party concerned.
9. Surety shall cause to be attached to this Bond a current and effective Power of Attorney evidencing the authority of the officer, agent, or representative who executed this Bond on behalf of Surety to execute, seal, and deliver such Bond and bind the Surety thereby.
10. This Bond is intended to conform to all applicable statutory requirements. Any applicable requirement of any applicable statute that has been omitted from this Bond shall be deemed to be included herein as if set forth at length. If any provision of this Bond conflicts with any applicable statute, then the provision of said statute shall govern and the remainder of this Bond that is not in conflict therewith shall continue in full force and effect.
11. The term "Bid" as used herein includes a Bid, offer, or proposal as applicable.

END OF DOCUMENT 00430 – BID BOND

MERCHANTS
BONDING COMPANY™
POWER OF ATTORNEY

Know All Persons By These Presents, that MERCHANTS BONDING COMPANY (MUTUAL) and MERCHANTS NATIONAL BONDING, INC., both being corporations of the State of Iowa (herein collectively called the "Companies") do hereby make, constitute and appoint, individually,

Pamela J Thompson; Steve P Farmer; Tyler D DeBord

their true and lawful Attorney(s)-in-Fact, to sign its name as surety(ies) and to execute, seal and acknowledge any and all bonds, undertakings, contracts and other written instruments in the nature thereof, on behalf of the Companies in their business of guaranteeing the fidelity of persons, guaranteeing the performance of contracts and executing or guaranteeing bonds and undertakings required or permitted in any actions or proceedings allowed by law.

This Power-of-Attorney is granted and is signed and sealed by facsimile under and by authority of the following By-Laws adopted by the Board of Directors of Merchants Bonding Company (Mutual) on April 23, 2011 and amended August 14, 2015 and adopted by the Board of Directors of Merchants National Bonding, Inc., on October 16, 2015.


"The President, Secretary, Treasurer, or any Assistant Treasurer or any Assistant Secretary or any Vice President shall have power and authority to appoint Attorneys-in-Fact, and to authorize them to execute on behalf of the Company, and attach the seal of the Company thereto, bonds and undertakings, recognizances, contracts of indemnity and other writings obligatory in the nature thereof."

"The signature of any authorized officer and the seal of the Company may be affixed by facsimile or electronic transmission to any Power of Attorney or Certification thereof authorizing the execution and delivery of any bond, undertaking, recognizance, or other suretyship obligations of the Company, and such signature and seal when so used shall have the same force and effect as though manually fixed."

In connection with obligations in favor of the Florida Department of Transportation only, it is agreed that the power and authority hereby given to the Attorney-in-Fact includes any and all consents for the release of retained percentages and/or final estimates on engineering and construction contracts required by the State of Florida Department of Transportation. It is fully understood that consenting to the State of Florida Department of Transportation making payment of the final estimate to the Contractor and/or its assignee, shall not relieve this surety company of any of its obligations under its bond.

In connection with obligations in favor of the Kentucky Department of Highways only, it is agreed that the power and authority hereby given to the Attorney-in-Fact cannot be modified or revoked unless prior written personal notice of such intent has been given to the Commissioner-Department of Highways of the Commonwealth of Kentucky at least thirty (30) days prior to the modification or revocation.

In Witness Whereof, the Companies have caused this instrument to be signed and sealed this 11th day of February, 2020.



MERCHANTS BONDING COMPANY (MUTUAL)
MERCHANTS NATIONAL BONDING, INC.

By

Larry Taylor
President

STATE OF IOWA
COUNTY OF DALLAS ss.

On this 11th day of February, 2020, before me appeared Larry Taylor, to me personally known, who being by me duly sworn did say that he is President of MERCHANTS BONDING COMPANY (MUTUAL) and MERCHANTS NATIONAL BONDING, INC.; and that the seals affixed to the foregoing instrument are the Corporate Seals of the Companies; and that the said instrument was signed and sealed in behalf of the Companies by authority of their respective Boards of Directors.





POLLY MASON
Commission Number 750576
My Commission Expires
January 07, 2023

Polly Mason
Notary Public


(Expiration of notary's commission
does not invalidate this instrument)

I, William Warner, Jr., Secretary of MERCHANTS BONDING COMPANY (MUTUAL) and MERCHANTS NATIONAL BONDING, INC., do hereby certify that the above and foregoing is a true and correct copy of the POWER-OF-ATTORNEY executed by said Companies, which is still in full force and effect and has not been amended or revoked.

In Witness Whereof, I have hereunto set my hand and affixed the seal of the Companies on this 22nd day of August, 2022.



William Warner Jr.
Secretary



ADDENDUM 1

August 19, 2022

ITB PW 56-22 Old Bethel Sidewalk Improvements

Please find the attached document and information below, for the above referenced Addendum 1. This Addendum is hereby made a part of the Contract Documents and Specifications of the above referenced project. All other requirements of the original Contract Documents and Specifications shall remain effective in their respective order.

I. This addendum is being issued to answer questions submitted by potential vendors:

Question #1: Plan sheet C15 shows the sidewalk installation behind or "off" the Right-of-Way (R/W). Is this correct?


Answer #1: Yes, the area behind the R/W is County property, specifically County Pond 10. Please see attached is pdf showing the pond and that it is County property.

Question #2: Sheet C3 details specific working hours; is this specific to work in the roadway, or does this include work off the roadway in the back of the R/W where the sidewalk will be installed?

Answer #2: Hours are for ALL work at those locations due to school hours.

The solicitation opening date remains August 31, 2022 at 3:00 p.m. (CST)

Okaloosa Map

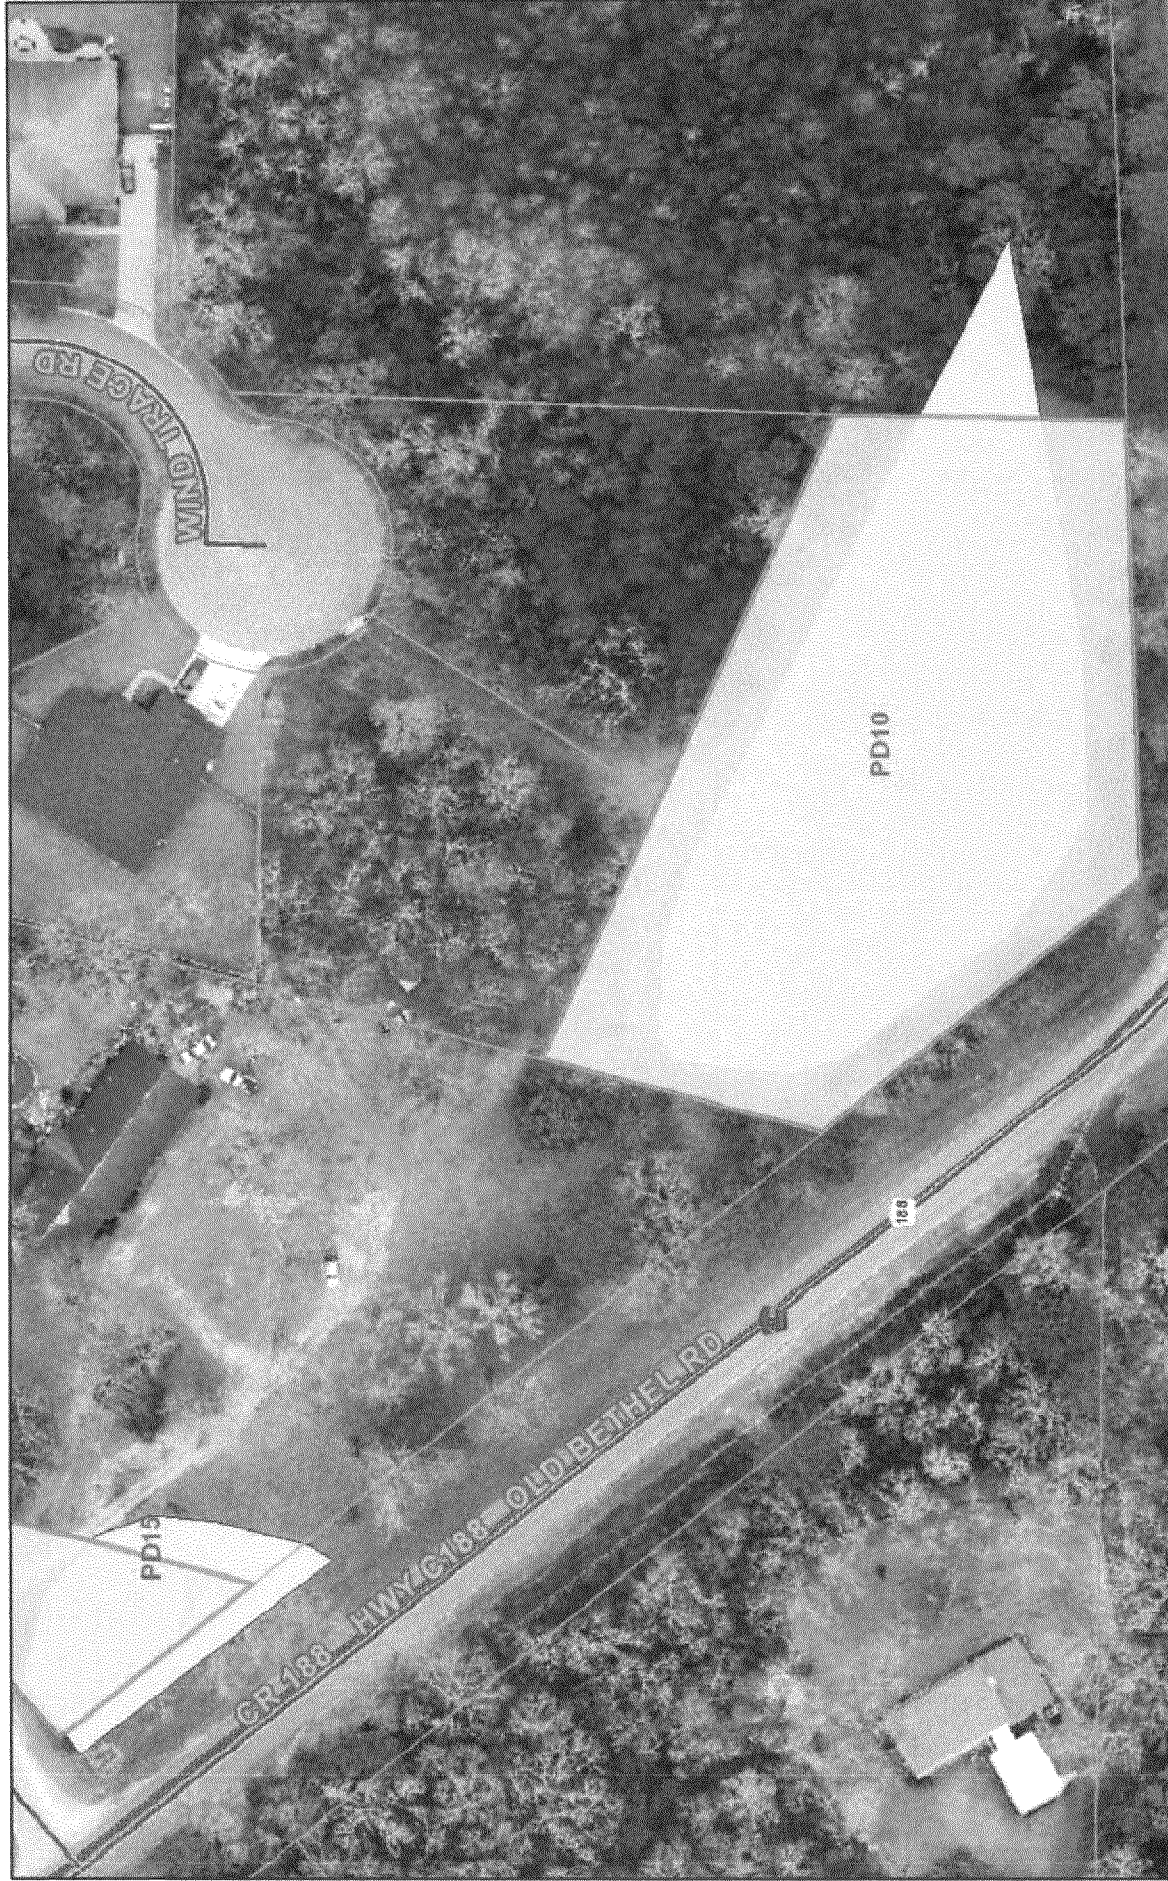

August 15, 2022

Street Routes

1:1,128



Sources: Esri, HERE, Garmin, USGS, Intermap, INCREMENT P, NRCan, Esri Japan, METI, Esri China (Hong Kong), Esri Korea, Esri (Thailand)

9- Federal Aid None (FA None)

6- Surface Transportation Program (STP)

Federal Aid Road

5 - Federal Aid Eligible National Highway System (NHS)

County Boundary

County Maintained Roads

Street Shields

DOCUMENT 00610 - PERFORMANCE BOND

CONTRACTOR (name and address):

LAS Contracting Corp
13701 N. Nebraska Ave.
Tampa, FL 33613

SURETY (name and address of principal place of business):

Merchants Bonding Company
6700 Westown Parkway
West Des Moines, IA 50266

OWNER (name and address): Okaloosa Board of County Commissioners
1250 N. Eglin Parkway
Shalimar, FL 32579

CONSTRUCTION CONTRACT

Effective Date of the Agreement: _____

Amount: \$979,214.00

Description (name and location): Old Bethel Rd Sidewalk Improvements

BOND

Bond Number: FLC86025

Date (not earlier than the Effective Date of the Agreement of the Construction Contract): _____

Amount: \$979,214.00

Modifications to this Bond Form: ☒ None ☐ See Paragraph 16

Surety and Contractor, intending to be legally bound hereby, subject to the terms set forth below, do each cause this Payment Bond to be duly executed by an authorized officer, agent, or representative.

CONTRACTOR AS PRINCIPAL

LAS Contracting Corp (seal)
Contractor's Name and Corporate Seal

By: _____
Signature

Jack Garover
Print Name

President
Title

Attest: _____
Signature

V.P.
Title

SURETY

Merchants Bonding Company (seal)
Surety's Name and Corporate Seal

By: _____
Signature (attach power of attorney)

Tyler D DeBord
Print Name

Attorney-In-Fact
Title

Attest: _____
Signature

Ashley Tyree, Account Manager
Title

Notes: (1) Provide supplemental execution by any additional parties, such as joint venturers. (2) Any singular reference to Contractor, Surety, Owner, or other party shall be considered plural where applicable.

1. The Contractor and Surety, jointly and severally, bind themselves, their heirs, executors, administrators, successors, and assigns to the Owner for the performance of the Construction Contract, which is incorporated herein by reference.

2. If the Contractor performs the Construction Contract, the Surety and the Contractor shall have no obligation under this Bond, except when applicable to participate in a conference as provided in Paragraph 3.

3. If there is no Owner Default under the Construction Contract, the Surety's obligation under this Bond shall arise after:

3.1 The Owner first provides notice to the Contractor and the Surety that the Owner is considering declaring a Contractor Default. Such notice shall indicate whether the Owner is requesting a conference among the Owner, Contractor, and Surety to discuss the Contractor's performance. If the Owner does not request a conference, the Surety may, within five (5) business days after receipt of the Owner's notice, request such a conference. If the Surety timely requests a conference, the Owner shall attend. Unless the Owner agrees otherwise, any conference requested under this Paragraph 3.1 shall be held within ten (10) business days of the Surety's receipt of the Owner's notice. If the Owner, the Contractor, and the Surety agree, the Contractor shall be allowed a reasonable time to perform the Construction Contract, but such an agreement shall not waive the Owner's right, if any, subsequently to declare a Contractor Default;

3.2 The Owner declares a Contractor Default, terminates the Construction Contract and notifies the Surety; and

3.3 The Owner has agreed to pay the Balance of the Contract Price in accordance with the terms of the Construction Contract to the Surety or to a contractor selected to perform the Construction Contract.

4. Failure on the part of the Owner to comply with the notice requirement in Paragraph 3.1 shall not constitute a failure to comply with a condition precedent to the Surety's obligations, or release the Surety from its obligations, except to the extent the Surety demonstrates actual prejudice.

5. When the Owner has satisfied the conditions of Paragraph 3, the Surety shall promptly and at the Surety's expense take one of the following actions:

5.1 Arrange for the Contractor, with the consent of the Owner, to perform and complete the Construction Contract;

5.2 Undertake to perform and complete the Construction Contract itself, through its agents or independent contractors;

5.3 Obtain bids or negotiated proposals from qualified contractors acceptable to the Owner for a contract for performance and completion of the Construction Contract, arrange for a contract to be prepared for execution by the Owner and a contractor selected with the Owners concurrence, to be secured with performance and payment bonds executed by a qualified surety equivalent to the bonds issued on the Construction Contract, and pay to the Owner the amount of damages as described in Paragraph 7 in excess of the Balance of the Contract Price incurred by the Owner as a result of the Contractor Default; or

5.4 Waive its right to perform and complete, arrange for completion, or obtain a new contractor, and with reasonable promptness under the circumstances:

5.4.1 After investigation, determine the amount for which it may be liable to the Owner and, as soon as practicable after the amount is determined, make payment to the Owner; or

5.4.2 Deny liability in whole or in part and notify the Owner, citing the reasons for denial.

6. If the Surety does not proceed as provided in Paragraph 5 with reasonable promptness, the Surety shall be deemed to be in default on this Bond seven days after receipt of an additional written notice from the Owner to the Surety demanding that the Surety perform its obligations under this Bond, and the Owner shall be entitled to enforce any remedy available to the Owner. If the Surety proceeds as provided in Paragraph 5.4, and the Owner refuses the payment or the Surety has denied liability, in whole or in part, without further notice the Owner shall be entitled to enforce any remedy available to the Owner.

7. If the Surety elects to act under Paragraph 5.1, 5.2, or 5.3, then the responsibilities of the Surety to the Owner shall not be greater than those of the Contractor under the Construction Contract, and the responsibilities of the Owner to the Surety shall not be greater than those of the Owner under the Construction Contract. Subject to the commitment by the Owner to pay the Balance of the Contract Price, the Surety is obligated, without duplication for:

7.1 the responsibilities of the Contractor for correction of defective work and completion of the Construction Contract;

7.2 additional legal, design professional, and delay costs resulting from the Contractor's Default, and resulting from the actions or failure to act of the Surety under Paragraph 5; and

7.3 liquidated damages, or if no liquidated damages are specified in the Construction Contract, actual damages caused by delayed performance or non-performance of the Contractor.

8. If the Surety elects to act under Paragraph 5.1, 5.3, or 5.4, the Surety's liability is limited to the amount of this Bond.

9. The Surety shall not be liable to the Owner or others for obligations of the Contractor that are unrelated to the Construction Contract, and the Balance of the Contract Price shall not be reduced or set off on account of any such unrelated obligations. No right of action shall accrue on this Bond to any person or entity other than the Owner or its heirs, executors, administrators, successors, and assigns.

10. The Surety hereby waives notice of any change, including changes of time, to the Construction Contract or to related subcontracts, purchase orders, and other obligations.

11. Any proceeding, legal or equitable, under this Bond may be instituted in any court of competent jurisdiction in the location in which the work or part of the work is located and shall be instituted within two years after a declaration of Contractor Default or within two years after the Contractor ceased working or within two years after the Surety refuses or fails to perform its obligations under this Bond, whichever occurs first. If the provisions of this paragraph are void or prohibited by law, the minimum periods of limitations available to sureties as a defense in the jurisdiction of the suit shall be applicable.

12. Notice to the Surety, the Owner, or the Contractor shall be mailed or delivered to the address shown on the page on which their signature appears.

13. When this Bond has been furnished to comply with a statutory or other legal requirement in the location where the construction was to be performed, any provision in this Bond conflicting with said statutory or legal requirement shall be deemed deleted herefrom and provisions conforming to such statutory or other legal requirement shall be deemed incorporated herein. When so furnished, the intent is that this

Bond shall be construed as a statutory bond and not as a common law bond.

14. Definitions

14.1 Balance of the Contract Price: The total amount payable by the Owner to the Contractor under the Construction Contract after all proper adjustments have been made including allowance for the Contractor for any amounts received or to be received by the Owner in settlement of insurance or other claims for damages to which the Contractor is entitled, reduced by all valid and proper payments made to or on behalf of the Contractor under the Construction Contract.

14.2 Construction Contract: The agreement between the Owner and Contractor identified on the cover page, including all Contract Documents and changes made to the agreement and the Contract Documents.

14.3 Contractor Default: Failure of the Contractor, which has not been remedied or waived, to perform or otherwise to comply with a material term of the Construction Contract.

14.4 Owner Default: Failure of the Owner, which has not been remedied or waived, to pay the Contractor as required under the Construction Contract or to perform and complete or comply with the other material terms of the Construction Contract.

14.5 Contract Documents: All the documents that comprise the agreement between the Owner and Contractor.

15. If this Bond is issued for an agreement between a contractor and subcontractor, the term Contractor in this Bond shall be deemed to be Subcontractor and the term Owner shall be deemed to be Contractor.

16. Modifications to this Bond are as follows:

END OF DOCUMENT 00610 – PERFORMANCE BOND

DOCUMENT 00620 – PAYMENT BOND

CONTRACTOR (name and address):

LAS Contracting Corp
13701 N. Nebraska Ave.
Tampa, FL 33613

SURETY (name and address of principal place of business):

Merchants Bonding Company
6700 Westown Parkway
West Des Moines, IA 50266

OWNER (name and address): Okaloosa Board of County Commissioners
1250 N. Eglin Parkway
Shalimar, FL 32579

CONSTRUCTION CONTRACT

Effective Date of the Agreement: _____

Amount: \$979,214.00

Description (name and location): Old Bethel Road Sidewalk Improvements

BOND

Bond Number: FLC86025

Date (not earlier than the Effective Date of the Agreement of the Construction Contract): _____

Amount: \$979,214.00

Modifications to this Bond Form: ☒ None ☐ See Paragraph 18

Surety and Contractor, intending to be legally bound hereby, subject to the terms set forth below, do each cause this Payment Bond to be duly executed by an authorized officer, agent, or representative.

CONTRACTOR AS PRINCIPAL

LAS Contracting Corp (seal)
Contractor's Name and Corporate Seal

By: _____
Signature

Print Name

Title

Attest: _____

Signature

Title

SURETY

Merchants Bonding Company (seal)
Surety's Name and Corporate Seal

By: _____
Signature (attach power of attorney)

Tyler D DeBord

Print Name

Attorney-In-Fact

Title

Attest: _____

Signature

Ashley Tyree, Account Manager

Title

Notes: (1) Provide supplemental execution by any additional parties, such as joint venturers. (2) Any singular reference to Contractor, Surety, Owner, or other party shall be considered plural where applicable.

1. The Contractor and Surety, jointly and severally, bind themselves, their heirs, executors, administrators, successors, and assigns to the Owner to pay for labor, materials, and equipment furnished for use in the performance of the Construction Contract, which is incorporated herein by reference, subject to the following terms.

2. If the Contractor promptly makes payment of all sums due to Claimants, and defends, indemnifies, and holds harmless the Owner from claims, demands, liens, or suits by any person or entity seeking payment for labor, materials, or equipment furnished for use in the performance of the Construction Contract, then the Surety and the Contractor shall have no obligation under this Bond.

3. If there is no Owner Default under the Construction Contract, the Surety's obligation to the Owner under this Bond shall arise after the Owner has promptly notified the Contractor and the Surety (at the address described in Paragraph 13) of claims, demands, liens, or suits against the Owner or the Owner's property by any person or entity seeking payment for labor, materials, or equipment furnished for use in the performance of the Construction Contract, and tendered defense of such claims, demands, liens, or suits to the Contractor and the Surety.

4. When the Owner has satisfied the conditions in Paragraph 3, the Surety shall promptly and at the Surety's expense defend, indemnify, and hold harmless the Owner against a duly tendered claim, demand, lien, or suit.

5. The Surety's obligations to a Claimant under this Bond shall arise after the following:

5.1 Claimants who do not have a direct contract with the Contractor,

5.1.1 have furnished a written notice of non-payment to the Contractor, stating with substantial accuracy the amount claimed and the name of the party to whom the materials were, or equipment was, furnished or supplied or for whom the labor was done or performed, within ninety (90) days after having last performed labor or last furnished materials or equipment included in the Claim; and

5.1.2 have sent a Claim to the Surety (at the address described in Paragraph 13).

5.2 Claimants who are employed by or have a direct contract with the Contractor have sent a Claim to the Surety (at the address described in Paragraph 13).

6. If a notice of non-payment required by Paragraph

5.1.1 is given by the Owner to the Contractor, that is sufficient to satisfy a Claimant's obligation to furnish a written notice of non-payment under Paragraph 5.1.1.

7. When a Claimant has satisfied the conditions of Paragraph 5.1 or 5.2, whichever is applicable, the Surety shall promptly and at the Surety's expense take the following actions:

7.1 Send an answer to the Claimant, with a copy to the Owner, within sixty (60) days after receipt of the Claim, stating the amounts that are undisputed and the basis for challenging any amounts that are disputed; and

7.2 Pay or arrange for payment of any undisputed amounts.

7.3 The Surety's failure to discharge its obligations under Paragraph 7.1 or 7.2 shall not be deemed to constitute a waiver

of defenses the Surety or Contractor may have or acquire as to a Claim, except as to undisputed amounts for which the Surety and Claimant have reached agreement. If, however, the Surety fails to discharge its obligations under Paragraph 7.1 or 7.2, the Surety shall indemnify the Claimant for the reasonable attorney's fees the Claimant incurs thereafter to recover any sums found to be due and owing to the Claimant.

8. The Surety's total obligation shall not exceed the amount of this Bond, plus the amount of reasonable attorney's fees provided under Paragraph 7.3, and the amount of this Bond shall be credited for any payments made in good faith by the Surety.

9. Amounts owed by the Owner to the Contractor under the Construction Contract shall be used for the performance of the Construction Contract and to satisfy claims, if any, under any construction performance bond. By the Contractor furnishing and the Owner accepting this Bond, they agree that all funds earned by the Contractor in the performance of the Construction Contract are dedicated to satisfy obligations of the Contractor and Surety under this Bond, subject to the Owner's priority to use the funds for the completion of the work.

10. The Surety shall not be liable to the Owner, Claimants, or others for obligations of the Contractor that are unrelated to the Construction Contract. The Owner shall not be liable for the payment of any costs or expenses of any Claimant under this Bond, and shall have under this Bond no obligation to make payments to or give notice on behalf of Claimants, or otherwise have any obligations to Claimants under this Bond.

11. The Surety hereby waives notice of any change, including changes of time, to the Construction Contract or to related subcontracts, purchase orders, and other obligations.

12. No suit or action shall be commenced by a Claimant under this Bond other than in a court of competent jurisdiction in the state in which the project that is the subject of the Construction Contract is located or after the expiration of one year from the date (1) on which the Claimant sent a Claim to the Surety pursuant to Paragraph 5.1.2 or 5.2, or (2) on which the last labor or service was performed by anyone or the last materials or equipment were furnished by anyone under the Construction Contract, whichever of (1) or (2) first occurs. If the provisions of this paragraph are void or prohibited by law, the minimum period of limitation available to sureties as a defense in the jurisdiction of the suit shall be applicable.

13. Notice and Claims to the Surety, the Owner, or the Contractor shall be mailed or delivered to the address shown on the page on which their signature appears. Actual receipt of notice or Claims, however accomplished, shall be sufficient compliance as of the date received.

14. When this Bond has been furnished to comply with a statutory or other legal requirement in the location where the construction was to be performed, any provision in this Bond conflicting with said statutory or legal requirement shall be deemed deleted herefrom and provisions conforming to such statutory or other legal requirement shall be deemed incorporated herein. When so furnished, the intent is that this Bond shall be construed as a statutory bond and not as a common law bond.

15. Upon requests by any person or entity appearing to be a potential beneficiary of this Bond, the Contractor and Owner shall promptly furnish a copy of this Bond or shall permit a copy to be made.

16. Definitions

16.1 Claim: A written statement by the Claimant including at a minimum:

1. The name of the Claimant;
2. The name of the person for whom the labor was done, or materials or equipment furnished;
3. A copy of the agreement or purchase order pursuant to which labor, materials, or equipment was furnished for use in the performance of the Construction Contract;
4. A brief description of the labor, materials, or equipment furnished;
5. The date on which the Claimant last performed labor or last furnished materials or equipment for use in the performance of the Construction Contract;
6. The total amount earned by the Claimant for labor, materials, or equipment furnished as of the date of the Claim;
7. The total amount of previous payments received by the Claimant; and
8. The total amount due and unpaid to the Claimant for labor, materials, or equipment furnished as of the date of the Claim.

16.2 Claimant: An individual or entity having a direct contract with the Contractor or with a subcontractor of the Contractor to furnish labor, materials, or equipment for use in the performance of the Construction Contract. The term Claimant also includes any individual or entity that has rightfully asserted a claim under an applicable mechanic's lien or similar

statute against the real property upon which the Project is located. The intent of this Bond shall be to include without limitation in the terms of "labor, materials, or equipment" that part of the water, gas, power, light, heat, oil, gasoline, telephone service, or rental equipment used in the Construction Contract, architectural and engineering services required for performance of the work of the Contractor and the Contractor's subcontractors, and all other items for which a mechanic's lien may be asserted in the jurisdiction where the labor, materials, or equipment were furnished.

16.3 Construction Contract: The agreement between the Owner and Contractor identified on the cover page, including all Contract Documents and all changes made to the agreement and the Contract Documents.

16.4 Owner Default: Failure of the Owner, which has not been remedied or waived, to pay the Contractor as required under the Construction Contract or to perform and complete or comply with the other material terms of the Construction Contract.

16.5 Contract Documents: All the documents that comprise the agreement between the Owner and Contractor.

17. If this Bond is issued for an agreement between a contractor and subcontractor, the term Contractor in this Bond shall be deemed to be Subcontractor and the term Owner shall be deemed to be Contractor.

18. Modifications to this Bond are as follows:

END OF DOCUMENT 00620 – PAYMENT BOND

MERCHANTS
BONDING COMPANY, INC.
POWER OF ATTORNEY

Know All Persons By These Presents, that MERCHANTS BONDING COMPANY (MUTUAL) and MERCHANTS NATIONAL BONDING, INC., both being corporations of the State of Iowa (herein collectively called the "Companies") do hereby make, constitute and appoint, individually,

Pamela J Thompson; Steve P Farmer; Tyler D DeBord

their true and lawful Attorney(s)-in-Fact, to sign its name as surety(ies) and to execute, seal and acknowledge any and all bonds, undertakings, contracts and other written instruments in the nature thereof, on behalf of the Companies in their business of guaranteeing the fidelity of persons, guaranteeing the performance of contracts and executing or guaranteeing bonds and undertakings required or permitted in any actions or proceedings allowed by law.

This Power-of-Attorney is granted and is signed and sealed by facsimile under and by authority of the following By-Laws adopted by the Board of Directors of Merchants Bonding Company (Mutual) on April 23, 2011 and amended August 14, 2015 and adopted by the Board of Directors of Merchants National Bonding, Inc., on October 16, 2015.


"The President, Secretary, Treasurer, or any Assistant Treasurer or any Assistant Secretary or any Vice President shall have power and authority to appoint Attorneys-in-Fact, and to authorize them to execute on behalf of the Company, and attach the seal of the Company thereto, bonds and undertakings, recognizances, contracts of indemnity and other writings obligatory in the nature thereof."

"The signature of any authorized officer and the seal of the Company may be affixed by facsimile or electronic transmission to any Power of Attorney or Certification thereof authorizing the execution and delivery of any bond, undertaking, recognizance, or other suretyship obligations of the Company, and such signature and seal when so used shall have the same force and effect as though manually fixed."

In connection with obligations in favor of the Florida Department of Transportation only, it is agreed that the power and authority hereby given to the Attorney-in-Fact includes any and all consents for the release of retained percentages and/or final estimates on engineering and construction contracts required by the State of Florida Department of Transportation. It is fully understood that consenting to the State of Florida Department of Transportation making payment of the final estimate to the Contractor and/or its assignee, shall not relieve this surety company of any of its obligations under its bond.

In connection with obligations in favor of the Kentucky Department of Highways only, it is agreed that the power and authority hereby given to the Attorney-in-Fact cannot be modified or revoked unless prior written personal notice of such intent has been given to the Commissioner-Department of Highways of the Commonwealth of Kentucky at least thirty (30) days prior to the modification or revocation.

In Witness Whereof, the Companies have caused this instrument to be signed and sealed this 11th day of February, 2020



MERCHANTS BONDING COMPANY (MUTUAL)
MERCHANTS NATIONAL BONDING, INC.

By

Larry Taylor
President

STATE OF IOWA
COUNTY OF DALLAS ss.

On this 11th day of February, 2020, before me appeared Larry Taylor, to me personally known, who being by me duly sworn did say that he is President of MERCHANTS BONDING COMPANY (MUTUAL) and MERCHANTS NATIONAL BONDING, INC.; and that the seals affixed to the foregoing instrument are the Corporate Seals of the Companies; and that the said instrument was signed and sealed in behalf of the Companies by authority of their respective Boards of Directors.





POLLY MASON
Commission Number 750576
My Commission Expires
January 07, 2023

Polly Mason
Notary Public

(Expiration of notary's commission
does not invalidate this instrument)

I, William Warner, Jr., Secretary of MERCHANTS BONDING COMPANY (MUTUAL) and MERCHANTS NATIONAL BONDING, INC., do hereby certify that the above and foregoing is a true and correct copy of the POWER-OF-ATTORNEY executed by said Companies, which is still in full force and effect and has not been amended or revoked.

In Witness Whereof, I have hereunto set my hand and affixed the seal of the Companies on this _____ day of _____



William Warner Jr.
Secretary



CERTIFICATE OF LIABILITY INSURANCE

DATE (MM/DD/YYYY)

9/21/2022

THIS CERTIFICATE IS ISSUED AS A MATTER OF INFORMATION ONLY AND CONFERS NO RIGHTS UPON THE CERTIFICATE HOLDER. THIS CERTIFICATE DOES NOT AFFIRMATIVELY OR NEGATIVELY AMEND, EXTEND OR ALTER THE COVERAGE AFFORDED BY THE POLICIES BELOW. THIS CERTIFICATE OF INSURANCE DOES NOT CONSTITUTE A CONTRACT BETWEEN THE ISSUING INSURER(S), AUTHORIZED REPRESENTATIVE OR PRODUCER, AND THE CERTIFICATE HOLDER.

IMPORTANT: If the certificate holder is an ADDITIONAL INSURED, the policy(ies) must have ADDITIONAL INSURED provisions or be endorsed. If SUBROGATION IS WAIVED, subject to the terms and conditions of the policy, certain policies may require an endorsement. A statement on this certificate does not confer rights to the certificate holder in lieu of such endorsement(s).

PRODUCER Halifax Insurance 1540 Cornerstone Blvd., Suite 200 Daytona Beach FL 32117	CONTACT NAME:	
	PHONE (A/C, No, Ext): 386-677-4761	FAX (A/C, No): 386-673-5370
	E-MAIL ADDRESS: email@HIPFlorida.com	
	INSURER(S) AFFORDING COVERAGE	NAIC #
	INSURER A : Auto-Owners Insurance Company	18988
	INSURER B : Markel American Insurance Company	28932
	INSURER C :	
	INSURER D :	
	INSURER E :	
	INSURER F :	

License#: L100460
LASCONT-01**INSURED**
Las Contracting Corp
Jack Gardner
PO Box 1275
San Antonio FL 33576-1275**COVERAGES****CERTIFICATE NUMBER:** 1221908674**REVISION NUMBER:**

THIS IS TO CERTIFY THAT THE POLICIES OF INSURANCE LISTED BELOW HAVE BEEN ISSUED TO THE INSURED NAMED ABOVE FOR THE POLICY PERIOD INDICATED. NOTWITHSTANDING ANY REQUIREMENT, TERM OR CONDITION OF ANY CONTRACT OR OTHER DOCUMENT WITH RESPECT TO WHICH THIS CERTIFICATE MAY BE ISSUED OR MAY PERTAIN, THE INSURANCE AFFORDED BY THE POLICIES DESCRIBED HEREIN IS SUBJECT TO ALL THE TERMS, EXCLUSIONS AND CONDITIONS OF SUCH POLICIES. LIMITS SHOWN MAY HAVE BEEN REDUCED BY PAID CLAIMS.

INSR LTR	TYPE OF INSURANCE	ADDL SUBR INSD WVD	POLICY NUMBER	POLICY EFF (MM/DD/YYYY)	POLICY EXP (MM/DD/YYYY)	LIMITS
A	<input checked="" type="checkbox"/> COMMERCIAL GENERAL LIABILITY <input type="checkbox"/> CLAIMS-MADE <input checked="" type="checkbox"/> OCCUR GEN'L AGGREGATE LIMIT APPLIES PER: <input checked="" type="checkbox"/> POLICY <input type="checkbox"/> PRO-JECT <input type="checkbox"/> LOC <input type="checkbox"/> OTHER:		72596968	1/25/2022	1/25/2023	EACH OCCURRENCE \$ 1,000,000 DAMAGE TO RENTED PREMISES (Ea occurrence) \$ 50,000 MED EXP (Any one person) \$ 5,000 PERSONAL & ADV INJURY \$ 1,000,000 GENERAL AGGREGATE \$ 2,000,000 PRODUCTS - COMP/OP AGG \$ 2,000,000 \$
A	AUTOMOBILE LIABILITY <input type="checkbox"/> ANY AUTO <input type="checkbox"/> OWNED AUTOS ONLY <input checked="" type="checkbox"/> SCHEDULED AUTOS <input type="checkbox"/> HIRED AUTOS ONLY <input type="checkbox"/> NON-OWNED AUTOS ONLY		4268766603	12/16/2021	12/16/2022	COMBINED SINGLE LIMIT (Ea accident) \$ 1,000,000 BODILY INJURY (Per person) \$ BODILY INJURY (Per accident) \$ PROPERTY DAMAGE (Per accident) \$ \$
	UMBRELLA LIAB <input type="checkbox"/> OCCUR EXCESS LIAB <input type="checkbox"/> CLAIMS-MADE DED <input type="checkbox"/> RETENTION \$ <input type="checkbox"/>					EACH OCCURRENCE \$ AGGREGATE \$ \$
B	WORKERS COMPENSATION AND EMPLOYERS' LIABILITY ANY PROPRIETOR/PARTNER/EXECUTIVE OFFICER/MEMBER EXCLUDED? (Mandatory in NH) If yes, describe under DESCRIPTION OF OPERATIONS below	Y/N <input type="checkbox"/> N/A	MWC0138081-02	11/12/2021	11/12/2022	<input checked="" type="checkbox"/> PER STATUTE <input type="checkbox"/> OTH-ER E.L. EACH ACCIDENT \$ 1,000,000 E.L. DISEASE - EA EMPLOYEE \$ 1,000,000 E.L. DISEASE - POLICY LIMIT \$ 1,000,000

DESCRIPTION OF OPERATIONS / LOCATIONS / VEHICLES (ACORD 101, Additional Remarks Schedule, may be attached if more space is required)

Job 56-22 Old Bethel Road Sidewalk Improvements

Certificate holder is additional insured with respect to General Liability when required under written contract. General Liability coverage is primary. A 30 day Notice of Cancellation will be provided to the certificate holder except for non-payment.

CERTIFICATE HOLDER**CANCELLATION**Oskaloosa County
5479A Old Bethel Rd.
Crestview FL 32536

SHOULD ANY OF THE ABOVE DESCRIBED POLICIES BE CANCELLED BEFORE THE EXPIRATION DATE THEREOF, NOTICE WILL BE DELIVERED IN ACCORDANCE WITH THE POLICY PROVISIONS.

AUTHORIZED REPRESENTATIVE

This document has important legal consequences; consultation with an attorney is encouraged with respect to its use or modification. This document should be adapted to the particular circumstances of the contemplated Project and the controlling Laws and Regulations.

**STANDARD GENERAL CONDITIONS
OF THE CONSTRUCTION CONTRACT**

Prepared by



Issued and Published Jointly by



These General Conditions have been prepared for use with the Agreement Between Owner and Contractor for Construction Contract (EJCDC® C-520, Stipulated Sum, or C-525, Cost-Plus, 2013 Editions). Their provisions are interrelated and a change in one may necessitate a change in the other.

To prepare supplementary conditions that are coordinated with the General Conditions, use EJCDC's Guide to the Preparation of Supplementary Conditions (EJCDC® C-800, 2013 Edition). The full EJCDC Construction series of documents is discussed in the Commentary on the 2013 EJCDC Construction Documents (EJCDC® C-001, 2013 Edition).

Copyright © 2013:

National Society of Professional Engineers
1420 King Street, Alexandria, VA 22314-2794
(703) 684-2882
www.nspe.org

American Council of Engineering Companies
1015 15th Street N.W., Washington, DC 20005
(202) 347-7474
www.acec.org

American Society of Civil Engineers
1801 Alexander Bell Drive, Reston, VA 20191-4400
(800) 548-2723
www.asce.org

The copyright for this document is owned jointly by the three sponsoring organizations listed above. The National Society of Professional Engineers is the Copyright Administrator for the EJCDC documents; please direct all inquiries regarding EJCDC copyrights to NSPE.

NOTE: EJCDC publications may be purchased at www.ejcdc.org, or from any of the sponsoring organizations above.

TABLE OF CONTENTS

	Page
<u>Article 1 – Definitions and Terminology</u>	7
<u>1.01 Defined Terms</u>	7
<u>1.02 Terminology</u>	10
<u>Article 2 – Preliminary Matters</u>	11
<u>2.01 Delivery of Bonds and Evidence of Insurance.....</u>	11
<u>2.02 Copies of Documents.....</u>	11
<u>2.03 Before Starting Construction</u>	11
<u>2.04 Preconstruction Conference; Designation of Authorized Representatives.....</u>	12
<u>2.05 Initial Acceptance of Schedules</u>	12
<u>2.06 Electronic Transmittals</u>	12
<u>Article 3 – Documents: Intent, Requirements, Reuse</u>	13
<u>3.01 Intent</u>	13
<u>3.02 Reference Standards.....</u>	13
<u>3.03 Reporting and Resolving Discrepancies.....</u>	13
<u>3.04 Requirements of the Contract Documents.....</u>	14
<u>3.05 Reuse of Documents</u>	14
<u>Article 4 – Commencement and Progress of the Work.....</u>	15
<u>4.01 Commencement of Contract Times; Notice to Proceed.....</u>	15
<u>4.02 Starting the Work</u>	15
<u>4.03 Reference Points.....</u>	15
<u>4.04 Progress Schedule.....</u>	15
<u>4.05 Delays in Contractor’s Progress.....</u>	15
<u>Article 5 – Availability of Lands; Subsurface and Physical Conditions; Hazardous Environmental Conditions</u>	16
<u>5.01 Availability of Lands</u>	16
<u>5.02 Use of Site and Other Areas.....</u>	16
<u>5.03 Subsurface and Physical Conditions</u>	17
<u>5.04 Differing Subsurface or Physical Conditions</u>	18
<u>5.05 Underground Facilities.....</u>	19
<u>5.06 Hazardous Environmental Conditions at Site</u>	20
<u>Article 6 – Bonds and Insurance</u>	22
<u>6.01 Performance, Payment, and Other Bonds.....</u>	22
<u>6.02 Insurance—General Provisions.....</u>	23

<u>6.03</u>	<u>Contractor's Insurance</u>	24
<u>6.04</u>	<u>Owner's Liability Insurance</u>	25
<u>6.05</u>	<u>Property Insurance</u>	26
<u>6.06</u>	<u>Waiver of Rights</u>	27
<u>6.07</u>	<u>Receipt and Application of Property Insurance Proceeds</u>	28
<u>Article 7 – Contractor's Responsibilities</u>		28
<u>7.01</u>	<u>Supervision and Superintendence</u>	28
<u>7.02</u>	<u>Labor; Working Hours</u>	29
<u>7.03</u>	<u>Services, Materials, and Equipment</u>	29
<u>7.04</u>	<u>"Or Equals"</u>	29
<u>7.05</u>	<u>Substitutes</u>	30
<u>7.06</u>	<u>Concerning Subcontractors, Suppliers, and Others</u>	31
<u>7.07</u>	<u>Patent Fees and Royalties</u>	32
<u>7.08</u>	<u>Permits</u>	33
<u>7.09</u>	<u>Taxes</u>	33
<u>7.10</u>	<u>Laws and Regulations</u>	33
<u>7.11</u>	<u>Record Documents</u>	34
<u>7.12</u>	<u>Safety and Protection</u>	34
<u>7.13</u>	<u>Safety Representative</u>	35
<u>7.14</u>	<u>Hazard Communication Programs</u>	35
<u>7.15</u>	<u>Emergencies</u>	35
<u>7.16</u>	<u>Shop Drawings, Samples, and Other Submittals</u>	35
<u>7.17</u>	<u>Contractor's General Warranty and Guarantee</u>	37
<u>7.18</u>	<u>Indemnification</u>	37
<u>7.19</u>	<u>Delegation of Professional Design Services</u>	38
<u>Article 8 – Other Work at the Site</u>		39
<u>8.01</u>	<u>Other Work</u>	39
<u>8.02</u>	<u>Coordination</u>	39
<u>8.03</u>	<u>Legal Relationships</u>	39
<u>Article 9 – Owner's Responsibilities</u>		40
<u>9.01</u>	<u>Communications to Contractor</u>	40
<u>9.02</u>	<u>Replacement of Engineer</u>	40
<u>9.03</u>	<u>Furnish Data</u>	40
<u>9.04</u>	<u>Pay When Due</u>	40

<u>9.05</u>	<u>Lands and Easements; Reports, Tests, and Drawings</u>	40
<u>9.06</u>	<u>Insurance</u>	41
<u>9.07</u>	<u>Change Orders</u>	41
<u>9.08</u>	<u>Inspections, Tests, and Approvals</u>	41
<u>9.09</u>	<u>Limitations on Owner's Responsibilities</u>	41
<u>9.10</u>	<u>Undisclosed Hazardous Environmental Condition</u>	41
<u>9.11</u>	<u>Evidence of Financial Arrangements</u>	41
<u>9.12</u>	<u>Safety Programs</u>	41
<u>Article 10 – Engineer's Status During Construction</u>		41
<u>10.01</u>	<u>Owner's Representative</u>	41
<u>10.02</u>	<u>Visits to Site</u>	41
<u>10.03</u>	<u>Project Representative</u>	42
<u>10.04</u>	<u>Rejecting Defective Work</u>	42
<u>10.05</u>	<u>Shop Drawings, Change Orders and Payments</u>	42
<u>10.06</u>	<u>Determinations for Unit Price Work</u>	42
<u>10.07</u>	<u>Decisions on Requirements of Contract Documents and Acceptability of Work</u>	42
<u>10.08</u>	<u>Limitations on Engineer's Authority and Responsibilities</u>	42
<u>10.09</u>	<u>Compliance with Safety Program</u>	43
<u>Article 11 – Amending the Contract Documents; Changes in the Work</u>		43
<u>11.01</u>	<u>Amending and Supplementing Contract Documents</u>	43
<u>11.02</u>	<u>Owner-Authorized Changes in the Work</u>	44
<u>11.03</u>	<u>Unauthorized Changes in the Work</u>	44
<u>11.04</u>	<u>Change of Contract Price</u>	44
<u>11.05</u>	<u>Change of Contract Times</u>	45
<u>11.06</u>	<u>Change Proposals</u>	45
<u>11.07</u>	<u>Execution of Change Orders</u>	46
<u>11.08</u>	<u>Notification to Surety</u>	46
<u>Article 12 – Claims</u>		46
<u>12.01</u>	<u>Claims</u>	46
<u>Article 13 – Cost of the Work; Allowances; Unit Price Work</u>		47
<u>13.01</u>	<u>Cost of the Work</u>	47
<u>13.02</u>	<u>Allowances</u>	49
<u>13.03</u>	<u>Unit Price Work</u>	50
<u>Article 14 – Tests and Inspections; Correction, Removal or Acceptance of Defective Work</u>		50
<u>14.01</u>	<u>Access to Work</u>	50

<u>14.02</u>	<u>Tests, Inspections, and Approvals</u>	50
<u>14.03</u>	<u>Defective Work</u>	51
<u>14.04</u>	<u>Acceptance of Defective Work</u>	52
<u>14.05</u>	<u>Uncovering Work</u>	52
<u>14.06</u>	<u>Owner May Stop the Work</u>	52
<u>14.07</u>	<u>Owner May Correct Defective Work</u>	53
<u>Article 15 – Payments to Contractor; Set-Offs; Completion; Correction Period</u>		53
<u>15.01</u>	<u>Progress Payments</u>	53
<u>15.02</u>	<u>Contractor’s Warranty of Title</u>	56
<u>15.03</u>	<u>Substantial Completion</u>	56
<u>15.04</u>	<u>Partial Use or Occupancy</u>	57
<u>15.05</u>	<u>Final Inspection</u>	57
<u>15.06</u>	<u>Final Payment</u>	57
<u>15.07</u>	<u>Waiver of Claims</u>	58
<u>15.08</u>	<u>Correction Period</u>	58
<u>Article 16 – Suspension of Work and Termination</u>		59
<u>16.01</u>	<u>Owner May Suspend Work</u>	59
<u>16.02</u>	<u>Owner May Terminate for Cause</u>	59
<u>16.03</u>	<u>Owner May Terminate For Convenience</u>	60
<u>16.04</u>	<u>Contractor May Stop Work or Terminate</u>	60
<u>Article 17 – Final Resolution of Disputes</u>		61
<u>17.01</u>	<u>Methods and Procedures</u>	61
<u>Article 18 – Miscellaneous</u>		61
<u>18.01</u>	<u>Giving Notice</u>	61
<u>18.02</u>	<u>Computation of Times</u>	61
<u>18.03</u>	<u>Cumulative Remedies</u>	61
<u>18.04</u>	<u>Limitation of Damages</u>	62
<u>18.05</u>	<u>No Waiver</u>	62
<u>18.06</u>	<u>Survival of Obligations</u>	62
<u>18.07</u>	<u>Controlling Law</u>	62
<u>18.08</u>	<u>Headings</u>	62

ARTICLE 1 – DEFINITIONS AND TERMINOLOGY**1.01 Defined Terms**

- A. Wherever used in the Bidding Requirements or Contract Documents, a term printed with initial capital letters, including the term's singular and plural forms, will have the meaning indicated in the definitions below. In addition to terms specifically defined, terms with initial capital letters in the Contract Documents include references to identified articles and paragraphs, and the titles of other documents or forms.
1. *Addenda*—Written or graphic instruments issued prior to the opening of Bids which clarify, correct, or change the Bidding Requirements or the proposed Contract Documents.
 2. *Agreement*—The written instrument, executed by Owner and Contractor, that sets forth the Contract Price and Contract Times, identifies the parties and the Engineer, and designates the specific items that are Contract Documents.
 3. *Application for Payment*—The form acceptable to Engineer which is to be used by Contractor during the course of the Work in requesting progress or final payments and which is to be accompanied by such supporting documentation as is required by the Contract Documents.
 4. *Bid*—The offer of a Bidder submitted on the prescribed form setting forth the prices for the Work to be performed.
 5. *Bidder*—An individual or entity that submits a Bid to Owner.
 6. *Bidding Documents*—The Bidding Requirements, the proposed Contract Documents, and all Addenda.
 7. *Bidding Requirements*—The advertisement or invitation to bid, Instructions to Bidders, Bid Bond or other Bid security, if any, the Bid Form, and the Bid with any attachments.
 8. *Change Order*—A document which is signed by Contractor and Owner and authorizes an addition, deletion, or revision in the Work or an adjustment in the Contract Price or the Contract Times, or other revision to the Contract, issued on or after the Effective Date of the Contract.
 9. *Change Proposal*—A written request by Contractor, duly submitted in compliance with the procedural requirements set forth herein, seeking an adjustment in Contract Price or Contract Times, or both; contesting an initial decision by Engineer concerning the requirements of the Contract Documents or the acceptability of Work under the Contract Documents; challenging a set-off against payments due; or seeking other relief with respect to the terms of the Contract.
 10. *Claim*—(a) A demand or assertion by Owner directly to Contractor, duly submitted in compliance with the procedural requirements set forth herein: seeking an adjustment of Contract Price or Contract Times, or both; contesting an initial decision by Engineer concerning the requirements of the Contract Documents or the acceptability of Work under the Contract Documents; contesting Engineer's decision regarding a Change Proposal; seeking resolution of a contractual issue that Engineer has declined to address; or seeking other relief with respect to the terms of the Contract; or (b) a demand or assertion by Contractor directly to Owner, duly submitted in compliance with the procedural requirements set forth herein, contesting Engineer's decision regarding a Change Proposal; or seeking resolution of a contractual issue that Engineer has declined to address. A demand for money or services by a third party is not a Claim.
 11. *Constituent of Concern*—Asbestos, petroleum, radioactive materials, polychlorinated biphenyls (PCBs), hazardous waste, and any substance, product, waste, or other material of any nature whatsoever that is or becomes listed, regulated, or addressed pursuant to (a) the Comprehensive Environmental Response, Compensation and Liability Act, 42 U.S.C. §§9601 et seq. ("CERCLA"); (b) the Hazardous Materials Transportation Act, 49 U.S.C. §§5101 et seq.; (c)

- the Resource Conservation and Recovery Act, 42 U.S.C. §§6901 et seq. ("RCRA"); (d) the Toxic Substances Control Act, 15 U.S.C. §§2601 et seq.; (e) the Clean Water Act, 33 U.S.C. §§1251 et seq.; (f) the Clean Air Act, 42 U.S.C. §§7401 et seq.; or (g) any other federal, state, or local statute, law, rule, regulation, ordinance, resolution, code, order, or decree regulating, relating to, or imposing liability or standards of conduct concerning, any hazardous, toxic, or dangerous waste, substance, or material.
12. *Contract*—The entire and integrated written contract between the Owner and Contractor concerning the Work.
 13. *Contract Documents*—Those items so designated in the Agreement, and which together comprise the Contract.
 14. *Contract Price*—The money that Owner has agreed to pay Contractor for completion of the Work in accordance with the Contract Documents. .
 15. *Contract Times*—The number of days or the dates by which Contractor shall: (a) achieve Milestones, if any; (b) achieve Substantial Completion; and (c) complete the Work.
 16. *Contractor*—The individual or entity with which Owner has contracted for performance of the Work.
 17. *Cost of the Work*—See Paragraph 13.01 for definition.
 18. *Drawings*—The part of the Contract that graphically shows the scope, extent, and character of the Work to be performed by Contractor.
 19. *Effective Date of the Contract*—The date, indicated in the Agreement, on which the Contract becomes effective.
 20. *Engineer*—The individual or entity named as such in the Agreement.
 21. *Field Order*—A written order issued by Engineer which requires minor changes in the Work but does not change the Contract Price or the Contract Times.
 22. *Hazardous Environmental Condition*—The presence at the Site of Constituents of Concern in such quantities or circumstances that may present a danger to persons or property exposed thereto. The presence at the Site of materials that are necessary for the execution of the Work, or that are to be incorporated in the Work, and that are controlled and contained pursuant to industry practices, Laws and Regulations, and the requirements of the Contract, does not establish a Hazardous Environmental Condition.
 23. *Laws and Regulations; Laws or Regulations*—Any and all applicable laws, statutes, rules, regulations, ordinances, codes, and orders of any and all governmental bodies, agencies, authorities, and courts having jurisdiction.
 24. *Liens*—Charges, security interests, or encumbrances upon Contract-related funds, real property, or personal property.
 25. *Milestone*—A principal event in the performance of the Work that the Contract requires Contractor to achieve by an intermediate completion date or by a time prior to Substantial Completion of all the Work.
 26. *Notice of Award*—The written notice by Owner to a Bidder of Owner's acceptance of the Bid.
 27. *Notice to Proceed*—A written notice by Owner to Contractor fixing the date on which the Contract Times will commence to run and on which Contractor shall start to perform the Work.
 28. *Owner*—The individual or entity with which Contractor has contracted regarding the Work, and which has agreed to pay Contractor for the performance of the Work, pursuant to the terms of the Contract.
 29. *Progress Schedule*—A schedule, prepared and maintained by Contractor, describing the sequence and duration of the activities comprising the Contractor's plan to accomplish the Work within the Contract Times.

30. *Project*—The total undertaking to be accomplished for Owner by engineers, contractors, and others, including planning, study, design, construction, testing, commissioning, and start-up, and of which the Work to be performed under the Contract Documents is a part.
31. *Project Manual*—The written documents prepared for, or made available for, procuring and constructing the Work, including but not limited to the Bidding Documents or other construction procurement documents, geotechnical and existing conditions information, the Agreement, bond forms, General Conditions, Supplementary Conditions, and Specifications. The contents of the Project Manual may be bound in one or more volumes.
32. *Resident Project Representative*—The authorized representative of Engineer assigned to assist Engineer at the Site. As used herein, the term Resident Project Representative or “RPR” includes any assistants or field staff of Resident Project Representative.
33. *Samples*—Physical examples of materials, equipment, or workmanship that are representative of some portion of the Work and that establish the standards by which such portion of the Work will be judged.
34. *Schedule of Submittals*—A schedule, prepared and maintained by Contractor, of required submittals and the time requirements for Engineer’s review of the submittals and the performance of related construction activities.
35. *Schedule of Values*—A schedule, prepared and maintained by Contractor, allocating portions of the Contract Price to various portions of the Work and used as the basis for reviewing Contractor’s Applications for Payment.
36. *Shop Drawings*—All drawings, diagrams, illustrations, schedules, and other data or information that are specifically prepared or assembled by or for Contractor and submitted by Contractor to illustrate some portion of the Work. Shop Drawings, whether approved or not, are not Drawings and are not Contract Documents.
37. *Site*—Lands or areas indicated in the Contract Documents as being furnished by Owner upon which the Work is to be performed, including rights-of-way and easements, and such other lands furnished by Owner which are designated for the use of Contractor.
38. *Specifications*—The part of the Contract that consists of written requirements for materials, equipment, systems, standards, and workmanship as applied to the Work, and certain administrative requirements and procedural matters applicable to the Work.
39. *Subcontractor*—An individual or entity having a direct contract with Contractor or with any other Subcontractor for the performance of a part of the Work.
40. *Substantial Completion*—The time at which the Work (or a specified part thereof) has progressed to the point where, in the opinion of Engineer, the Work (or a specified part thereof) is sufficiently complete, in accordance with the Contract Documents, so that the Work (or a specified part thereof) can be utilized for the purposes for which it is intended. The terms “substantially complete” and “substantially completed” as applied to all or part of the Work refer to Substantial Completion thereof.
41. *Successful Bidder*—The Bidder whose Bid the Owner accepts, and to which the Owner makes an award of contract, subject to stated conditions.
42. *Supplementary Conditions*—The part of the Contract that amends or supplements these General Conditions.
43. *Supplier*—A manufacturer, fabricator, supplier, distributor, materialman, or vendor having a direct contract with Contractor or with any Subcontractor to furnish materials or equipment to be incorporated in the Work by Contractor or a Subcontractor.
44. *Technical Data*—Those items expressly identified as Technical Data in the Supplementary Conditions, with respect to either (a) subsurface conditions at the Site, or physical conditions relating to existing surface or subsurface structures at the Site (except Underground Facilities)

EJCDC® -, Standard General Conditions of the Construction Contract.

Copyright © 2013 National Society of Professional Engineers, American Council of Engineering Companies, and American Society of Civil Engineers. All rights reserved.

or (b) Hazardous Environmental Conditions at the Site. If no such express identifications of Technical Data have been made with respect to conditions at the Site, then the data contained in boring logs, recorded measurements of subsurface water levels, laboratory test results, and other factual, objective information regarding conditions at the Site that are set forth in any geotechnical or environmental report prepared for the Project and made available to Contractor are hereby defined as Technical Data with respect to conditions at the Site under Paragraphs 5.03, 5.04, and 5.06.

45. *Underground Facilities*—All underground pipelines, conduits, ducts, cables, wires, manholes, vaults, tanks, tunnels, or other such facilities or attachments, and any encasements containing such facilities, including but not limited to those that convey electricity, gases, steam, liquid petroleum products, telephone or other communications, fiber optic transmissions, cable television, water, wastewater, storm water, other liquids or chemicals, or traffic or other control systems.
46. *Unit Price Work*—Work to be paid for on the basis of unit prices.
47. *Work*—The entire construction or the various separately identifiable parts thereof required to be provided under the Contract Documents. Work includes and is the result of performing or providing all labor, services, and documentation necessary to produce such construction; furnishing, installing, and incorporating all materials and equipment into such construction; and may include related services such as testing, start-up, and commissioning, all as required by the Contract Documents.
48. *Work Change Directive*—A written directive to Contractor issued on or after the Effective Date of the Contract, signed by Owner and recommended by Engineer, ordering an addition, deletion, or revision in the Work.

1.02 Terminology

- A. The words and terms discussed in the following paragraphs are not defined but, when used in the Bidding Requirements or Contract Documents, have the indicated meaning.
- B. *Intent of Certain Terms or Adjectives*:
 1. The Contract Documents include the terms “as allowed,” “as approved,” “as ordered,” “as directed” or terms of like effect or import to authorize an exercise of professional judgment by Engineer. In addition, the adjectives “reasonable,” “suitable,” “acceptable,” “proper,” “satisfactory,” or adjectives of like effect or import are used to describe an action or determination of Engineer as to the Work. It is intended that such exercise of professional judgment, action, or determination will be solely to evaluate, in general, the Work for compliance with the information in the Contract Documents and with the design concept of the Project as a functioning whole as shown or indicated in the Contract Documents (unless there is a specific statement indicating otherwise). The use of any such term or adjective is not intended to and shall not be effective to assign to Engineer any duty or authority to supervise or direct the performance of the Work, or any duty or authority to undertake responsibility contrary to the provisions of Article 10 or any other provision of the Contract Documents.
- C. *Day*:
 1. The word “day” means a calendar day of 24 hours measured from midnight to the next midnight.
- D. *Defective*:
 1. The word “defective,” when modifying the word “Work,” refers to Work that is unsatisfactory, faulty, or deficient in that it:
 - a. does not conform to the Contract Documents; or
 - b. does not meet the requirements of any applicable inspection, reference standard, test, or approval referred to in the Contract Documents; or

- c. has been damaged prior to Engineer's recommendation of final payment (unless responsibility for the protection thereof has been assumed by Owner at Substantial Completion in accordance with Paragraph 15.03 or 15.04).
- E. *Furnish, Install, Perform, Provide:*
 - 1. The word "furnish," when used in connection with services, materials, or equipment, shall mean to supply and deliver said services, materials, or equipment to the Site (or some other specified location) ready for use or installation and in usable or operable condition.
 - 2. The word "install," when used in connection with services, materials, or equipment, shall mean to put into use or place in final position said services, materials, or equipment complete and ready for intended use.
 - 3. The words "perform" or "provide," when used in connection with services, materials, or equipment, shall mean to furnish and install said services, materials, or equipment complete and ready for intended use.
 - 4. If the Contract Documents establish an obligation of Contractor with respect to specific services, materials, or equipment, but do not expressly use any of the four words "furnish," "install," "perform," or "provide," then Contractor shall furnish and install said services, materials, or equipment complete and ready for intended use.
- F. Unless stated otherwise in the Contract Documents, words or phrases that have a well-known technical or construction industry or trade meaning are used in the Contract Documents in accordance with such recognized meaning.

ARTICLE 2 – PRELIMINARY MATTERS

2.01 Delivery of Bonds and Evidence of Insurance

- A. *Bonds:* When Contractor delivers the executed counterparts of the Agreement to Owner, Contractor shall also deliver to Owner such bonds as Contractor may be required to furnish.
- B. *Evidence of Contractor's Insurance:* When Contractor delivers the executed counterparts of the Agreement to Owner, Contractor shall also deliver to Owner, with copies to each named insured and additional insured (as identified in the Supplementary Conditions or elsewhere in the Contract), the certificates and other evidence of insurance required to be provided by Contractor in accordance with Article 6.
- C. *Evidence of Owner's Insurance:* After receipt of the executed counterparts of the Agreement and all required bonds and insurance documentation, Owner shall promptly deliver to Contractor, with copies to each named insured and additional insured (as identified in the Supplementary Conditions or otherwise), the certificates and other evidence of insurance required to be provided by Owner under Article 6.

2.02 Copies of Documents

- A. Owner shall furnish to Contractor four printed copies of the Contract (including one fully executed counterpart of the Agreement), and one copy in electronic portable document format (PDF). Additional printed copies will be furnished upon request at the cost of reproduction.
- B. Owner shall maintain and safeguard at least one original printed record version of the Contract, including Drawings and Specifications signed and sealed by Engineer and other design professionals. Owner shall make such original printed record version of the Contract available to Contractor for review. Owner may delegate the responsibilities under this provision to Engineer.

2.03 Before Starting Construction

- A. *Preliminary Schedules:* Within 10 days after the Effective Date of the Contract (or as otherwise specifically required by the Contract Documents), Contractor shall submit to Engineer for timely review:

1. a preliminary Progress Schedule indicating the times (numbers of days or dates) for starting and completing the various stages of the Work, including any Milestones specified in the Contract;
2. a preliminary Schedule of Submittals; and
3. a preliminary Schedule of Values for all of the Work which includes quantities and prices of items which when added together equal the Contract Price and subdivides the Work into component parts in sufficient detail to serve as the basis for progress payments during performance of the Work. Such prices will include an appropriate amount of overhead and profit applicable to each item of Work.

2.04 Preconstruction Conference; Designation of Authorized Representatives

- A. Before any Work at the Site is started, a conference attended by Owner, Contractor, Engineer, and others as appropriate will be held to establish a working understanding among the parties as to the Work and to discuss the schedules referred to in Paragraph 2.03.A, procedures for handling Shop Drawings, Samples, and other submittals, processing Applications for Payment, electronic or digital transmittals, and maintaining required records.
- B. At this conference Owner and Contractor each shall designate, in writing, a specific individual to act as its authorized representative with respect to the services and responsibilities under the Contract. Such individuals shall have the authority to transmit and receive information, render decisions relative to the Contract, and otherwise act on behalf of each respective party.

2.05 Initial Acceptance of Schedules

- A. At least 10 days before submission of the first Application for Payment a conference, attended by Contractor, Engineer, and others as appropriate, will be held to review for acceptability to Engineer as provided below the schedules submitted in accordance with Paragraph 2.03.A. Contractor shall have an additional 10 days to make corrections and adjustments and to complete and resubmit the schedules. No progress payment shall be made to Contractor until acceptable schedules are submitted to Engineer.
 1. The Progress Schedule will be acceptable to Engineer if it provides an orderly progression of the Work to completion within the Contract Times. Such acceptance will not impose on Engineer responsibility for the Progress Schedule, for sequencing, scheduling, or progress of the Work, nor interfere with or relieve Contractor from Contractor's full responsibility therefor.
 2. Contractor's Schedule of Submittals will be acceptable to Engineer if it provides a workable arrangement for reviewing and processing the required submittals.
 3. Contractor's Schedule of Values will be acceptable to Engineer as to form and substance if it provides a reasonable allocation of the Contract Price to the component parts of the Work.

2.06 Electronic Transmittals

- A. Except as otherwise stated elsewhere in the Contract, the Owner, Engineer, and Contractor may transmit, and shall accept, Project-related correspondence, text, data, documents, drawings, information, and graphics, including but not limited to Shop Drawings and other submittals, in electronic media or digital format, either directly, or through access to a secure Project website.
- B. If the Contract does not establish protocols for electronic or digital transmittals, then Owner, Engineer, and Contractor shall jointly develop such protocols.
- C. When transmitting items in electronic media or digital format, the transmitting party makes no representations as to long term compatibility, usability, or readability of the items resulting from the recipient's use of software application packages, operating systems, or computer hardware differing from those used in the drafting or transmittal of the items, or from those established in applicable transmittal protocols.

ARTICLE 3 – DOCUMENTS: INTENT, REQUIREMENTS, REUSE**3.01 Intent**

- A. The Contract Documents are complementary; what is required by one is as binding as if required by all.
- B. It is the intent of the Contract Documents to describe a functionally complete project (or part thereof) to be constructed in accordance with the Contract Documents.
- C. Unless otherwise stated in the Contract Documents, if there is a discrepancy between the electronic or digital versions of the Contract Documents (including any printed copies derived from such electronic or digital versions) and the printed record version, the printed record version shall govern.
- D. The Contract supersedes prior negotiations, representations, and agreements, whether written or oral.
- E. Engineer will issue clarifications and interpretations of the Contract Documents as provided herein.

3.02 Reference Standards

- A. Standards Specifications, Codes, Laws and Regulations
 - 1. Reference in the Contract Documents to standard specifications, manuals, reference standards, or codes of any technical society, organization, or association, or to Laws or Regulations, whether such reference be specific or by implication, shall mean the standard specification, manual, reference standard, code, or Laws or Regulations in effect at the time of opening of Bids (or on the Effective Date of the Contract if there were no Bids), except as may be otherwise specifically stated in the Contract Documents.
 - 2. No provision of any such standard specification, manual, reference standard, or code, or any instruction of a Supplier, shall be effective to change the duties or responsibilities of Owner, Contractor, or Engineer, or any of their subcontractors, consultants, agents, or employees, from those set forth in the part of the Contract Documents prepared by or for Engineer. No such provision or instruction shall be effective to assign to Owner, Engineer, or any of their officers, directors, members, partners, employees, agents, consultants, or subcontractors, any duty or authority to supervise or direct the performance of the Work or any duty or authority to undertake responsibility inconsistent with the provisions of the part of the Contract Documents prepared by or for Engineer.

3.03 Reporting and Resolving Discrepancies

- A. *Reporting Discrepancies:*
 - 1. *Contractor's Verification of Figures and Field Measurements:* Before undertaking each part of the Work, Contractor shall carefully study the Contract Documents, and check and verify pertinent figures and dimensions therein, particularly with respect to applicable field measurements. Contractor shall promptly report in writing to Engineer any conflict, error, ambiguity, or discrepancy that Contractor discovers, or has actual knowledge of, and shall not proceed with any Work affected thereby until the conflict, error, ambiguity, or discrepancy is resolved, by a clarification or interpretation by Engineer, or by an amendment or supplement to the Contract Documents issued pursuant to Paragraph 11.01.
 - 2. *Contractor's Review of Contract Documents:* If, before or during the performance of the Work, Contractor discovers any conflict, error, ambiguity, or discrepancy within the Contract Documents, or between the Contract Documents and (a) any applicable Law or Regulation, (b) actual field conditions, (c) any standard specification, manual, reference standard, or code, or (d) any instruction of any Supplier, then Contractor shall promptly report it to Engineer in writing. Contractor shall not proceed with the Work affected thereby (except in an emergency as required by Paragraph 7.15) until the conflict, error, ambiguity, or discrepancy is resolved,

by a clarification or interpretation by Engineer, or by an amendment or supplement to the Contract Documents issued pursuant to Paragraph 11.01.

3. Contractor shall not be liable to Owner or Engineer for failure to report any conflict, error, ambiguity, or discrepancy in the Contract Documents unless Contractor had actual knowledge thereof.

B. *Resolving Discrepancies:*

1. Except as may be otherwise specifically stated in the Contract Documents, the provisions of the part of the Contract Documents prepared by or for Engineer shall take precedence in resolving any conflict, error, ambiguity, or discrepancy between such provisions of the Contract Documents and:
 - a. the provisions of any standard specification, manual, reference standard, or code, or the instruction of any Supplier (whether or not specifically incorporated by reference as a Contract Document); or
 - b. the provisions of any Laws or Regulations applicable to the performance of the Work (unless such an interpretation of the provisions of the Contract Documents would result in violation of such Law or Regulation).

3.04 Requirements of the Contract Documents

- A. During the performance of the Work and until final payment, Contractor and Owner shall submit to the Engineer all matters in question concerning the requirements of the Contract Documents (sometimes referred to as requests for information or interpretation—RFIs), or relating to the acceptability of the Work under the Contract Documents, as soon as possible after such matters arise. Engineer will be the initial interpreter of the requirements of the Contract Documents, and judge of the acceptability of the Work thereunder.
- B. Engineer will, with reasonable promptness, render a written clarification, interpretation, or decision on the issue submitted, or initiate an amendment or supplement to the Contract Documents. Engineer's written clarification, interpretation, or decision will be final and binding on Contractor, unless it appeals by submitting a Change Proposal, and on Owner, unless it appeals by filing a Claim.
- C. If a submitted matter in question concerns terms and conditions of the Contract Documents that do not involve (1) the performance or acceptability of the Work under the Contract Documents, (2) the design (as set forth in the Drawings, Specifications, or otherwise), or (3) other engineering or technical matters, then Engineer will promptly give written notice to Owner and Contractor that Engineer is unable to provide a decision or interpretation. If Owner and Contractor are unable to agree on resolution of such a matter in question, either party may pursue resolution as provided in Article 12.

3.05 Reuse of Documents

- A. Contractor and its Subcontractors and Suppliers shall not:
 1. have or acquire any title to or ownership rights in any of the Drawings, Specifications, or other documents (or copies of any thereof) prepared by or bearing the seal of Engineer or its consultants, including electronic media editions, or reuse any such Drawings, Specifications, other documents, or copies thereof on extensions of the Project or any other project without written consent of Owner and Engineer and specific written verification or adaptation by Engineer; or
 2. have or acquire any title or ownership rights in any other Contract Documents, reuse any such Contract Documents for any purpose without Owner's express written consent, or violate any copyrights pertaining to such Contract Documents.
- B. The prohibitions of this Paragraph 3.05 will survive final payment, or termination of the Contract. Nothing herein shall preclude Contractor from retaining copies of the Contract Documents for record purposes.

ARTICLE 4 – COMMENCEMENT AND PROGRESS OF THE WORK

- 4.01 Commencement of Contract Times; Notice to Proceed
- A. The Contract Times will commence to run on the thirtieth day after the Effective Date of the Contract or, if a Notice to Proceed is given, on the day indicated in the Notice to Proceed. A Notice to Proceed may be given at any time within 30 days after the Effective Date of the Contract. In no event will the Contract Times commence to run later than the sixtieth day after the day of Bid opening or the thirtieth day after the Effective Date of the Contract, whichever date is earlier.
- 4.02 Starting the Work
- A. Contractor shall start to perform the Work on the date when the Contract Times commence to run. No Work shall be done at the Site prior to such date.
- 4.03 Reference Points
- A. Owner shall provide engineering surveys to establish reference points for construction which in Engineer's judgment are necessary to enable Contractor to proceed with the Work. Contractor shall be responsible for laying out the Work, shall protect and preserve the established reference points and property monuments, and shall make no changes or relocations without the prior written approval of Owner. Contractor shall report to Engineer whenever any reference point or property monument is lost or destroyed or requires relocation because of necessary changes in grades or locations, and shall be responsible for the accurate replacement or relocation of such reference points or property monuments by professionally qualified personnel.
- 4.04 Progress Schedule
- A. Contractor shall adhere to the Progress Schedule established in accordance with Paragraph 2.05 as it may be adjusted from time to time as provided below.
1. Contractor shall submit to Engineer for acceptance (to the extent indicated in Paragraph 2.05) proposed adjustments in the Progress Schedule that will not result in changing the Contract Times.
 2. Proposed adjustments in the Progress Schedule that will change the Contract Times shall be submitted in accordance with the requirements of Article 11.
- B. Contractor shall carry on the Work and adhere to the Progress Schedule during all disputes or disagreements with Owner. No Work shall be delayed or postponed pending resolution of any disputes or disagreements, or during any appeal process, except as permitted by Paragraph 16.04, or as Owner and Contractor may otherwise agree in writing.
- 4.05 Delays in Contractor's Progress
- A. If Owner, Engineer, or anyone for whom Owner is responsible, delays, disrupts, or interferes with the performance or progress of the Work, then Contractor shall be entitled to an equitable adjustment in the Contract Times and Contract Price. Contractor's entitlement to an adjustment of the Contract Times is conditioned on such adjustment being essential to Contractor's ability to complete the Work within the Contract Times.
- B. Contractor shall not be entitled to an adjustment in Contract Price or Contract Times for delay, disruption, or interference caused by or within the control of Contractor. Delay, disruption, and interference attributable to and within the control of a Subcontractor or Supplier shall be deemed to be within the control of Contractor.
- C. If Contractor's performance or progress is delayed, disrupted, or interfered with by unanticipated causes not the fault of and beyond the control of Owner, Contractor, and those for which they are responsible, then Contractor shall be entitled to an equitable adjustment in Contract Times. Contractor's entitlement to an adjustment of the Contract Times is conditioned on such adjustment being essential to Contractor's ability to complete the Work within the Contract Times. Such an adjustment shall be Contractor's sole and exclusive remedy for the delays, disruption, and

interference described in this paragraph. Causes of delay, disruption, or interference that may give rise to an adjustment in Contract Times under this paragraph include but are not limited to the following:

1. severe and unavoidable natural catastrophes such as fires, floods, epidemics, and earthquakes;
 2. abnormal weather conditions;
 3. acts or failures to act of utility owners (other than those performing other work at or adjacent to the Site by arrangement with the Owner, as contemplated in Article 8); and
 4. acts of war or terrorism.
- D. Delays, disruption, and interference to the performance or progress of the Work resulting from the existence of a differing subsurface or physical condition, an Underground Facility that was not shown or indicated by the Contract Documents, or not shown or indicated with reasonable accuracy, and those resulting from Hazardous Environmental Conditions, are governed by Article 5.
- E. Paragraph 8.03 governs delays, disruption, and interference to the performance or progress of the Work resulting from the performance of certain other work at or adjacent to the Site.
- F. Contractor shall not be entitled to an adjustment in Contract Price or Contract Times for any delay, disruption, or interference if such delay is concurrent with a delay, disruption, or interference caused by or within the control of Contractor.
- G. Contractor must submit any Change Proposal seeking an adjustment in Contract Price or Contract Times under this paragraph within 30 days of the commencement of the delaying, disrupting, or interfering event.

ARTICLE 5 – AVAILABILITY OF LANDS; SUBSURFACE AND PHYSICAL CONDITIONS; HAZARDOUS ENVIRONMENTAL CONDITIONS

5.01 Availability of Lands

- A. Owner shall furnish the Site. Owner shall notify Contractor of any encumbrances or restrictions not of general application but specifically related to use of the Site with which Contractor must comply in performing the Work.
- B. Upon reasonable written request, Owner shall furnish Contractor with a current statement of record legal title and legal description of the lands upon which permanent improvements are to be made and Owner's interest therein as necessary for giving notice of or filing a mechanic's or construction lien against such lands in accordance with applicable Laws and Regulations.
- C. Contractor shall provide for all additional lands and access thereto that may be required for temporary construction facilities or storage of materials and equipment.

5.02 Use of Site and Other Areas

- A. *Limitation on Use of Site and Other Areas:*
 1. Contractor shall confine construction equipment, temporary construction facilities, the storage of materials and equipment, and the operations of workers to the Site, adjacent areas that Contractor has arranged to use through construction easements or otherwise, and other adjacent areas permitted by Laws and Regulations, and shall not unreasonably encumber the Site and such other adjacent areas with construction equipment or other materials or equipment. Contractor shall assume full responsibility for (a) damage to the Site; (b) damage to any such other adjacent areas used for Contractor's operations; (c) damage to any other adjacent land or areas; and (d) for injuries and losses sustained by the owners or occupants of any such land or areas; provided that such damage or injuries result from the performance of the Work or from other actions or conduct of the Contractor or those for which Contractor is responsible.

2. If a damage or injury claim is made by the owner or occupant of any such land or area because of the performance of the Work, or because of other actions or conduct of the Contractor or those for which Contractor is responsible, Contractor shall (a) take immediate corrective or remedial action as required by Paragraph 7.12, or otherwise; (b) promptly attempt to settle the claim as to all parties through negotiations with such owner or occupant, or otherwise resolve the claim by arbitration or other dispute resolution proceeding, or at law; and (c) to the fullest extent permitted by Laws and Regulations, indemnify and hold harmless Owner and Engineer, and the officers, directors, members, partners, employees, agents, consultants and subcontractors of each and any of them from and against any such claim, and against all costs, losses, and damages (including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals and all court or arbitration or other dispute resolution costs) arising out of or relating to any claim or action, legal or equitable, brought by any such owner or occupant against Owner, Engineer, or any other party indemnified hereunder to the extent caused directly or indirectly, in whole or in part by, or based upon, Contractor's performance of the Work, or because of other actions or conduct of the Contractor or those for which Contractor is responsible.
- B. *Removal of Debris During Performance of the Work:* During the progress of the Work the Contractor shall keep the Site and other adjacent areas free from accumulations of waste materials, rubbish, and other debris. Removal and disposal of such waste materials, rubbish, and other debris shall conform to applicable Laws and Regulations.
- C. *Cleaning:* Prior to Substantial Completion of the Work Contractor shall clean the Site and the Work and make it ready for utilization by Owner. At the completion of the Work Contractor shall remove from the Site and adjacent areas all tools, appliances, construction equipment and machinery, and surplus materials and shall restore to original condition all property not designated for alteration by the Contract Documents.
- D. *Loading of Structures:* Contractor shall not load nor permit any part of any structure to be loaded in any manner that will endanger the structure, nor shall Contractor subject any part of the Work or adjacent structures or land to stresses or pressures that will endanger them.

5.03 Subsurface and Physical Conditions

- A. *Reports and Drawings:* The Supplementary Conditions identify:
 1. those reports known to Owner of explorations and tests of subsurface conditions at or adjacent to the Site;
 2. those drawings known to Owner of physical conditions relating to existing surface or subsurface structures at the Site (except Underground Facilities); and
 3. Technical Data contained in such reports and drawings.
- B. *Reliance by Contractor on Technical Data Authorized:* Contractor may rely upon the accuracy of the Technical Data expressly identified in the Supplementary Conditions with respect to such reports and drawings, but such reports and drawings are not Contract Documents. If no such express identification has been made, then Contractor may rely upon the accuracy of the Technical Data (as defined in Article 1) contained in any geotechnical or environmental report prepared for the Project and made available to Contractor. Except for such reliance on Technical Data, Contractor may not rely upon or make any claim against Owner or Engineer, or any of their officers, directors, members, partners, employees, agents, consultants, or subcontractors, with respect to:
 1. the completeness of such reports and drawings for Contractor's purposes, including, but not limited to, any aspects of the means, methods, techniques, sequences, and procedures of construction to be employed by Contractor, and safety precautions and programs incident thereto; or

2. other data, interpretations, opinions, and information contained in such reports or shown or indicated in such drawings; or
3. any Contractor interpretation of or conclusion drawn from any Technical Data or any such other data, interpretations, opinions, or information.

5.04 Differing Subsurface or Physical Conditions

- A. *Notice by Contractor:* If Contractor believes that any subsurface or physical condition that is uncovered or revealed at the Site either:
1. is of such a nature as to establish that any Technical Data on which Contractor is entitled to rely as provided in Paragraph 5.03 is materially inaccurate; or
 2. is of such a nature as to require a change in the Drawings or Specifications; or
 3. differs materially from that shown or indicated in the Contract Documents; or
 4. is of an unusual nature, and differs materially from conditions ordinarily encountered and generally recognized as inherent in work of the character provided for in the Contract Documents;
- then Contractor shall, promptly after becoming aware thereof and before further disturbing the subsurface or physical conditions or performing any Work in connection therewith (except in an emergency as required by Paragraph 7.15), notify Owner and Engineer in writing about such condition. Contractor shall not further disturb such condition or perform any Work in connection therewith (except with respect to an emergency) until receipt of a written statement permitting Contractor to do so.
- B. *Engineer's Review:* After receipt of written notice as required by the preceding paragraph, Engineer will promptly review the subsurface or physical condition in question; determine the necessity of Owner's obtaining additional exploration or tests with respect to the condition; conclude whether the condition falls within any one or more of the differing site condition categories in Paragraph 5.04.A above; obtain any pertinent cost or schedule information from Contractor; prepare recommendations to Owner regarding the Contractor's resumption of Work in connection with the subsurface or physical condition in question and the need for any change in the Drawings or Specifications; and advise Owner in writing of Engineer's findings, conclusions, and recommendations.
- C. *Owner's Statement to Contractor Regarding Site Condition:* After receipt of Engineer's written findings, conclusions, and recommendations, Owner shall issue a written statement to Contractor (with a copy to Engineer) regarding the subsurface or physical condition in question, addressing the resumption of Work in connection with such condition, indicating whether any change in the Drawings or Specifications will be made, and adopting or rejecting Engineer's written findings, conclusions, and recommendations, in whole or in part.
- D. *Possible Price and Times Adjustments:*
1. Contractor shall be entitled to an equitable adjustment in Contract Price or Contract Times, or both, to the extent that the existence of a differing subsurface or physical condition, or any related delay, disruption, or interference, causes an increase or decrease in Contractor's cost of, or time required for, performance of the Work; subject, however, to the following:
 - a. such condition must fall within any one or more of the categories described in Paragraph 5.04.A;
 - b. with respect to Work that is paid for on a unit price basis, any adjustment in Contract Price will be subject to the provisions of Paragraph 13.03; and,
 - c. Contractor's entitlement to an adjustment of the Contract Times is conditioned on such adjustment being essential to Contractor's ability to complete the Work within the Contract Times.

2. Contractor shall not be entitled to any adjustment in the Contract Price or Contract Times with respect to a subsurface or physical condition if:
 - a. Contractor knew of the existence of such condition at the time Contractor made a commitment to Owner with respect to Contract Price and Contract Times by the submission of a Bid or becoming bound under a negotiated contract, or otherwise; or
 - b. the existence of such condition reasonably could have been discovered or revealed as a result of any examination, investigation, exploration, test, or study of the Site and contiguous areas expressly required by the Bidding Requirements or Contract Documents to be conducted by or for Contractor prior to Contractor's making such commitment; or
 - c. Contractor failed to give the written notice as required by Paragraph 5.04.A.
3. If Owner and Contractor agree regarding Contractor's entitlement to and the amount or extent of any adjustment in the Contract Price or Contract Times, or both, then any such adjustment shall be set forth in a Change Order.
4. Contractor may submit a Change Proposal regarding its entitlement to or the amount or extent of any adjustment in the Contract Price or Contract Times, or both, no later than 30 days after Owner's issuance of the Owner's written statement to Contractor regarding the subsurface or physical condition in question.

5.05 Underground Facilities

- A. *Contractor's Responsibilities:* The information and data shown or indicated in the Contract Documents with respect to existing Underground Facilities at or adjacent to the Site is based on information and data furnished to Owner or Engineer by the owners of such Underground Facilities, including Owner, or by others. Unless it is otherwise expressly provided in the Supplementary Conditions:
 1. Owner and Engineer do not warrant or guarantee the accuracy or completeness of any such information or data provided by others; and
 2. the cost of all of the following will be included in the Contract Price, and Contractor shall have full responsibility for:
 - a. reviewing and checking all information and data regarding existing Underground Facilities at the Site;
 - b. locating all Underground Facilities shown or indicated in the Contract Documents as being at the Site;
 - c. coordination of the Work with the owners (including Owner) of such Underground Facilities, during construction; and
 - d. the safety and protection of all existing Underground Facilities at the Site, and repairing any damage thereto resulting from the Work.
- B. *Notice by Contractor:* If Contractor believes that an Underground Facility that is uncovered or revealed at the Site was not shown or indicated in the Contract Documents, or was not shown or indicated with reasonable accuracy, then Contractor shall, promptly after becoming aware thereof and before further disturbing conditions affected thereby or performing any Work in connection therewith (except in an emergency as required by Paragraph 7.15), identify the owner of such Underground Facility and give written notice to that owner and to Owner and Engineer.
- C. *Engineer's Review:* Engineer will promptly review the Underground Facility and conclude whether such Underground Facility was not shown or indicated in the Contract Documents, or was not shown or indicated with reasonable accuracy; obtain any pertinent cost or schedule information from Contractor; prepare recommendations to Owner regarding the Contractor's resumption of Work in connection with the Underground Facility in question; determine the extent, if any, to which a change is required in the Drawings or Specifications to reflect and document the consequences of the existence or location of the Underground Facility; and advise Owner in writing

EJCDC® -, Standard General Conditions of the Construction Contract.

Copyright © 2013 National Society of Professional Engineers, American Council of Engineering Companies, and American Society of Civil Engineers. All rights reserved.

of Engineer's findings, conclusions, and recommendations. During such time, Contractor shall be responsible for the safety and protection of such Underground Facility.

- D. *Owner's Statement to Contractor Regarding Underground Facility:* After receipt of Engineer's written findings, conclusions, and recommendations, Owner shall issue a written statement to Contractor (with a copy to Engineer) regarding the Underground Facility in question, addressing the resumption of Work in connection with such Underground Facility, indicating whether any change in the Drawings or Specifications will be made, and adopting or rejecting Engineer's written findings, conclusions, and recommendations in whole or in part.
- E. *Possible Price and Times Adjustments:*
1. Contractor shall be entitled to an equitable adjustment in the Contract Price or Contract Times, or both, to the extent that any existing Underground Facility at the Site that was not shown or indicated in the Contract Documents, or was not shown or indicated with reasonable accuracy, or any related delay, disruption, or interference, causes an increase or decrease in Contractor's cost of, or time required for, performance of the Work; subject, however, to the following:
 - a. Contractor did not know of and could not reasonably have been expected to be aware of or to have anticipated the existence or actual location of the Underground Facility in question;
 - b. With respect to Work that is paid for on a unit price basis, any adjustment in Contract Price will be subject to the provisions of Paragraph 13.03;
 - c. Contractor's entitlement to an adjustment of the Contract Times is conditioned on such adjustment being essential to Contractor's ability to complete the Work within the Contract Times; and
 - d. Contractor gave the notice required in Paragraph 5.05.B.
 2. If Owner and Contractor agree regarding Contractor's entitlement to and the amount or extent of any adjustment in the Contract Price or Contract Times, or both, then any such adjustment shall be set forth in a Change Order.
 3. Contractor may submit a Change Proposal regarding its entitlement to or the amount or extent of any adjustment in the Contract Price or Contract Times, or both, no later than 30 days after Owner's issuance of the Owner's written statement to Contractor regarding the Underground Facility in question.

5.06 Hazardous Environmental Conditions at Site

- A. *Reports and Drawings:* The Supplementary Conditions identify:
1. those reports and drawings known to Owner relating to Hazardous Environmental Conditions that have been identified at or adjacent to the Site; and
 2. Technical Data contained in such reports and drawings.
- B. *Reliance by Contractor on Technical Data Authorized:* Contractor may rely upon the accuracy of the Technical Data expressly identified in the Supplementary Conditions with respect to such reports and drawings, but such reports and drawings are not Contract Documents. If no such express identification has been made, then Contractor may rely on the accuracy of the Technical Data (as defined in Article 1) contained in any geotechnical or environmental report prepared for the Project and made available to Contractor. Except for such reliance on Technical Data, Contractor may not rely upon or make any claim against Owner or Engineer, or any of their officers, directors, members, partners, employees, agents, consultants, or subcontractors with respect to:
1. the completeness of such reports and drawings for Contractor's purposes, including, but not limited to, any aspects of the means, methods, techniques, sequences and procedures of construction to be employed by Contractor and safety precautions and programs incident thereto; or

2. other data, interpretations, opinions and information contained in such reports or shown or indicated in such drawings; or
 3. any Contractor interpretation of or conclusion drawn from any Technical Data or any such other data, interpretations, opinions or information.
- C. Contractor shall not be responsible for removing or remediating any Hazardous Environmental Condition encountered, uncovered, or revealed at the Site unless such removal or remediation is expressly identified in the Contract Documents to be within the scope of the Work.
- D. Contractor shall be responsible for controlling, containing, and duly removing all Constituents of Concern brought to the Site by Contractor, Subcontractors, Suppliers, or anyone else for whom Contractor is responsible, and for any associated costs; and for the costs of removing and remediating any Hazardous Environmental Condition created by the presence of any such Constituents of Concern.
- E. If Contractor encounters, uncovers, or reveals a Hazardous Environmental Condition whose removal or remediation is not expressly identified in the Contract Documents as being within the scope of the Work, or if Contractor or anyone for whom Contractor is responsible creates a Hazardous Environmental Condition, then Contractor shall immediately: (1) secure or otherwise isolate such condition; (2) stop all Work in connection with such condition and in any area affected thereby (except in an emergency as required by Paragraph 7.15); and (3) notify Owner and Engineer (and promptly thereafter confirm such notice in writing). Owner shall promptly consult with Engineer concerning the necessity for Owner to retain a qualified expert to evaluate such condition or take corrective action, if any. Promptly after consulting with Engineer, Owner shall take such actions as are necessary to permit Owner to timely obtain required permits and provide Contractor the written notice required by Paragraph 5.06.F. If Contractor or anyone for whom Contractor is responsible created the Hazardous Environmental Condition in question, then Owner may remove and remediate the Hazardous Environmental Condition, and impose a set-off against payments to account for the associated costs.
- F. Contractor shall not resume Work in connection with such Hazardous Environmental Condition or in any affected area until after Owner has obtained any required permits related thereto, and delivered written notice to Contractor either (1) specifying that such condition and any affected area is or has been rendered safe for the resumption of Work, or (2) specifying any special conditions under which such Work may be resumed safely.
- G. If Owner and Contractor cannot agree as to entitlement to or on the amount or extent, if any, of any adjustment in Contract Price or Contract Times, or both, as a result of such Work stoppage or such special conditions under which Work is agreed to be resumed by Contractor, then within 30 days of Owner's written notice regarding the resumption of Work, Contractor may submit a Change Proposal, or Owner may impose a set-off.
- H. If after receipt of such written notice Contractor does not agree to resume such Work based on a reasonable belief it is unsafe, or does not agree to resume such Work under such special conditions, then Owner may order the portion of the Work that is in the area affected by such condition to be deleted from the Work, following the contractual change procedures in Article 11. Owner may have such deleted portion of the Work performed by Owner's own forces or others in accordance with Article 8.
- I. To the fullest extent permitted by Laws and Regulations, Owner shall indemnify and hold harmless Contractor, Subcontractors, and Engineer, and the officers, directors, members, partners, employees, agents, consultants, and subcontractors of each and any of them from and against all claims, costs, losses, and damages (including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals and all court or arbitration or other dispute resolution costs) arising out of or relating to a Hazardous Environmental Condition, provided that

such Hazardous Environmental Condition (1) was not shown or indicated in the Drawings, Specifications, or other Contract Documents, identified as Technical Data entitled to limited reliance pursuant to Paragraph 5.06.B, or identified in the Contract Documents to be included within the scope of the Work, and (2) was not created by Contractor or by anyone for whom Contractor is responsible. Nothing in this Paragraph 5.06.I shall obligate Owner to indemnify any individual or entity from and against the consequences of that individual's or entity's own negligence.

- J. To the fullest extent permitted by Laws and Regulations, Contractor shall indemnify and hold harmless Owner and Engineer, and the officers, directors, members, partners, employees, agents, consultants, and subcontractors of each and any of them from and against all claims, costs, losses, and damages (including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals and all court or arbitration or other dispute resolution costs) arising out of or relating to the failure to control, contain, or remove a Constituent of Concern brought to the Site by Contractor or by anyone for whom Contractor is responsible, or to a Hazardous Environmental Condition created by Contractor or by anyone for whom Contractor is responsible. Nothing in this Paragraph 5.06.J shall obligate Contractor to indemnify any individual or entity from and against the consequences of that individual's or entity's own negligence.
- K. The provisions of Paragraphs 5.03, 5.04, and 5.05 do not apply to the presence of Constituents of Concern or to a Hazardous Environmental Condition uncovered or revealed at the Site.

ARTICLE 6 – BONDS AND INSURANCE

6.01 Performance, Payment, and Other Bonds

- A. Contractor shall furnish a performance bond and a payment bond, each in an amount at least equal to the Contract Price, as security for the faithful performance and payment of all of Contractor's obligations under the Contract. These bonds shall remain in effect until one year after the date when final payment becomes due or until completion of the correction period specified in Paragraph 15.08, whichever is later, except as provided otherwise by Laws or Regulations, the Supplementary Conditions, or other specific provisions of the Contract. Contractor shall also furnish such other bonds as are required by the Supplementary Conditions or other specific provisions of the Contract.
- B. All bonds shall be in the form prescribed by the Contract except as provided otherwise by Laws or Regulations, and shall be executed by such sureties as are named in "Companies Holding Certificates of Authority as Acceptable Sureties on Federal Bonds and as Acceptable Reinsuring Companies" as published in Circular 570 (as amended and supplemented) by the Financial Management Service, Surety Bond Branch, U.S. Department of the Treasury. A bond signed by an agent or attorney-in-fact must be accompanied by a certified copy of that individual's authority to bind the surety. The evidence of authority shall show that it is effective on the date the agent or attorney-in-fact signed the accompanying bond.
- C. Contractor shall obtain the required bonds from surety companies that are duly licensed or authorized in the jurisdiction in which the Project is located to issue bonds in the required amounts.
- D. If the surety on a bond furnished by Contractor is declared bankrupt or becomes insolvent, or its right to do business is terminated in any state or jurisdiction where any part of the Project is located, or the surety ceases to meet the requirements above, then Contractor shall promptly notify Owner and Engineer and shall, within 20 days after the event giving rise to such notification, provide another bond and surety, both of which shall comply with the bond and surety requirements above.

- E. If Contractor has failed to obtain a required bond, Owner may exclude the Contractor from the Site and exercise Owner's termination rights under Article 16.
- F. Upon request, Owner shall provide a copy of the payment bond to any Subcontractor, Supplier, or other person or entity claiming to have furnished labor or materials used in the performance of the Work.

6.02 Insurance—General Provisions

- A. Owner and Contractor shall obtain and maintain insurance as required in this Article and in the Supplementary Conditions.
- B. All insurance required by the Contract to be purchased and maintained by Owner or Contractor shall be obtained from insurance companies that are duly licensed or authorized, in the state or jurisdiction in which the Project is located, to issue insurance policies for the required limits and coverages. Unless a different standard is indicated in the Supplementary Conditions, all companies that provide insurance policies required under this Contract shall have an A.M. Best rating of A-VII or better.
- C. Contractor shall deliver to Owner, with copies to each named insured and additional insured (as identified in this Article, in the Supplementary Conditions, or elsewhere in the Contract), certificates of insurance establishing that Contractor has obtained and is maintaining the policies, coverages, and endorsements required by the Contract. Upon request by Owner or any other insured, Contractor shall also furnish other evidence of such required insurance, including but not limited to copies of policies and endorsements, and documentation of applicable self-insured retentions and deductibles. Contractor may block out (redact) any confidential premium or pricing information contained in any policy or endorsement furnished under this provision.
- D. Owner shall deliver to Contractor, with copies to each named insured and additional insured (as identified in this Article, the Supplementary Conditions, or elsewhere in the Contract), certificates of insurance establishing that Owner has obtained and is maintaining the policies, coverages, and endorsements required of Owner by the Contract (if any). Upon request by Contractor or any other insured, Owner shall also provide other evidence of such required insurance (if any), including but not limited to copies of policies and endorsements, and documentation of applicable self-insured retentions and deductibles. Owner may block out (redact) any confidential premium or pricing information contained in any policy or endorsement furnished under this provision.
- E. Failure of Owner or Contractor to demand such certificates or other evidence of the other party's full compliance with these insurance requirements, or failure of Owner or Contractor to identify a deficiency in compliance from the evidence provided, shall not be construed as a waiver of the other party's obligation to obtain and maintain such insurance.
- F. If either party does not purchase or maintain all of the insurance required of such party by the Contract, such party shall notify the other party in writing of such failure to purchase prior to the start of the Work, or of such failure to maintain prior to any change in the required coverage.
- G. If Contractor has failed to obtain and maintain required insurance, Owner may exclude the Contractor from the Site, impose an appropriate set-off against payment, and exercise Owner's termination rights under Article 16.
- H. Without prejudice to any other right or remedy, if a party has failed to obtain required insurance, the other party may elect to obtain equivalent insurance to protect such other party's interests at the expense of the party who was required to provide such coverage, and the Contract Price shall be adjusted accordingly.
- I. Owner does not represent that insurance coverage and limits established in this Contract necessarily will be adequate to protect Contractor or Contractor's interests.

- J. The insurance and insurance limits required herein shall not be deemed as a limitation on Contractor's liability under the indemnities granted to Owner and other individuals and entities in the Contract.

6.03 Contractor's Insurance

- A. *Workers' Compensation*: Contractor shall purchase and maintain workers' compensation and employer's liability insurance for:
1. claims under workers' compensation, disability benefits, and other similar employee benefit acts.
 2. United States Longshoreman and Harbor Workers' Compensation Act and Jones Act coverage (if applicable).
 3. claims for damages because of bodily injury, occupational sickness or disease, or death of Contractor's employees (by stop-gap endorsement in monopolist worker's compensation states).
 4. Foreign voluntary worker compensation (if applicable).
- B. *Commercial General Liability—Claims Covered*: Contractor shall purchase and maintain commercial general liability insurance, covering all operations by or on behalf of Contractor, on an occurrence basis, against:
1. claims for damages because of bodily injury, sickness or disease, or death of any person other than Contractor's employees.
 2. claims for damages insured by reasonably available personal injury liability coverage.
 3. claims for damages, other than to the Work itself, because of injury to or destruction of tangible property wherever located, including loss of use resulting therefrom.
- C. *Commercial General Liability—Form and Content*: Contractor's commercial liability policy shall be written on a 1996 (or later) ISO commercial general liability form (occurrence form) and include the following coverages and endorsements:
1. Products and completed operations coverage:
 - a. Such insurance shall be maintained for three years after final payment.
 - b. Contractor shall furnish Owner and each other additional insured (as identified in the Supplementary Conditions or elsewhere in the Contract) evidence of continuation of such insurance at final payment and three years thereafter.
 2. Blanket contractual liability coverage, to the extent permitted by law, including but not limited to coverage of Contractor's contractual indemnity obligations in Paragraph 7.18.
 3. Broad form property damage coverage.
 4. Severability of interest.
 5. Underground, explosion, and collapse coverage.
 6. Personal injury coverage.
 7. Additional insured endorsements that include both ongoing operations and products and completed operations coverage through ISO Endorsements CG 20 10 10 01 and CG 20 37 10 01 (together); or CG 20 10 07 04 and CG 20 37 07 04 (together); or their equivalent.
 8. For design professional additional insureds, ISO Endorsement CG 20 32 07 04, "Additional Insured—Engineers, Architects or Surveyors Not Engaged by the Named Insured" or its equivalent.
- D. *Automobile liability*: Contractor shall purchase and maintain automobile liability insurance against claims for damages because of bodily injury or death of any person or property damage arising out of the ownership, maintenance, or use of any motor vehicle. The automobile liability policy shall be written on an occurrence basis.
- E. *Umbrella or excess liability*: Contractor shall purchase and maintain umbrella or excess liability insurance written over the underlying employer's liability, commercial general liability, and

automobile liability insurance described in the paragraphs above. Subject to industry-standard exclusions, the coverage afforded shall follow form as to each and every one of the underlying policies.

- F. *Contractor's pollution liability insurance*: Contractor shall purchase and maintain a policy covering third-party injury and property damage claims, including clean-up costs, as a result of pollution conditions arising from Contractor's operations and completed operations. This insurance shall be maintained for no less than three years after final completion.
- G. *Additional insureds*: The Contractor's commercial general liability, automobile liability, umbrella or excess, and pollution liability policies shall include and list as additional insureds Owner and Engineer, and any individuals or entities identified in the Supplementary Conditions; include coverage for the respective officers, directors, members, partners, employees, agents, consultants, and subcontractors of each and any of all such additional insureds; and the insurance afforded to these additional insureds shall provide primary coverage for all claims covered thereby (including as applicable those arising from both ongoing and completed operations) on a non-contributory basis. Contractor shall obtain all necessary endorsements to support these requirements.
- H. *Contractor's professional liability insurance*: If Contractor will provide or furnish professional services under this Contract, through a delegation of professional design services or otherwise, then Contractor shall be responsible for purchasing and maintaining applicable professional liability insurance. This insurance shall provide protection against claims arising out of performance of professional design or related services, and caused by a negligent error, omission, or act for which the insured party is legally liable. It shall be maintained throughout the duration of the Contract and for a minimum of two years after Substantial Completion. If such professional design services are performed by a Subcontractor, and not by Contractor itself, then the requirements of this paragraph may be satisfied through the purchasing and maintenance of such insurance by such Subcontractor.
- I. *General provisions*: The policies of insurance required by this Paragraph 6.03 shall:
 - 1. include at least the specific coverages provided in this Article.
 - 2. be written for not less than the limits of liability provided in this Article and in the Supplementary Conditions, or required by Laws or Regulations, whichever is greater.
 - 3. contain a provision or endorsement that the coverage afforded will not be canceled, materially changed, or renewal refused until at least 10 days prior written notice has been given to Contractor. Within three days of receipt of any such written notice, Contractor shall provide a copy of the notice to Owner, Engineer, and each other insured under the policy.
 - 4. remain in effect at least until final payment (and longer if expressly required in this Article) and at all times thereafter when Contractor may be correcting, removing, or replacing defective Work as a warranty or correction obligation, or otherwise, or returning to the Site to conduct other tasks arising from the Contract Documents.
 - 5. be appropriate for the Work being performed and provide protection from claims that may arise out of or result from Contractor's performance of the Work and Contractor's other obligations under the Contract Documents, whether it is to be performed by Contractor, any Subcontractor or Supplier, or by anyone directly or indirectly employed by any of them to perform any of the Work, or by anyone for whose acts any of them may be liable.
- J. The coverage requirements for specific policies of insurance must be met by such policies, and not by reference to excess or umbrella insurance provided in other policies.

6.04 Owner's Liability Insurance

- A. In addition to the insurance required to be provided by Contractor under Paragraph 6.03, Owner, at Owner's option, may purchase and maintain at Owner's expense Owner's own liability insurance as will protect Owner against claims which may arise from operations under the Contract Documents.

- B. Owner's liability policies, if any, operate separately and independently from policies required to be provided by Contractor, and Contractor cannot rely upon Owner's liability policies for any of Contractor's obligations to the Owner, Engineer, or third parties.

6.05 Property Insurance

- A. *Builder's Risk*: Unless otherwise provided in the Supplementary Conditions, Contractor shall purchase and maintain builder's risk insurance upon the Work on a completed value basis, in the amount of the full insurable replacement cost thereof (subject to such deductible amounts as may be provided in the Supplementary Conditions or required by Laws and Regulations). This insurance shall:
 - 1. include the Owner and Contractor as named insureds, and all Subcontractors, and any individuals or entities required by the Supplementary Conditions to be insured under such builder's risk policy, as insureds or named insureds. For purposes of the remainder of this Paragraph 6.05, Paragraphs 6.06 and 6.07, and any corresponding Supplementary Conditions, the parties required to be insured shall collectively be referred to as "insureds."
 - 2. be written on a builder's risk "all risk" policy form that shall at least include insurance for physical loss or damage to the Work, temporary buildings, falsework, and materials and equipment in transit, and shall insure against at least the following perils or causes of loss: fire; lightning; windstorm; riot; civil commotion; terrorism; vehicle impact; aircraft; smoke; theft; vandalism and malicious mischief; mechanical breakdown, boiler explosion, and artificially generated electric current; earthquake; volcanic activity, and other earth movement; flood; collapse; explosion; debris removal; demolition occasioned by enforcement of Laws and Regulations; water damage (other than that caused by flood); and such other perils or causes of loss as may be specifically required by the Supplementary Conditions. If insurance against mechanical breakdown, boiler explosion, and artificially generated electric current; earthquake; volcanic activity, and other earth movement; or flood, are not commercially available under builder's risk policies, by endorsement or otherwise, such insurance may be provided through other insurance policies acceptable to Owner and Contractor.
 - 3. cover, as insured property, at least the following: (a) the Work and all materials, supplies, machinery, apparatus, equipment, fixtures, and other property of a similar nature that are to be incorporated into or used in the preparation, fabrication, construction, erection, or completion of the Work, including Owner-furnished or assigned property; (b) spare parts inventory required within the scope of the Contract; and (c) temporary works which are not intended to form part of the permanent constructed Work but which are intended to provide working access to the Site, or to the Work under construction, or which are intended to provide temporary support for the Work under construction, including scaffolding, form work, fences, shoring, falsework, and temporary structures.
 - 4. cover expenses incurred in the repair or replacement of any insured property (including but not limited to fees and charges of engineers and architects).
 - 5. extend to cover damage or loss to insured property while in temporary storage at the Site or in a storage location outside the Site (but not including property stored at the premises of a manufacturer or Supplier).
 - 6. extend to cover damage or loss to insured property while in transit.
 - 7. allow for partial occupation or use of the Work by Owner, such that those portions of the Work that are not yet occupied or used by Owner shall remain covered by the builder's risk insurance.
 - 8. allow for the waiver of the insurer's subrogation rights, as set forth below.
 - 9. provide primary coverage for all losses and damages caused by the perils or causes of loss covered.

10. not include a co-insurance clause.
 11. include an exception for ensuing losses from physical damage or loss with respect to any defective workmanship, design, or materials exclusions.
 12. include performance/hot testing and start-up.
 13. be maintained in effect, subject to the provisions herein regarding Substantial Completion and partial occupancy or use of the Work by Owner, until the Work is complete.
- B. *Notice of Cancellation or Change:* All the policies of insurance (and the certificates or other evidence thereof) required to be purchased and maintained in accordance with this Paragraph 6.05 will contain a provision or endorsement that the coverage afforded will not be canceled or materially changed or renewal refused until at least 10 days prior written notice has been given to the purchasing policyholder. Within three days of receipt of any such written notice, the purchasing policyholder shall provide a copy of the notice to each other insured.
- C. *Deductibles:* The purchaser of any required builder's risk or property insurance shall pay for costs not covered because of the application of a policy deductible.
- D. *Partial Occupancy or Use by Owner:* If Owner will occupy or use a portion or portions of the Work prior to Substantial Completion of all the Work as provided in Paragraph 15.04, then Owner (directly, if it is the purchaser of the builder's risk policy, or through Contractor) will provide notice of such occupancy or use to the builder's risk insurer. The builder's risk insurance shall not be canceled or permitted to lapse on account of any such partial use or occupancy; rather, those portions of the Work that are occupied or used by Owner may come off the builder's risk policy, while those portions of the Work not yet occupied or used by Owner shall remain covered by the builder's risk insurance.
- E. *Additional Insurance:* If Contractor elects to obtain other special insurance to be included in or supplement the builder's risk or property insurance policies provided under this Paragraph 6.05, it may do so at Contractor's expense.
- F. *Insurance of Other Property:* If the express insurance provisions of the Contract do not require or address the insurance of a property item or interest, such as tools, construction equipment, or other personal property owned by Contractor, a Subcontractor, or an employee of Contractor or a Subcontractor, then the entity or individual owning such property item will be responsible for deciding whether to insure it, and if so in what amount.

6.06 Waiver of Rights

- A. All policies purchased in accordance with Paragraph 6.05, expressly including the builder's risk policy, shall contain provisions to the effect that in the event of payment of any loss or damage the insurers will have no rights of recovery against any insureds thereunder, or against Engineer or its consultants, or their officers, directors, members, partners, employees, agents, consultants, or subcontractors. Owner and Contractor waive all rights against each other and the respective officers, directors, members, partners, employees, agents, consultants, and subcontractors of each and any of them, for all losses and damages caused by, arising out of, or resulting from any of the perils or causes of loss covered by such policies and any other property insurance applicable to the Work; and, in addition, waive all such rights against Engineer, its consultants, all Subcontractors, all individuals or entities identified in the Supplementary Conditions as insureds, and the officers, directors, members, partners, employees, agents, consultants, and subcontractors of each and any of them, under such policies for losses and damages so caused. None of the above waivers shall extend to the rights that any party making such waiver may have to the proceeds of insurance held by Owner or Contractor as trustee or fiduciary, or otherwise payable under any policy so issued.
- B. Owner waives all rights against Contractor, Subcontractors, and Engineer, and the officers, directors, members, partners, employees, agents, consultants and subcontractors of each and any of them, for:

1. loss due to business interruption, loss of use, or other consequential loss extending beyond direct physical loss or damage to Owner's property or the Work caused by, arising out of, or resulting from fire or other perils whether or not insured by Owner; and
 2. loss or damage to the completed Project or part thereof caused by, arising out of, or resulting from fire or other insured peril or cause of loss covered by any property insurance maintained on the completed Project or part thereof by Owner during partial occupancy or use pursuant to Paragraph 15.04, after Substantial Completion pursuant to Paragraph 15.03, or after final payment pursuant to Paragraph 15.06.
- C. Any insurance policy maintained by Owner covering any loss, damage or consequential loss referred to in Paragraph 6.06.B shall contain provisions to the effect that in the event of payment of any such loss, damage, or consequential loss, the insurers will have no rights of recovery against Contractor, Subcontractors, or Engineer, or the officers, directors, members, partners, employees, agents, consultants, or subcontractors of each and any of them.
- D. Contractor shall be responsible for assuring that the agreement under which a Subcontractor performs a portion of the Work contains provisions whereby the Subcontractor waives all rights against Owner, Contractor, all individuals or entities identified in the Supplementary Conditions as insureds, the Engineer and its consultants, and the officers, directors, members, partners, employees, agents, consultants, and subcontractors of each and any of them, for all losses and damages caused by, arising out of, relating to, or resulting from any of the perils or causes of loss covered by builder's risk insurance and any other property insurance applicable to the Work.
- 6.07 Receipt and Application of Property Insurance Proceeds
- A. Any insured loss under the builder's risk and other policies of insurance required by Paragraph 6.05 will be adjusted and settled with the named insured that purchased the policy. Such named insured shall act as fiduciary for the other insureds, and give notice to such other insureds that adjustment and settlement of a claim is in progress. Any other insured may state its position regarding a claim for insured loss in writing within 15 days after notice of such claim.
- B. Proceeds for such insured losses may be made payable by the insurer either jointly to multiple insureds, or to the named insured that purchased the policy in its own right and as fiduciary for other insureds, subject to the requirements of any applicable mortgage clause. A named insured receiving insurance proceeds under the builder's risk and other policies of insurance required by Paragraph 6.05 shall distribute such proceeds in accordance with such agreement as the parties in interest may reach, or as otherwise required under the dispute resolution provisions of this Contract or applicable Laws and Regulations.
- C. If no other special agreement is reached, the damaged Work shall be repaired or replaced, the money so received applied on account thereof, and the Work and the cost thereof covered by Change Order, if needed.

ARTICLE 7 – CONTRACTOR'S RESPONSIBILITIES

7.01 Supervision and Superintendence

- A. Contractor shall supervise, inspect, and direct the Work competently and efficiently, devoting such attention thereto and applying such skills and expertise as may be necessary to perform the Work in accordance with the Contract Documents. Contractor shall be solely responsible for the means, methods, techniques, sequences, and procedures of construction.
- B. At all times during the progress of the Work, Contractor shall assign a competent resident superintendent who shall not be replaced without written notice to Owner and Engineer except under extraordinary circumstances.

7.02 Labor; Working Hours

- A. Contractor shall provide competent, suitably qualified personnel to survey and lay out the Work and perform construction as required by the Contract Documents. Contractor shall at all times maintain good discipline and order at the Site.
- B. Except as otherwise required for the safety or protection of persons or the Work or property at the Site or adjacent thereto, and except as otherwise stated in the Contract Documents, all Work at the Site shall be performed during regular working hours, Monday through Friday. Contractor will not perform Work on a Saturday, Sunday, or any legal holiday. Contractor may perform Work outside regular working hours or on Saturdays, Sundays, or legal holidays only with Owner's written consent, which will not be unreasonably withheld.

7.03 Services, Materials, and Equipment

- A. Unless otherwise specified in the Contract Documents, Contractor shall provide and assume full responsibility for all services, materials, equipment, labor, transportation, construction equipment and machinery, tools, appliances, fuel, power, light, heat, telephone, water, sanitary facilities, temporary facilities, and all other facilities and incidentals necessary for the performance, testing, start up, and completion of the Work, whether or not such items are specifically called for in the Contract Documents.
- B. All materials and equipment incorporated into the Work shall be of good quality and new, except as otherwise provided in the Contract Documents. All special warranties and guarantees required by the Specifications shall expressly run to the benefit of Owner. If required by Engineer, Contractor shall furnish satisfactory evidence (including reports of required tests) as to the source, kind, and quality of materials and equipment.
- C. All materials and equipment shall be stored, applied, installed, connected, erected, protected, used, cleaned, and conditioned in accordance with instructions of the applicable Supplier, except as otherwise may be provided in the Contract Documents.

7.04 "Or Equals"

- A. Whenever an item of material or equipment is specified or described in the Contract Documents by using the name of a proprietary item or the name of a particular Supplier, the Contract Price has been based upon Contractor furnishing such item as specified. The specification or description of such an item is intended to establish the type, function, appearance, and quality required. Unless the specification or description contains or is followed by words reading that no like, equivalent, or "or equal" item is permitted, Contractor may request that Engineer authorize the use of other items of material or equipment, or items from other proposed suppliers under the circumstances described below.
 - 1. If Engineer in its sole discretion determines that an item of material or equipment proposed by Contractor is functionally equal to that named and sufficiently similar so that no change in related Work will be required, Engineer shall deem it an "or equal" item. For the purposes of this paragraph, a proposed item of material or equipment will be considered functionally equal to an item so named if:
 - a. in the exercise of reasonable judgment Engineer determines that:
 - 1) it is at least equal in materials of construction, quality, durability, appearance, strength, and design characteristics;
 - 2) it will reliably perform at least equally well the function and achieve the results imposed by the design concept of the completed Project as a functioning whole;
 - 3) it has a proven record of performance and availability of responsive service; and
 - 4) it is not objectionable to Owner.
 - b. Contractor certifies that, if approved and incorporated into the Work:
 - 1) there will be no increase in cost to the Owner or increase in Contract Times; and

EJCDC® -, Standard General Conditions of the Construction Contract.

Copyright © 2013 National Society of Professional Engineers, American Council of Engineering Companies, and American Society of Civil Engineers. All rights reserved.

- 2) it will conform substantially to the detailed requirements of the item named in the Contract Documents.
- B. *Contractor's Expense*: Contractor shall provide all data in support of any proposed "or equal" item at Contractor's expense.
- C. *Engineer's Evaluation and Determination*: Engineer will be allowed a reasonable time to evaluate each "or-equal" request. Engineer may require Contractor to furnish additional data about the proposed "or-equal" item. Engineer will be the sole judge of acceptability. No "or-equal" item will be ordered, furnished, installed, or utilized until Engineer's review is complete and Engineer determines that the proposed item is an "or-equal", which will be evidenced by an approved Shop Drawing or other written communication. Engineer will advise Contractor in writing of any negative determination.
- D. *Effect of Engineer's Determination*: Neither approval nor denial of an "or-equal" request shall result in any change in Contract Price. The Engineer's denial of an "or-equal" request shall be final and binding, and may not be reversed through an appeal under any provision of the Contract Documents.
- E. *Treatment as a Substitution Request*: If Engineer determines that an item of material or equipment proposed by Contractor does not qualify as an "or-equal" item, Contractor may request that Engineer considered the proposed item as a substitute pursuant to Paragraph 7.05.

7.05 Substitutes

- A. Unless the specification or description of an item of material or equipment required to be furnished under the Contract Documents contains or is followed by words reading that no substitution is permitted, Contractor may request that Engineer authorize the use of other items of material or equipment under the circumstances described below. To the extent possible such requests shall be made before commencement of related construction at the Site.
 1. Contractor shall submit sufficient information as provided below to allow Engineer to determine if the item of material or equipment proposed is functionally equivalent to that named and an acceptable substitute therefor. Engineer will not accept requests for review of proposed substitute items of material or equipment from anyone other than Contractor.
 2. The requirements for review by Engineer will be as set forth in Paragraph 7.05.B, as supplemented by the Specifications, and as Engineer may decide is appropriate under the circumstances.
 3. Contractor shall make written application to Engineer for review of a proposed substitute item of material or equipment that Contractor seeks to furnish or use. The application:
 - a. shall certify that the proposed substitute item will:
 - 1) perform adequately the functions and achieve the results called for by the general design,
 - 2) be similar in substance to that specified, and
 - 3) be suited to the same use as that specified.
 - b. will state:
 - 1) the extent, if any, to which the use of the proposed substitute item will necessitate a change in Contract Times,
 - 2) whether use of the proposed substitute item in the Work will require a change in any of the Contract Documents (or in the provisions of any other direct contract with Owner for other work on the Project) to adapt the design to the proposed substitute item, and
 - 3) whether incorporation or use of the proposed substitute item in connection with the Work is subject to payment of any license fee or royalty.

- c. will identify:
 - 1) all variations of the proposed substitute item from that specified, and
 - 2) available engineering, sales, maintenance, repair, and replacement services.
 - d. shall contain an itemized estimate of all costs or credits that will result directly or indirectly from use of such substitute item, including but not limited to changes in Contract Price, shared savings, costs of redesign, and claims of other contractors affected by any resulting change.
- B. *Engineer's Evaluation and Determination:* Engineer will be allowed a reasonable time to evaluate each substitute request, and to obtain comments and direction from Owner. Engineer may require Contractor to furnish additional data about the proposed substitute item. Engineer will be the sole judge of acceptability. No substitute will be ordered, furnished, installed, or utilized until Engineer's review is complete and Engineer determines that the proposed item is an acceptable substitute. Engineer's determination will be evidenced by a Field Order or a proposed Change Order accounting for the substitution itself and all related impacts, including changes in Contract Price or Contract Times. Engineer will advise Contractor in writing of any negative determination.
- C. *Special Guarantee:* Owner may require Contractor to furnish at Contractor's expense a special performance guarantee or other surety with respect to any substitute.
- D. *Reimbursement of Engineer's Cost:* Engineer will record Engineer's costs in evaluating a substitute proposed or submitted by Contractor. Whether or not Engineer approves a substitute so proposed or submitted by Contractor, Contractor shall reimburse Owner for the reasonable charges of Engineer for evaluating each such proposed substitute. Contractor shall also reimburse Owner for the reasonable charges of Engineer for making changes in the Contract Documents (or in the provisions of any other direct contract with Owner) resulting from the acceptance of each proposed substitute.
- E. *Contractor's Expense:* Contractor shall provide all data in support of any proposed substitute at Contractor's expense.
- F. *Effect of Engineer's Determination:* If Engineer approves the substitution request, Contractor shall execute the proposed Change Order and proceed with the substitution. The Engineer's denial of a substitution request shall be final and binding, and may not be reversed through an appeal under any provision of the Contract Documents. Contractor may challenge the scope of reimbursement costs imposed under Paragraph 7.05.D, by timely submittal of a Change Proposal.

7.06 Concerning Subcontractors, Suppliers, and Others

- A. Contractor may retain Subcontractors and Suppliers for the performance of parts of the Work. Such Subcontractors and Suppliers must be acceptable to Owner.
- B. Contractor shall retain specific Subcontractors, Suppliers, or other individuals or entities for the performance of designated parts of the Work if required by the Contract to do so.
- C. Subsequent to the submittal of Contractor's Bid or final negotiation of the terms of the Contract, Owner may not require Contractor to retain any Subcontractor, Supplier, or other individual or entity to furnish or perform any of the Work against which Contractor has reasonable objection.
- D. Prior to entry into any binding subcontract or purchase order, Contractor shall submit to Owner the identity of the proposed Subcontractor or Supplier (unless Owner has already deemed such proposed Subcontractor or Supplier acceptable, during the bidding process or otherwise). Such proposed Subcontractor or Supplier shall be deemed acceptable to Owner unless Owner raises a substantive, reasonable objection within five days.
- E. Owner may require the replacement of any Subcontractor, Supplier, or other individual or entity retained by Contractor to perform any part of the Work. Owner also may require Contractor to retain specific replacements; provided, however, that Owner may not require a replacement to which Contractor has a reasonable objection. If Contractor has submitted the identity of certain

Subcontractors, Suppliers, or other individuals or entities for acceptance by Owner, and Owner has accepted it (either in writing or by failing to make written objection thereto), then Owner may subsequently revoke the acceptance of any such Subcontractor, Supplier, or other individual or entity so identified solely on the basis of substantive, reasonable objection after due investigation. Contractor shall submit an acceptable replacement for the rejected Subcontractor, Supplier, or other individual or entity.

- F. If Owner requires the replacement of any Subcontractor, Supplier, or other individual or entity retained by Contractor to perform any part of the Work, then Contractor shall be entitled to an adjustment in Contract Price or Contract Times, or both, with respect to the replacement; and Contractor shall initiate a Change Proposal for such adjustment within 30 days of Owner's requirement of replacement.
- G. No acceptance by Owner of any such Subcontractor, Supplier, or other individual or entity, whether initially or as a replacement, shall constitute a waiver of the right of Owner to the completion of the Work in accordance with the Contract Documents.
- H. On a monthly basis Contractor shall submit to Engineer a complete list of all Subcontractors and Suppliers having a direct contract with Contractor, and of all other Subcontractors and Suppliers known to Contractor at the time of submittal.
- I. Contractor shall be fully responsible to Owner and Engineer for all acts and omissions of the Subcontractors, Suppliers, and other individuals or entities performing or furnishing any of the Work just as Contractor is responsible for Contractor's own acts and omissions.
- J. Contractor shall be solely responsible for scheduling and coordinating the work of Subcontractors, Suppliers, and all other individuals or entities performing or furnishing any of the Work.
- K. Contractor shall restrict all Subcontractors, Suppliers, and such other individuals or entities performing or furnishing any of the Work from communicating with Engineer or Owner, except through Contractor or in case of an emergency, or as otherwise expressly allowed herein.
- L. The divisions and sections of the Specifications and the identifications of any Drawings shall not control Contractor in dividing the Work among Subcontractors or Suppliers or delineating the Work to be performed by any specific trade.
- M. All Work performed for Contractor by a Subcontractor or Supplier shall be pursuant to an appropriate contractual agreement that specifically binds the Subcontractor or Supplier to the applicable terms and conditions of the Contract Documents for the benefit of Owner and Engineer.
- N. Owner may furnish to any Subcontractor or Supplier, to the extent practicable, information about amounts paid to Contractor on account of Work performed for Contractor by the particular Subcontractor or Supplier.
- O. Nothing in the Contract Documents:
 - 1. shall create for the benefit of any such Subcontractor, Supplier, or other individual or entity any contractual relationship between Owner or Engineer and any such Subcontractor, Supplier, or other individual or entity; nor
 - 2. shall create any obligation on the part of Owner or Engineer to pay or to see to the payment of any money due any such Subcontractor, Supplier, or other individual or entity except as may otherwise be required by Laws and Regulations.

7.07 Patent Fees and Royalties

- A. Contractor shall pay all license fees and royalties and assume all costs incident to the use in the performance of the Work or the incorporation in the Work of any invention, design, process, product, or device which is the subject of patent rights or copyrights held by others. If a particular invention, design, process, product, or device is specified in the Contract Documents for use in the performance of the Work and if, to the actual knowledge of Owner or Engineer, its use is subject to

patent rights or copyrights calling for the payment of any license fee or royalty to others, the existence of such rights shall be disclosed by Owner in the Contract Documents.

- B. To the fullest extent permitted by Laws and Regulations, Owner shall indemnify and hold harmless Contractor, and its officers, directors, members, partners, employees, agents, consultants, and subcontractors from and against all claims, costs, losses, and damages (including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals, and all court or arbitration or other dispute resolution costs) arising out of or relating to any infringement of patent rights or copyrights incident to the use in the performance of the Work or resulting from the incorporation in the Work of any invention, design, process, product, or device specified in the Contract Documents, but not identified as being subject to payment of any license fee or royalty to others required by patent rights or copyrights.
- C. To the fullest extent permitted by Laws and Regulations, Contractor shall indemnify and hold harmless Owner and Engineer, and the officers, directors, members, partners, employees, agents, consultants and subcontractors of each and any of them from and against all claims, costs, losses, and damages (including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals and all court or arbitration or other dispute resolution costs) arising out of or relating to any infringement of patent rights or copyrights incident to the use in the performance of the Work or resulting from the incorporation in the Work of any invention, design, process, product, or device not specified in the Contract Documents.

7.08 Permits

- A. Unless otherwise provided in the Contract Documents, Contractor shall obtain and pay for all construction permits and licenses. Owner shall assist Contractor, when necessary, in obtaining such permits and licenses. Contractor shall pay all governmental charges and inspection fees necessary for the prosecution of the Work which are applicable at the time of the submission of Contractor's Bid (or when Contractor became bound under a negotiated contract). Owner shall pay all charges of utility owners for connections for providing permanent service to the Work

7.09 Taxes

- A. Contractor shall pay all sales, consumer, use, and other similar taxes required to be paid by Contractor in accordance with the Laws and Regulations of the place of the Project which are applicable during the performance of the Work.

7.10 Laws and Regulations

- A. Contractor shall give all notices required by and shall comply with all Laws and Regulations applicable to the performance of the Work. Except where otherwise expressly required by applicable Laws and Regulations, neither Owner nor Engineer shall be responsible for monitoring Contractor's compliance with any Laws or Regulations.
- B. If Contractor performs any Work or takes any other action knowing or having reason to know that it is contrary to Laws or Regulations, Contractor shall bear all resulting costs and losses, and shall indemnify and hold harmless Owner and Engineer, and the officers, directors, members, partners, employees, agents, consultants, and subcontractors of each and any of them from and against all claims, costs, losses, and damages (including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals and all court or arbitration or other dispute resolution costs) arising out of or relating to such Work or other action. It shall not be Contractor's responsibility to make certain that the Work described in the Contract Documents is in accordance with Laws and Regulations, but this shall not relieve Contractor of Contractor's obligations under Paragraph 3.03.
- C. Owner or Contractor may give notice to the other party of any changes after the submission of Contractor's Bid (or after the date when Contractor became bound under a negotiated contract) in Laws or Regulations having an effect on the cost or time of performance of the Work, including but

not limited to changes in Laws or Regulations having an effect on procuring permits and on sales, use, value-added, consumption, and other similar taxes. If Owner and Contractor are unable to agree on entitlement to or on the amount or extent, if any, of any adjustment in Contract Price or Contract Times resulting from such changes, then within 30 days of such notice Contractor may submit a Change Proposal, or Owner may initiate a Claim.

7.11 Record Documents

- A. Contractor shall maintain in a safe place at the Site one printed record copy of all Drawings, Specifications, Addenda, Change Orders, Work Change Directives, Field Orders, written interpretations and clarifications, and approved Shop Drawings. Contractor shall keep such record documents in good order and annotate them to show changes made during construction. These record documents, together with all approved Samples, will be available to Engineer for reference. Upon completion of the Work, Contractor shall deliver these record documents to Engineer.

7.12 Safety and Protection

- A. Contractor shall be solely responsible for initiating, maintaining, and supervising all safety precautions and programs in connection with the Work. Such responsibility does not relieve Subcontractors of their responsibility for the safety of persons or property in the performance of their work, nor for compliance with applicable safety Laws and Regulations. Contractor shall take all necessary precautions for the safety of, and shall provide the necessary protection to prevent damage, injury, or loss to:
1. all persons on the Site or who may be affected by the Work;
 2. all the Work and materials and equipment to be incorporated therein, whether in storage on or off the Site; and
 3. other property at the Site or adjacent thereto, including trees, shrubs, lawns, walks, pavements, roadways, structures, other work in progress, utilities, and Underground Facilities not designated for removal, relocation, or replacement in the course of construction.
- B. Contractor shall comply with all applicable Laws and Regulations relating to the safety of persons or property, or to the protection of persons or property from damage, injury, or loss; and shall erect and maintain all necessary safeguards for such safety and protection. Contractor shall notify Owner; the owners of adjacent property, Underground Facilities, and other utilities; and other contractors and utility owners performing work at or adjacent to the Site, when prosecution of the Work may affect them, and shall cooperate with them in the protection, removal, relocation, and replacement of their property or work in progress.
- C. Contractor shall comply with the applicable requirements of Owner's safety programs, if any. The Supplementary Conditions identify any Owner's safety programs that are applicable to the Work.
- D. Contractor shall inform Owner and Engineer of the specific requirements of Contractor's safety program with which Owner's and Engineer's employees and representatives must comply while at the Site.
- E. All damage, injury, or loss to any property referred to in Paragraph 7.12.A.2 or 7.12.A.3 caused, directly or indirectly, in whole or in part, by Contractor, any Subcontractor, Supplier, or any other individual or entity directly or indirectly employed by any of them to perform any of the Work, or anyone for whose acts any of them may be liable, shall be remedied by Contractor at its expense (except damage or loss attributable to the fault of Drawings or Specifications or to the acts or omissions of Owner or Engineer or anyone employed by any of them, or anyone for whose acts any of them may be liable, and not attributable, directly or indirectly, in whole or in part, to the fault or negligence of Contractor or any Subcontractor, Supplier, or other individual or entity directly or indirectly employed by any of them).
- F. Contractor's duties and responsibilities for safety and protection shall continue until such time as all the Work is completed and Engineer has issued a notice to Owner and Contractor in accordance

EJCDC® -, Standard General Conditions of the Construction Contract.

Copyright © 2013 National Society of Professional Engineers, American Council of Engineering Companies, and American Society of Civil Engineers. All rights reserved.

with Paragraph 15.06.B that the Work is acceptable (except as otherwise expressly provided in connection with Substantial Completion).

- G. Contractor's duties and responsibilities for safety and protection shall resume whenever Contractor or any Subcontractor or Supplier returns to the Site to fulfill warranty or correction obligations, or to conduct other tasks arising from the Contract Documents.

7.13 Safety Representative

- A. Contractor shall designate a qualified and experienced safety representative at the Site whose duties and responsibilities shall be the prevention of accidents and the maintaining and supervising of safety precautions and programs.

7.14 Hazard Communication Programs

- A. Contractor shall be responsible for coordinating any exchange of material safety data sheets or other hazard communication information required to be made available to or exchanged between or among employers at the Site in accordance with Laws or Regulations.

7.15 Emergencies

- A. In emergencies affecting the safety or protection of persons or the Work or property at the Site or adjacent thereto, Contractor is obligated to act to prevent threatened damage, injury, or loss. Contractor shall give Engineer prompt written notice if Contractor believes that any significant changes in the Work or variations from the Contract Documents have been caused thereby or are required as a result thereof. If Engineer determines that a change in the Contract Documents is required because of the action taken by Contractor in response to such an emergency, a Work Change Directive or Change Order will be issued.

7.16 Shop Drawings, Samples, and Other Submittals

A. *Shop Drawing and Sample Submittal Requirements:*

1. Before submitting a Shop Drawing or Sample, Contractor shall have:
 - a. reviewed and coordinated the Shop Drawing or Sample with other Shop Drawings and Samples and with the requirements of the Work and the Contract Documents;
 - b. determined and verified all field measurements, quantities, dimensions, specified performance and design criteria, installation requirements, materials, catalog numbers, and similar information with respect thereto;
 - c. determined and verified the suitability of all materials and equipment offered with respect to the indicated application, fabrication, shipping, handling, storage, assembly, and installation pertaining to the performance of the Work; and
 - d. determined and verified all information relative to Contractor's responsibilities for means, methods, techniques, sequences, and procedures of construction, and safety precautions and programs incident thereto.
2. Each submittal shall bear a stamp or specific written certification that Contractor has satisfied Contractor's obligations under the Contract Documents with respect to Contractor's review of that submittal, and that Contractor approves the submittal.
3. With each submittal, Contractor shall give Engineer specific written notice of any variations that the Shop Drawing or Sample may have from the requirements of the Contract Documents. This notice shall be set forth in a written communication separate from the Shop Drawings or Sample submittal; and, in addition, in the case of Shop Drawings by a specific notation made on each Shop Drawing submitted to Engineer for review and approval of each such variation.

- B. *Submittal Procedures for Shop Drawings and Samples:* Contractor shall submit Shop Drawings and Samples to Engineer for review and approval in accordance with the accepted Schedule of Submittals. Each submittal will be identified as Engineer may require.

1. *Shop Drawings:*

- a. Contractor shall submit the number of copies required in the Specifications.

EJCDC® -, Standard General Conditions of the Construction Contract.

Copyright © 2013 National Society of Professional Engineers, American Council of Engineering Companies, and American Society of Civil Engineers. All rights reserved.

- b. Data shown on the Shop Drawings will be complete with respect to quantities, dimensions, specified performance and design criteria, materials, and similar data to show Engineer the services, materials, and equipment Contractor proposes to provide and to enable Engineer to review the information for the limited purposes required by Paragraph 7.16.D.
 2. *Samples:*
 - a. Contractor shall submit the number of Samples required in the Specifications.
 - b. Contractor shall clearly identify each Sample as to material, Supplier, pertinent data such as catalog numbers, the use for which intended and other data as Engineer may require to enable Engineer to review the submittal for the limited purposes required by Paragraph 7.16.D.
 3. Where a Shop Drawing or Sample is required by the Contract Documents or the Schedule of Submittals, any related Work performed prior to Engineer's review and approval of the pertinent submittal will be at the sole expense and responsibility of Contractor.
- C. *Other Submittals:* Contractor shall submit other submittals to Engineer in accordance with the accepted Schedule of Submittals, and pursuant to the applicable terms of the Specifications.
- D. *Engineer's Review:*
 1. Engineer will provide timely review of Shop Drawings and Samples in accordance with the Schedule of Submittals acceptable to Engineer. Engineer's review and approval will be only to determine if the items covered by the submittals will, after installation or incorporation in the Work, conform to the information given in the Contract Documents and be compatible with the design concept of the completed Project as a functioning whole as indicated by the Contract Documents.
 2. Engineer's review and approval will not extend to means, methods, techniques, sequences, or procedures of construction or to safety precautions or programs incident thereto.
 3. Engineer's review and approval of a separate item as such will not indicate approval of the assembly in which the item functions.
 4. Engineer's review and approval of a Shop Drawing or Sample shall not relieve Contractor from responsibility for any variation from the requirements of the Contract Documents unless Contractor has complied with the requirements of Paragraph 7.16.A.3 and Engineer has given written approval of each such variation by specific written notation thereof incorporated in or accompanying the Shop Drawing or Sample. Engineer will document any such approved variation from the requirements of the Contract Documents in a Field Order.
 5. Engineer's review and approval of a Shop Drawing or Sample shall not relieve Contractor from responsibility for complying with the requirements of Paragraph 7.16.A and B.
 6. Engineer's review and approval of a Shop Drawing or Sample, or of a variation from the requirements of the Contract Documents, shall not, under any circumstances, change the Contract Times or Contract Price, unless such changes are included in a Change Order.
 7. Neither Engineer's receipt, review, acceptance or approval of a Shop Drawing, Sample, or other submittal shall result in such item becoming a Contract Document.
 8. Contractor shall perform the Work in compliance with the requirements and commitments set forth in approved Shop Drawings and Samples, subject to the provisions of Paragraph 7.16.D.4.
- E. *Resubmittal Procedures:*
 1. Contractor shall make corrections required by Engineer and shall return the required number of corrected copies of Shop Drawings and submit, as required, new Samples for review and approval. Contractor shall direct specific attention in writing to revisions other than the corrections called for by Engineer on previous submittals.

2. Contractor shall furnish required submittals with sufficient information and accuracy to obtain required approval of an item with no more than three submittals. Engineer will record Engineer's time for reviewing a fourth or subsequent submittal of a Shop Drawings, sample, or other item requiring approval, and Contractor shall be responsible for Engineer's charges to Owner for such time. Owner may impose a set-off against payments due to Contractor to secure reimbursement for such charges.
3. If Contractor requests a change of a previously approved submittal item, Contractor shall be responsible for Engineer's charges to Owner for its review time, and Owner may impose a set-off against payments due to Contractor to secure reimbursement for such charges, unless the need for such change is beyond the control of Contractor.

7.17 Contractor's General Warranty and Guarantee

- A. Contractor warrants and guarantees to Owner that all Work will be in accordance with the Contract Documents and will not be defective. Engineer and its officers, directors, members, partners, employees, agents, consultants, and subcontractors shall be entitled to rely on Contractor's warranty and guarantee.
- B. Contractor's warranty and guarantee hereunder excludes defects or damage caused by:
 1. abuse, modification, or improper maintenance or operation by persons other than Contractor, Subcontractors, Suppliers, or any other individual or entity for whom Contractor is responsible; or
 2. normal wear and tear under normal usage.
- C. Contractor's obligation to perform and complete the Work in accordance with the Contract Documents shall be absolute. None of the following will constitute an acceptance of Work that is not in accordance with the Contract Documents or a release of Contractor's obligation to perform the Work in accordance with the Contract Documents:
 1. observations by Engineer;
 2. recommendation by Engineer or payment by Owner of any progress or final payment;
 3. the issuance of a certificate of Substantial Completion by Engineer or any payment related thereto by Owner;
 4. use or occupancy of the Work or any part thereof by Owner;
 5. any review and approval of a Shop Drawing or Sample submittal;
 6. the issuance of a notice of acceptability by Engineer;
 7. any inspection, test, or approval by others; or
 8. any correction of defective Work by Owner.
- D. If the Contract requires the Contractor to accept the assignment of a contract entered into by Owner, then the specific warranties, guarantees, and correction obligations contained in the assigned contract shall govern with respect to Contractor's performance obligations to Owner for the Work described in the assigned contract.

7.18 Indemnification

- A. To the fullest extent permitted by Laws and Regulations, and in addition to any other obligations of Contractor under the Contract or otherwise, Contractor shall indemnify and hold harmless Owner and Engineer, and the officers, directors, members, partners, employees, agents, consultants and subcontractors of each and any of them from and against all claims, costs, losses, and damages (including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals and all court or arbitration or other dispute resolution costs) arising out of or relating to the performance of the Work, provided that any such claim, cost, loss, or damage is attributable to bodily injury, sickness, disease, or death, or to injury to or destruction of tangible property (other than the Work itself), including the loss of use resulting therefrom but only to the extent caused by any negligent act or omission of Contractor, any Subcontractor, any Supplier, or any individual or

EJCDC® -, Standard General Conditions of the Construction Contract.

Copyright © 2013 National Society of Professional Engineers, American Council of Engineering Companies, and American Society of Civil Engineers. All rights reserved.

entity directly or indirectly employed by any of them to perform any of the Work or anyone for whose acts any of them may be liable.

- B. In any and all claims against Owner or Engineer or any of their officers, directors, members, partners, employees, agents, consultants, or subcontractors by any employee (or the survivor or personal representative of such employee) of Contractor, any Subcontractor, any Supplier, or any individual or entity directly or indirectly employed by any of them to perform any of the Work, or anyone for whose acts any of them may be liable, the indemnification obligation under Paragraph 7.18.A shall not be limited in any way by any limitation on the amount or type of damages, compensation, or benefits payable by or for Contractor or any such Subcontractor, Supplier, or other individual or entity under workers' compensation acts, disability benefit acts, or other employee benefit acts.
- C. The indemnification obligations of Contractor under Paragraph 7.18.A shall not extend to the liability of Engineer and Engineer's officers, directors, members, partners, employees, agents, consultants and subcontractors arising out of:
 - 1. the preparation or approval of, or the failure to prepare or approve maps, Drawings, opinions, reports, surveys, Change Orders, designs, or Specifications; or
 - 2. giving directions or instructions, or failing to give them, if that is the primary cause of the injury or damage.

7.19 Delegation of Professional Design Services

- A. Contractor will not be required to provide professional design services unless such services are specifically required by the Contract Documents for a portion of the Work or unless such services are required to carry out Contractor's responsibilities for construction means, methods, techniques, sequences and procedures. Contractor shall not be required to provide professional services in violation of applicable Laws and Regulations.
- B. If professional design services or certifications by a design professional related to systems, materials, or equipment are specifically required of Contractor by the Contract Documents, Owner and Engineer will specify all performance and design criteria that such services must satisfy. Contractor shall cause such services or certifications to be provided by a properly licensed professional, whose signature and seal shall appear on all drawings, calculations, specifications, certifications, and other submittals prepared by such professional. Shop Drawings and other submittals related to the Work designed or certified by such professional, if prepared by others, shall bear such professional's written approval when submitted to Engineer.
- C. Owner and Engineer shall be entitled to rely upon the adequacy, accuracy, and completeness of the services, certifications, or approvals performed by such design professionals, provided Owner and Engineer have specified to Contractor all performance and design criteria that such services must satisfy.
- D. Pursuant to this paragraph, Engineer's review and approval of design calculations and design drawings will be only for the limited purpose of checking for conformance with performance and design criteria given and the design concept expressed in the Contract Documents. Engineer's review and approval of Shop Drawings and other submittals (except design calculations and design drawings) will be only for the purpose stated in Paragraph 7.16.D.1.
- E. Contractor shall not be responsible for the adequacy of the performance or design criteria specified by Owner or Engineer.

ARTICLE 8 – OTHER WORK AT THE SITE**8.01 Other Work**

- A. In addition to and apart from the Work under the Contract Documents, the Owner may perform other work at or adjacent to the Site. Such other work may be performed by Owner's employees, or through contracts between the Owner and third parties. Owner may also arrange to have third-party utility owners perform work on their utilities and facilities at or adjacent to the Site.
- B. If Owner performs other work at or adjacent to the Site with Owner's employees, or through contracts for such other work, then Owner shall give Contractor written notice thereof prior to starting any such other work. If Owner has advance information regarding the start of any utility work at or adjacent to the Site, Owner shall provide such information to Contractor.
- C. Contractor shall afford each other contractor that performs such other work, each utility owner performing other work, and Owner, if Owner is performing other work with Owner's employees, proper and safe access to the Site, and provide a reasonable opportunity for the introduction and storage of materials and equipment and the execution of such other work. Contractor shall do all cutting, fitting, and patching of the Work that may be required to properly connect or otherwise make its several parts come together and properly integrate with such other work. Contractor shall not endanger any work of others by cutting, excavating, or otherwise altering such work; provided, however, that Contractor may cut or alter others' work with the written consent of Engineer and the others whose work will be affected.
- D. If the proper execution or results of any part of Contractor's Work depends upon work performed by others under this Article 8, Contractor shall inspect such other work and promptly report to Engineer in writing any delays, defects, or deficiencies in such other work that render it unavailable or unsuitable for the proper execution and results of Contractor's Work. Contractor's failure to so report will constitute an acceptance of such other work as fit and proper for integration with Contractor's Work except for latent defects and deficiencies in such other work.

8.02 Coordination

- A. If Owner intends to contract with others for the performance of other work at or adjacent to the Site, to perform other work at or adjacent to the Site with Owner's employees, or to arrange to have utility owners perform work at or adjacent to the Site, the following will be set forth in the Supplementary Conditions or provided to Contractor prior to the start of any such other work:
 - 1. the identity of the individual or entity that will have authority and responsibility for coordination of the activities among the various contractors;
 - 2. an itemization of the specific matters to be covered by such authority and responsibility; and
 - 3. the extent of such authority and responsibilities.
- B. Unless otherwise provided in the Supplementary Conditions, Owner shall have sole authority and responsibility for such coordination.

8.03 Legal Relationships

- A. If, in the course of performing other work at or adjacent to the Site for Owner, the Owner's employees, any other contractor working for Owner, or any utility owner for whom the Owner is responsible causes damage to the Work or to the property of Contractor or its Subcontractors, or delays, disrupts, interferes with, or increases the scope or cost of the performance of the Work, through actions or inaction, then Contractor shall be entitled to an equitable adjustment in the Contract Price or the Contract Times, or both. Contractor must submit any Change Proposal seeking an equitable adjustment in the Contract Price or the Contract Times under this paragraph within 30 days of the damaging, delaying, disrupting, or interfering event. The entitlement to, and extent of, any such equitable adjustment shall take into account information (if any) regarding such other work that was provided to Contractor in the Contract Documents prior to the submittal of the Bid

or the final negotiation of the terms of the Contract. When applicable, any such equitable adjustment in Contract Price shall be conditioned on Contractor assigning to Owner all Contractor's rights against such other contractor or utility owner with respect to the damage, delay, disruption, or interference that is the subject of the adjustment. Contractor's entitlement to an adjustment of the Contract Times is conditioned on such adjustment being essential to Contractor's ability to complete the Work within the Contract Times.

- B. Contractor shall take reasonable and customary measures to avoid damaging, delaying, disrupting, or interfering with the work of Owner, any other contractor, or any utility owner performing other work at or adjacent to the Site. If Contractor fails to take such measures and as a result damages, delays, disrupts, or interferes with the work of any such other contractor or utility owner, then Owner may impose a set-off against payments due to Contractor, and assign to such other contractor or utility owner the Owner's contractual rights against Contractor with respect to the breach of the obligations set forth in this paragraph.
- C. When Owner is performing other work at or adjacent to the Site with Owner's employees, Contractor shall be liable to Owner for damage to such other work, and for the reasonable direct delay, disruption, and interference costs incurred by Owner as a result of Contractor's failure to take reasonable and customary measures with respect to Owner's other work. In response to such damage, delay, disruption, or interference, Owner may impose a set-off against payments due to Contractor.
- D. If Contractor damages, delays, disrupts, or interferes with the work of any other contractor, or any utility owner performing other work at or adjacent to the Site, through Contractor's failure to take reasonable and customary measures to avoid such impacts, or if any claim arising out of Contractor's actions, inactions, or negligence in performance of the Work at or adjacent to the Site is made by any such other contractor or utility owner against Contractor, Owner, or Engineer, then Contractor shall (1) promptly attempt to settle the claim as to all parties through negotiations with such other contractor or utility owner, or otherwise resolve the claim by arbitration or other dispute resolution proceeding or at law, and (2) indemnify and hold harmless Owner and Engineer, and the officers, directors, members, partners, employees, agents, consultants and subcontractors of each and any of them from and against any such claims, and against all costs, losses, and damages (including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals and all court or arbitration or other dispute resolution costs) arising out of or relating to such damage, delay, disruption, or interference.

ARTICLE 9 – OWNER'S RESPONSIBILITIES

9.01 Communications to Contractor

- A. Except as otherwise provided in these General Conditions, Owner shall issue all communications to Contractor through Engineer.

9.02 Replacement of Engineer

- A. Owner may at its discretion appoint an engineer to replace Engineer, provided Contractor makes no reasonable objection to the replacement engineer. The replacement engineer's status under the Contract Documents shall be that of the former Engineer.

9.03 Furnish Data

- A. Owner shall promptly furnish the data required of Owner under the Contract Documents.

9.04 Pay When Due

- A. Owner shall make payments to Contractor when they are due as provided in the Agreement.

9.05 Lands and Easements; Reports, Tests, and Drawings

- A. Owner's duties with respect to providing lands and easements are set forth in Paragraph 5.01.

EJCDC® -, Standard General Conditions of the Construction Contract.

Copyright © 2013 National Society of Professional Engineers, American Council of Engineering Companies,
and American Society of Civil Engineers. All rights reserved.

- B. Owner's duties with respect to providing engineering surveys to establish reference points are set forth in Paragraph 4.03.
 - C. Article 5 refers to Owner's identifying and making available to Contractor copies of reports of explorations and tests of conditions at the Site, and drawings of physical conditions relating to existing surface or subsurface structures at the Site.
- 9.06 Insurance
- A. Owner's responsibilities, if any, with respect to purchasing and maintaining liability and property insurance are set forth in Article 6.
- 9.07 Change Orders
- A. Owner's responsibilities with respect to Change Orders are set forth in Article 11.
- 9.08 Inspections, Tests, and Approvals
- A. Owner's responsibility with respect to certain inspections, tests, and approvals is set forth in Paragraph 14.02.B.
- 9.09 Limitations on Owner's Responsibilities
- A. The Owner shall not supervise, direct, or have control or authority over, nor be responsible for, Contractor's means, methods, techniques, sequences, or procedures of construction, or the safety precautions and programs incident thereto, or for any failure of Contractor to comply with Laws and Regulations applicable to the performance of the Work. Owner will not be responsible for Contractor's failure to perform the Work in accordance with the Contract Documents.
- 9.10 Undisclosed Hazardous Environmental Condition
- A. Owner's responsibility in respect to an undisclosed Hazardous Environmental Condition is set forth in Paragraph 5.06.
- 9.11 Evidence of Financial Arrangements
- A. Upon request of Contractor, Owner shall furnish Contractor reasonable evidence that financial arrangements have been made to satisfy Owner's obligations under the Contract Documents (including obligations under proposed changes in the Work).
- 9.12 Safety Programs
- A. While at the Site, Owner's employees and representatives shall comply with the specific applicable requirements of Contractor's safety programs of which Owner has been informed.
 - B. Owner shall furnish copies of any applicable Owner safety programs to Contractor.

ARTICLE 10 – ENGINEER'S STATUS DURING CONSTRUCTION

- 10.01 Owner's Representative
- A. Engineer will be Owner's representative during the construction period. The duties and responsibilities and the limitations of authority of Engineer as Owner's representative during construction are set forth in the Contract.
- 10.02 Visits to Site
- A. Engineer will make visits to the Site at intervals appropriate to the various stages of construction as Engineer deems necessary in order to observe as an experienced and qualified design professional the progress that has been made and the quality of the various aspects of Contractor's executed Work. Based on information obtained during such visits and observations, Engineer, for the benefit of Owner, will determine, in general, if the Work is proceeding in accordance with the Contract Documents. Engineer will not be required to make exhaustive or continuous inspections on the Site to check the quality or quantity of the Work. Engineer's efforts will be directed toward providing for Owner a greater degree of confidence that the completed Work will conform generally to the Contract Documents. On the basis of such visits and observations, Engineer will keep Owner informed of the progress of the Work and will endeavor to guard Owner against defective Work.

- B. Engineer's visits and observations are subject to all the limitations on Engineer's authority and responsibility set forth in Paragraph 10.08. Particularly, but without limitation, during or as a result of Engineer's visits or observations of Contractor's Work, Engineer will not supervise, direct, control, or have authority over or be responsible for Contractor's means, methods, techniques, sequences, or procedures of construction, or the safety precautions and programs incident thereto, or for any failure of Contractor to comply with Laws and Regulations applicable to the performance of the Work.
- 10.03 Project Representative
- A. If Owner and Engineer have agreed that Engineer will furnish a Resident Project Representative to represent Engineer at the Site and assist Engineer in observing the progress and quality of the Work, then the authority and responsibilities of any such Resident Project Representative will be as provided in the Supplementary Conditions, and limitations on the responsibilities thereof will be as provided in Paragraph 10.08. If Owner designates another representative or agent to represent Owner at the Site who is not Engineer's consultant, agent, or employee, the responsibilities and authority and limitations thereon of such other individual or entity will be as provided in the Supplementary Conditions.
- 10.04 Rejecting Defective Work
- A. Engineer has the authority to reject Work in accordance with Article 14.
- 10.05 Shop Drawings, Change Orders and Payments
- A. Engineer's authority, and limitations thereof, as to Shop Drawings and Samples, are set forth in Paragraph 7.16.
 - B. Engineer's authority, and limitations thereof, as to design calculations and design drawings submitted in response to a delegation of professional design services, if any, are set forth in Paragraph 7.19.
 - C. Engineer's authority as to Change Orders is set forth in Article 11.
 - D. Engineer's authority as to Applications for Payment is set forth in Article 15.
- 10.06 Determinations for Unit Price Work
- A. Engineer will determine the actual quantities and classifications of Unit Price Work performed by Contractor as set forth in Paragraph 13.03.
- 10.07 Decisions on Requirements of Contract Documents and Acceptability of Work
- A. Engineer will render decisions regarding the requirements of the Contract Documents, and judge the acceptability of the Work, pursuant to the specific procedures set forth herein for initial interpretations, Change Proposals, and acceptance of the Work. In rendering such decisions and judgments, Engineer will not show partiality to Owner or Contractor, and will not be liable to Owner, Contractor, or others in connection with any proceedings, interpretations, decisions, or judgments conducted or rendered in good faith.
- 10.08 Limitations on Engineer's Authority and Responsibilities
- A. Neither Engineer's authority or responsibility under this Article 10 or under any other provision of the Contract, nor any decision made by Engineer in good faith either to exercise or not exercise such authority or responsibility or the undertaking, exercise, or performance of any authority or responsibility by Engineer, shall create, impose, or give rise to any duty in contract, tort, or otherwise owed by Engineer to Contractor, any Subcontractor, any Supplier, any other individual or entity, or to any surety for or employee or agent of any of them.
 - B. Engineer will not supervise, direct, control, or have authority over or be responsible for Contractor's means, methods, techniques, sequences, or procedures of construction, or the safety precautions and programs incident thereto, or for any failure of Contractor to comply with Laws and Regulations applicable to the performance of the Work. Engineer will not be responsible for Contractor's failure to perform the Work in accordance with the Contract Documents.

- C. Engineer will not be responsible for the acts or omissions of Contractor or of any Subcontractor, any Supplier, or of any other individual or entity performing any of the Work.
- D. Engineer's review of the final Application for Payment and accompanying documentation and all maintenance and operating instructions, schedules, guarantees, bonds, certificates of inspection, tests and approvals, and other documentation required to be delivered by Paragraph 15.06.A will only be to determine generally that their content complies with the requirements of, and in the case of certificates of inspections, tests, and approvals, that the results certified indicate compliance with the Contract Documents.
- E. The limitations upon authority and responsibility set forth in this Paragraph 10.08 shall also apply to the Resident Project Representative, if any.

10.09 Compliance with Safety Program

- A. While at the Site, Engineer's employees and representatives will comply with the specific applicable requirements of Owner's and Contractor's safety programs (if any) of which Engineer has been informed.

ARTICLE 11 – AMENDING THE CONTRACT DOCUMENTS; CHANGES IN THE WORK

11.01 Amending and Supplementing Contract Documents

- A. The Contract Documents may be amended or supplemented by a Change Order, a Work Change Directive, or a Field Order.
 - 1. Change Orders:
 - a. If an amendment or supplement to the Contract Documents includes a change in the Contract Price or the Contract Times, such amendment or supplement must be set forth in a Change Order. A Change Order also may be used to establish amendments and supplements of the Contract Documents that do not affect the Contract Price or Contract Times.
 - b. Owner and Contractor may amend those terms and conditions of the Contract Documents that do not involve (1) the performance or acceptability of the Work, (2) the design (as set forth in the Drawings, Specifications, or otherwise), or (3) other engineering or technical matters, without the recommendation of the Engineer. Such an amendment shall be set forth in a Change Order.
 - 2. Work Change Directives: A Work Change Directive will not change the Contract Price or the Contract Times but is evidence that the parties expect that the modification ordered or documented by a Work Change Directive will be incorporated in a subsequently issued Change Order, following negotiations by the parties as to the Work Change Directive's effect, if any, on the Contract Price and Contract Times; or, if negotiations are unsuccessful, by a determination under the terms of the Contract Documents governing adjustments, expressly including Paragraph 11.04 regarding change of Contract Price. Contractor must submit any Change Proposal seeking an adjustment of the Contract Price or the Contract Times, or both, no later than 30 days after the completion of the Work set out in the Work Change Directive. Owner must submit any Claim seeking an adjustment of the Contract Price or the Contract Times, or both, no later than 60 days after issuance of the Work Change Directive.
 - 3. Field Orders: Engineer may authorize minor changes in the Work if the changes do not involve an adjustment in the Contract Price or the Contract Times and are compatible with the design concept of the completed Project as a functioning whole as indicated by the Contract Documents. Such changes will be accomplished by a Field Order and will be binding on Owner and also on Contractor, which shall perform the Work involved promptly. If Contractor believes that a Field Order justifies an adjustment in the Contract Price or Contract Times, or

both, then before proceeding with the Work at issue, Contractor shall submit a Change Proposal as provided herein.

11.02 Owner-Authorized Changes in the Work

- A. Without invalidating the Contract and without notice to any surety, Owner may, at any time or from time to time, order additions, deletions, or revisions in the Work. Such changes shall be supported by Engineer's recommendation, to the extent the change involves the design (as set forth in the Drawings, Specifications, or otherwise), or other engineering or technical matters. Such changes may be accomplished by a Change Order, if Owner and Contractor have agreed as to the effect, if any, of the changes on Contract Times or Contract Price; or by a Work Change Directive. Upon receipt of any such document, Contractor shall promptly proceed with the Work involved; or, in the case of a deletion in the Work, promptly cease construction activities with respect to such deleted Work. Added or revised Work shall be performed under the applicable conditions of the Contract Documents. Nothing in this paragraph shall obligate Contractor to undertake work that Contractor reasonably concludes cannot be performed in a manner consistent with Contractor's safety obligations under the Contract Documents or Laws and Regulations.

11.03 Unauthorized Changes in the Work

- A. Contractor shall not be entitled to an increase in the Contract Price or an extension of the Contract Times with respect to any work performed that is not required by the Contract Documents, as amended, modified, or supplemented, except in the case of an emergency as provided in Paragraph 7.15 or in the case of uncovering Work as provided in Paragraph 14.05.

11.04 Change of Contract Price

- A. The Contract Price may only be changed by a Change Order. Any Change Proposal for an adjustment in the Contract Price shall comply with the provisions of Paragraph 11.06. Any Claim for an adjustment of Contract Price shall comply with the provisions of Article 12.
- B. An adjustment in the Contract Price will be determined as follows:
1. where the Work involved is covered by unit prices contained in the Contract Documents, then by application of such unit prices to the quantities of the items involved (subject to the provisions of Paragraph 13.03); or
 2. where the Work involved is not covered by unit prices contained in the Contract Documents, then by a mutually agreed lump sum (which may include an allowance for overhead and profit not necessarily in accordance with Paragraph 11.04.C.2); or
 3. where the Work involved is not covered by unit prices contained in the Contract Documents and the parties do not reach mutual agreement to a lump sum, then on the basis of the Cost of the Work (determined as provided in Paragraph 13.01) plus a Contractor's fee for overhead and profit (determined as provided in Paragraph 11.04.C).
- C. Contractor's Fee: When applicable, the Contractor's fee for overhead and profit shall be determined as follows:
1. a mutually acceptable fixed fee; or
 2. if a fixed fee is not agreed upon, then a fee based on the following percentages of the various portions of the Cost of the Work:
 - a. for costs incurred under Paragraphs 13.01.B.1 and 13.01.B.2, the Contractor's fee shall be 15 percent;
 - b. for costs incurred under Paragraph 13.01.B.3, the Contractor's fee shall be five percent;
 - c. where one or more tiers of subcontracts are on the basis of Cost of the Work plus a fee and no fixed fee is agreed upon, the intent of Paragraphs 11.04.C.2.a and 11.04.C.2.b is that the Contractor's fee shall be based on: (1) a fee of 15 percent of the costs incurred under Paragraphs 13.01.A.1 and 13.01.A.2 by the Subcontractor that actually performs the Work, at whatever tier, and (2) with respect to Contractor itself and to any

Subcontractors of a tier higher than that of the Subcontractor that actually performs the Work, a fee of five percent of the amount (fee plus underlying costs incurred) attributable to the next lower tier Subcontractor; provided, however, that for any such subcontracted work the maximum total fee to be paid by Owner shall be no greater than 27 percent of the costs incurred by the Subcontractor that actually performs the work;

- d. no fee shall be payable on the basis of costs itemized under Paragraphs 13.01.B.4, 13.01.B.5, and 13.01.C;
- e. the amount of credit to be allowed by Contractor to Owner for any change which results in a net decrease in cost will be the amount of the actual net decrease in cost plus a deduction in Contractor's fee by an amount equal to five percent of such net decrease; and
- f. when both additions and credits are involved in any one change, the adjustment in Contractor's fee shall be computed on the basis of the net change in accordance with Paragraphs 11.04.C.2.a through 11.04.C.2.e, inclusive.

11.05 Change of Contract Times

- A. The Contract Times may only be changed by a Change Order. Any Change Proposal for an adjustment in the Contract Times shall comply with the provisions of Paragraph 11.06. Any Claim for an adjustment in the Contract Times shall comply with the provisions of Article 12.
- B. An adjustment of the Contract Times shall be subject to the limitations set forth in Paragraph 4.05, concerning delays in Contractor's progress.

11.06 Change Proposals

- A. Contractor shall submit a Change Proposal to Engineer to request an adjustment in the Contract Times or Contract Price; appeal an initial decision by Engineer concerning the requirements of the Contract Documents or relating to the acceptability of the Work under the Contract Documents; contest a set-off against payment due; or seek other relief under the Contract. The Change Proposal shall specify any proposed change in Contract Times or Contract Price, or both, or other proposed relief, and explain the reason for the proposed change, with citations to any governing or applicable provisions of the Contract Documents.
 - 1. Procedures: Contractor shall submit each Change Proposal to Engineer promptly (but in no event later than 30 days) after the start of the event giving rise thereto, or after such initial decision. The Contractor shall submit supporting data, including the proposed change in Contract Price or Contract Time (if any), to the Engineer and Owner within 15 days after the submittal of the Change Proposal. The supporting data shall be accompanied by a written statement that the supporting data are accurate and complete, and that any requested time or price adjustment is the entire adjustment to which Contractor believes it is entitled as a result of said event. Engineer will advise Owner regarding the Change Proposal, and consider any comments or response from Owner regarding the Change Proposal.
 - 2. Engineer's Action: Engineer will review each Change Proposal and, within 30 days after receipt of the Contractor's supporting data, either deny the Change Proposal in whole, approve it in whole, or deny it in part and approve it in part. Such actions shall be in writing, with a copy provided to Owner and Contractor. If Engineer does not take action on the Change Proposal within 30 days, then either Owner or Contractor may at any time thereafter submit a letter to the other party indicating that as a result of Engineer's inaction the Change Proposal is deemed denied, thereby commencing the time for appeal of the denial under Article 12.
 - 3. Binding Decision: Engineer's decision will be final and binding upon Owner and Contractor, unless Owner or Contractor appeals the decision by filing a Claim under Article 12.
- B. Resolution of Certain Change Proposals: If the Change Proposal does not involve the design (as set forth in the Drawings, Specifications, or otherwise), the acceptability of the Work, or other

engineering or technical matters, then Engineer will notify the parties that the Engineer is unable to resolve the Change Proposal. For purposes of further resolution of such a Change Proposal, such notice shall be deemed a denial, and Contractor may choose to seek resolution under the terms of Article 12.

11.07 Execution of Change Orders

- A. Owner and Contractor shall execute appropriate Change Orders covering:
1. changes in the Contract Price or Contract Times which are agreed to by the parties, including any undisputed sum or amount of time for Work actually performed in accordance with a Work Change Directive;
 2. changes in Contract Price resulting from an Owner set-off, unless Contractor has duly contested such set-off;
 3. changes in the Work which are: (a) ordered by Owner pursuant to Paragraph 11.02, (b) required because of Owner's acceptance of defective Work under Paragraph 14.04 or Owner's correction of defective Work under Paragraph 14.07, or (c) agreed to by the parties, subject to the need for Engineer's recommendation if the change in the Work involves the design (as set forth in the Drawings, Specifications, or otherwise), or other engineering or technical matters; and
 4. changes in the Contract Price or Contract Times, or other changes, which embody the substance of any final and binding results under Paragraph 11.06, or Article 12.
- B. If Owner or Contractor refuses to execute a Change Order that is required to be executed under the terms of this Paragraph 11.07, it shall be deemed to be of full force and effect, as if fully executed.

11.08 Notification to Surety

- A. If the provisions of any bond require notice to be given to a surety of any change affecting the general scope of the Work or the provisions of the Contract Documents (including, but not limited to, Contract Price or Contract Times), the giving of any such notice will be Contractor's responsibility. The amount of each applicable bond will be adjusted to reflect the effect of any such change.

ARTICLE 12 – CLAIMS

12.01 Claims

- A. Claims Process: The following disputes between Owner and Contractor shall be submitted to the Claims process set forth in this Article:
1. Appeals by Owner or Contractor of Engineer's decisions regarding Change Proposals;
 2. Owner demands for adjustments in the Contract Price or Contract Times, or other relief under the Contract Documents; and
 3. Disputes that Engineer has been unable to address because they do not involve the design (as set forth in the Drawings, Specifications, or otherwise), the acceptability of the Work, or other engineering or technical matters.
- B. Submittal of Claim: The party submitting a Claim shall deliver it directly to the other party to the Contract promptly (but in no event later than 30 days) after the start of the event giving rise thereto; in the case of appeals regarding Change Proposals within 30 days of the decision under appeal. The party submitting the Claim shall also furnish a copy to the Engineer, for its information only. The responsibility to substantiate a Claim shall rest with the party making the Claim. In the case of a Claim by Contractor seeking an increase in the Contract Times or Contract Price, or both, Contractor shall certify that the Claim is made in good faith, that the supporting data are accurate and complete, and that to the best of Contractor's knowledge and belief the amount of time or money requested accurately reflects the full amount to which Contractor is entitled.

- C. Review and Resolution: The party receiving a Claim shall review it thoroughly, giving full consideration to its merits. The two parties shall seek to resolve the Claim through the exchange of information and direct negotiations. The parties may extend the time for resolving the Claim by mutual agreement. All actions taken on a Claim shall be stated in writing and submitted to the other party, with a copy to Engineer.
- D. Mediation:
 - 1. At any time after initiation of a Claim, Owner and Contractor may mutually agree to mediation of the underlying dispute. The agreement to mediate shall stay the Claim submittal and response process.
 - 2. If Owner and Contractor agree to mediation, then after 60 days from such agreement, either Owner or Contractor may unilaterally terminate the mediation process, and the Claim submittal and decision process shall resume as of the date of the termination. If the mediation proceeds but is unsuccessful in resolving the dispute, the Claim submittal and decision process shall resume as of the date of the conclusion of the mediation, as determined by the mediator.
 - 3. Owner and Contractor shall each pay one-half of the mediator's fees and costs.
- E. Partial Approval: If the party receiving a Claim approves the Claim in part and denies it in part, such action shall be final and binding unless within 30 days of such action the other party invokes the procedure set forth in Article 17 for final resolution of disputes.
- F. Denial of Claim: If efforts to resolve a Claim are not successful, the party receiving the Claim may deny it by giving written notice of denial to the other party. If the receiving party does not take action on the Claim within 90 days, then either Owner or Contractor may at any time thereafter submit a letter to the other party indicating that as a result of the inaction, the Claim is deemed denied, thereby commencing the time for appeal of the denial. A denial of the Claim shall be final and binding unless within 30 days of the denial the other party invokes the procedure set forth in Article 17 for the final resolution of disputes.
- G. Final and Binding Results: If the parties reach a mutual agreement regarding a Claim, whether through approval of the Claim, direct negotiations, mediation, or otherwise; or if a Claim is approved in part and denied in part, or denied in full, and such actions become final and binding; then the results of the agreement or action on the Claim shall be incorporated in a Change Order to the extent they affect the Contract, including the Work, the Contract Times, or the Contract Price.

ARTICLE 13 – COST OF THE WORK; ALLOWANCES; UNIT PRICE WORK

13.01 Cost of the Work

- A. Purposes for Determination of Cost of the Work: The term Cost of the Work means the sum of all costs necessary for the proper performance of the Work at issue, as further defined below. The provisions of this Paragraph 13.01 are used for two distinct purposes:
 - 1. To determine Cost of the Work when Cost of the Work is a component of the Contract Price, under cost-plus-fee, time-and-materials, or other cost-based terms; or
 - 2. To determine the value of a Change Order, Change Proposal, Claim, set-off, or other adjustment in Contract Price. When the value of any such adjustment is determined on the basis of Cost of the Work, Contractor is entitled only to those additional or incremental costs required because of the change in the Work or because of the event giving rise to the adjustment.
- B. Costs Included: Except as otherwise may be agreed to in writing by Owner, costs included in the Cost of the Work shall be in amounts no higher than those prevailing in the locality of the Project, shall not include any of the costs itemized in Paragraph 13.01.C, and shall include only the following items:

1. Payroll costs for employees in the direct employ of Contractor in the performance of the Work under schedules of job classifications agreed upon by Owner and Contractor. Such employees shall include, without limitation, superintendents, foremen, and other personnel employed full time on the Work. Payroll costs for employees not employed full time on the Work shall be apportioned on the basis of their time spent on the Work. Payroll costs shall include, but not be limited to, salaries and wages plus the cost of fringe benefits, which shall include social security contributions, unemployment, excise, and payroll taxes, workers' compensation, health and retirement benefits, bonuses, sick leave, and vacation and holiday pay applicable thereto. The expenses of performing Work outside of regular working hours, on Saturday, Sunday, or legal holidays, shall be included in the above to the extent authorized by Owner.
2. Cost of all materials and equipment furnished and incorporated in the Work, including costs of transportation and storage thereof, and Suppliers' field services required in connection therewith. All cash discounts shall accrue to Contractor unless Owner deposits funds with Contractor with which to make payments, in which case the cash discounts shall accrue to Owner. All trade discounts, rebates, and refunds and returns from sale of surplus materials and equipment shall accrue to Owner, and Contractor shall make provisions so that they may be obtained.
3. Payments made by Contractor to Subcontractors for Work performed by Subcontractors. If required by Owner, Contractor shall obtain competitive bids from subcontractors acceptable to Owner and Contractor and shall deliver such bids to Owner, who will then determine, with the advice of Engineer, which bids, if any, will be acceptable. If any subcontract provides that the Subcontractor is to be paid on the basis of Cost of the Work plus a fee, the Subcontractor's Cost of the Work and fee shall be determined in the same manner as Contractor's Cost of the Work and fee as provided in this Paragraph 13.01.
4. Costs of special consultants (including but not limited to engineers, architects, testing laboratories, surveyors, attorneys, and accountants) employed for services specifically related to the Work.
5. Supplemental costs including the following:
 - a. The proportion of necessary transportation, travel, and subsistence expenses of Contractor's employees incurred in discharge of duties connected with the Work.
 - b. Cost, including transportation and maintenance, of all materials, supplies, equipment, machinery, appliances, office, and temporary facilities at the Site, and hand tools not owned by the workers, which are consumed in the performance of the Work, and cost, less market value, of such items used but not consumed which remain the property of Contractor.
 - c. Rentals of all construction equipment and machinery, and the parts thereof, whether rented from Contractor or others in accordance with rental agreements approved by Owner with the advice of Engineer, and the costs of transportation, loading, unloading, assembly, dismantling, and removal thereof. All such costs shall be in accordance with the terms of said rental agreements. The rental of any such equipment, machinery, or parts shall cease when the use thereof is no longer necessary for the Work.
 - d. Sales, consumer, use, and other similar taxes related to the Work, and for which Contractor is liable, as imposed by Laws and Regulations.
 - e. Deposits lost for causes other than negligence of Contractor, any Subcontractor, or anyone directly or indirectly employed by any of them or for whose acts any of them may be liable, and royalty payments and fees for permits and licenses.
 - f. Losses and damages (and related expenses) caused by damage to the Work, not compensated by insurance or otherwise, sustained by Contractor in connection with the

EJCDC® -, Standard General Conditions of the Construction Contract.

Copyright © 2013 National Society of Professional Engineers, American Council of Engineering Companies, and American Society of Civil Engineers. All rights reserved.

performance of the Work (except losses and damages within the deductible amounts of property insurance established in accordance with Paragraph 6.05), provided such losses and damages have resulted from causes other than the negligence of Contractor, any Subcontractor, or anyone directly or indirectly employed by any of them or for whose acts any of them may be liable. Such losses shall include settlements made with the written consent and approval of Owner. No such losses, damages, and expenses shall be included in the Cost of the Work for the purpose of determining Contractor's fee.

- g. The cost of utilities, fuel, and sanitary facilities at the Site.
 - h. Minor expenses such as communication service at the Site, express and courier services, and similar petty cash items in connection with the Work.
 - i. The costs of premiums for all bonds and insurance that Contractor is required by the Contract Documents to purchase and maintain.
- C. Costs Excluded: The term Cost of the Work shall not include any of the following items:
- 1. Payroll costs and other compensation of Contractor's officers, executives, principals (of partnerships and sole proprietorships), general managers, safety managers, engineers, architects, estimators, attorneys, auditors, accountants, purchasing and contracting agents, expeditors, timekeepers, clerks, and other personnel employed by Contractor, whether at the Site or in Contractor's principal or branch office for general administration of the Work and not specifically included in the agreed upon schedule of job classifications referred to in Paragraph 13.01.B.1 or specifically covered by Paragraph 13.01.B.4. The payroll costs and other compensation excluded here are to be considered administrative costs covered by the Contractor's fee.
 - 2. Expenses of Contractor's principal and branch offices other than Contractor's office at the Site.
 - 3. Any part of Contractor's capital expenses, including interest on Contractor's capital employed for the Work and charges against Contractor for delinquent payments.
 - 4. Costs due to the negligence of Contractor, any Subcontractor, or anyone directly or indirectly employed by any of them or for whose acts any of them may be liable, including but not limited to, the correction of defective Work, disposal of materials or equipment wrongly supplied, and making good any damage to property.
 - 5. Other overhead or general expense costs of any kind and the costs of any item not specifically and expressly included in Paragraph 13.01.B.
- D. Contractor's Fee: When the Work as a whole is performed on the basis of cost-plus, Contractor's fee shall be determined as set forth in the Agreement. When the value of any Work covered by a Change Order, Change Proposal, Claim, set-off, or other adjustment in Contract Price is determined on the basis of Cost of the Work, Contractor's fee shall be determined as set forth in Paragraph 11.04.C.
- E. Documentation: Whenever the Cost of the Work for any purpose is to be determined pursuant to this Article 13, Contractor will establish and maintain records thereof in accordance with generally accepted accounting practices and submit in a form acceptable to Engineer an itemized cost breakdown together with supporting data.

13.02 Allowances

- A. It is understood that Contractor has included in the Contract Price all allowances so named in the Contract Documents and shall cause the Work so covered to be performed for such sums and by such persons or entities as may be acceptable to Owner and Engineer.
- B. Cash Allowances: Contractor agrees that:
 - 1. the cash allowances include the cost to Contractor (less any applicable trade discounts) of materials and equipment required by the allowances to be delivered at the Site, and all applicable taxes; and

2. Contractor's costs for unloading and handling on the Site, labor, installation, overhead, profit, and other expenses contemplated for the cash allowances have been included in the Contract Price and not in the allowances, and no demand for additional payment on account of any of the foregoing will be valid.
- C. Contingency Allowance: Contractor agrees that a contingency allowance, if any, is for the sole use of Owner to cover unanticipated costs.
- D. Prior to final payment, an appropriate Change Order will be issued as recommended by Engineer to reflect actual amounts due Contractor on account of Work covered by allowances, and the Contract Price shall be correspondingly adjusted.

13.03 Unit Price Work

- A. Where the Contract Documents provide that all or part of the Work is to be Unit Price Work, initially the Contract Price will be deemed to include for all Unit Price Work an amount equal to the sum of the unit price for each separately identified item of Unit Price Work times the estimated quantity of each item as indicated in the Agreement.
- B. The estimated quantities of items of Unit Price Work are not guaranteed and are solely for the purpose of comparison of Bids and determining an initial Contract Price. Payments to Contractor for Unit Price Work will be based on actual quantities.
- C. Each unit price will be deemed to include an amount considered by Contractor to be adequate to cover Contractor's overhead and profit for each separately identified item.
- D. Engineer will determine the actual quantities and classifications of Unit Price Work performed by Contractor. Engineer will review with Contractor the Engineer's preliminary determinations on such matters before rendering a written decision thereon (by recommendation of an Application for Payment or otherwise). Engineer's written decision thereon will be final and binding (except as modified by Engineer to reflect changed factual conditions or more accurate data) upon Owner and Contractor, subject to the provisions of the following paragraph.
- E. Within 30 days of Engineer's written decision under the preceding paragraph, Contractor may submit a Change Proposal, or Owner may file a Claim, seeking an adjustment in the Contract Price if:
 1. the quantity of any item of Unit Price Work performed by Contractor differs materially and significantly from the estimated quantity of such item indicated in the Agreement;
 2. there is no corresponding adjustment with respect to any other item of Work; and
 3. Contractor believes that it is entitled to an increase in Contract Price as a result of having incurred additional expense or Owner believes that Owner is entitled to a decrease in Contract Price, and the parties are unable to agree as to the amount of any such increase or decrease.

ARTICLE 14 – TESTS AND INSPECTIONS; CORRECTION, REMOVAL OR ACCEPTANCE OF DEFECTIVE WORK

14.01 Access to Work

- A. Owner, Engineer, their consultants and other representatives and personnel of Owner, independent testing laboratories, and authorities having jurisdiction will have access to the Site and the Work at reasonable times for their observation, inspection, and testing. Contractor shall provide them proper and safe conditions for such access and advise them of Contractor's safety procedures and programs so that they may comply therewith as applicable.

14.02 Tests, Inspections, and Approvals

- A. Contractor shall give Engineer timely notice of readiness of the Work (or specific parts thereof) for all required inspections and tests, and shall cooperate with inspection and testing personnel to facilitate required inspections and tests.

- B. Owner shall retain and pay for the services of an independent inspector, testing laboratory, or other qualified individual or entity to perform all inspections and tests expressly required by the Contract Documents to be furnished and paid for by Owner, except that costs incurred in connection with tests or inspections of covered Work shall be governed by the provisions of Paragraph 14.05.
- C. If Laws or Regulations of any public body having jurisdiction require any Work (or part thereof) specifically to be inspected, tested, or approved by an employee or other representative of such public body, Contractor shall assume full responsibility for arranging and obtaining such inspections, tests, or approvals, pay all costs in connection therewith, and furnish Engineer the required certificates of inspection or approval.
- D. Contractor shall be responsible for arranging, obtaining, and paying for all inspections and tests required:
 - 1. by the Contract Documents, unless the Contract Documents expressly allocate responsibility for a specific inspection or test to Owner;
 - 2. to attain Owner's and Engineer's acceptance of materials or equipment to be incorporated in the Work;
 - 3. by manufacturers of equipment furnished under the Contract Documents;
 - 4. for testing, adjusting, and balancing of mechanical, electrical, and other equipment to be incorporated into the Work; and
 - 5. for acceptance of materials, mix designs, or equipment submitted for approval prior to Contractor's purchase thereof for incorporation in the Work.Such inspections and tests shall be performed by independent inspectors, testing laboratories, or other qualified individuals or entities acceptable to Owner and Engineer.
- E. If the Contract Documents require the Work (or part thereof) to be approved by Owner, Engineer, or another designated individual or entity, then Contractor shall assume full responsibility for arranging and obtaining such approvals.
- F. If any Work (or the work of others) that is to be inspected, tested, or approved is covered by Contractor without written concurrence of Engineer, Contractor shall, if requested by Engineer, uncover such Work for observation. Such uncovering shall be at Contractor's expense unless Contractor had given Engineer timely notice of Contractor's intention to cover the same and Engineer had not acted with reasonable promptness in response to such notice.

14.03 Defective Work

- A. Contractor's Obligation: It is Contractor's obligation to assure that the Work is not defective.
- B. Engineer's Authority: Engineer has the authority to determine whether Work is defective, and to reject defective Work.
- C. Notice of Defects: Prompt notice of all defective Work of which Owner or Engineer has actual knowledge will be given to Contractor.
- D. Correction, or Removal and Replacement: Promptly after receipt of written notice of defective Work, Contractor shall correct all such defective Work, whether or not fabricated, installed, or completed, or, if Engineer has rejected the defective Work, remove it from the Project and replace it with Work that is not defective.
- E. Preservation of Warranties: When correcting defective Work, Contractor shall take no action that would void or otherwise impair Owner's special warranty and guarantee, if any, on said Work.
- F. Costs and Damages: In addition to its correction, removal, and replacement obligations with respect to defective Work, Contractor shall pay all claims, costs, losses, and damages arising out of or relating to defective Work, including but not limited to the cost of the inspection, testing, correction, removal, replacement, or reconstruction of such defective Work, fines levied against Owner by governmental authorities because the Work is defective, and the costs of repair or

replacement of work of others resulting from defective Work. Prior to final payment, if Owner and Contractor are unable to agree as to the measure of such claims, costs, losses, and damages resulting from defective Work, then Owner may impose a reasonable set-off against payments due under Article 15.

14.04 Acceptance of Defective Work

- A. If, instead of requiring correction or removal and replacement of defective Work, Owner prefers to accept it, Owner may do so (subject, if such acceptance occurs prior to final payment, to Engineer's confirmation that such acceptance is in general accord with the design intent and applicable engineering principles, and will not endanger public safety). Contractor shall pay all claims, costs, losses, and damages attributable to Owner's evaluation of and determination to accept such defective Work (such costs to be approved by Engineer as to reasonableness), and for the diminished value of the Work to the extent not otherwise paid by Contractor. If any such acceptance occurs prior to final payment, the necessary revisions in the Contract Documents with respect to the Work shall be incorporated in a Change Order. If the parties are unable to agree as to the decrease in the Contract Price, reflecting the diminished value of Work so accepted, then Owner may impose a reasonable set-off against payments due under Article 15. If the acceptance of defective Work occurs after final payment, Contractor shall pay an appropriate amount to Owner.

14.05 Uncovering Work

- A. Engineer has the authority to require additional inspection or testing of the Work, whether or not the Work is fabricated, installed, or completed.
- B. If any Work is covered contrary to the written request of Engineer, then Contractor shall, if requested by Engineer, uncover such Work for Engineer's observation, and then replace the covering, all at Contractor's expense.
- C. If Engineer considers it necessary or advisable that covered Work be observed by Engineer or inspected or tested by others, then Contractor, at Engineer's request, shall uncover, expose, or otherwise make available for observation, inspection, or testing as Engineer may require, that portion of the Work in question, and provide all necessary labor, material, and equipment.
 - 1. If it is found that the uncovered Work is defective, Contractor shall be responsible for all claims, costs, losses, and damages arising out of or relating to such uncovering, exposure, observation, inspection, and testing, and of satisfactory replacement or reconstruction (including but not limited to all costs of repair or replacement of work of others); and pending Contractor's full discharge of this responsibility the Owner shall be entitled to impose a reasonable set-off against payments due under Article 15.
 - 2. If the uncovered Work is not found to be defective, Contractor shall be allowed an increase in the Contract Price or an extension of the Contract Times, or both, directly attributable to such uncovering, exposure, observation, inspection, testing, replacement, and reconstruction. If the parties are unable to agree as to the amount or extent thereof, then Contractor may submit a Change Proposal within 30 days of the determination that the Work is not defective.

14.06 Owner May Stop the Work

- A. If the Work is defective, or Contractor fails to supply sufficient skilled workers or suitable materials or equipment, or fails to perform the Work in such a way that the completed Work will conform to the Contract Documents, then Owner may order Contractor to stop the Work, or any portion thereof, until the cause for such order has been eliminated; however, this right of Owner to stop the Work shall not give rise to any duty on the part of Owner to exercise this right for the benefit of Contractor, any Subcontractor, any Supplier, any other individual or entity, or any surety for, or employee or agent of any of them.

14.07 Owner May Correct Defective Work

- A. If Contractor fails within a reasonable time after written notice from Engineer to correct defective Work, or to remove and replace rejected Work as required by Engineer, or if Contractor fails to perform the Work in accordance with the Contract Documents, or if Contractor fails to comply with any other provision of the Contract Documents, then Owner may, after seven days written notice to Contractor, correct or remedy any such deficiency.
- B. In exercising the rights and remedies under this Paragraph 14.07, Owner shall proceed expeditiously. In connection with such corrective or remedial action, Owner may exclude Contractor from all or part of the Site, take possession of all or part of the Work and suspend Contractor's services related thereto, and incorporate in the Work all materials and equipment stored at the Site or for which Owner has paid Contractor but which are stored elsewhere. Contractor shall allow Owner, Owner's representatives, agents and employees, Owner's other contractors, and Engineer and Engineer's consultants access to the Site to enable Owner to exercise the rights and remedies under this paragraph.
- C. All claims, costs, losses, and damages incurred or sustained by Owner in exercising the rights and remedies under this Paragraph 14.07 will be charged against Contractor as set-offs against payments due under Article 15. Such claims, costs, losses and damages will include but not be limited to all costs of repair, or replacement of work of others destroyed or damaged by correction, removal, or replacement of Contractor's defective Work.
- D. Contractor shall not be allowed an extension of the Contract Times because of any delay in the performance of the Work attributable to the exercise by Owner of Owner's rights and remedies under this Paragraph 14.07.

ARTICLE 15 – PAYMENTS TO CONTRACTOR; SET-OFFS; COMPLETION; CORRECTION PERIOD**15.01 Progress Payments**

- A. Basis for Progress Payments: The Schedule of Values established as provided in Article 2 will serve as the basis for progress payments and will be incorporated into a form of Application for Payment acceptable to Engineer. Progress payments on account of Unit Price Work will be based on the number of units completed during the pay period, as determined under the provisions of Paragraph 13.03. Progress payments for cost-based Work will be based on Cost of the Work completed by Contractor during the pay period.
- B. Applications for Payments:
 - 1. At least 20 days before the date established in the Agreement for each progress payment (but not more often than once a month), Contractor shall submit to Engineer for review an Application for Payment filled out and signed by Contractor covering the Work completed as of the date of the Application and accompanied by such supporting documentation as is required by the Contract Documents. If payment is requested on the basis of materials and equipment not incorporated in the Work but delivered and suitably stored at the Site or at another location agreed to in writing, the Application for Payment shall also be accompanied by a bill of sale, invoice, or other documentation warranting that Owner has received the materials and equipment free and clear of all Liens, and evidence that the materials and equipment are covered by appropriate property insurance, a warehouse bond, or other arrangements to protect Owner's interest therein, all of which must be satisfactory to Owner.
 - 2. Beginning with the second Application for Payment, each Application shall include an affidavit of Contractor stating that all previous progress payments received on account of the Work have been applied on account to discharge Contractor's legitimate obligations associated with prior Applications for Payment.

3. The amount of retainage with respect to progress payments will be as stipulated in the Agreement.
- C. Review of Applications:
 1. Engineer will, within 10 days after receipt of each Application for Payment, including each resubmittal, either indicate in writing a recommendation of payment and present the Application to Owner, or return the Application to Contractor indicating in writing Engineer's reasons for refusing to recommend payment. In the latter case, Contractor may make the necessary corrections and resubmit the Application.
 2. Engineer's recommendation of any payment requested in an Application for Payment will constitute a representation by Engineer to Owner, based on Engineer's observations of the executed Work as an experienced and qualified design professional, and on Engineer's review of the Application for Payment and the accompanying data and schedules, that to the best of Engineer's knowledge, information and belief:
 - a. the Work has progressed to the point indicated;
 - b. the quality of the Work is generally in accordance with the Contract Documents (subject to an evaluation of the Work as a functioning whole prior to or upon Substantial Completion, the results of any subsequent tests called for in the Contract Documents, a final determination of quantities and classifications for Unit Price Work under Paragraph 13.03, and any other qualifications stated in the recommendation); and
 - c. the conditions precedent to Contractor's being entitled to such payment appear to have been fulfilled in so far as it is Engineer's responsibility to observe the Work.
 3. By recommending any such payment Engineer will not thereby be deemed to have represented that:
 - a. inspections made to check the quality or the quantity of the Work as it has been performed have been exhaustive, extended to every aspect of the Work in progress, or involved detailed inspections of the Work beyond the responsibilities specifically assigned to Engineer in the Contract; or
 - b. there may not be other matters or issues between the parties that might entitle Contractor to be paid additionally by Owner or entitle Owner to withhold payment to Contractor.
 4. Neither Engineer's review of Contractor's Work for the purposes of recommending payments nor Engineer's recommendation of any payment, including final payment, will impose responsibility on Engineer:
 - a. to supervise, direct, or control the Work, or
 - b. for the means, methods, techniques, sequences, or procedures of construction, or the safety precautions and programs incident thereto, or
 - c. for Contractor's failure to comply with Laws and Regulations applicable to Contractor's performance of the Work, or
 - d. to make any examination to ascertain how or for what purposes Contractor has used the money paid on account of the Contract Price, or
 - e. to determine that title to any of the Work, materials, or equipment has passed to Owner free and clear of any Liens.
 5. Engineer may refuse to recommend the whole or any part of any payment if, in Engineer's opinion, it would be incorrect to make the representations to Owner stated in Paragraph 15.01.C.2.
 6. Engineer will recommend reductions in payment (set-offs) necessary in Engineer's opinion to protect Owner from loss because:
 - a. the Work is defective, requiring correction or replacement;

- b. the Contract Price has been reduced by Change Orders;
 - c. Owner has been required to correct defective Work in accordance with Paragraph 14.07, or has accepted defective Work pursuant to Paragraph 14.04;
 - d. Owner has been required to remove or remediate a Hazardous Environmental Condition for which Contractor is responsible; or
 - e. Engineer has actual knowledge of the occurrence of any of the events that would constitute a default by Contractor and therefore justify termination for cause under the Contract Documents.
- D. Payment Becomes Due:
 - 1. Ten days after presentation of the Application for Payment to Owner with Engineer's recommendation, the amount recommended (subject to any Owner set-offs) will become due, and when due will be paid by Owner to Contractor.
- E. Reductions in Payment by Owner:
 - 1. In addition to any reductions in payment (set-offs) recommended by Engineer, Owner is entitled to impose a set-off against payment based on any of the following:
 - a. claims have been made against Owner on account of Contractor's conduct in the performance or furnishing of the Work, or Owner has incurred costs, losses, or damages on account of Contractor's conduct in the performance or furnishing of the Work, including but not limited to claims, costs, losses, or damages from workplace injuries, adjacent property damage, non-compliance with Laws and Regulations, and patent infringement;
 - b. Contractor has failed to take reasonable and customary measures to avoid damage, delay, disruption, and interference with other work at or adjacent to the Site;
 - c. Contractor has failed to provide and maintain required bonds or insurance;
 - d. Owner has been required to remove or remediate a Hazardous Environmental Condition for which Contractor is responsible;
 - e. Owner has incurred extra charges or engineering costs related to submittal reviews, evaluations of proposed substitutes, tests and inspections, or return visits to manufacturing or assembly facilities;
 - f. the Work is defective, requiring correction or replacement;
 - g. Owner has been required to correct defective Work in accordance with Paragraph 14.07, or has accepted defective Work pursuant to Paragraph 14.04;
 - h. the Contract Price has been reduced by Change Orders;
 - i. an event that would constitute a default by Contractor and therefore justify a termination for cause has occurred;
 - j. liquidated damages have accrued as a result of Contractor's failure to achieve Milestones, Substantial Completion, or final completion of the Work;
 - k. Liens have been filed in connection with the Work, except where Contractor has delivered a specific bond satisfactory to Owner to secure the satisfaction and discharge of such Liens;
 - l. there are other items entitling Owner to a set off against the amount recommended.
 - 2. If Owner imposes any set-off against payment, whether based on its own knowledge or on the written recommendations of Engineer, Owner will give Contractor immediate written notice (with a copy to Engineer) stating the reasons for such action and the specific amount of the reduction, and promptly pay Contractor any amount remaining after deduction of the amount so withheld. Owner shall promptly pay Contractor the amount so withheld, or any adjustment thereto agreed to by Owner and Contractor, if Contractor remedies the reasons for such

action. The reduction imposed shall be binding on Contractor unless it duly submits a Change Proposal contesting the reduction.

3. Upon a subsequent determination that Owner's refusal of payment was not justified, the amount wrongfully withheld shall be treated as an amount due as determined by Paragraph 15.01.C.1 and subject to interest as provided in the Agreement.

15.02 Contractor's Warranty of Title

- A. Contractor warrants and guarantees that title to all Work, materials, and equipment furnished under the Contract will pass to Owner free and clear of (1) all Liens and other title defects, and (2) all patent, licensing, copyright, or royalty obligations, no later than seven days after the time of payment by Owner.

15.03 Substantial Completion

- A. When Contractor considers the entire Work ready for its intended use Contractor shall notify Owner and Engineer in writing that the entire Work is substantially complete and request that Engineer issue a certificate of Substantial Completion. Contractor shall at the same time submit to Owner and Engineer an initial draft of punch list items to be completed or corrected before final payment.
- B. Promptly after Contractor's notification, Owner, Contractor, and Engineer shall make an inspection of the Work to determine the status of completion. If Engineer does not consider the Work substantially complete, Engineer will notify Contractor in writing giving the reasons therefor.
- C. If Engineer considers the Work substantially complete, Engineer will deliver to Owner a preliminary certificate of Substantial Completion which shall fix the date of Substantial Completion. Engineer shall attach to the certificate a punch list of items to be completed or corrected before final payment. Owner shall have seven days after receipt of the preliminary certificate during which to make written objection to Engineer as to any provisions of the certificate or attached punch list. If, after considering the objections to the provisions of the preliminary certificate, Engineer concludes that the Work is not substantially complete, Engineer will, within 14 days after submission of the preliminary certificate to Owner, notify Contractor in writing that the Work is not substantially complete, stating the reasons therefor. If Owner does not object to the provisions of the certificate, or if despite consideration of Owner's objections Engineer concludes that the Work is substantially complete, then Engineer will, within said 14 days, execute and deliver to Owner and Contractor a final certificate of Substantial Completion (with a revised punch list of items to be completed or corrected) reflecting such changes from the preliminary certificate as Engineer believes justified after consideration of any objections from Owner.
- D. At the time of receipt of the preliminary certificate of Substantial Completion, Owner and Contractor will confer regarding Owner's use or occupancy of the Work following Substantial Completion, review the builder's risk insurance policy with respect to the end of the builder's risk coverage, and confirm the transition to coverage of the Work under a permanent property insurance policy held by Owner. Unless Owner and Contractor agree otherwise in writing, Owner shall bear responsibility for security, operation, protection of the Work, property insurance, maintenance, heat, and utilities upon Owner's use or occupancy of the Work.
- E. After Substantial Completion the Contractor shall promptly begin work on the punch list of items to be completed or corrected prior to final payment. In appropriate cases Contractor may submit monthly Applications for Payment for completed punch list items, following the progress payment procedures set forth above.
- F. Owner shall have the right to exclude Contractor from the Site after the date of Substantial Completion subject to allowing Contractor reasonable access to remove its property and complete or correct items on the punch list.

15.04 Partial Use or Occupancy

- A. Prior to Substantial Completion of all the Work, Owner may use or occupy any substantially completed part of the Work which has specifically been identified in the Contract Documents, or which Owner, Engineer, and Contractor agree constitutes a separately functioning and usable part of the Work that can be used by Owner for its intended purpose without significant interference with Contractor's performance of the remainder of the Work, subject to the following conditions:
1. At any time, Owner may request in writing that Contractor permit Owner to use or occupy any such part of the Work that Owner believes to be substantially complete. If and when Contractor agrees that such part of the Work is substantially complete, Contractor, Owner, and Engineer will follow the procedures of Paragraph 15.03.A through E for that part of the Work.
 2. At any time, Contractor may notify Owner and Engineer in writing that Contractor considers any such part of the Work substantially complete and request Engineer to issue a certificate of Substantial Completion for that part of the Work.
 3. Within a reasonable time after either such request, Owner, Contractor, and Engineer shall make an inspection of that part of the Work to determine its status of completion. If Engineer does not consider that part of the Work to be substantially complete, Engineer will notify Owner and Contractor in writing giving the reasons therefor. If Engineer considers that part of the Work to be substantially complete, the provisions of Paragraph 15.03 will apply with respect to certification of Substantial Completion of that part of the Work and the division of responsibility in respect thereof and access thereto.
 4. No use or occupancy or separate operation of part of the Work may occur prior to compliance with the requirements of Paragraph 6.05 regarding builder's risk or other property insurance.

15.05 Final Inspection

- A. Upon written notice from Contractor that the entire Work or an agreed portion thereof is complete, Engineer will promptly make a final inspection with Owner and Contractor and will notify Contractor in writing of all particulars in which this inspection reveals that the Work, or agreed portion thereof, is incomplete or defective. Contractor shall immediately take such measures as are necessary to complete such Work or remedy such deficiencies.

15.06 Final Payment

- A. Application for Payment:
1. After Contractor has, in the opinion of Engineer, satisfactorily completed all corrections identified during the final inspection and has delivered, in accordance with the Contract Documents, all maintenance and operating instructions, schedules, guarantees, bonds, certificates or other evidence of insurance, certificates of inspection, annotated record documents (as provided in Paragraph 7.11), and other documents, Contractor may make application for final payment.
 2. The final Application for Payment shall be accompanied (except as previously delivered) by:
 - a. all documentation called for in the Contract Documents;
 - b. consent of the surety, if any, to final payment;
 - c. satisfactory evidence that all title issues have been resolved such that title to all Work, materials, and equipment has passed to Owner free and clear of any Liens or other title defects, or will so pass upon final payment.
 - d. a list of all disputes that Contractor believes are unsettled; and
 - e. complete and legally effective releases or waivers (satisfactory to Owner) of all Lien rights arising out of the Work, and of Liens filed in connection with the Work.
 3. In lieu of the releases or waivers of Liens specified in Paragraph 15.06.A.2 and as approved by Owner, Contractor may furnish receipts or releases in full and an affidavit of Contractor that:

(a) the releases and receipts include all labor, services, material, and equipment for which a Lien could be filed; and (b) all payrolls, material and equipment bills, and other indebtedness connected with the Work for which Owner might in any way be responsible, or which might in any way result in liens or other burdens on Owner's property, have been paid or otherwise satisfied. If any Subcontractor or Supplier fails to furnish such a release or receipt in full, Contractor may furnish a bond or other collateral satisfactory to Owner to indemnify Owner against any Lien, or Owner at its option may issue joint checks payable to Contractor and specified Subcontractors and Suppliers.

B. Engineer's Review of Application and Acceptance:

1. If, on the basis of Engineer's observation of the Work during construction and final inspection, and Engineer's review of the final Application for Payment and accompanying documentation as required by the Contract Documents, Engineer is satisfied that the Work has been completed and Contractor's other obligations under the Contract have been fulfilled, Engineer will, within ten days after receipt of the final Application for Payment, indicate in writing Engineer's recommendation of final payment and present the Application for Payment to Owner for payment. Such recommendation shall account for any set-offs against payment that are necessary in Engineer's opinion to protect Owner from loss for the reasons stated above with respect to progress payments. At the same time Engineer will also give written notice to Owner and Contractor that the Work is acceptable, subject to the provisions of Paragraph 15.07. Otherwise, Engineer will return the Application for Payment to Contractor, indicating in writing the reasons for refusing to recommend final payment, in which case Contractor shall make the necessary corrections and resubmit the Application for Payment.

C. Completion of Work: The Work is complete (subject to surviving obligations) when it is ready for final payment as established by the Engineer's written recommendation of final payment.

D. Payment Becomes Due: Thirty days after the presentation to Owner of the final Application for Payment and accompanying documentation, the amount recommended by Engineer (less any further sum Owner is entitled to set off against Engineer's recommendation, including but not limited to set-offs for liquidated damages and set-offs allowed under the provisions above with respect to progress payments) will become due and shall be paid by Owner to Contractor.

15.07 Waiver of Claims

- A. The making of final payment will not constitute a waiver by Owner of claims or rights against Contractor. Owner expressly reserves claims and rights arising from unsettled Liens, from defective Work appearing after final inspection pursuant to Paragraph 15.05, from Contractor's failure to comply with the Contract Documents or the terms of any special guarantees specified therein, from outstanding Claims by Owner, or from Contractor's continuing obligations under the Contract Documents.
- B. The acceptance of final payment by Contractor will constitute a waiver by Contractor of all claims and rights against Owner other than those pending matters that have been duly submitted or appealed under the provisions of Article 17.

15.08 Correction Period

- A. If within one year after the date of Substantial Completion (or such longer period of time as may be prescribed by the terms of any applicable special guarantee required by the Contract Documents, or by any specific provision of the Contract Documents), any Work is found to be defective, or if the repair of any damages to the Site, adjacent areas that Contractor has arranged to use through construction easements or otherwise, and other adjacent areas used by Contractor as permitted by Laws and Regulations, is found to be defective, then Contractor shall promptly, without cost to Owner and in accordance with Owner's written instructions:
 1. correct the defective repairs to the Site or such other adjacent areas;

EJCDC® -, Standard General Conditions of the Construction Contract.

Copyright © 2013 National Society of Professional Engineers, American Council of Engineering Companies, and American Society of Civil Engineers. All rights reserved.

2. correct such defective Work;
 3. if the defective Work has been rejected by Owner, remove it from the Project and replace it with Work that is not defective, and
 4. satisfactorily correct or repair or remove and replace any damage to other Work, to the work of others, or to other land or areas resulting therefrom.
- B. If Contractor does not promptly comply with the terms of Owner's written instructions, or in an emergency where delay would cause serious risk of loss or damage, Owner may have the defective Work corrected or repaired or may have the rejected Work removed and replaced. Contractor shall pay all claims, costs, losses, and damages (including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals and all court or arbitration or other dispute resolution costs) arising out of or relating to such correction or repair or such removal and replacement (including but not limited to all costs of repair or replacement of work of others).
- C. In special circumstances where a particular item of equipment is placed in continuous service before Substantial Completion of all the Work, the correction period for that item may start to run from an earlier date if so provided in the Specifications.
- D. Where defective Work (and damage to other Work resulting therefrom) has been corrected or removed and replaced under this paragraph, the correction period hereunder with respect to such Work will be extended for an additional period of one year after such correction or removal and replacement has been satisfactorily completed.
- E. Contractor's obligations under this paragraph are in addition to all other obligations and warranties. The provisions of this paragraph shall not be construed as a substitute for, or a waiver of, the provisions of any applicable statute of limitation or repose.

ARTICLE 16 – SUSPENSION OF WORK AND TERMINATION

16.01 Owner May Suspend Work

- A. At any time and without cause, Owner may suspend the Work or any portion thereof for a period of not more than 90 consecutive days by written notice to Contractor and Engineer. Such notice will fix the date on which Work will be resumed. Contractor shall resume the Work on the date so fixed. Contractor shall be entitled to an adjustment in the Contract Price or an extension of the Contract Times, or both, directly attributable to any such suspension. Any Change Proposal seeking such adjustments shall be submitted no later than 30 days after the date fixed for resumption of Work.

16.02 Owner May Terminate for Cause

- A. The occurrence of any one or more of the following events will constitute a default by Contractor and justify termination for cause:
1. Contractor's persistent failure to perform the Work in accordance with the Contract Documents (including, but not limited to, failure to supply sufficient skilled workers or suitable materials or equipment or failure to adhere to the Progress Schedule);
 2. Failure of Contractor to perform or otherwise to comply with a material term of the Contract Documents;
 3. Contractor's disregard of Laws or Regulations of any public body having jurisdiction; or
 4. Contractor's repeated disregard of the authority of Owner or Engineer.
- B. If one or more of the events identified in Paragraph 16.02.A occurs, then after giving Contractor (and any surety) ten days written notice that Owner is considering a declaration that Contractor is in default and termination of the contract, Owner may proceed to:
1. declare Contractor to be in default, and give Contractor (and any surety) notice that the Contract is terminated; and
 2. enforce the rights available to Owner under any applicable performance bond.

- C. Subject to the terms and operation of any applicable performance bond, if Owner has terminated the Contract for cause, Owner may exclude Contractor from the Site, take possession of the Work, incorporate in the Work all materials and equipment stored at the Site or for which Owner has paid Contractor but which are stored elsewhere, and complete the Work as Owner may deem expedient.
- D. Owner may not proceed with termination of the Contract under Paragraph 16.02.B if Contractor within seven days of receipt of notice of intent to terminate begins to correct its failure to perform and proceeds diligently to cure such failure.
- E. If Owner proceeds as provided in Paragraph 16.02.B, Contractor shall not be entitled to receive any further payment until the Work is completed. If the unpaid balance of the Contract Price exceeds the cost to complete the Work, including all related claims, costs, losses, and damages (including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals) sustained by Owner, such excess will be paid to Contractor. If the cost to complete the Work including such related claims, costs, losses, and damages exceeds such unpaid balance, Contractor shall pay the difference to Owner. Such claims, costs, losses, and damages incurred by Owner will be reviewed by Engineer as to their reasonableness and, when so approved by Engineer, incorporated in a Change Order. When exercising any rights or remedies under this paragraph, Owner shall not be required to obtain the lowest price for the Work performed.
- F. Where Contractor's services have been so terminated by Owner, the termination will not affect any rights or remedies of Owner against Contractor then existing or which may thereafter accrue, or any rights or remedies of Owner against Contractor or any surety under any payment bond or performance bond. Any retention or payment of money due Contractor by Owner will not release Contractor from liability.
- G. If and to the extent that Contractor has provided a performance bond under the provisions of Paragraph 6.01.A, the provisions of that bond shall govern over any inconsistent provisions of Paragraphs 16.02.B and 16.02.D.

16.03 Owner May Terminate For Convenience

- A. Upon seven days written notice to Contractor and Engineer, Owner may, without cause and without prejudice to any other right or remedy of Owner, terminate the Contract. In such case, Contractor shall be paid for (without duplication of any items):
 - 1. completed and acceptable Work executed in accordance with the Contract Documents prior to the effective date of termination, including fair and reasonable sums for overhead and profit on such Work;
 - 2. expenses sustained prior to the effective date of termination in performing services and furnishing labor, materials, or equipment as required by the Contract Documents in connection with uncompleted Work, plus fair and reasonable sums for overhead and profit on such expenses; and
 - 3. other reasonable expenses directly attributable to termination, including costs incurred to prepare a termination for convenience cost proposal.
- B. Contractor shall not be paid on account of loss of anticipated overhead, profits, or revenue, or other economic loss arising out of or resulting from such termination.

16.04 Contractor May Stop Work or Terminate

- A. If, through no act or fault of Contractor, (1) the Work is suspended for more than 90 consecutive days by Owner or under an order of court or other public authority, or (2) Engineer fails to act on any Application for Payment within 30 days after it is submitted, or (3) Owner fails for 30 days to pay Contractor any sum finally determined to be due, then Contractor may, upon seven days written notice to Owner and Engineer, and provided Owner or Engineer do not remedy such

suspension or failure within that time, terminate the contract and recover from Owner payment on the same terms as provided in Paragraph 16.03.

- B. In lieu of terminating the Contract and without prejudice to any other right or remedy, if Engineer has failed to act on an Application for Payment within 30 days after it is submitted, or Owner has failed for 30 days to pay Contractor any sum finally determined to be due, Contractor may, seven days after written notice to Owner and Engineer, stop the Work until payment is made of all such amounts due Contractor, including interest thereon. The provisions of this paragraph are not intended to preclude Contractor from submitting a Change Proposal for an adjustment in Contract Price or Contract Times or otherwise for expenses or damage directly attributable to Contractor's stopping the Work as permitted by this paragraph.

ARTICLE 17 – FINAL RESOLUTION OF DISPUTES

17.01 Methods and Procedures

- A. Disputes Subject to Final Resolution: The following disputed matters are subject to final resolution under the provisions of this Article:
1. A timely appeal of an approval in part and denial in part of a Claim, or of a denial in full; and
 2. Disputes between Owner and Contractor concerning the Work or obligations under the Contract Documents, and arising after final payment has been made.
- B. Final Resolution of Disputes: For any dispute subject to resolution under this Article, Owner or Contractor may:
1. elect in writing to invoke the dispute resolution process provided for in the Supplementary Conditions; or
 2. agree with the other party to submit the dispute to another dispute resolution process; or
 3. if no dispute resolution process is provided for in the Supplementary Conditions or mutually agreed to, give written notice to the other party of the intent to submit the dispute to a court of competent jurisdiction.

ARTICLE 18 – MISCELLANEOUS

18.01 Giving Notice

- A. Whenever any provision of the Contract Documents requires the giving of written notice, it will be deemed to have been validly given if:
1. delivered in person, by a commercial courier service or otherwise, to the individual or to a member of the firm or to an officer of the corporation for which it is intended; or
 2. delivered at or sent by registered or certified mail, postage prepaid, to the last business address known to the sender of the notice.

18.02 Computation of Times

- A. When any period of time is referred to in the Contract by days, it will be computed to exclude the first and include the last day of such period. If the last day of any such period falls on a Saturday or Sunday or on a day made a legal holiday by the law of the applicable jurisdiction, such day will be omitted from the computation.

18.03 Cumulative Remedies

- A. The duties and obligations imposed by these General Conditions and the rights and remedies available hereunder to the parties hereto are in addition to, and are not to be construed in any way as a limitation of, any rights and remedies available to any or all of them which are otherwise imposed or available by Laws or Regulations, by special warranty or guarantee, or by other provisions of the Contract. The provisions of this paragraph will be as effective as if repeated specifically in the

Contract Documents in connection with each particular duty, obligation, right, and remedy to which they apply.

18.04 Limitation of Damages

- A. With respect to any and all Change Proposals, Claims, disputes subject to final resolution, and other matters at issue, neither Owner nor Engineer, nor any of their officers, directors, members, partners, employees, agents, consultants, or subcontractors, shall be liable to Contractor for any claims, costs, losses, or damages sustained by Contractor on or in connection with any other project or anticipated project.

18.05 No Waiver

- A. A party's non-enforcement of any provision shall not constitute a waiver of that provision, nor shall it affect the enforceability of that provision or of the remainder of this Contract.

18.06 Survival of Obligations

- A. All representations, indemnifications, warranties, and guarantees made in, required by, or given in accordance with the Contract, as well as all continuing obligations indicated in the Contract, will survive final payment, completion, and acceptance of the Work or termination or completion of the Contract or termination of the services of Contractor.

18.07 Controlling Law

- A. This Contract is to be governed by the law of the state in which the Project is located.

18.08 Headings

- A. Article and paragraph headings are inserted for convenience only and do not constitute parts of these General Conditions.

END OF DOCUMENT 00700 – GENERAL CONDITIONS

DOCUMENT 00800 – SUPPLEMENTARY CONDITIONS

GENERAL

These Supplementary Conditions amend or supplement the Standard General Conditions of the Construction Contract, EJCDC® C-700 (2013 Edition). All provisions that are not so amended or supplemented remain in full force and effect.

The terms used in these Supplementary Conditions have the meanings stated in the General Conditions. Additional terms used in these Supplementary Conditions have the meanings stated below, which are applicable to both the singular and plural thereof.

ARTICLE 2 – PRELIMINARY MATTERS**2.02 Copies of Documents**

Delete Paragraph 2.02.A in its entirety and insert the following in its place.

- A. Owner shall furnish to Contractor one printed copy of the Contract including one fully executed counterpart of the Agreement. An electronic portable document format (PDF) may be requested by Contractor.

2.03 Before Starting Construction

Delete Paragraph 2.03 in its entirety.

2.04 Preconstruction Conference; Designation of Authorized Representatives

Delete Paragraph 2.04.A in its entirety and insert the following in its place:

- A. Before any Work at the Site is started, a conference attended by Owner, Contractor, Engineer, and others as appropriate will be held to establish a working understanding among the parties as to the Work and to discuss the schedules, procedures for handling Shop Drawings, Samples, and other submittals, processing Applications for Payment, electronic or digital transmittals, and maintaining required records.

2.05 Initial Acceptance of Schedules

Delete Paragraph 2.05 in its entirety.

ARTICLE 3 – DOCUMENTS: INTENT, REQUIREMENTS, REUSE**3.04 Requirements of the Contract Documents**

Delete Paragraph 3.04.C in its entirety and insert the following:

- C. If a submitted matter in question concerns terms and conditions of the Contract Documents that do not involve (1) the performance or acceptability of the Work under the Contract Documents, (2) the design (as set forth in the Drawings, Specifications, or otherwise), or (3) other engineering or technical matters, then Engineer will promptly give written notice to Owner and Contractor that Engineer is unable to provide a decision or interpretation. If Owner and Contractor are unable to agree on resolution of such a matter in question, either party may pursue resolution as provided FDOT Section 5-12 Claims by Contractor.

ARTICLE 4 – COMMENCEMENT AND PROGRESS OF THE WORK**4.01 Commencement of Contract Times; Notice to Proceed**

Delete Paragraph 4.01.A in its entirety and insert the following in its place.

- A. The Contract Times will commence to run on the thirtieth day after the Effective Date of the Contract or, if a Notice to Proceed is given, on the day indicated in the Notice to Proceed. A Notice

to Proceed may be given at any time within 30 days after the Effective Date of the Contract. In no event will the Contract Times commence to run later than the one hundred twenty-fifth (125th) day after the day of Bid opening or the thirtieth day after the Effective Date of the Contract, whichever date is earlier.

ARTICLE 5 – AVAILABILITY OF LANDS; SUBSURFACE AND PHYSICAL CONDITIONS; HAZARDOUS ENVIRONMENTAL CONDITIONS

5.02 Use of Site and Other Areas

Delete Paragraph 5.02.A.2 in its entirety and insert the following:

2. If a damage or injury claim is made by the owner or occupant of any such land or area because of the performance of the Work, or because of other actions or conduct of the Contractor or those for which Contractor is responsible, Contractor shall (a) take immediate corrective or remedial action as required by Paragraph 7.12, or otherwise; (b) promptly attempt to settle the claim as to all parties through negotiations with such owner or occupant, or otherwise resolve the claim by mediation, or at law; and (c) indemnify and hold harmless Owner and Engineer, and the officers, directors, members, partners, employees, agents, consultants and subcontractors of each and any of them from and against any such claim, and against all costs, losses, and damages (including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals and all court or mediation costs) arising out of or relating to any claim or action, legal or equitable, brought by any such owner or occupant against Owner, Engineer, or any other party indemnified hereunder to the extent caused directly or indirectly, in whole or in part by, or based upon, Contractor's performance of the Work, or because of other actions or conduct of the Contractor or those for which Contractor is responsible.

5.03 Subsurface and Physical Conditions

Delete Paragraphs 5.03.A and 5.03.B in their entirety and insert the following:

- A. No reports of explorations or tests of subsurface conditions at or adjacent to the Site, or drawings of physical conditions relating to existing surface or subsurface structures at the Site, are known to Owner.

5.06 Hazardous Environmental Conditions

Delete Paragraphs 5.06.B and 5.06.I in their entirety.

Delete Paragraphs 5.06.A and 5.06.J in their entirety and insert the following:

- A. No reports or drawings related to Hazardous Environmental Conditions at the Site are known to Owner.
- J. Contractor shall indemnify and hold harmless Owner and Engineer, and the officers, directors, members, partners, employees, agents, consultants, and subcontractors of each and any of them from and against all claims, costs, losses, and damages (including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals and all court or mediation or other dispute resolution costs) arising out of or relating to the failure to control, contain, or remove a Constituent of Concern brought to the Site by Contractor or by anyone for whom Contractor is responsible, or to a Hazardous Environmental Condition created by Contractor or by anyone for whom Contractor is responsible. Nothing in this Paragraph 5.06.J shall obligate Contractor to indemnify any individual or entity from and against the consequences of that individual's or entity's own negligence.

ARTICLE 6 – BONDS AND INSURANCE

6.01 Performance, Payment and Other Bonds

Add the following paragraph immediately after Paragraph 6.01.C:

1. All bonds shall be written by a surety with no less than an "A" rating by national rating agency. All sureties must be on the U.S. Department of Treasury's Listing of Approved Sureties (Department Circular 570) and bonds must be within the Treasury's underwriting limitation.

6.02 Insurance – General Requirements

Delete Paragraph 6.02.B in its entirety and insert the following:

- B. All insurance required by the Contract to be purchased and maintained by OWNER and CONTRACTOR shall be obtained from insurance companies that are duly licensed or authorized, in the state or jurisdiction in which the Project is located, to issue insurance policies for the required limits and coverages. All companies that provide insurance policies required under this CONTRACT shall have a minimum A+, Class X or higher in the Bests Key Rating Guide.

Add the following new paragraphs immediately after Paragraph 6.02.J:

- K. Where applicable, Okaloosa County Board of County Commissioners shall be shown as an Additional Insured on all applicable insurance policies except Workers Compensation Insurance.
- L. Where applicable, a waiver of subrogation should be included on all Workers Compensation Insurance policies.

6.03 Contractor's Insurance

Add the following new paragraph immediately after Paragraph 6.03.J:

- K. The limits of liability for the insurance required by Paragraph 6.03 of the General Conditions shall provide coverage for not less than the following amounts or greater where required by Laws and Regulations:
 1. Workers' Compensation, and related coverages under Paragraphs 6.03.A.1 and A.2 of the General Conditions:

State:	<u>Statutory</u>
Federal, if applicable (e.g., Longshoreman's):	<u>Statutory</u>
Employer's Liability:	
Bodily injury, each accident	\$ <u>500,000</u>
Bodily injury by disease, each employee	\$ <u>500,000</u>
Bodily injury/disease aggregate	\$ <u>500,000</u>

2. Contractor's Commercial General Liability under Paragraphs 6.03.B and 6.03.C of the General Conditions:

General Aggregate	\$ <u>1,000,000</u>
Products - Completed Operations Aggregate	\$ <u>1,000,000</u>
Personal and Advertising Injury	\$ <u>1,000,000</u>
Each Occurrence (Bodily Injury and Property Damage)	\$ <u>1,000,000</u>

3. Automobile Liability under Paragraph 6.03.D. of the General Conditions:

Bodily Injury:	
Each person	\$ <u>1,000,000</u>
Each accident	\$ <u>1,000,000</u>
Property Damage:	
Each accident	\$ <u>500,000</u>
[or]	
Combined Single Limit of	\$ <u>1,000,000</u>

4. Additional Insureds: In addition to Owner (Okaloosa County Board of County Commissioners) include as additional insureds the following: DRMP, Inc, 2111 Thomas Dr., Panama City Beach, FL 32408.

5. Contractor's Pollution under Paragraph 6.03.F of the General Conditions

Each Occurrence	\$ <u>Not Required</u>
General Aggregate	\$ <u>Not Required</u>

6. Contractor's Professional Liability under Paragraph 6.03.H of the General Conditions

Each Occurrence	\$ <u>Not Required</u>
Annual Aggregate	\$ <u>Not Required</u>

Delete Paragraph 6.03.C.1 in its entirety and insert the following in its place:

1. Products and completed operations coverage:
 - a. Such insurance shall be maintained for two years after final payment.
 - b. Contractor shall furnish Owner and each other additional insured (as identified in the Supplementary Conditions or elsewhere in the Contract) evidence continuation of such insurance at final payment and two years thereafter.

ARTICLE 7 – CONTRACTOR'S RESPONSIBILITIES

7.02 Labor; Working Hours

Delete Paragraph 7.02 B. in its entirety and insert the following:

In the absence of any Laws or Regulations to the contrary, Contractor may only perform work from Sta 56+10 to Sta 41+50 between the hours of 8:00 AM to 1:00 PM during normal school days (all materials must be removed by 1:00 PM); from Sta 41+50 to Sta 35+00 from 8:00 AM to 1:30 PM; from Sta 31+50 to Sta 1+00 will be done during normal business hours. Weekend and holiday work will be assessed on a case by case basis.

7.07 Patent Fees and Royalties

Delete Paragraphs 7.07.B and C in their entirety and replace with the following:

- C. Contractor shall indemnify and hold harmless Owner and Engineer, and the officers, directors, members, partners, employees, agents, consultants and subcontractors of each and any of them from and against all claims, costs, losses, and damages (including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals and all court or mediation or other dispute resolution costs) arising out of or relating to any infringement of patent rights or copyrights incident to the use in the performance of the Work or resulting from the incorporation in the Work of any invention, design, process, product, or device not specified in the Contract Documents.

7.10 Laws and Regulations

Delete Paragraph 7.10.B in its entirety and replace with the following:

- B. If Contractor performs any Work or takes any other action knowing or having reason to know that it is contrary to Laws or Regulations, Contractor shall bear all resulting costs and losses, and shall indemnify and hold harmless Owner and Engineer, and the officers, directors, members, partners, employees, agents, consultants, and subcontractors of each and any of them from and against all claims, costs, losses, and damages (including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals and all court or mediation or other dispute resolution costs) arising out of or relating to such Work or other action. It shall not be Contractor's responsibility to make certain that the Work described in the Contract Documents is in accordance

with Laws and Regulations, but this shall not relieve Contractor of Contractor's obligations under Paragraph 3.03.

7.18 Indemnification

Delete Paragraph 7.18.A in its entirety and insert the following:

- A. Contractor shall indemnify and hold harmless the Owner and the design Engineer, and the officers, directors, members, partners, employees, agents, consultants and subcontractors of each and any of them from and against all claims, costs, losses, and damages (including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals and all court or mediation or other dispute resolution costs) arising out of or relating to the performance of the Work, provided that any such claim, cost, loss, or damage is attributable to bodily injury, sickness, disease, or death, or to injury to or destruction of tangible property (other than the Work itself), including the loss of use resulting therefrom but only to the extent caused by any negligent act or omission of Contractor, any Subcontractor, any Supplier, or any individual or entity directly or indirectly employed by any of them to perform any of the Work or anyone for whose acts any of them may be liable.

ARTICLE 8 – OTHER WORK AT THE SITE

8.03 Legal Relationships

Delete Paragraph 8.03.D in its entirety and insert the following:

- D. If Contractor damages, delays, disrupts, or interferes with the work of any other contractor, or any utility owner performing other work at or adjacent to the Site, through Contractor's failure to take reasonable and customary measures to avoid such impacts, or if any claim arising out of Contractor's actions, inactions, or negligence in performance of the Work at or adjacent to the Site is made by any such other contractor or utility owner against Contractor, Owner, or Engineer (both Design and CEI), then Contractor shall (1) promptly attempt to settle the claim as to all parties through negotiations with such other contractor or utility owner, or otherwise resolve the claim by mediation or other dispute resolution proceeding or at law, and (2) indemnify and hold harmless Owner and Engineer, and the officers, directors, members, partners, employees, agents, consultants and subcontractors of each and any of them from and against any such claims, and against all costs, losses, and damages (including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals and all court or mediation or other dispute resolution costs) arising out of or relating to such damage, delay, disruption, or interference.

ARTICLE 10 – ENGINEER'S STATUS DURING CONSTRUCTION

10.03 Project Representative

Add the following new paragraphs immediately after Paragraph 10.03.A:

- B. The Resident Project Representative (RPR) will be Engineer's representative at the Site, will act as directed by and under the supervision of Engineer, and will confer with Engineer regarding RPR's actions.
 - 1. General: RPR's dealings in matters pertaining to the Work in general shall be with Engineer and Contractor. RPR's dealings with Subcontractors shall only be through or with the full knowledge and approval of Contractor. RPR shall generally communicate with Owner only with the knowledge of and under the direction of Engineer.
 - 2. Schedules: Review the progress schedule, schedule of Shop Drawing and Sample submittals, and Schedule of Values prepared by Contractor and consult with Engineer concerning acceptability.
 - 3. Conferences and Meetings: Attend meetings with Contractor, such as preconstruction conferences, progress meetings, job conferences, and other Project-related meetings, and prepare and circulate copies of minutes thereof.

4. Liaison:
 - a. Serve as Engineer's liaison with Contractor. Working principally through Contractor's authorized representative or designee, assist in providing information regarding the provisions and intent of the Contract Documents.
 - b. Assist Engineer in serving as Owner's liaison with Contractor when Contractor's operations affect Owner's on-Site operations.
 - c. Assist in obtaining from Owner additional details or information, when required for proper execution of the Work.
5. Interpretation of Contract Documents: Report to Engineer when clarifications and interpretations of the Contract Documents are needed and transmit to Contractor clarifications and interpretations as issued by Engineer.
6. Shop Drawings and Samples:
 - a. Record date of receipt of Samples and Contractor-approved Shop Drawings.
 - b. Receive Samples which are furnished at the Site by Contractor, and notify Engineer of availability of Samples for examination.
 - c. Advise Engineer and Contractor of the commencement of any portion of the Work requiring a Shop Drawing or Sample submittal for which RPR believes that the submittal has not been approved by Engineer.
7. Modifications: Consider and evaluate Contractor's suggestions for modifications in Drawings or Specifications and report such suggestions, together with RPR's recommendations, if any, to Engineer. Transmit to Contractor in writing decisions as issued by Engineer.
8. Review of Work and Rejection of Defective Work:
 - a. Conduct on-Site observations of Contractor's work in progress to assist Engineer in determining if the Work is in general proceeding in accordance with the Contract Documents.
 - b. Report to Engineer whenever RPR believes that any part of Contractor's work in progress is defective, will not produce a completed Project that conforms generally to the Contract Documents, or will imperil the integrity of the design concept of the completed Project as a functioning whole as indicated in the Contract Documents, or has been damaged, or does not meet the requirements of any inspection, test or approval required to be made; and advise Engineer of that part of work in progress that RPR believes should be corrected or rejected or should be uncovered for observation, or requires special testing, inspection or approval.
9. Inspections, Tests, and System Start-ups:
 - a. Verify that tests, equipment, and systems start-ups and operating and maintenance training are conducted in the presence of appropriate Owner's personnel, and that Contractor maintains adequate records thereof.
 - b. Observe, record, and report to Engineer appropriate details relative to the test procedures and systems start-ups.
10. Records:
 - a. Prepare a daily report or keep a diary or log book, recording Contractor's hours on the Site, Subcontractors present at the Site, weather conditions, data relative to questions of Change Orders, Field Orders, Work Change Directives, or changed conditions, Site visitors, deliveries of equipment or materials, daily activities, decisions, observations in general, and specific observations in more detail as in the case of observing test procedures; and send copies to Engineer.
 - b. Record names, addresses, fax numbers, e-mail addresses, web site locations, and telephone numbers of all Contractors, Subcontractors, and major Suppliers of materials and equipment.
 - c. Maintain records for use in preparing Project documentation.
11. Reports:

- a. Furnish to Engineer periodic reports as required of progress of the Work and of Contractor's compliance with the Progress Schedule and schedule of Shop Drawing and Sample submittals.
 - b. Draft and recommend to Engineer proposed Change Orders, Work Change Directives, and Field Orders. Obtain backup material from Contractor.
 - c. Immediately notify Engineer of the occurrence of any Site accidents, emergencies, acts of God endangering the Work, force majeure or delay events, damage to property by fire or other causes, or the discovery of any Constituent of Concern or Hazardous Environmental Condition.
12. Payment Requests: Review applications for payment with Contractor for compliance with the established procedure for their submission and forward with recommendations to Engineer, noting particularly the relationship of the payment requested to the Schedule of Values, Work completed, and materials and equipment delivered at the Site but not incorporated in the Work.
13. Certificates, Operation and Maintenance Manuals: During the course of the Work, verify that materials and equipment certificates, operation and maintenance manuals and other data required by the Contract Documents to be assembled and furnished by Contractor are applicable to the items actually installed and in accordance with the Contract Documents, and have these documents delivered to Engineer for review and forwarding to Owner prior to payment for that part of the Work.
14. Completion:
 - a. Participate in Engineer's visits to the Site to determine Substantial Completion, assist in the determination of Substantial Completion and the preparation of a punch list of items to be completed or corrected.
 - b. Participate in Engineer's final visit to the Site to determine completion of the Work, in the company of Owner and Contractor, and prepare a final punch list of items to be completed and deficiencies to be remedied.
 - c. Observe whether all items on the final list have been completed or corrected and make recommendations to Engineer concerning acceptance and issuance of the notice of acceptability of the work.
- C. The RPR shall not:
 1. Authorize any deviation from the Contract Documents or substitution of materials or equipment (including "or-equal" items).
 2. Exceed limitations of Engineer's authority as set forth in the Contract Documents.
 3. Undertake any of the responsibilities of Contractor, Subcontractors, or Suppliers.
 4. Advise on, issue directions relative to, or assume control over any aspect of the means, methods, techniques, sequences or procedures of Contractor's work.
 5. Advise on, issue directions regarding, or assume control over security or safety practices, precautions, and programs in connection with the activities or operations of Owner or Contractor.
 6. Participate in specialized field or laboratory tests or inspections conducted off-site by others except as specifically authorized by Engineer.
 7. Accept Shop Drawing or Sample submittals from anyone other than Contractor.
 8. Authorize Owner to occupy the Project in whole or in part.

ARTICLE 13 – COST OF THE WORK; ALLOWANCES; UNIT PRICE WORK

13.03 Unit Price Work

Delete Paragraph 13.03.E in its entirety and insert the following in its place:

- E. The unit price of an item of Unit Price Work shall be subject to reevaluation and adjustment under the following conditions:

1. if the extended price of a particular item of Unit Price Work amounts to 5 percent or more of the Contract Price (based on estimated quantities at the time of Contract formation) and the variation in the quantity of that particular item of Unit Price Work actually furnished or performed by Contractor differs by more than 25 percent from the estimated quantity of such item indicated in the Agreement; and
2. if there is no corresponding adjustment with respect to any other item of Work; and
3. if Contractor believes that Contractor has incurred additional expense as a result thereof, Contractor may submit a Change Proposal, or if Owner believes that the quantity variation entitles Owner to an adjustment in the unit price, Owner may make a Claim, seeking an adjustment in the Contract Price.

ARTICLE 15 – PAYMENTS TO CONTRACTOR; SET-OFFS; COMPLETION; CORRECTION PERIOD

15.01 Progress Payments

Delete Paragraph 15.01.B.1 in its entirety and insert the following in its place:

B. Applications for Payment

1. Application for payment shall generally be submitted on a monthly basis (no more than once per month), Contractor shall submit to Engineer for review an Application for Payment form approved by the Owner filled out and signed by Contractor covering the Work completed as of the date of the Application and accompanied by such supporting documentation as is required by the Contract Documents. If payment is requested on the basis of materials and equipment not incorporated in the Work but delivered and suitably stored at the Site or at another location agreed to in writing, the Application for Payment shall also be accompanied by a bill of sale, invoice, or other documentation warranting that Owner has received the materials and equipment free and clear of all Liens, and evidence that the materials and equipment are covered by appropriate property insurance, a warehouse bond, or other arrangements to protect Owner's interest therein, all of which must be

Delete Paragraph 15.01.C.1 in its entirety and insert the following in its place:

C. Review of Application

1. Engineer will within 5 business days after receipt of each Application for Payment, including each resubmittal, either indicate in writing a recommendation of payment and present the Application to Owner, or return the Application to Contractor indicating in writing Engineer's reasons for refusing to recommend payment. In the latter case, Contractor may make the necessary corrections and resubmit the Application.

15.03 Substantial Completion

Add the following new subparagraph to Paragraph 15.03.B:

1. If some or all of the Work has been determined not to be at a point of Substantial Completion and will require re-inspection or re-testing by Engineer, the cost of such re-inspection or re-testing, including the cost of time, travel and living expenses, shall be paid by Contractor to Owner. If Contractor does not pay, or the parties are unable to agree as to the amount owed, then Owner may impose a reasonable set-off against payments due under Article 15.

15.08 Correction Period

Delete Paragraph 15.08.B in its entirety and insert the following in its place:

B. If Contractor does not promptly comply with the terms of Owner's written instructions, or in an emergency where delay would cause serious risk of loss or damage, Owner may have the defective Work corrected or repaired or may have the rejected Work removed and replaced. Contractor shall pay all claims, costs, losses, and damages (including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals and all court or mediation or other dispute resolution costs) arising out of or relating to such correction or repair or such removal and replacement (including but not limited to all costs of repair or replacement of work of others)

ARTICLE 16 – SUSPENSION OF WORK AND TERMINATION**16.04 Contractor May Stop Work or Terminate**

Delete Paragraphs 16.04.A and 16.04.B in their entirety and insert the following in their place:

- A. If, through no act or fault of Contractor, (1) the Work is suspended for more than 90 consecutive days by Owner or under an order of court or other public authority, or (2) Engineer fails to act on any Application for Payment within 30 days after it is submitted, or (3) Owner fails for 60 days to pay Contractor any sum finally determined to be due, then Contractor may, upon seven days written notice to Owner and Engineer, and provided Owner or Engineer do not remedy such suspension or failure within that time, terminate the contract and recover from Owner payment on the same terms as provided in Paragraph 16.03.
- B. In lieu of terminating the Contract and without prejudice to any other right or remedy, if Engineer has failed to act on an Application for Payment within 30 days after it is submitted, or Owner has failed for 60 days to pay Contractor any sum finally determined to be due, Contractor may, seven days after written notice to Owner and Engineer, stop the Work until payment is made of all such amounts due Contractor, including interest thereon. The provisions of this paragraph are not intended to preclude Contractor from submitting a Change Proposal for an adjustment in Contract Price or Contract Times or otherwise for expenses or damage directly attributable to Contractor's stopping the Work as permitted by this paragraph.

ARTICLE 18 – MISCELLANEOUS**18.07 Controlling Law**

Delete paragraph 18.07.A in its entirety and replace the following in its place:

- A. This Contract shall be interpreted in accordance with the laws of the State of Florida without regard to its principles of conflicts of laws. The parties agree that venue for any legal proceedings arising out of this Contract shall be in the state courts of Okaloosa County, Florida.

Add the following two sub articles to Article 18.

18.09 Coordination of Contract Documents

- A. The following documents are integral parts of the Contract; a requirement occurring in one is as binding as though occurring in all. All parts of the Contract are complementary and describe and provide for a complete Work. In addition to the work and materials specified in the Standard Specifications as being included in any specific pay item, include in such pay items additional, incidental work not specifically mentioned, when so shown in the plans, or if indicated, or obvious and apparent, as being necessary for the proper completion of the Work under such pay item and not stipulated as being covered under other pay items.
- B. In cases of discrepancy, the governing order of the documents is as follows:
 - 1. Modifications issued after the execution of the Agreement
 - 2. Agreement between Owner & Contractor for Construction Contract
 - 3. Addenda issued after the Bid Specifications were advertised to potential Bidders
 - 4. Supplementary Conditions
 - 5. FDOT Standard Specifications for Road & Bridge Construction, Latest Edition
 - 6. EJCDC General Conditions, 2013 Edition
 - 7. Technical Specifications
 - 8. Construction Drawings
 - 9. Computed dimensions govern over scaled dimensions

18.10 Construction Closeout Requirements to County

- A. Immediately after being notified by the Engineer that all other requirements of the Agreement have been completed Contractor shall complete the following items

1. Signed Release of Liens;
2. Certificate of Insurance for two year period, letter from Contractor stating Certificate of Insurance will be maintained for two (2) years;
3. Certifications from Surety that Payment/Performance Bond shall remain in effect one year following final payment;
4. Consent of Surety for Final Payment;
5. Final Invoice with Engineer's Recommendation, final payment of this Contract shall be made within sixty (60) days after completion by the Contractor of all Work covered by the Agreement and acceptance of such Work by the County;
6. Record (As-Built) Drawing

END OF DOCUMENT 00800 – SUPPLEMENTARY CONDITION

PART 1 - GENERAL**1.01 Work Covered by the Contract Documents**

- A. The project intent is to construct a sidewalk along Old Bethel Rd going west from Davidson Middle School.
- B. The WORK covered by the CONTRACT Documents include – constructing sidewalk, and other associated work including clearing and grubbing, earthwork, maintenance of traffic, concrete retaining walls, and other improvements and other WORK as shown on the construction drawings and described in the specifications.

1.02 Work Sequence

- A. The work sequence will be determined by the CONTRACTOR.

1.03 Contractor's Use of Premises

- A. The CONTRACTOR may use the Permanent Drainage Easements within the construction limits and the area within any temporary construction easement.
- B. CONTRACTOR shall assume full responsibility for safety at the work site for all workers and visitors.
- C. The CONTRACTOR shall send proper notices, make all necessary arrangements, and perform all services required in the care and maintenance of all OWNER and public utilities within the construction limits.

PART 2 - PRODUCTS OMITTED**PART 3 - EXECUTION OMITTED**

END OF DOCUMENT 01010 – SUMMARY OF WORK

PART 1 - GENERAL

1.01 Related Documents

- A. Drawings and general provisions of CONTRACT, including General and Supplementary Conditions and other Division 1 Specification Sections, apply to this Section.

1.02 Summary

- A. This Section specifies administrative and supervisory requirements necessary for Project coordination including, but not necessarily limited to:
 - 1. Coordination.
 - 2. Administrative and supervisory personnel.
 - 3. General installation provisions.
 - 4. Cleaning and protection.

1.03 Coordination

- A. Coordination: Coordinate construction activities included under various sections of these Specifications to assure efficient and orderly installation of each part of the WORK. Coordinate construction operations included under different sections of the Specifications that are dependent upon each other for proper installation, connection, and operation.
 - 1. Where installation of one part of the WORK is dependent on installation of other components, either before or after its own installation, schedule construction activities in the sequence required to obtain the best results.
 - 2. Where availability of space is limited, coordinate installation of different components to assure maximum accessibility for required maintenance, service and repair.
 - 3. Make adequate provisions to accommodate items scheduled for later installation.
- B. Where necessary, prepare memoranda for distribution to each party involved outlining special procedures required for coordination. Include such items as required notices, reports, and attendance at meetings.
 - 1. Prepare similar memoranda for the OWNER and separate CONTRACTORS where coordination of their WORK is required.
- C. Administrative Procedures: Coordinate scheduling and timing of required administrative procedures with other construction activities to avoid conflicts and ensure orderly progress of the WORK. Such administrative activities include, but are not limited to, the following:
 - 1. Preparation of schedules.
 - 2. Installation and removal of temporary facilities.
 - 3. Delivery and processing of submittals.
 - 4. Progress meetings.
 - 5. Project Close-out activities.

1.04 Submittal

- A. Coordination Drawings: Prepare and submit coordination Drawings where close and careful coordination is required for installation of products and materials fabricated off-site by separate entities, and where limited space availability necessitates maximum utilization of space for efficient installation of different components.
 - 1. Show the interrelationship of components shown on separate Shop Drawings.
 - 2. Indicate required installation sequences.
 - 3. Comply with requirements contained in Section 00700 Article 7.16
- B. Staff Names: Within 15 days of Notice to Proceed, submit a list of the CONTRACTOR's principal staff assignments, including the Superintendent and other personnel in attendance at the site; identify individuals, their duties and responsibilities; list their addresses and telephone numbers.

PART 2 - PRODUCTS OMITTED

PART 3 - EXECUTION

3.01 General Installation Provisions

- A. Inspection of Conditions: Require the Installer of each major component to inspect both the substrate and conditions under which WORK is to be performed. Do not proceed until unsatisfactory conditions have been corrected in an acceptable manner.
- B. Manufacturer's Instructions: Comply with manufacturer's installation instructions and recommendations, to the extent that those instructions and recommendations are more explicit or stringent than requirements contained in Contract Documents.
- C. Inspect materials or equipment immediately upon delivery and again prior to installation. Reject damaged and defective items.
- D. Provide attachment and connection devices and methods necessary for securing WORK. Secure WORK true to line and level. Allow for expansion and building movement.
- E. Visual Effects: Provide uniform joint widths in exposed WORK. Arrange joints in exposed WORK to obtain the best visual effect. Refer questionable choices to the Architect for final decision.
- F. Recheck measurements and dimensions, before starting each installation.
- G. Install each component during weather conditions and Project status that will ensure the best possible results. Isolate each part of the completed construction from incompatible material as necessary to prevent deterioration.
- H. Coordinate temporary enclosures with required inspections and tests, to minimize the necessity of uncovering completed construction for that purpose.
- I. Mounting Heights: Where mounting heights are not indicated, install individual components at standard mounting heights recognized within the industry for the particular application indicated. Refer questionable mounting height decisions to the Architect for final decision.

3.02 Cleaning and Protection

- A. During handling and installation, clean and protect construction in progress and adjoining materials in place. Apply protective covering where required to ensure protection from damage or deterioration at Substantial Completion.
- B. Clean and maintain completed construction as frequently as necessary through the remainder of the construction period. Adjust and lubricate operable components to ensure operability without damaging effects.
- C. Limiting Exposures: Supervise construction activities to ensure that no part of the construction, completed or in progress, is subject to harmful, dangerous, damaging, or otherwise deleterious exposure during the construction period. Where applicable, such exposures include, but are not limited to, the following:
 - 1. Excessive static or dynamic loading
 - 2. Excessive internal or external pressures
 - 3. Excessively high or low temperatures
 - 4. Thermal shock
 - 5. Excessively high or low humidity
 - 6. Air contamination or pollution
 - 7. Water
 - 8. Solvents
 - 9. Chemicals
 - 10. Puncture
 - 11. Abrasion
 - 12. Heavy traffic
 - 13. Soiling, staining and corrosion
 - 14. Bacteria
 - 15. Rodent and insect infestation

16. Combustion
17. Electrical current
18. Improper lubrication
19. Unusual wear or other misuse
20. Contact between incompatible materials
21. Misalignment
22. Excessive weathering
23. Unprotected storage
24. Improper shipping or handling
25. Theft
26. Vandalism

END OF DOCUMENT 01040 – PROJECT COORDINATION

PART 1 – GENERAL

1.01 Warranties

- A. The CONTRACTOR shall provide a warranty on all materials and workmanship for at least one (1) year (min.) from the date of Substantial Completion as per the General Conditions.
- B. Additional Warranties apply to individual products, materials and / or assemblies; refer to each of the respective Specification sections to obtain the minimum required warranty information.

1.02 Operation Manuals

- A. The CONTRACTOR shall file (in one place) all operation, maintenance or other manuals received with equipment and upon completion of project, they must be presented to the OWNER with a notification, in writing, to the ENGINEER that this has been accomplished.

PART 2 - PRODUCTS OMITTED

PART 3 - EXECUTION OMITTED

END OF DOCUMENT 01350 – WARRANTIES AND MANUALS

PART 1 – GENERAL

1.01 Temporary Services

A. Toilet Facilities

1. The CONTRACTOR shall provide temporary, on-site toilet facilities for the duration of construction. Cleaning shall be conducted in accordance with 2.07.

B. General Utilities

1. Water: The CONTRACTOR shall pay and provide for water needed for the Project during Construction.
2. Power: The CONTRACTOR shall pay for electricity used for the Project during the Construction. CONTRACTOR shall coordinate with Gulf Power for connection.
 - a. Comply with applicable requirements of NEMA, NECA and UL standards and governing regulations. Install temporary lighting of adequate illumination levels to perform the WORK specified as needed.
 - b. Comply with NECA pertaining to installation of temporary wiring service and grounding. Provide transformers, and over current protective devices at main distribution panel for power and light circuitry.
 - c. Provide disconnects for equipment circuits.

1.02 Protection of Occupants

- A. Provide all warning signs, temporary fencing, barricades, supports, partitions, etc. as required to provide protection to the occupants, and to exclude unauthorized persons from the WORK areas.
- B. Comply with recognized standards and code requirements for erection of barricades where needed to prevent accidents. Paint with appropriate colors and warning signs to inform personnel at the site and the public of the hazard being protected against. Provide lighting where needed, including flashing red lights where appropriate.

1.03 Lifting Devices and Hoisting

- A. Provide cranes, hoists, towers and other lifting devices necessary for the proper and efficient movement of materials; provide operating personnel for equipment as required. Equipment shall be provided with proper guys, bracing and other safety devices as required by Local or State codes.
- B. Remove towers and hoisting equipment when they are no longer needed, or as directed by the Architect.

1.10 First Aid Supplies

- A. Comply with governing regulations and recognized recommendations within the construction industry.

1.11 Rodent and Pest Control

- A. The CONTRACTOR shall retain a local exterminator and/or pest control company to perform extermination and control procedures at regular intervals so that the project will be relatively free of pests and their residues at all times during the construction project.
- B. Any pest control operations will be done in a lawful manner using environmentally safe materials.

1.12 Collection and Disposal of Waste

- A. Establish a system for collection and disposal of waste materials. Enforce requirements strictly. Do not hold collected materials longer than seven (7) days during normal weather or three (3) days when the daily temperature is expected to rise above 80 degrees F. (27 degrees C). Store wastes in a covered/closed container.
- B. Handle waste materials that are hazardous, dangerous, or unsanitary separately from other waste by

containerizing.

- C. Dispose of all waste material in a lawful manner.

1.13 Site Drainage

- A. Utilize the existing facilities for temporary drainage where feasible.
- B. Maintain the existing site, existing building and construction areas free of water.
- C. Dispose of rainwater in a lawful manner which will not result in flooding in project, nor endanger either existing or new WORK or temporary facilities.
- D. Take necessary measures to prevent erosion.

1.14 Environmental Protection

- A. Conduct all construction activities, by means and methods that comply with any and all environmental regulations, to minimize the possibility that air, waterways and subsoil might be contaminated or polluted, or that other undesirable effects might result from the performance of WORK at the site.

1.15 General Protection

- A. Provide protection from damage, dust, etc. to all items in vicinity of the CONTRACT WORK including, but not limited to, existing building surfaces, finishes, items of equipment, utilities, etc. The CONTRACTOR will repair any new damage caused and / or created due to this construction project, to Owner's satisfaction at no additional cost to Owner. (Non-Construction related damage would be exempt from this clause)

PART 2 – PRODUCTS OMITTED

PART 3 - EXECUTION

3.01 General Operations

- A. Supervision: Limit the availability of temporary services and facilities to essential and intended uses to minimize waste and abuse.
 - 1. Do not permit temporary installation to be abused or endangered.
- B. Maintenance: Operate and maintain temporary services and facilities in good operating condition and in a safe and efficient manner until removal is authorized.
 - 1. Do not overload services or facilities.
 - 2. Protect from damage by freezing temperatures and/or similar elements.
 - 3. Do not allow unsanitary and/or hazardous conditions to develop or persist on site.
- C. Maintain operation of temporary enclosures, heating, cooling, humidity control, ventilation and similar facilities on a 24-hour basis where required to achieve indicated results and avoid the possibility of damage to the WORK or to temporary facilities.

3.02 General Removal

- A. Remove each temporary service and facility promptly when need has ended, or when it is replaced by use of a permanent facility, but no later than Substantial Completion.
- B. Complete or, if necessary, restore permanent WORK delayed because of interference with the temporary service or facility.
- C. Repair all damaged WORK, clean exposed surfaces and replace any WORK which cannot be repaired.
- D. Clean and renovate any permanent services and/or facilities that may have been used to provide a temporary service and/or facilities during the construction period.

END OF DOCUMENT 01500 – TEMPORARY FACILITIES

PART 1 - GENERAL

1.01 Related Documents

- A. Drawings and general provisions of Contract, including General and Supplementary General Conditions and other Division-0 Specification sections, apply to the WORK of this section.

1.02 Description of Requirements

- A. Definitions: Close-out is hereby defined to include general requirements near end of the Contract Time, in preparation for final acceptance, final payment and normal termination of contract.
- B. Specific requirements for individual units of WORK are specified in sections of Division 0 through 16. Time of close-out is directly related to the "Substantial Completion", and must be a single time period for entire WORK.

1.03 Prerequisites to Substantial Completion

- A. General: Prior to requesting the ENGINEER's inspection for certification of Substantial Completion, complete the following and list any known exceptions (if any) in request.
 - 1. The in-progress payment request will coincident with or first following date claimed, show either 100% completion for portion of WORK claimed as "Substantially Complete", or list incomplete items, value of incompleteness, and reasons for the items being incomplete.
 - 2. Include any supporting documentation required for completion as indicated in these Contract Documents.
 - 3. Submit statement showing accounting of any changes to the Contract Sum.
 - 4. Contractor shall notify and advise the OWNER of any pending insurance change over requirements.
 - 5. Submit specific warranties, workmanship / maintenance bonds, maintenance agreements, final certifications and similar documents.
 - 6. Obtain and submit releases enabling OWNER's full and unrestricted use of the WORK and access to services and utilities, including, where required, Occupancy Permits, operating certificates, and similar releases.
 - 7. Deliver tools, spare parts, extra stocks of materials, and similar physical items to the OWNER.
 - 8. Complete the start-up testing of the systems, and deliver the instructions of the operating systems to the OWNER and / or maintenance personnel. Discontinue (or change over) and remove from project site all temporary facilities and services, along with any construction tools and facilities, mock-ups, and similar elements.
 - 9. Complete the final cleaning up requirements, including the touch-up of any marred surfaces as required.
 - 10. Touch-up and otherwise repair and restore marred exposed finishes.

1.04 Inspection Procedures

- A. Upon the receipt of the Contractor's request. The Engineer of Record will either proceed with the inspection or advise the Contractor of any prerequisites not fulfilled.
- B. Following the initial inspection, the Engineer of Record will either prepare a Certificate of Substantial Completion, or advise the Contractor of WORK that must be performed prior to the issuance of the certificate; and repeat the inspection when requested and assured that WORK has been substantially completed.
- C. The Contractor shall prepare a type written "punch-list" of items to be completed and attach it to the Substantial Completion Form. Results of the completed inspection will form initial "punch-list" for the final acceptance.

1.05 Prerequisites to Final Acceptance

- A. General: Prior to requesting the ENGINEER's final construction review for certification of final acceptance and final payment, as required by General Conditions, complete the following and list any known exceptions (if any) in request:
 - 1. Submit final payment request with final releases and supporting documentation not previously submitted and/or accepted. Include certificates of insurance for products and completed operations where required.
 - 2. Submit updated final statement, accounting for additional (final) changes to Contract Sum.
 - 3. Submit a certified copy of ENGINEER's "final punch-list" of itemized WORK to be completed or corrected, stating that each item has been completed or otherwise resolved for acceptance, endorsed and dated by the ENGINEER.
 - 4. Submit Consent of Surety.
 - 5. Submit Certified and Notarized Lien Release stating that all parties have been or will be paid (showing amounts).
 - 6. Submit final liquidated damages settlement statement, acceptable to OWNER.
 - 7. Revise and submit evidence of final, continuing insurance coverage complying with insurance requirements.
- B. Review Procedure: Upon receipt of Contractor's notice that WORK has been completed, including punch-list items resulting from earlier construction reviews, and excepting incomplete items delayed because of acceptable circumstances. The ENGINEER will re-inspect the WORK.
- C. Upon completion of review, the ENGINEER will either prepare the Certificate of Final Acceptance or advise the Contractor of WORK not completed or of obligations not fulfilled as required for final acceptance.
- D. If necessary, procedure will be repeated.

1.06 Equipment Close-out

- A. General Operating / Maintenance Instructions: Arrange for each installer of the WORK that requires a continuing maintenance or operation, to meet with OWNER's personnel, at the project site, to provide basic instructions needed for the proper operation and any type of equipment maintenance.
 - 1. Include instructions by manufacturer's representatives where installers are not experts in the required procedures.
 - 2. Review maintenance manuals, record documentation, tools, spare parts and materials, lubricants, fuels, identification system, control sequences, hazards, cleaning and similar procedures and facilities.
 - 3. For operational equipment, demonstrate start-up, shut-down, emergency operations, noise and vibration adjustments, safety, economy /efficiency adjustments, and similar operations.
 - 4. Review maintenance and operations in relation with applicable warranties, agreements to maintain, bonds, and similar continuing commitments

1.07 Final Cleaning

- A. For any special cleaning requirements for the specific units of WORK, would be specified in individual sections, of Divisions 2 through 16.
- B. General cleaning during the progress of WORK is specified in General Conditions and as temporary services in "Temporary Facilities" section of this Division.
- C. Provide final cleaning of the WORK, at time indicated, consisting of cleaning each surface or unit of WORK to normal "clean" condition as expected for a first-class building cleaning and maintenance program.
- D. Comply with the manufacturer's instructions for cleaning operations. The following are examples, but not by way of limitation, of cleaning levels required:
 - 1. Remove labels which are not required as permanent labels.

2. Clean transparent materials, including mirrors and window/door glass, to a polished condition, removing any substances which are noticeable as a vision obscuring material. Replace broken glass and all damaged transparent materials.
3. Clean all exposed exterior and interior hard-surfaced finishes, to a dirt-free condition, free of dust, stains, films and similar noticeable distracting substances. Except as otherwise indicated, avoid disturbance of natural weathering of exterior surfaces. Restore reflective surfaces to the original reflective condition.
4. Wipe surfaces of mechanical and electrical equipment clean; remove any excess lubrication and other substances.
5. Remove debris and surface dust from limited-access spaces including roofs, plenums, shafts, attics and similar spaces.
6. Clean all light fixtures and lamps so as to function with full efficiency.
7. Clean the project site (within limits of construction), including landscape areas, of litter and foreign substances. Sweep paved areas to a broom-clean condition; remove stains, petro-chemical spills and other foreign deposits.
- E. Removal of Protection: Except as otherwise indicated or requested by the ENGINEER and / or OWNER. Remove all temporary protection devices and facilities.
- F. Comply with safety standards and governing regulations for the cleaning operations. Do not burn waste materials at site, or bury any debris or excess materials on the OWNER's property, or discharge volatile or other harmful or dangerous materials into the drainage systems. Remove all waste materials from site and dispose of in a lawful manner.
- G. When extra materials are remaining after the completion of associated WORK, which have become the OWNER's property, dispose of these to OWNER's best advantage as directed.

END OF DOCUMENT 01700 – PROJECT CLOSE-OUT

PART 1 – GENERAL

1.01 Related Documents

- A. Drawings and general provisions of CONTRACT, including General and Supplementary General Conditions and other Division-0 Specification sections, apply to the WORK of this section.

1.02 Summary

- A. Section includes administrative and procedural requirements for the record set of documents, including the following;
 - 1. Record Set of Drawings.
 - 2. Record Set of Specifications.
- B. Related Sections:
 - 1. Section 01700 - Project Close-Out.

1.03 Record Document Submittal

- A. Submit the following copies of the Record Documents during or prior to the Project Close-out:
 - 1. Provide one complete full size color copies, of the "marked-up" record set of drawings.
 - 2. Provide one complete "marked-up" record set of specifications.
- B. Copies are to be distributed, one of each type to the OWNER.

1.04 Use and Storage

- A. Store the Record Documents in the field office apart from the documents used for the construction. Do not use the Record Documents for construction purposes. Maintain Record Documents in good order and in a clean, dry, legible condition. Make all documents and samples available at all times for the OWNER, ENGINEERS and / or Building Inspectors as needed.
- B. Each CONTRACTOR is responsible for obtaining, recording, and maintaining the Record Documents information for its own WORK. The CONTRACTOR is responsible for coordinating the information, where information from more than one CONTRACTOR is to be integrated with the information from other CONTRACTORS to form one combined record.

1.05 Record Drawings

- A. Mark the Record Drawings to show the actual installation where the locations vary from the installation locations shown originally. Give particular attention to information on the concealed elements that would be difficult to identify or measure and record later. Items required to be marked include, but are not limited to, the following:
 - 1. Measured horizontal and vertical locations of underground utilities and other appurtenances, referenced to permanent surface improvements.
 - 2. Locations of concealed internal utilities and appurtenances.
 - 3. Actual equipment locations.
 - 4. Revisions to routing of piping and conduits.
 - 5. Duct size and routing.
 - 6. Depths of foundations below the first floor.
 - 7. Revisions to electrical circuitry.
 - 8. Dimensional changes to the Drawings.
 - 9. Revisions to details on the Drawings.
 - 10. Details not on the original CONTRACT Drawings.
 - 11. Changes made following the OWNER's written orders.
 - 12. Changes made by Addendum, Change Orders, Requests for Information (RFIs), or ENGINEER's Supplemental Instructions (ASIs).

- B. Mark the Record Drawings and Shop Drawings completely and accurately. Utilize personnel proficient at recording graphic information in the production of the marked-up Record Documents.

1.06 Record Specifications

- A. Mark the Record Specifications to show Addendums, Change Orders, Requests for Information (RFIs), or ENGINEER's Supplemental Instructions (ASIs).
- B. Indicate on the Record Specifications the actual product that was installed where the installation varies from the Specifications, addenda and CONTRACT modifications.
 - 1. Give particular attention to information on concealed products and the installations that cannot be readily identified and recorded later.
 - 2. Mark the Record copy with the propriety name and model number of products, materials and equipment furnished, including substitutions and product options selected.
 - 3. Record the name of manufacturer, supplier, installer and other necessary to provide a record of selections made.
 - 4. For each principal product, indicate whether the record Product Data has been submitted in the operation and maintenance manuals instead of submitted as record Product Data.
 - 5. Note related Change Orders and turnover drawings where applicable.

PART 2 – PRODUCT OMITTED

PART 3 – EXECUTION

3.01 Preparation

- A. Daily mark the Record Documents to show the actual conditions where the installation varies from that shown originally. Require the individual or entity who obtained the record data, whether that individual or entity is the Installer, Sub-contractor or similar entity to provide the information for the preparation of the corresponding marked-up Record Set of Drawings.
 - 1. Give particular attention to information on concealed elements that would be difficult to identify or measure and record later.
 - 2. Accurately record information in an acceptable drawing technique.
 - 3. Record data as soon as possible after obtaining it.
 - 4. Record and check the mark-up before enclosing the concealed installations.
 - 5. Record the changes and modifications as they occur. Do not wait until the end of the Project.

3.02 Recording

- A. During construction, maintain an extra set of the CONTRACT Documents specifically for the purpose of creating the Record Documents. Keep them separate from the set used for construction.
 - 1. Stamp each sheet of the Record Drawings and the cover of the Record Specifications in the lower right-hand corner with a reasonably large ink stamp to read "Record Set".
 - 2. Mark Record Set Documents with a red pencil or pen. Use other colors to distinguish between changes for different categories of the WORK at the same location or for clarity. (All marks shall be photo reproducible.)
 - 3. Mark the record documents completely and accurately.
 - 4. Indicate any additional important information that was either shown schematically or omitted from the CONTRACT Documents.
 - 5. Mark the Record Documents to indicate actual WORK done that deviates from the CONTRACT Documents.
- B. Maintain the Record Documents in good order and in a clean, dry, legible condition.
- C. Make all Record Documents and samples available at all times for the OWNER, ENGINEERs and / or Building Inspectors as needed.
- D. After completing the preparation of the Record Documents, prepare the drawings and specifications for distribution.

- E. Submit the Record Documents, whether or not any changes and / or additional information was recorded.

END OF DOCUMENT 01750 – RECORD DOCUMENTS



Okaloosa County

Old Bethel Road Sidewalk

100% Design Construction Cost Estimate

DATE: 6/9/2022

ITEM NO.	DESCRIPTION	EST. QTY.	UNIT	UNIT PRICE	CONTRACT PRICE
101-1	MOBILIZATION (15%)	1	LS		
102-1	MAINTENANCE OF TRAFFIC (2.5%)	1	LS		
104-10-3	SEDIMENT BARRIER	285	LF		
110-1-1	CLEARING AND GRUBBING (includes tree removals and concrete/asphalt removal)	1.60	AC		
120-1	REGULAR EXCAVATION (CAD QUANTITY)	116	CY		
120-6	EMBANKMENT (CAD QUANTITY)	935	CY		
400-1-11	CONCRETE CLASS NS, GRAVITY WALL INDEX 400-011	135	CY		
515-2311	PEDESTRIAN/ BICYCLE RAILING, ALUMINUM ONLY, 42" TYPE 1	816	LF		
425-1541	INLETS, DT BOT, TYPE D, <10'	4	EA		
430-174-118	PIPE CULVERT, OPT MATL, 18" S/CD	38	LF		
430175224	PIPE CULVERT, OPTIONAL MATERIAL, OTHER SHAPE-ELIP/ARCH, 24"S/CD	304	LF		
425-2-41	MANHOLES, P-7, <10'	2	EA		
430-982-125	MITERED END SECT, OPTIONAL, RD, 18" SD	4	EA		
430-984-629	MITERED END SECT, OPTIONAL - ELLIPTICAL / ARCH, 24" SD	1	EA		
522-1	CONCRETE SIDEWALKS AND DRIVEWAYS, 4" THICK	3,419	SY		
522-2	CONCRETE SIDEWALKS AND DRIVEWAYS, 6" THICK	101	SY		
520-1-10	CONC. CURB AND GUTTER TYPE F MOD. (18")	115	LF		
334-1-12	SUPERPAVE ASPHALTIC CONCRETE, TRAFFIC B (TYPE SP-9.5 and SP-12.5)	41	TN		
527-2	DETECTABLE WARNINGS	325	SF		
570-1-2	PERFORMANCE TURF (SODDING) (CENTIPEDE)	3,810	SY		
630-2-11	CONDUIT, FURNISH & INSTALL, OPEN TRENCH	117	LF		
635-2-11	PULL & SPLICE BOX, F&I, 13" x 24" COVER SIZE	4	EA		
700-1-11	SINGLE POST SIGN, F&I GROUND MOUNT, UP TO 12 SF	8	EA		
700-1-12	SINGLE POST SIGN, F&I GROUND MOUNT, 12-20 SF	2	EA		
700-1-60	SINGLE POST SIGN, REMOVE	8	EA		
711-11-123	THERMO, STAND, WHITE, 12" SOLID	920	LF		
711-11-125	THERMO, STAND, WHITE, 24" SOLID	145	LF		
700-12-12	SIGN BEACON, F&I GROUND MOUNT- AC POWERED, TWO BEACONS	2	EA		
711-14125	THERMOPLASTIC, PREFORMED, WHITE, SOLID, 24" FOR CROSSWALK	140	LF		
711-17-11	THERMOPLASTIC, REMOVE EXISTING THERMOPLASTIC PAVEMENT MARKINGS- SURFACE TO R	167	SF		
550 10440	FENCING, WOOD FENCE, 7.1-8.0'	163	LF		
0550 10222	FENCING, TYPE B, 5.1-6.0, W/ VINYL COATING	214	LF		
0110 7 1	MAILBOX, F & I	10	EA		
				TOTAL	

OLD BETHEL ROAD SIDEWALK DESIGN

OKALOOSA COUNTY, FLORIDA



COMMISSIONERS

PAUL MIXON
CAROLYN KETCHEL
NATHAN BOYLES
TREY GOODWIN
MELPONDER

COUNTY ADMINISTRATOR

JOHN HOFSTAD


PUBLIC WORKS DIRECTOR

JASON AUTREY

PROJECT SHEET INDEX

C1	COVER
C2 - C3	GENERAL NOTES & LEGEND
C4 - C5	TYPICAL SECTIONS
C6 - C28	PLAN AND PROFILE
C29 - C49	CROSS SECTIONS
C50	SCHOOL SIGNING AND STRIPING PLAN
C51	SIGNALIZATION PLAN
C52	FROSION CONTROL DETAILS


NOTE: ATTENTION IS DIRECTED TO THE FACT THAT THESE PLANS MAY HAVE BEEN ALTERED IN SIZE BY REPRODUCTION. THIS MUST BE CONSIDERED WHEN OBTAINING SCALED DATA.



1625 Summit Lake Drive Tallahassee FL 32317

JUNE 2022

DRMP PROJECT NO.* 18-0297.008

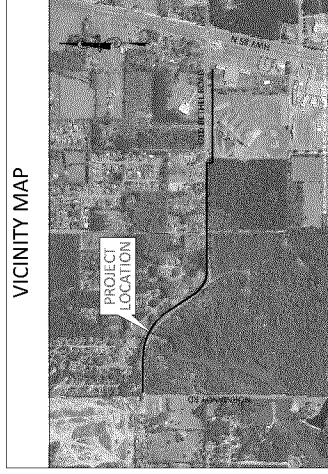

VICINITY MAP

SITE ADDRESS: OLD BETHEL ROAD CRESTVIEW FLORIDA 32536

GOVERNING STANDARDS AND SPECIFICATIONS:
FLORIDA DEPARTMENT OF TRANSPORTATION, 2022-2023 STANDARD PLANS FOR ROAD AND
BRIDGE CONSTRUCTION AS APPENDED HEREIN, AND JANUARY 2021 STANDARD SPECIFICATIONS
FOR ROAD AND BRIDGE CONSTRUCTION, AS AMENDED BY CONTRACT DOCUMENTS

FOR DESIGN STANDARDS GO TO THE FOLLOWING WEB SITE:

FOR THE STANDARD SPECIFICATIONS FOR ROAD AND BRIDGE CONSTRUCTION VIEW THE "JULY 2022 STANDARD SPECIFICATION EBOOK" PDF AT THE FOLLOWING WEBSITE:

CONSULTANT CONTACTS:

SURVEY
GUSTIN, COTHER & TUOKER, INC.
121 HART STREET
NICEVILLE, FL 32578
ALLEN E. TUOKER 850-678-5141

CIVIL ENGINEERING
DRMP, INC.
1625 SUMMIT LAKE DRIVE
TALLAHASSEE, FL 32317
BEN LENNON, P.E. 850-692-5659

CALL 48 HOURS
BEFORE YOU DIG


IT'S THE LAW!
DIAL 811

Know what's below
Call before you dig.




SUNSHINE STATE ONE CALL OF FLORIDA, INC.



 <p>DRMP 1821 SOUTHWEST LAKE DRIVE TALLAHASSEE, FL 32317 Phone 904.502.8500 FAX 904.502.8501 WWW.DRMP.COM</p>	Certificate of Authorization No. 2048 FIDELITY & SURETY COMPANY OF FLORIDA 18-0297 008		SHEET NO. 1 PROJECT NO. 18-0297 008	SCALE: AS SHOWN DATE: 06/03/2022	DRAWING: C1
	OLD BETHEL ROAD SIDEWALK DESIGN COVER		DESIGNED BY: SBL DRAWN BY: RAJ CHECKED BY: DSP APPROVED BY: GRL	REVISIONS NO. DATE DESCRIPTION BY	

THE DESIGN SHOWN HEREIN IS BASED ON A LIMITED TOPOGRAPHIC SURVEY PERFORMED BY GUSTIN, COTHRN & TUCKER, INC. ON 3/4/22. BOTH HORIZONTAL AND VERTICAL DATUM ARE ASSUMED. BASELINE AND CONTROL MONUMENTATION FOR THE PROJECT AREA ARE PROVIDED IN THE PLANS. RIGHT OF WAY LOCATION SHOWN IS APPROXIMATE AND IS BASED ON FOUND PROPERTY CORNERS.

CONTRACTOR SHALL CHECK PLANS FOR CONFLICTS AND DISCREPANCIES PRIOR TO CONSTRUCTION. THE CONTRACTOR SHALL NOTIFY THE AGENT OF ANY CONFLICTS BEFORE PERFORMING WORK IN THE AFFECTED AREA. IN THE EVENT THE CONTRACTOR DISCOVERS ANY ERRORS OR OMISSIONS IN THE PLANS OR SPECIFICATIONS, HE SHALL IMMEDIATELY NOTIFY THE OWNER AND ENGINEER.

CONTRACTOR SHALL BE RESPONSIBLE TO PROVIDE ALL REASONABLE AND PRUDENT PRECAUTIONS FOR THE SAFE AND SECURE PROTECTION OF ALL INCOMPLETE WORK, MATERIALS AND EQUIPMENT STORED ONSITE AND OFFSITE, AND ANY UNAUTHORIZED ACCESS TO SUCH. CONTRACTOR SHALL ERECT AND MAINTAIN, AS REQUIRED BY EXISTING CONDITIONS AND PROGRESS OF THE WORK, ALL REASONABLE AND REQUIRED SAFEGUARDS FOR THE SAFETY AND PROTECTION OF ALL PERSONNEL, EQUIPMENT OR MATERIALS, INCLUDING BUT NOT LIMITED TO, POSTING OF DANGER SIGNS AND OTHER WARNING AGAINST HAZARDS, PROMULGATING SAFETY REGULATIONS AND NOTIFYING OWNERS AND USERS OF ADJACENT UTILITIES OF THE EXISTENCE OF HAZARDS AND SAFETY REGULATIONS. CONTRACTOR SHALL, AT ALL TIMES, UTILIZE ALL NORMALLY ACCEPTED AND REASONABLY EXPECTED SAFETY PRACTICES AND COMPLY WITH ALL APPLICABLE FEDERAL, STATE, AND LOCAL LAWS, ORDINANCES, RULES, STATUTES, REGULATIONS OR PERMIT CONDITIONS, AND GUIDELINES AND RECOMMENDATIONS PERTAINING TO THE SAFE UTILIZATION OF ALL EQUIPMENT AND MATERIALS, AS PUBLISHED BY MANUFACTURER OR SUPPLIER.

4. ANY EXISTING SIGN THAT CONFLICTS WITH THE PROPOSED IMPROVEMENTS SHALL BE RE-LOCATED AT THE DIRECTION OF THE ENGINEER.

5. TRAFFIC CONTROL DURING THE PROJECT SHALL BE IN ACCORDANCE WITH FDOT INDICES IN THE 600 SERIES.

6. PRIOR TO INITIATING ANY EXCAVATION (INCLUDING, BUT NOT LIMITED TO, TUNNELS, DITCHES, SWALES, CONTRACTOR SHALL REVIEW AND MAKE ARRANGEMENTS TO COMPLY IN EVERY RESPECT WITH THE PROVISIONS OF ALL APPLICABLE FEDERAL, STATE AND LOCAL LAWS, ORDINANCES, RULES, STATUTES, REGULATIONS OR OTHER CONDITIONS, INCLUDING BUT NOT LIMITED TO CFA 102A SUBPART 17, AND CSH&T 102A SUBPART 17.01, AND TO THE REQUIREMENTS OF THE STATE OF FLORIDA, INCLUDING THE REQUIREMENTS OF THE FLORIDA DEPARTMENT OF TRANSPORTATION, AND TO TAKE ALL OTHER REASONABLE AND PRUDENT STEPS TO ENSURE THAT ACCESS TO EXCAVATIONS BY UNAUTHORIZED INDIVIDUALS IS PREVENTED.

- CONTRACTOR FURTHER AGREES THAT CONTRACTOR AND ITS SUBCONTRACTORS SHALL NOT CAUSE THE IMPROPER DISCHARGE, RELEASE OR DISPOSAL OF ANY HAZARDOUS MATERIALS OR SUBSTANCES CREATED BY ITS WORK ON OR ABOUT THE JOB SITE. IN THE EVENT OF ANY SPILL, RELEASE OR ANY OTHER REPORTABLE OCCURRENCE, CONTRACTOR SHALL TAKE ALL SUCH ACTIONS AS MAY BE NECESSARY TO MINIMIZE THE DELETERIOUS EFFECTS OF SUCH SPILL ON ANY PERSON OR PROPERTY, NOTIFY THE APPROPRIATE GOVERNMENT AGENCY AND NOTIFY OWNER IN WRITING.
- CONTRACTOR AND ITS SUBCONTRACTORS SHALL, UPON COMPLETION OF PERFORMANCE OF ALL DUTIES UNDER THIS CONTRACT, REMOVE ALL SUPPLIES, MATERIALS AND WASTE CONTAINING HAZARDOUS MATERIALS FROM THE JOB SITE. CONTRACTOR SHALL BEAR ALL FINANCIAL RESPONSIBILITY, BETWEEN THE PARTIES OF THE CONTRACT, FOR COMPLIANCE WITH THE PROVISIONS OF THESE GENERAL NOTES, SPECIFICATIONS OR AGREEMENT BETWEEN OWNER AND CONTRACTOR.

WATER DISTRIBUTION ADJUSTMENT NOTES

1. WATER METERS IN CONFLICT WITH CONSTRUCTION WILL BE RELOCATED BY OKALOOSA COUNTY.

- WASTEWATER ADJUSTMENT NOTES

.....

- [illegible]

BRL	NO.	DATE	DESCRIPTION	SIGNED BY	BRL
				NAME BY	RAJ
				CHECKED BY	DSP
				APPROVED BY	BRL
R E V I S I O N					

38

EN
AKE

NAME _____

DATE _____

WISN	
------	--

ON

THE
SAO
ME
SIHU

DE
ON
CR
OT

WERS • 2648 • CC


1


3


PROJECT NO.:


DATE: _____


11

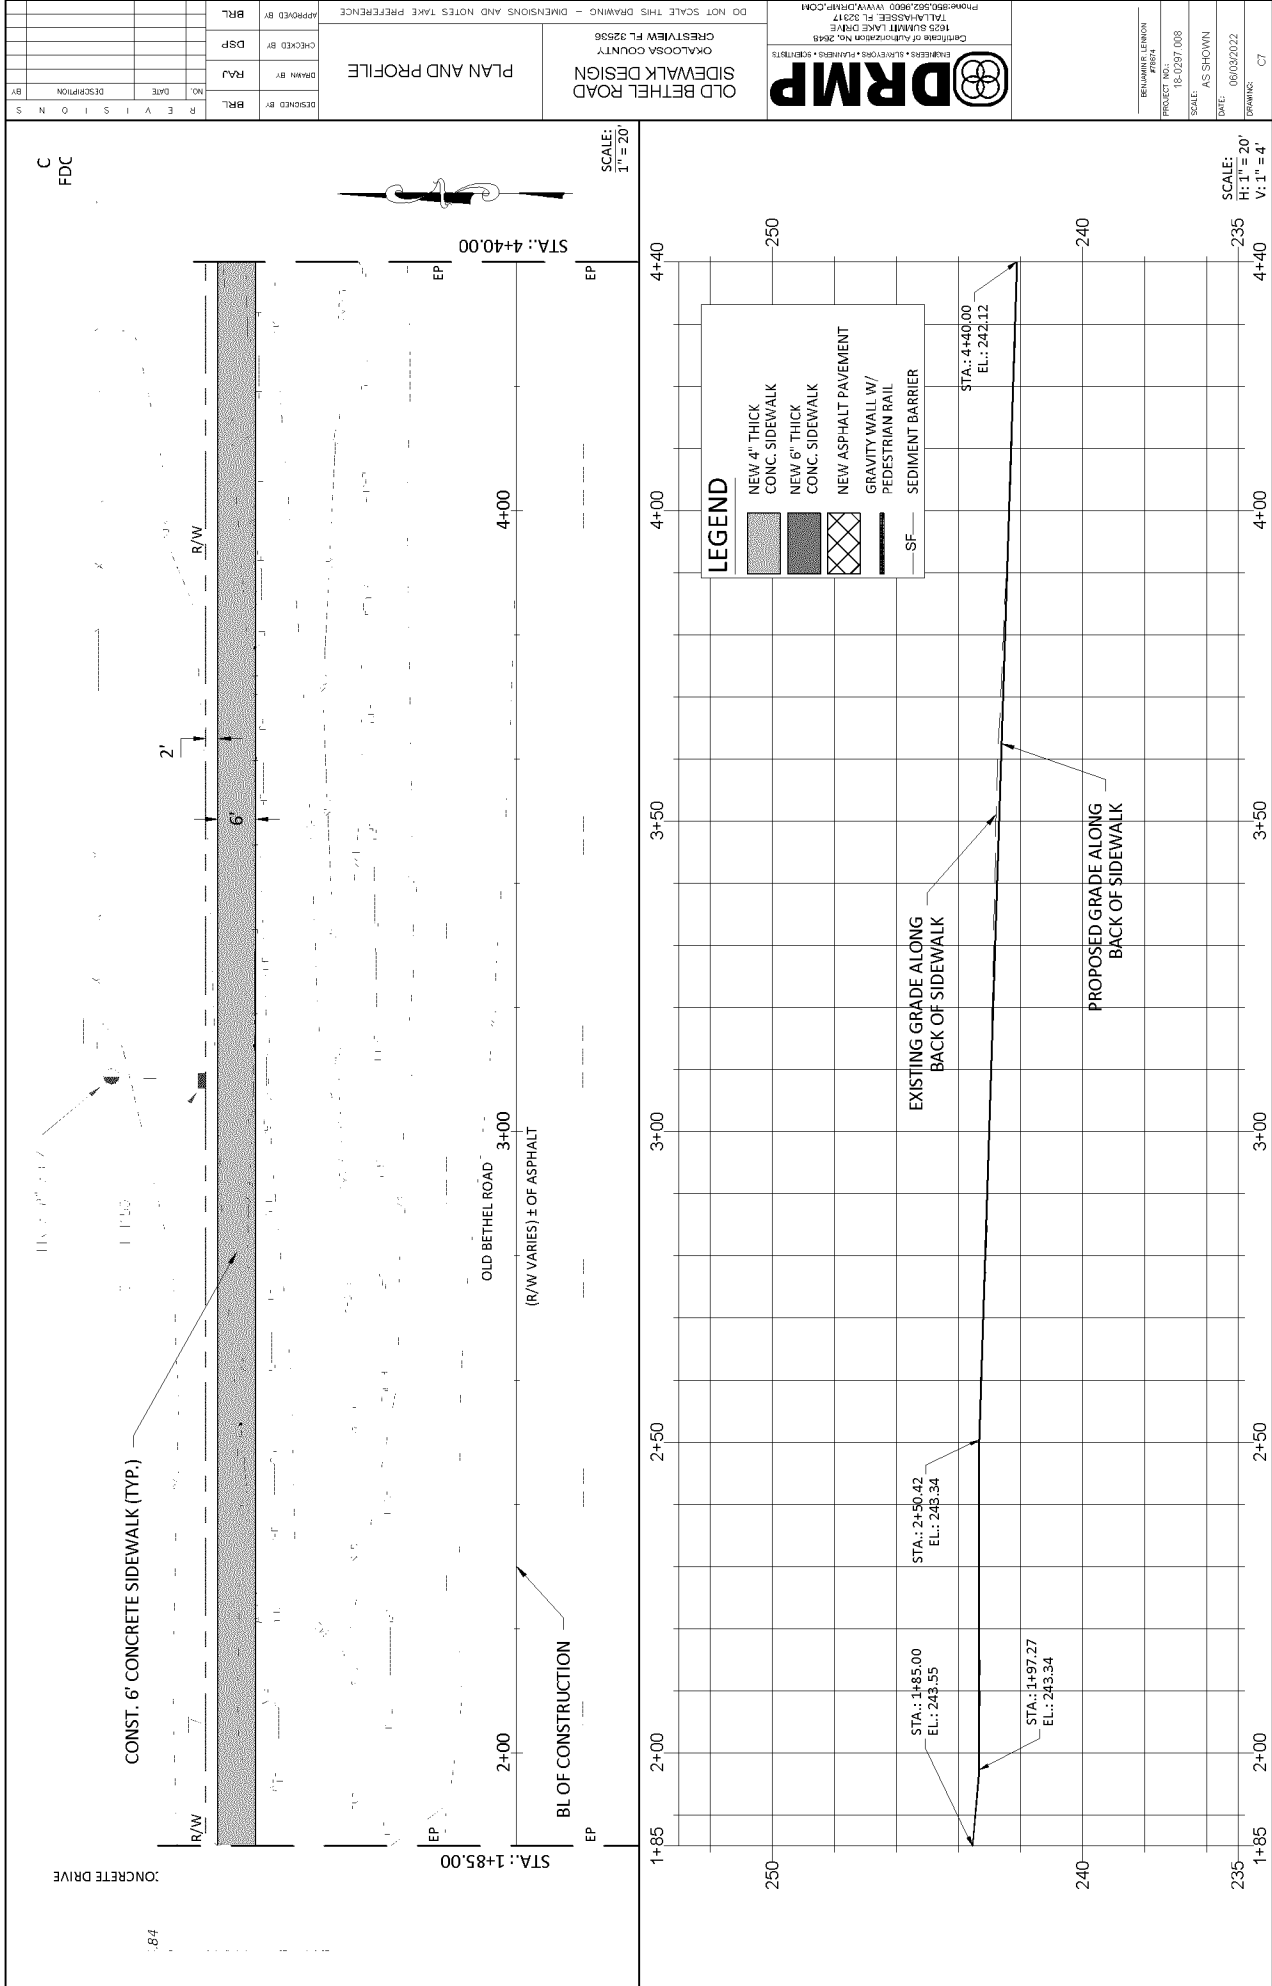


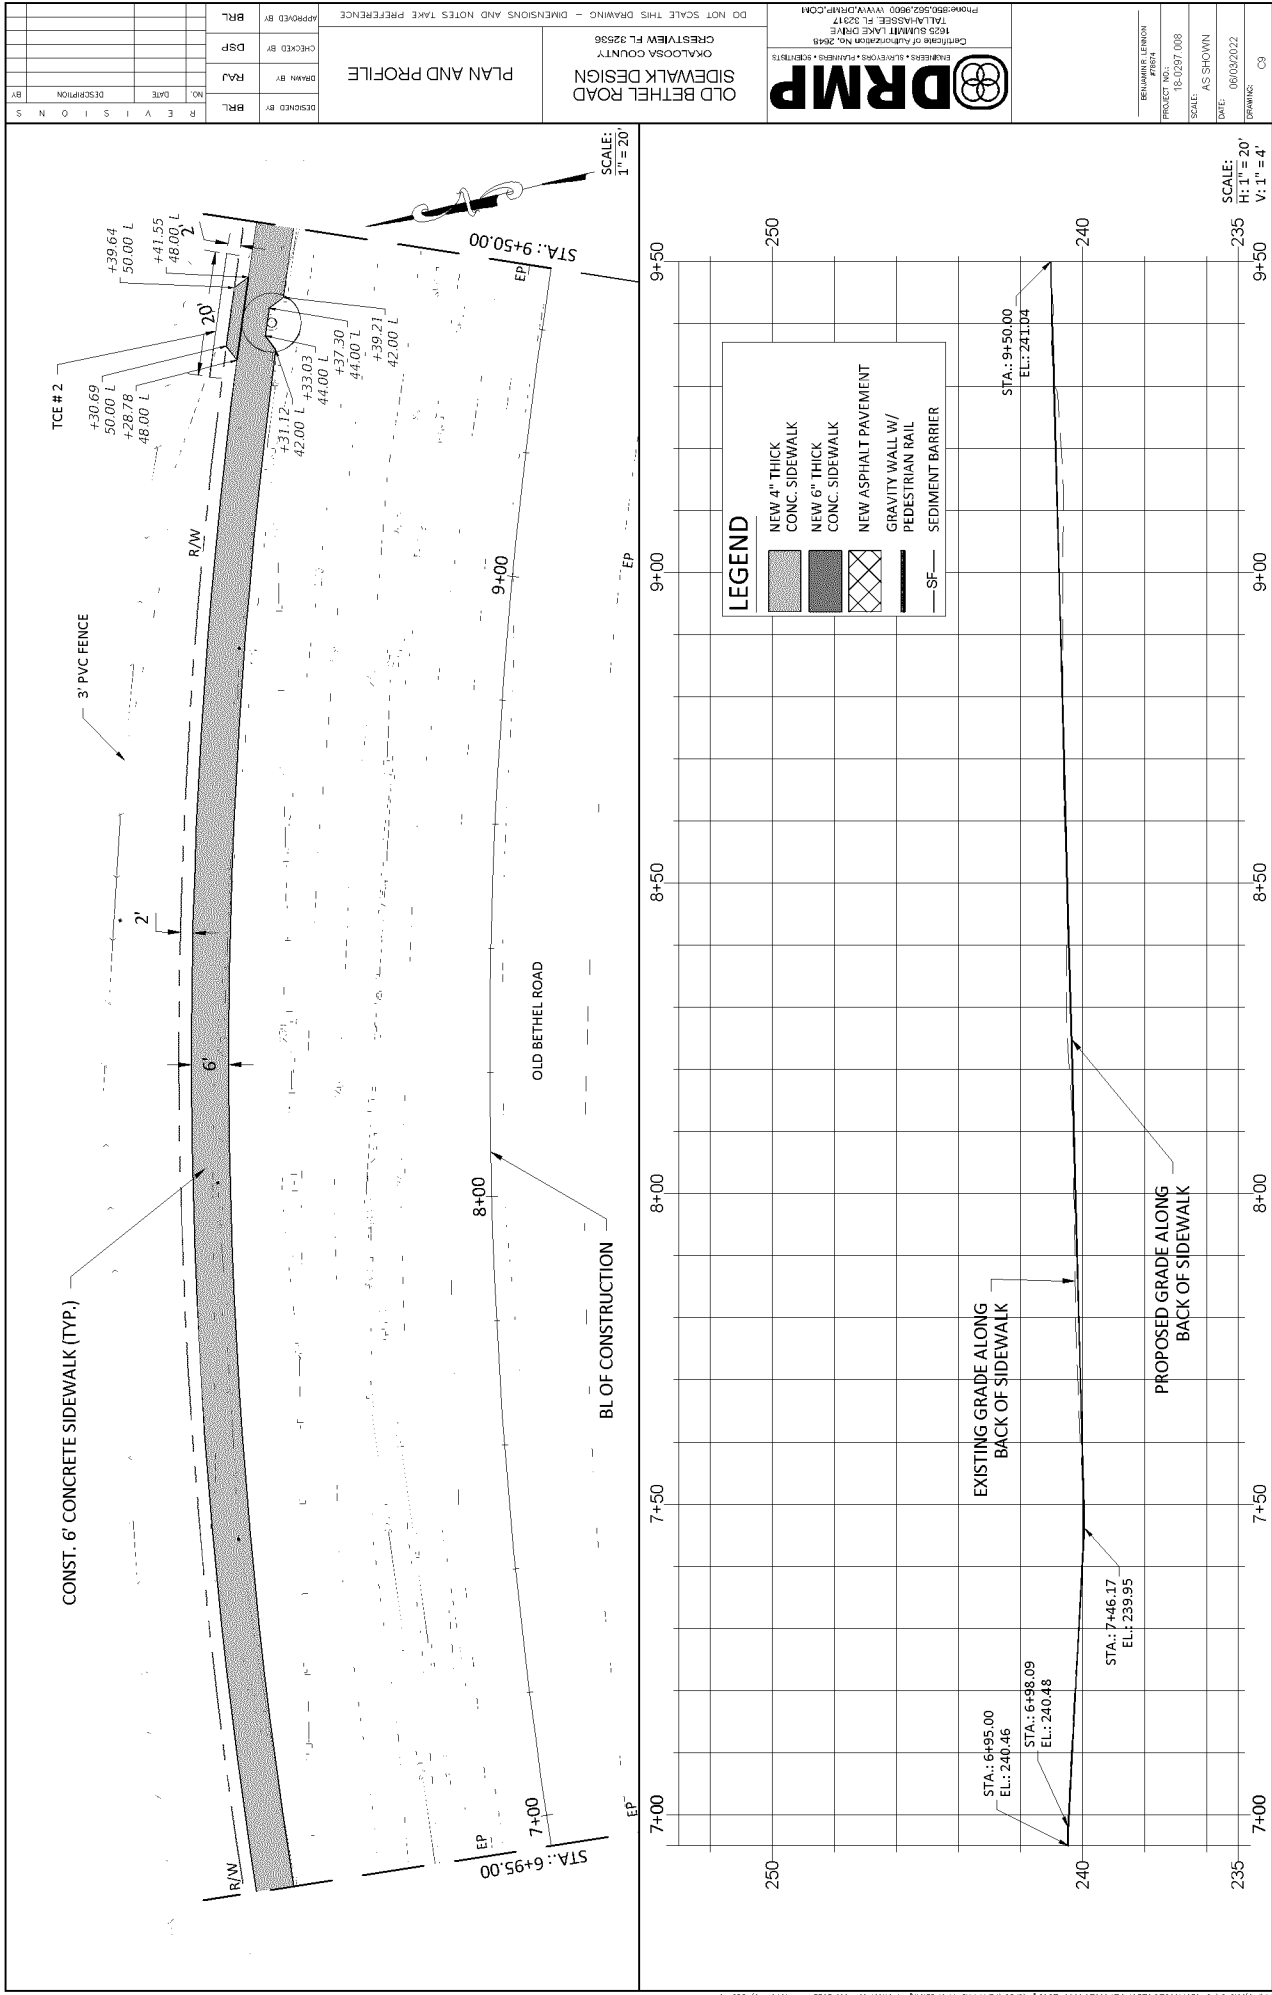


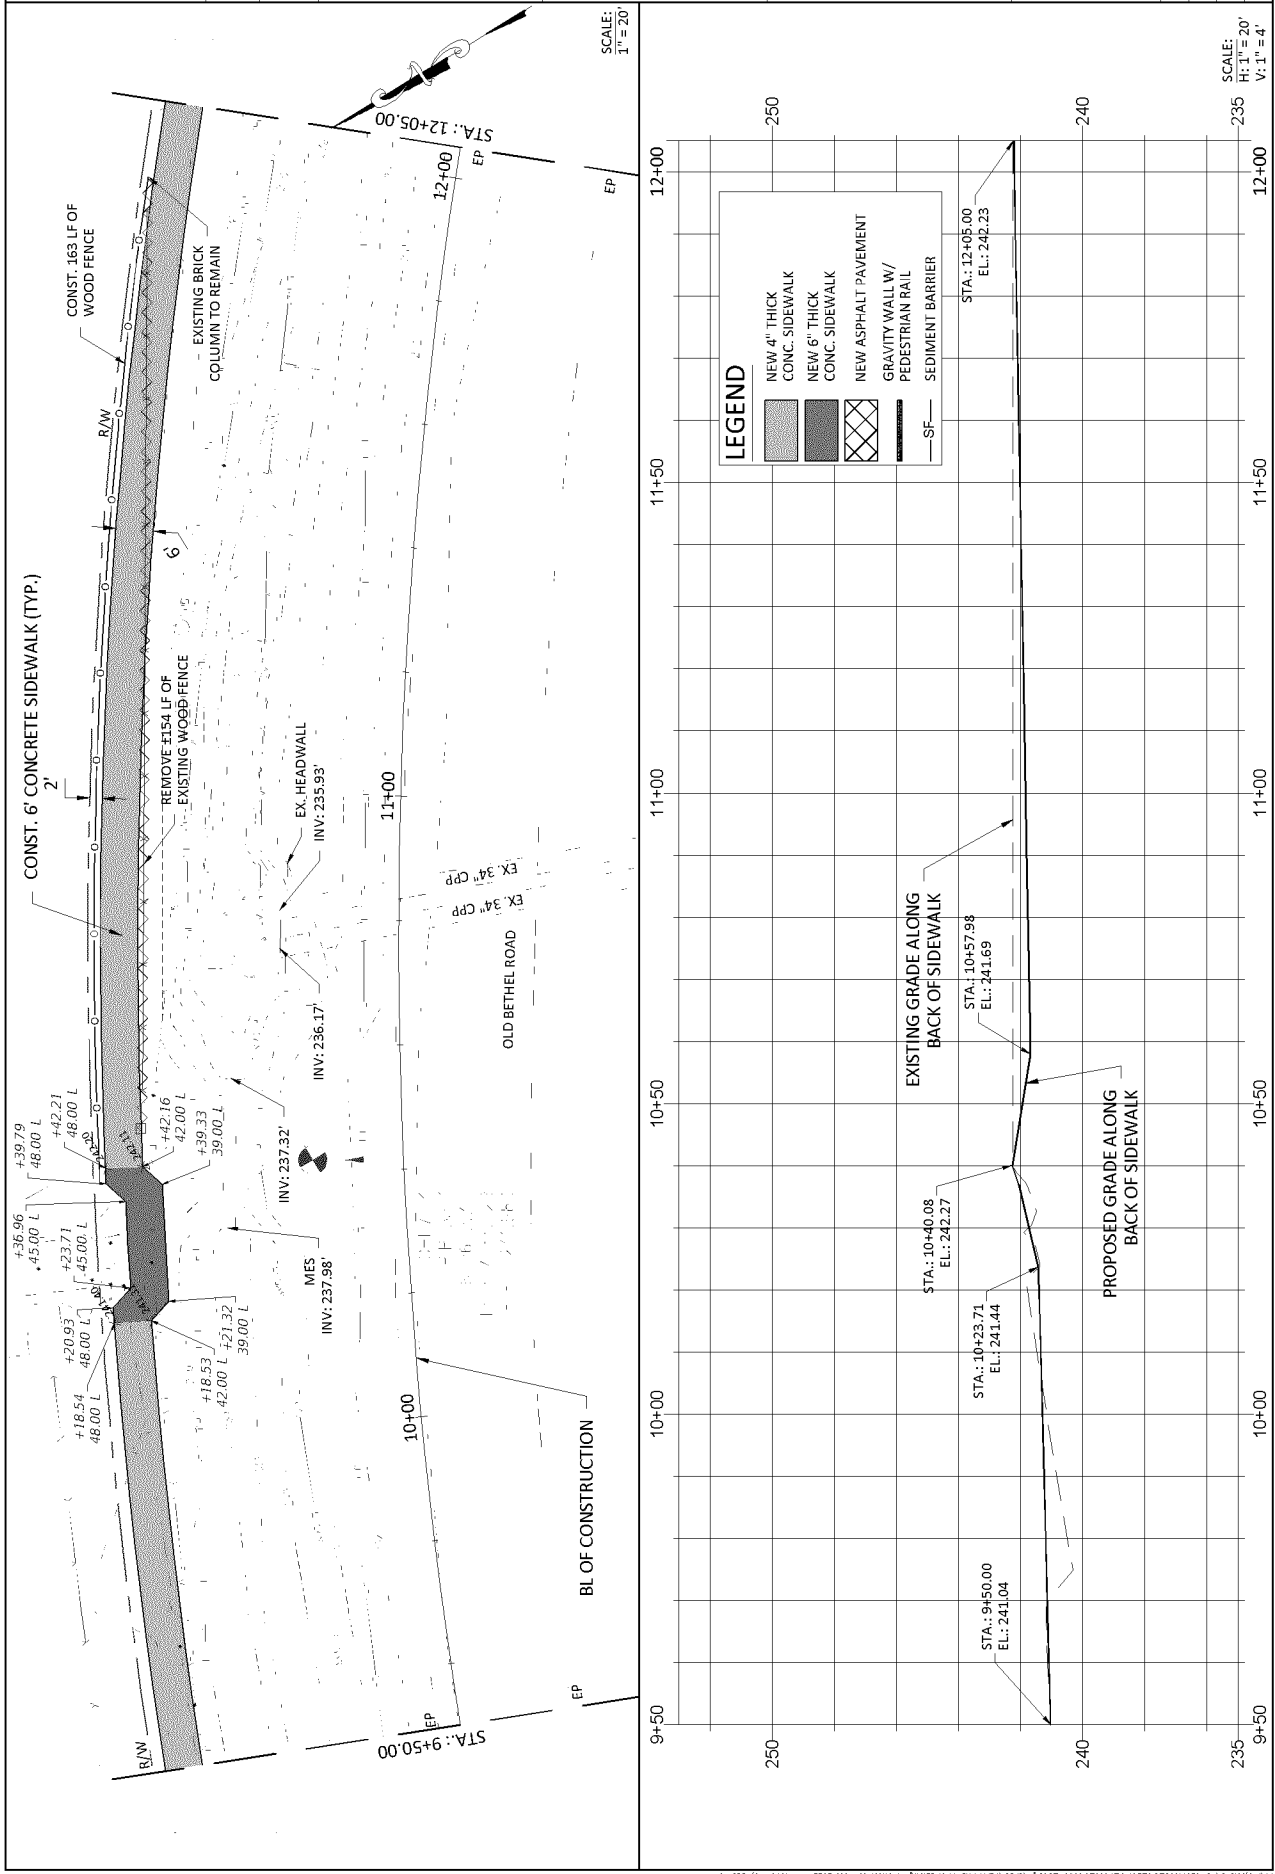

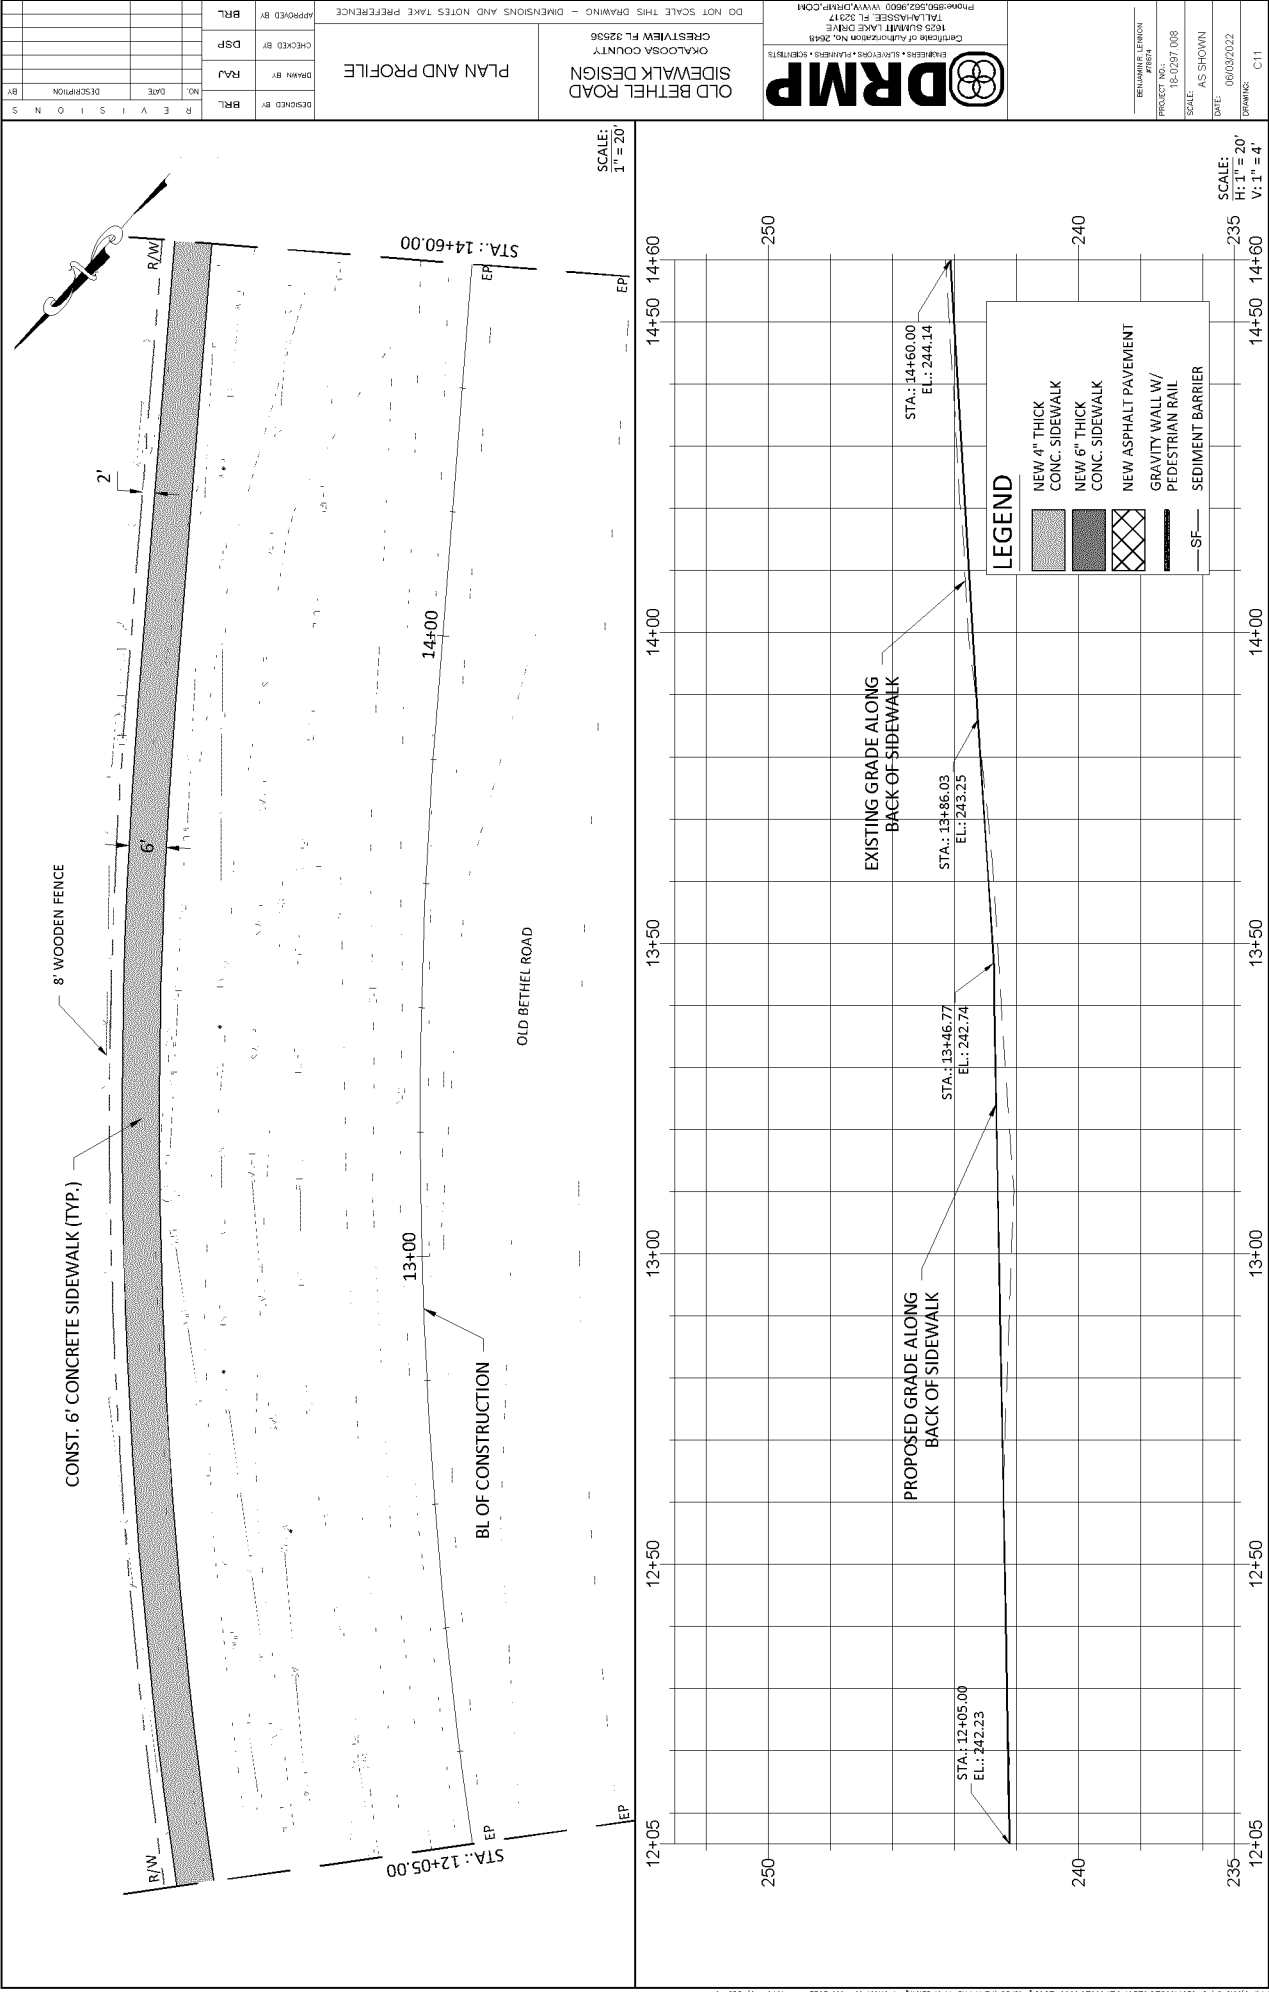

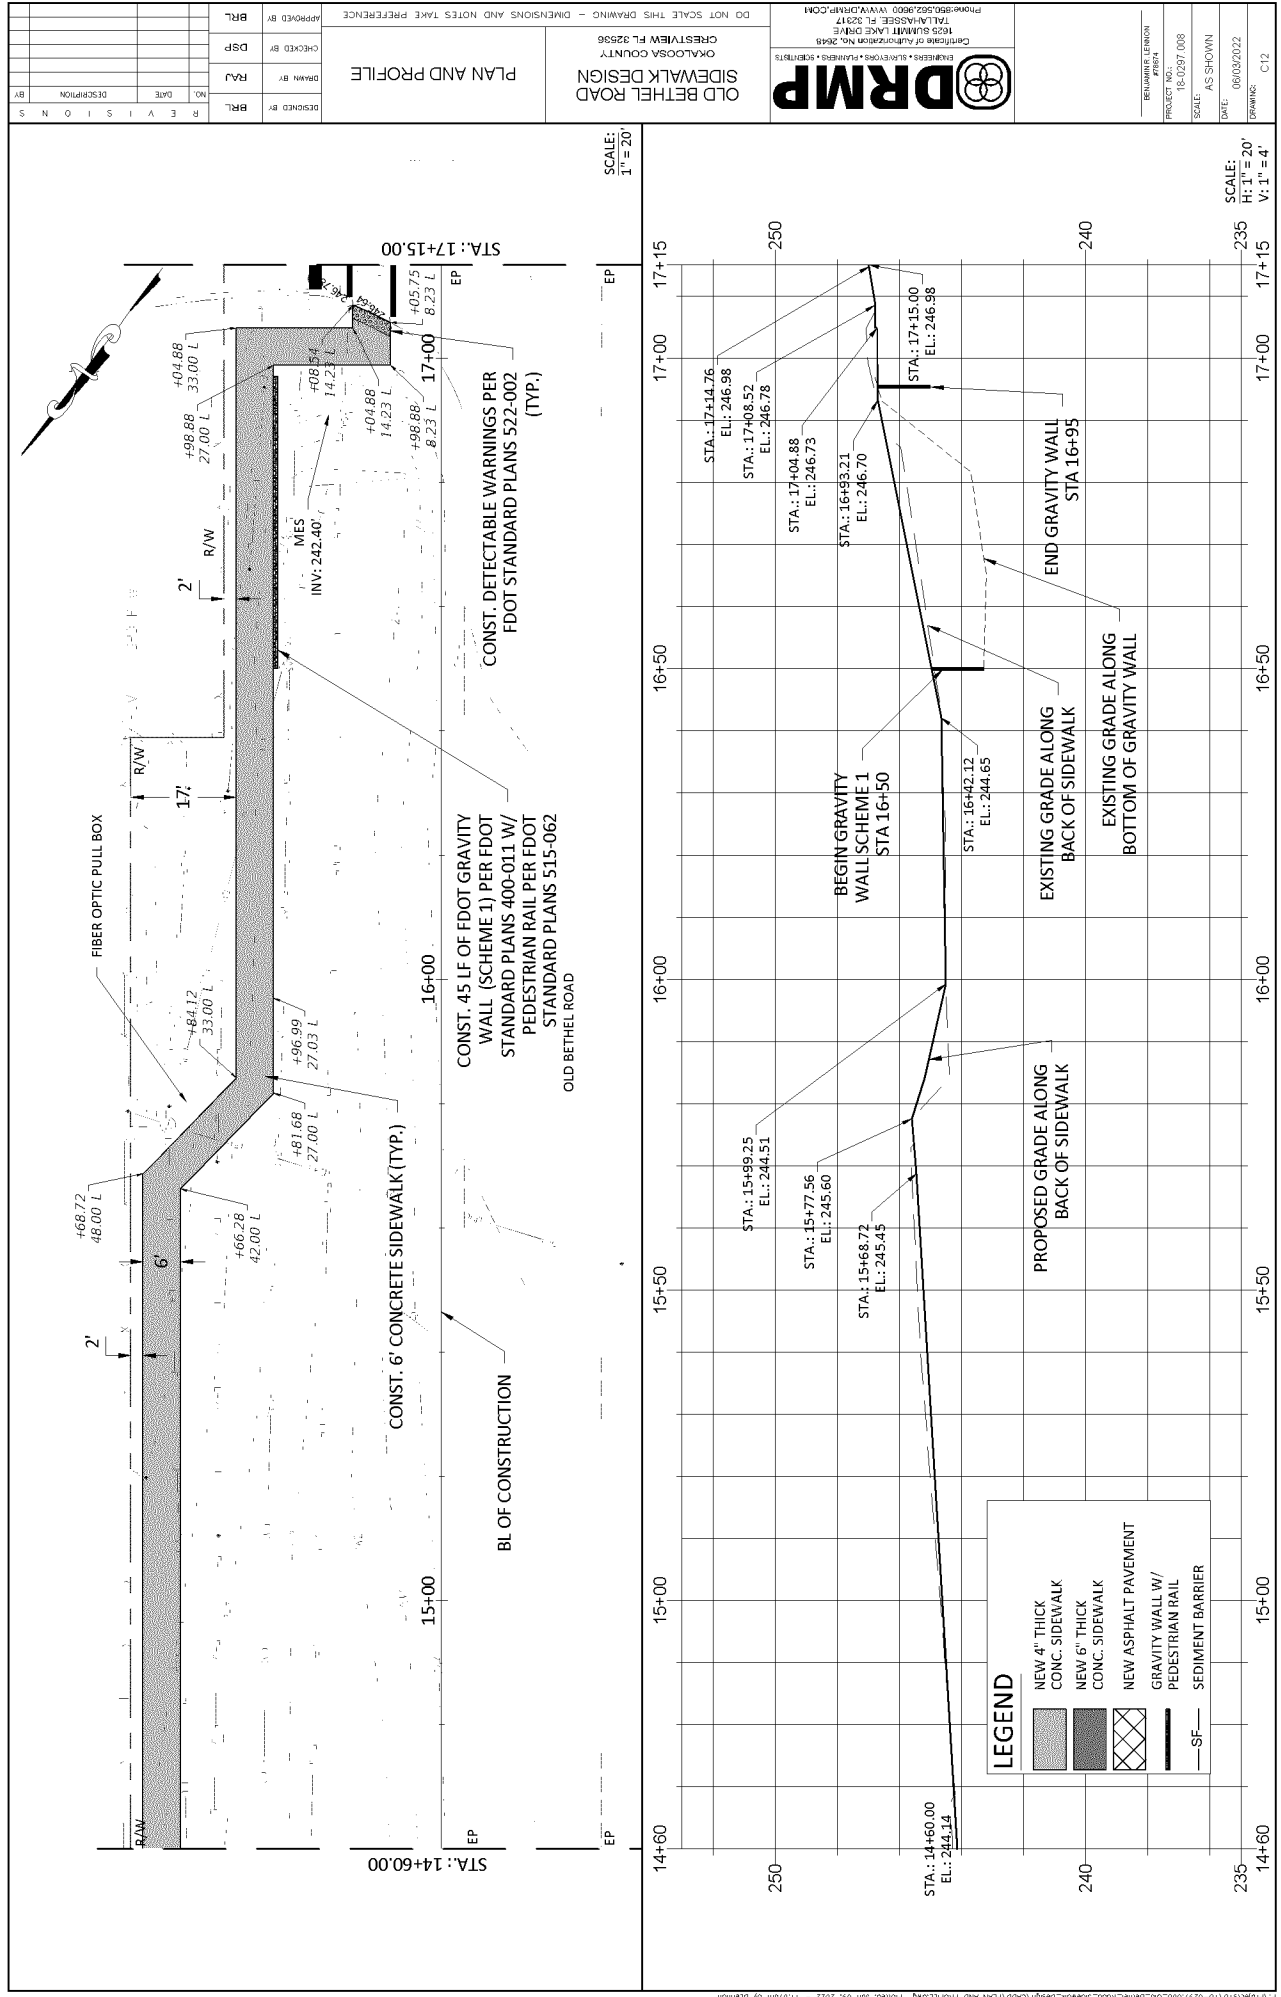

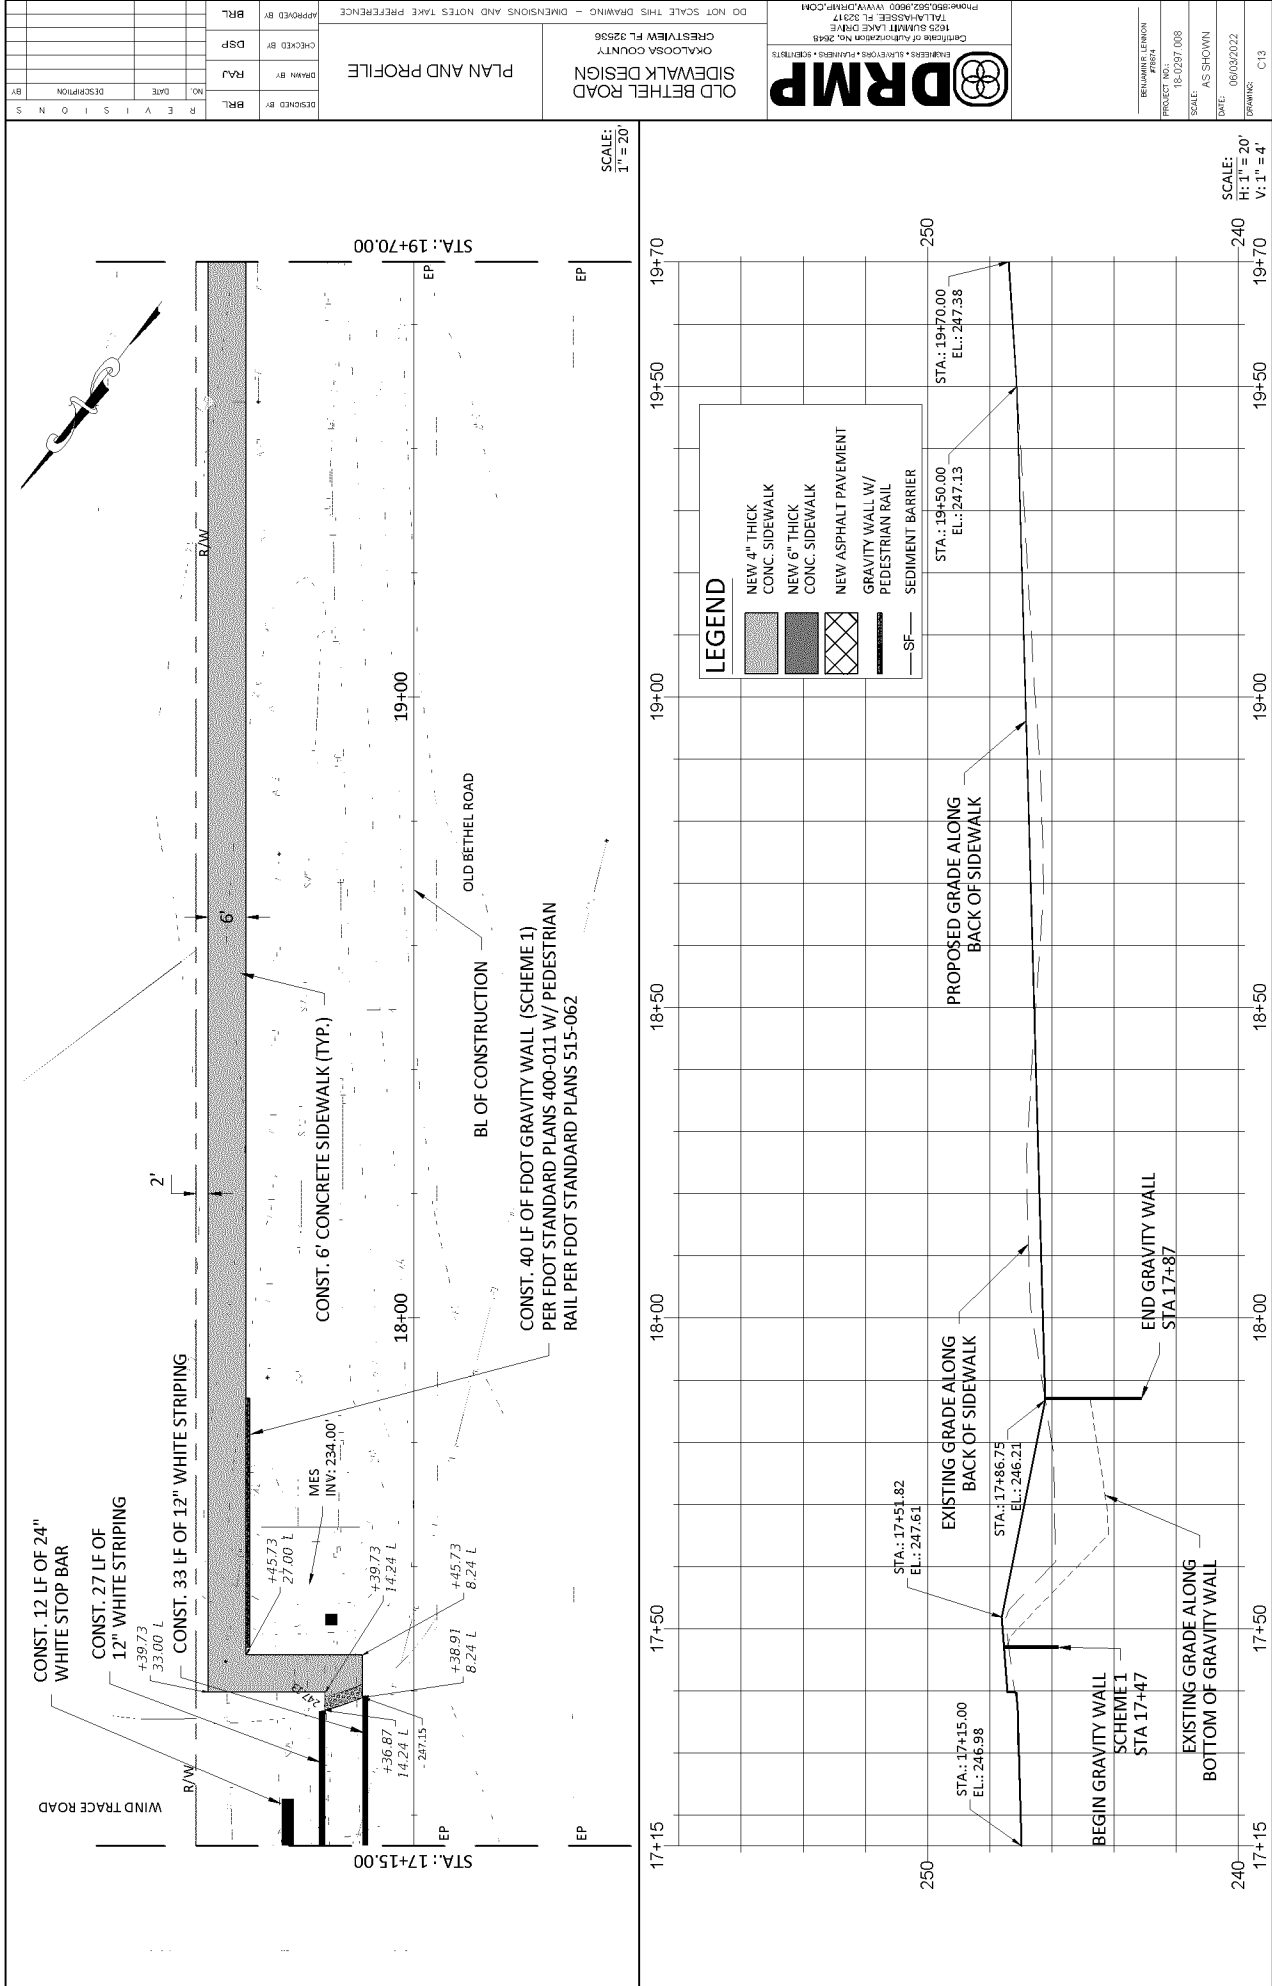

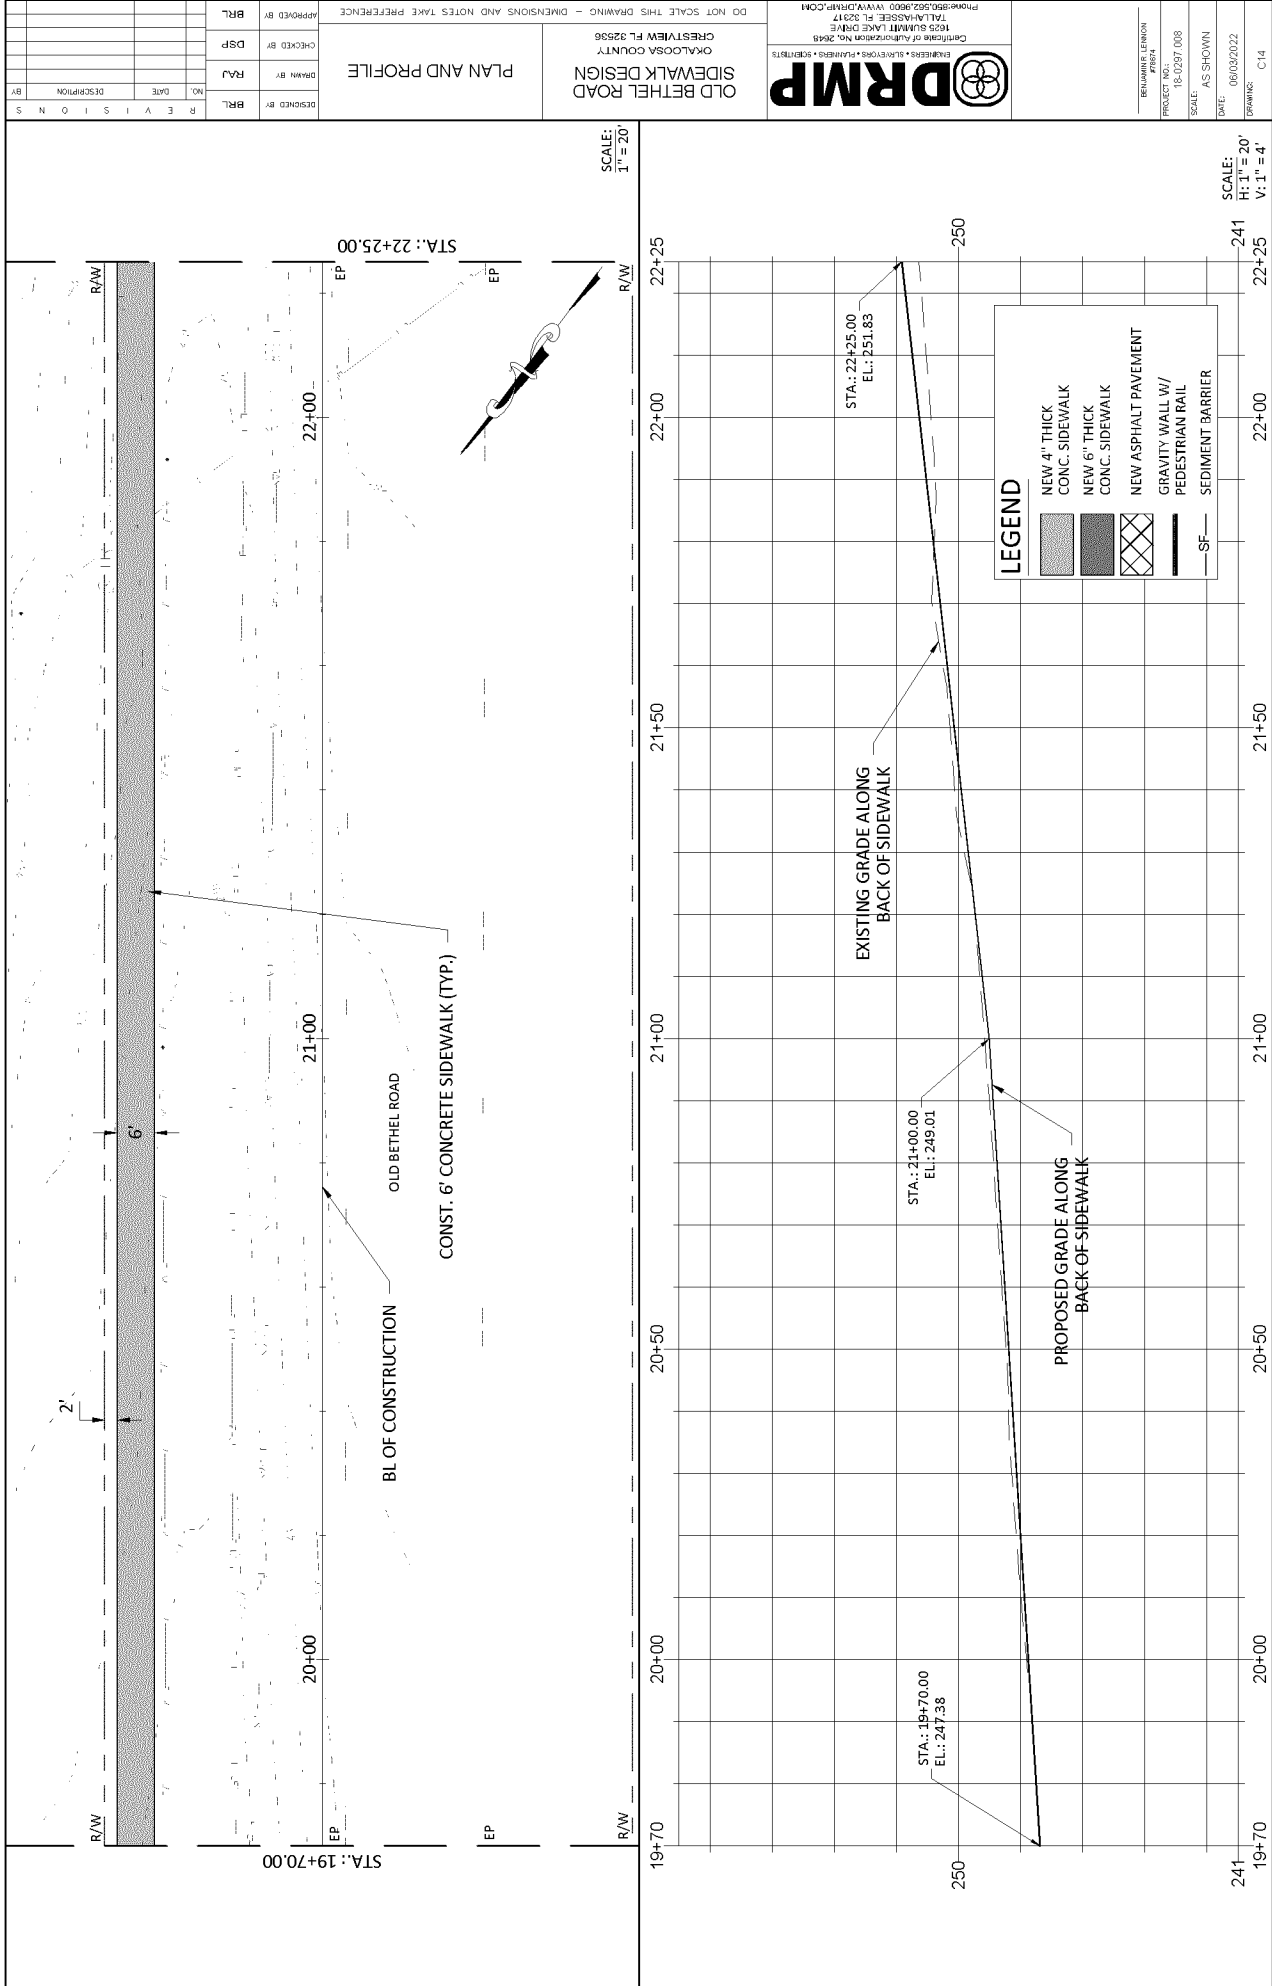




DRMP

DRMP

1625 SUMMIT LAKE DRIVE
TALLAHASSEE, FL 32317
Phone: 850.502.9800 | WWW.DRMP.COM


CRESTVIEW FL 32836
OKALOOSA COUNTY


DO NOT SCALE THIS DRAWING - DIMENSIONS AND NOTES TAKE PRECEDENCE


PLAN AND PROFILE


DESIGNED BY	BRL
DRAWN BY	RAJ
CHECKED BY	DSP
APPROVED BY	BRL
NO.	
DATE	
DESCRIPTION	
BY	


DATE: 08/03/2022
DRAWING: C14
PROJECT NO.: 19-0397-008
SCALE: AS SHOWN
REVISIONS: 1
BY: BRL


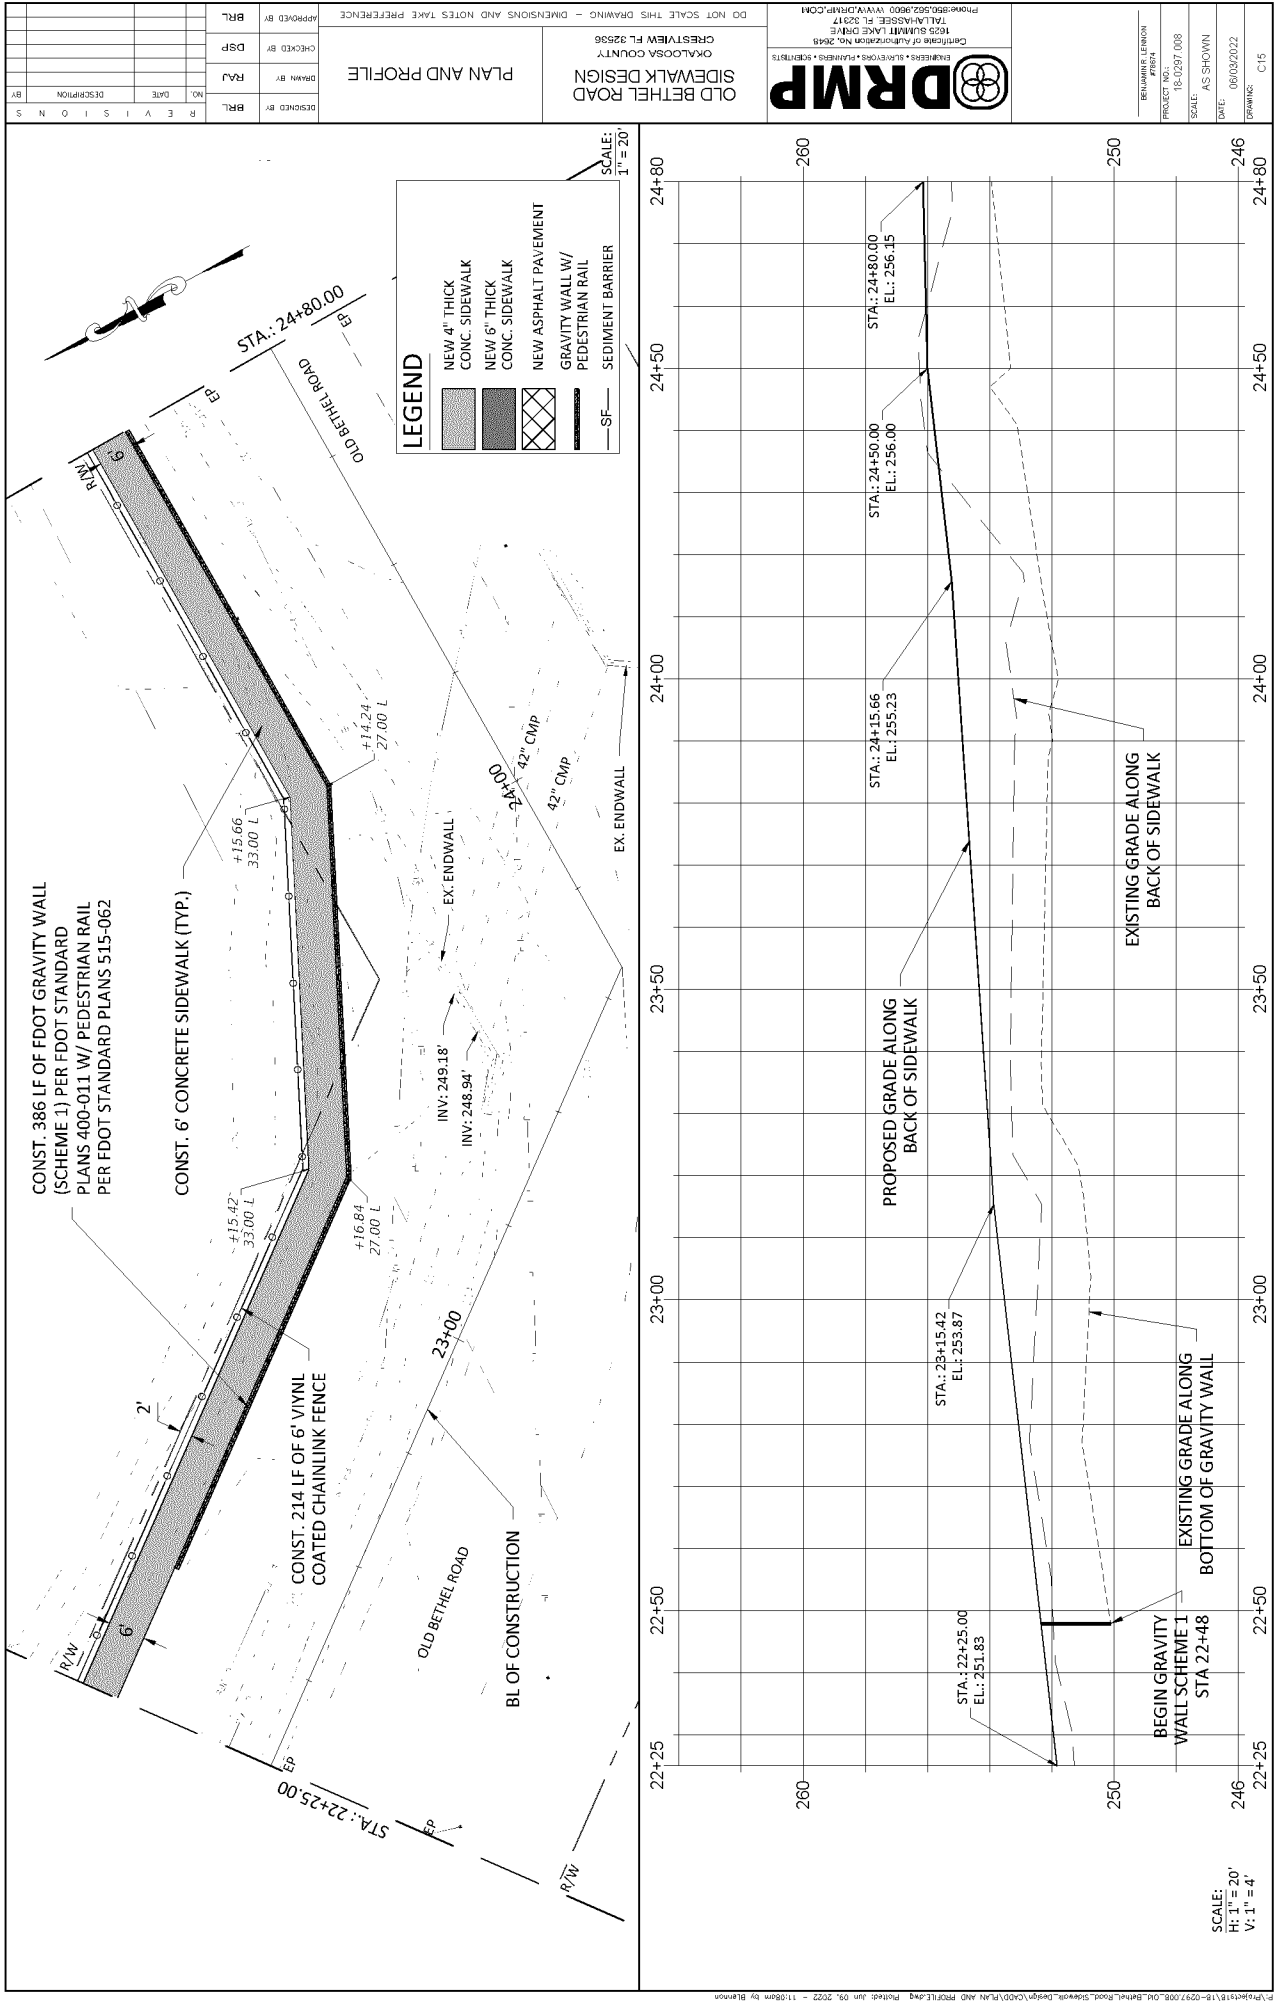


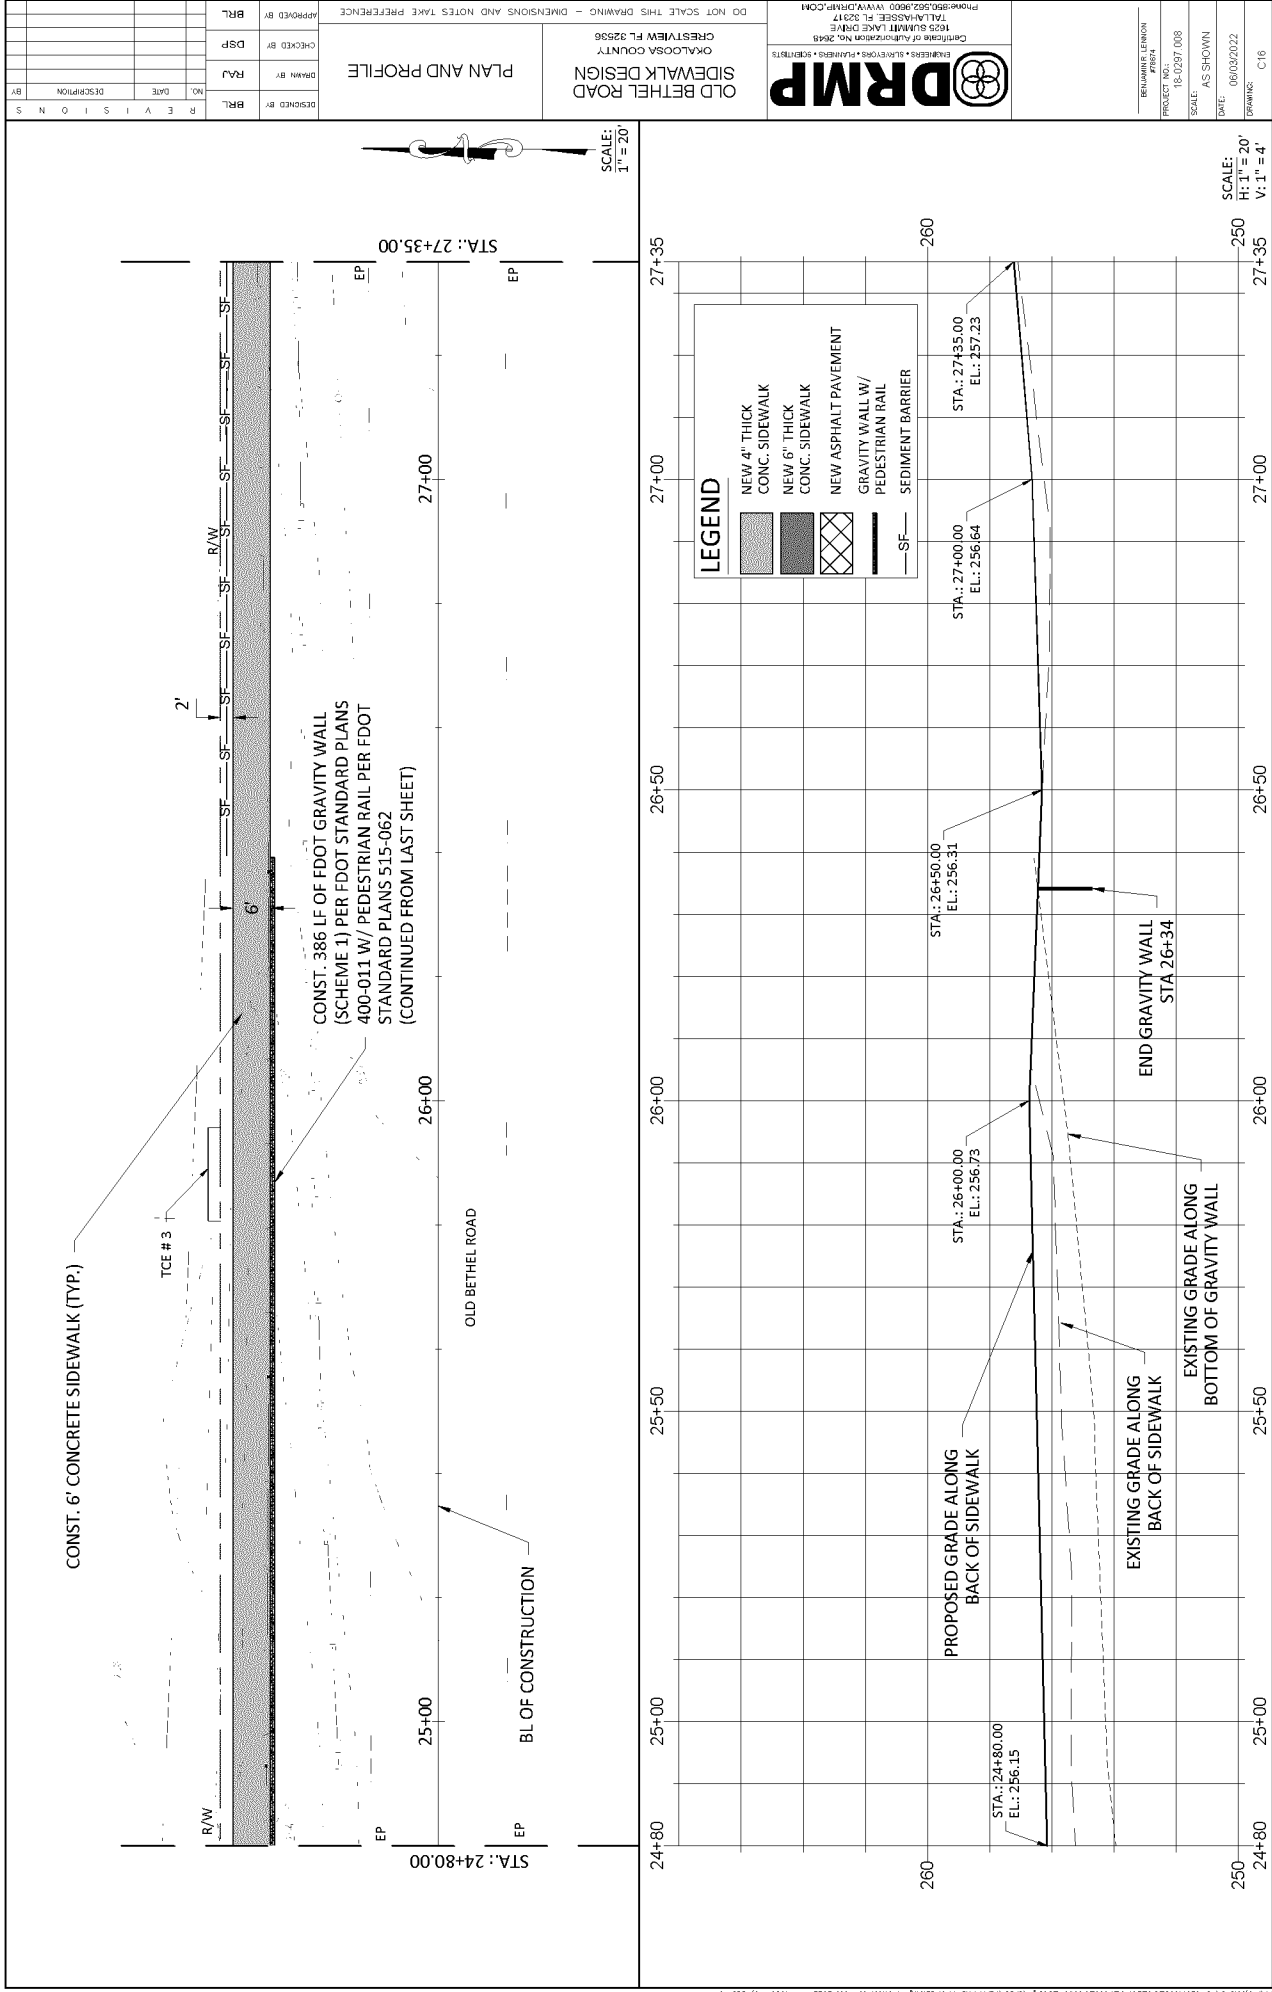

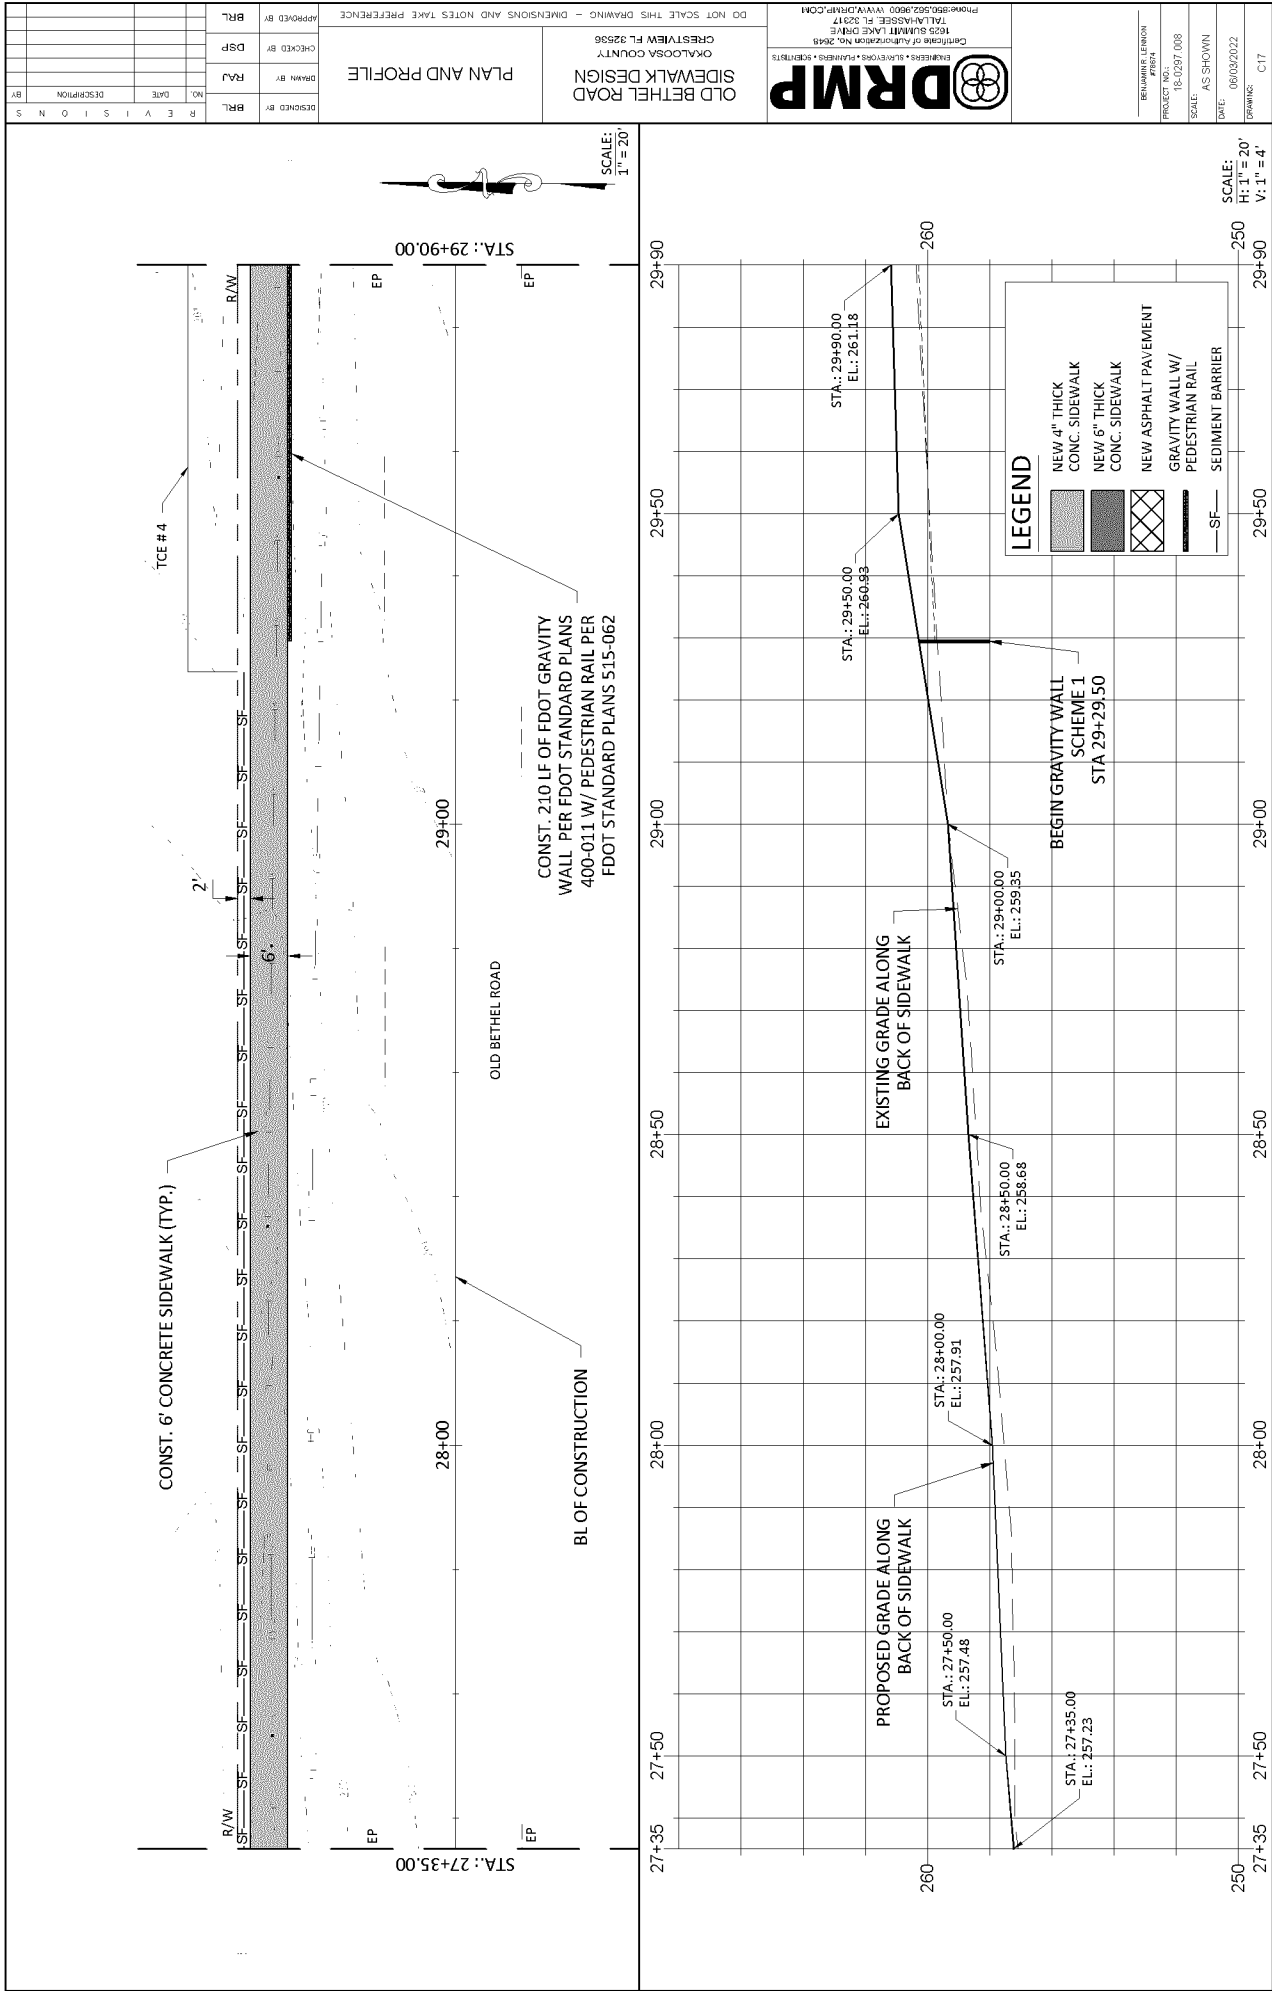

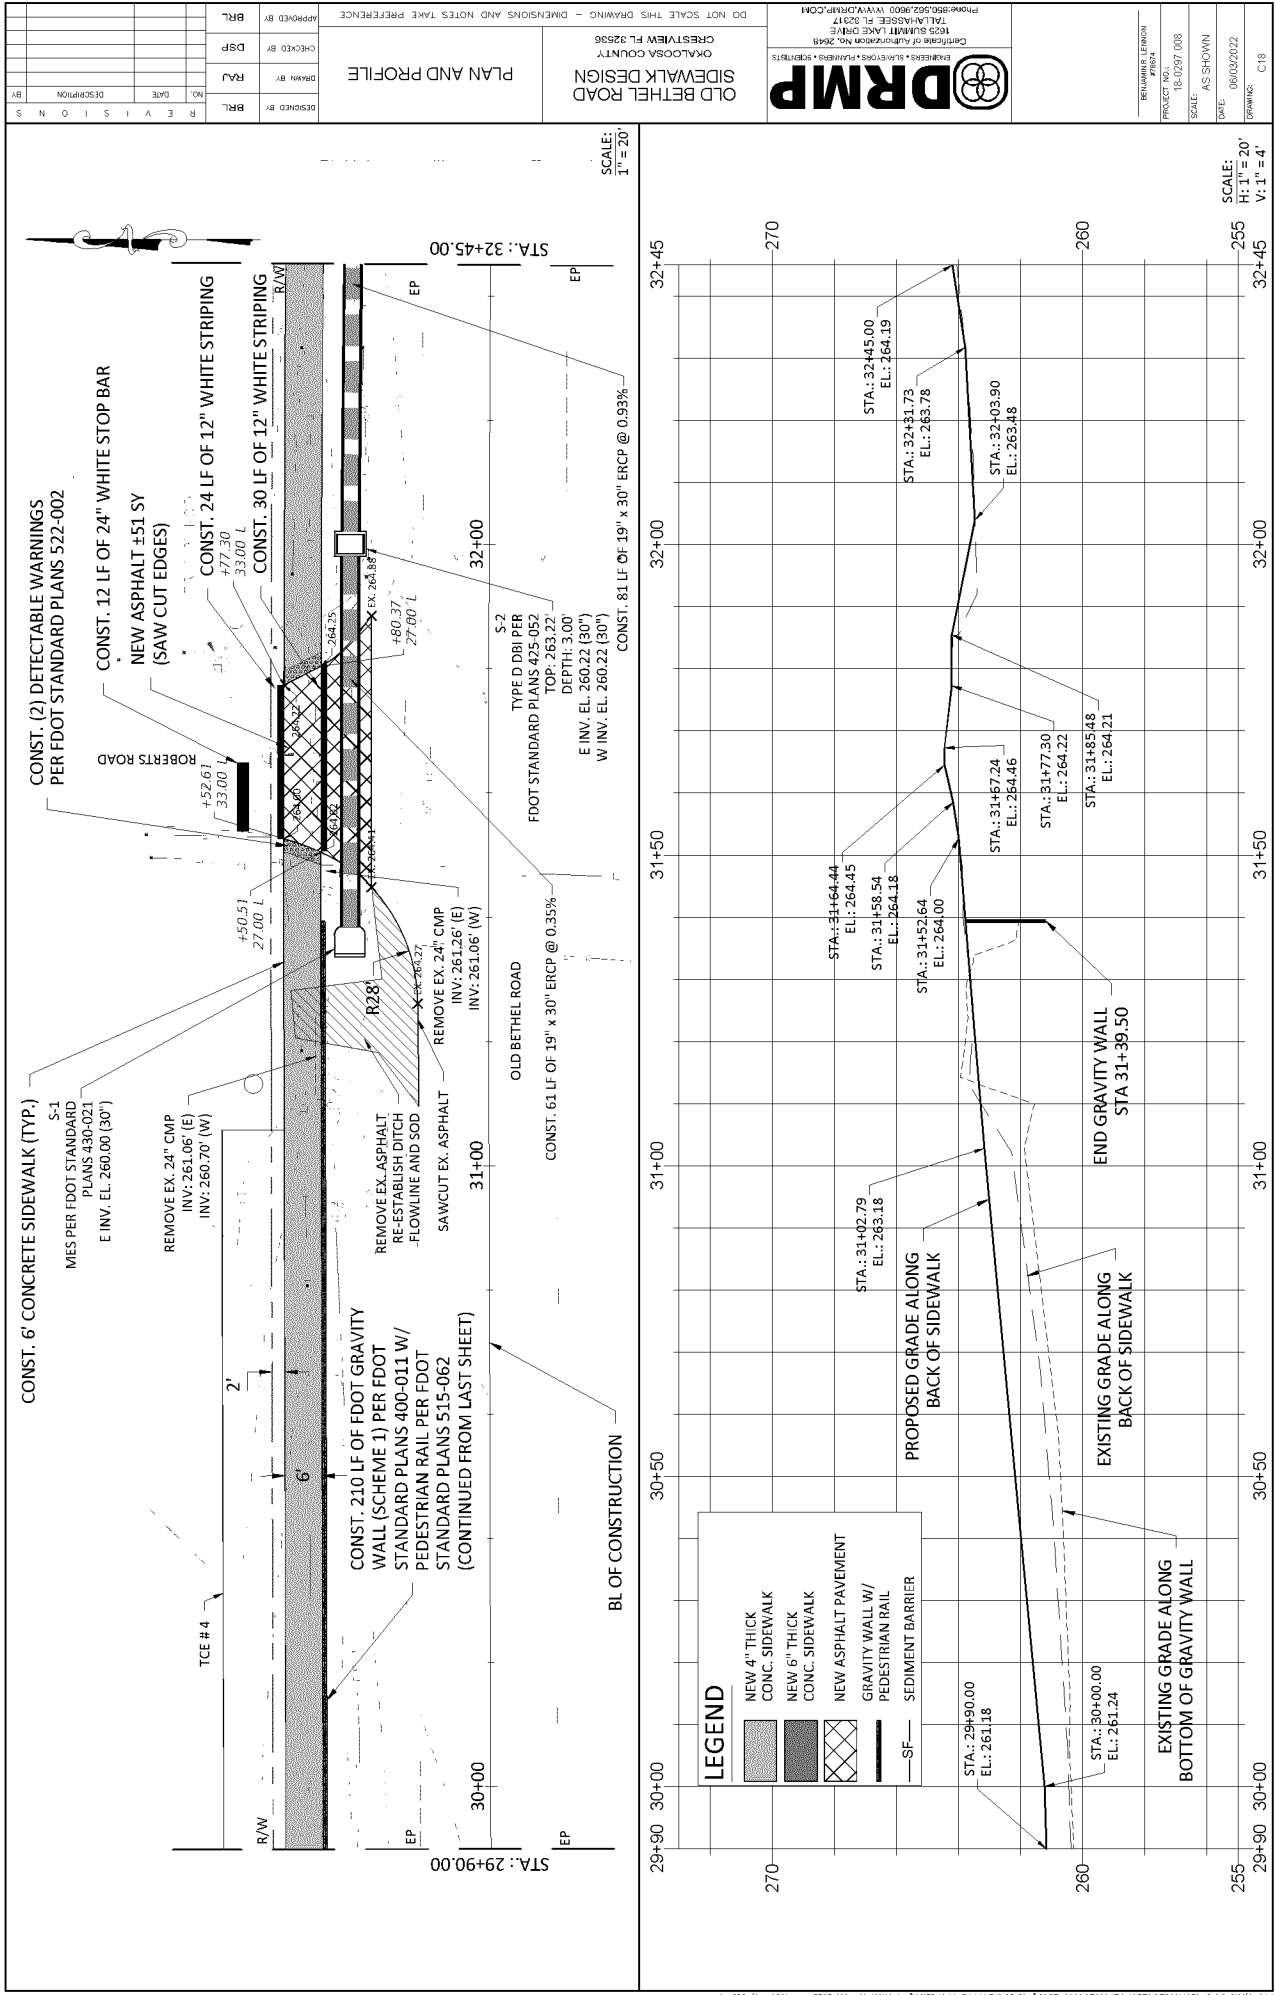

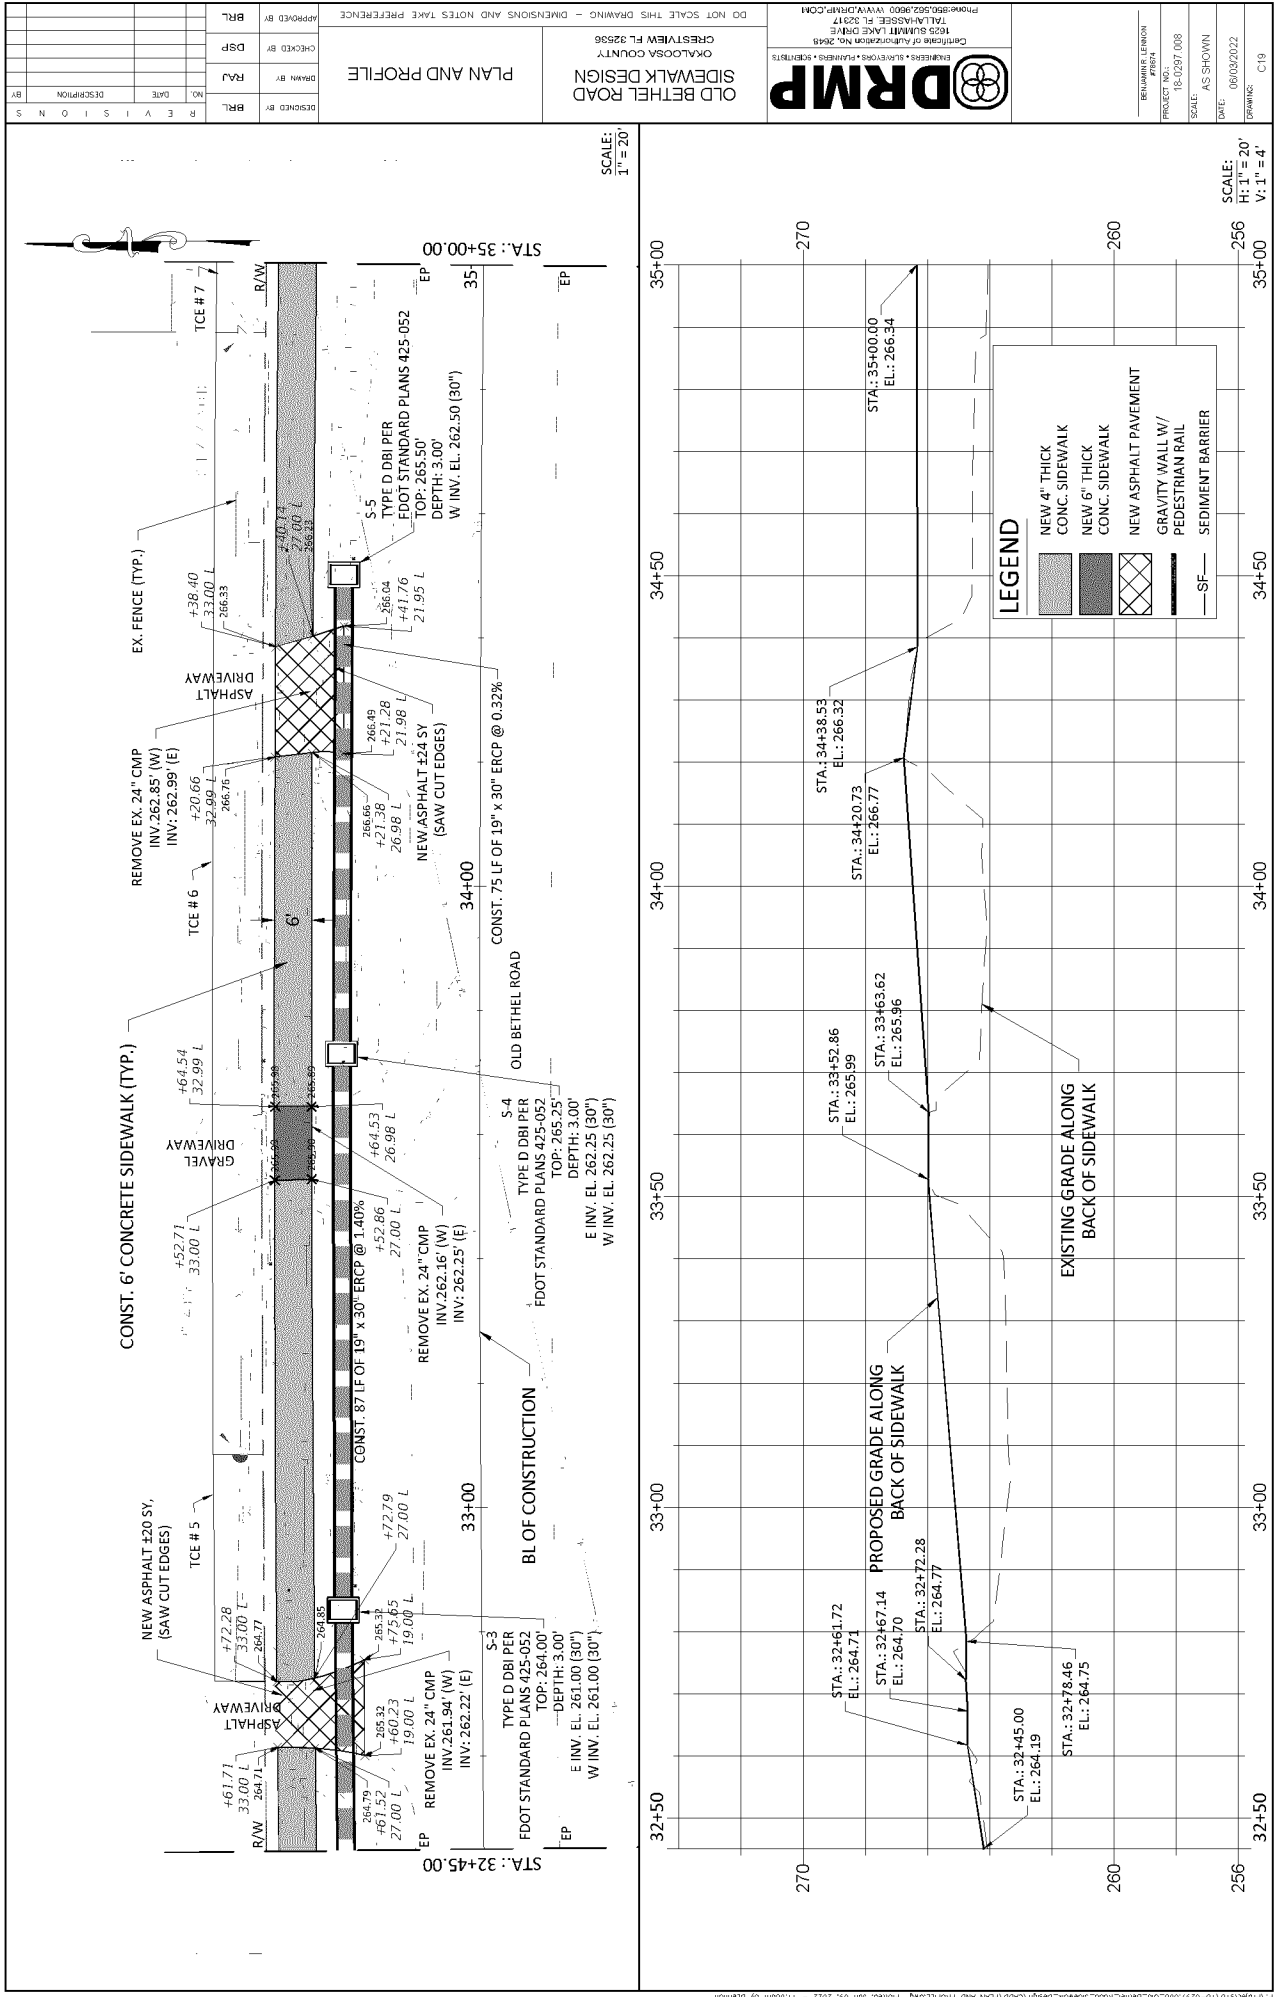

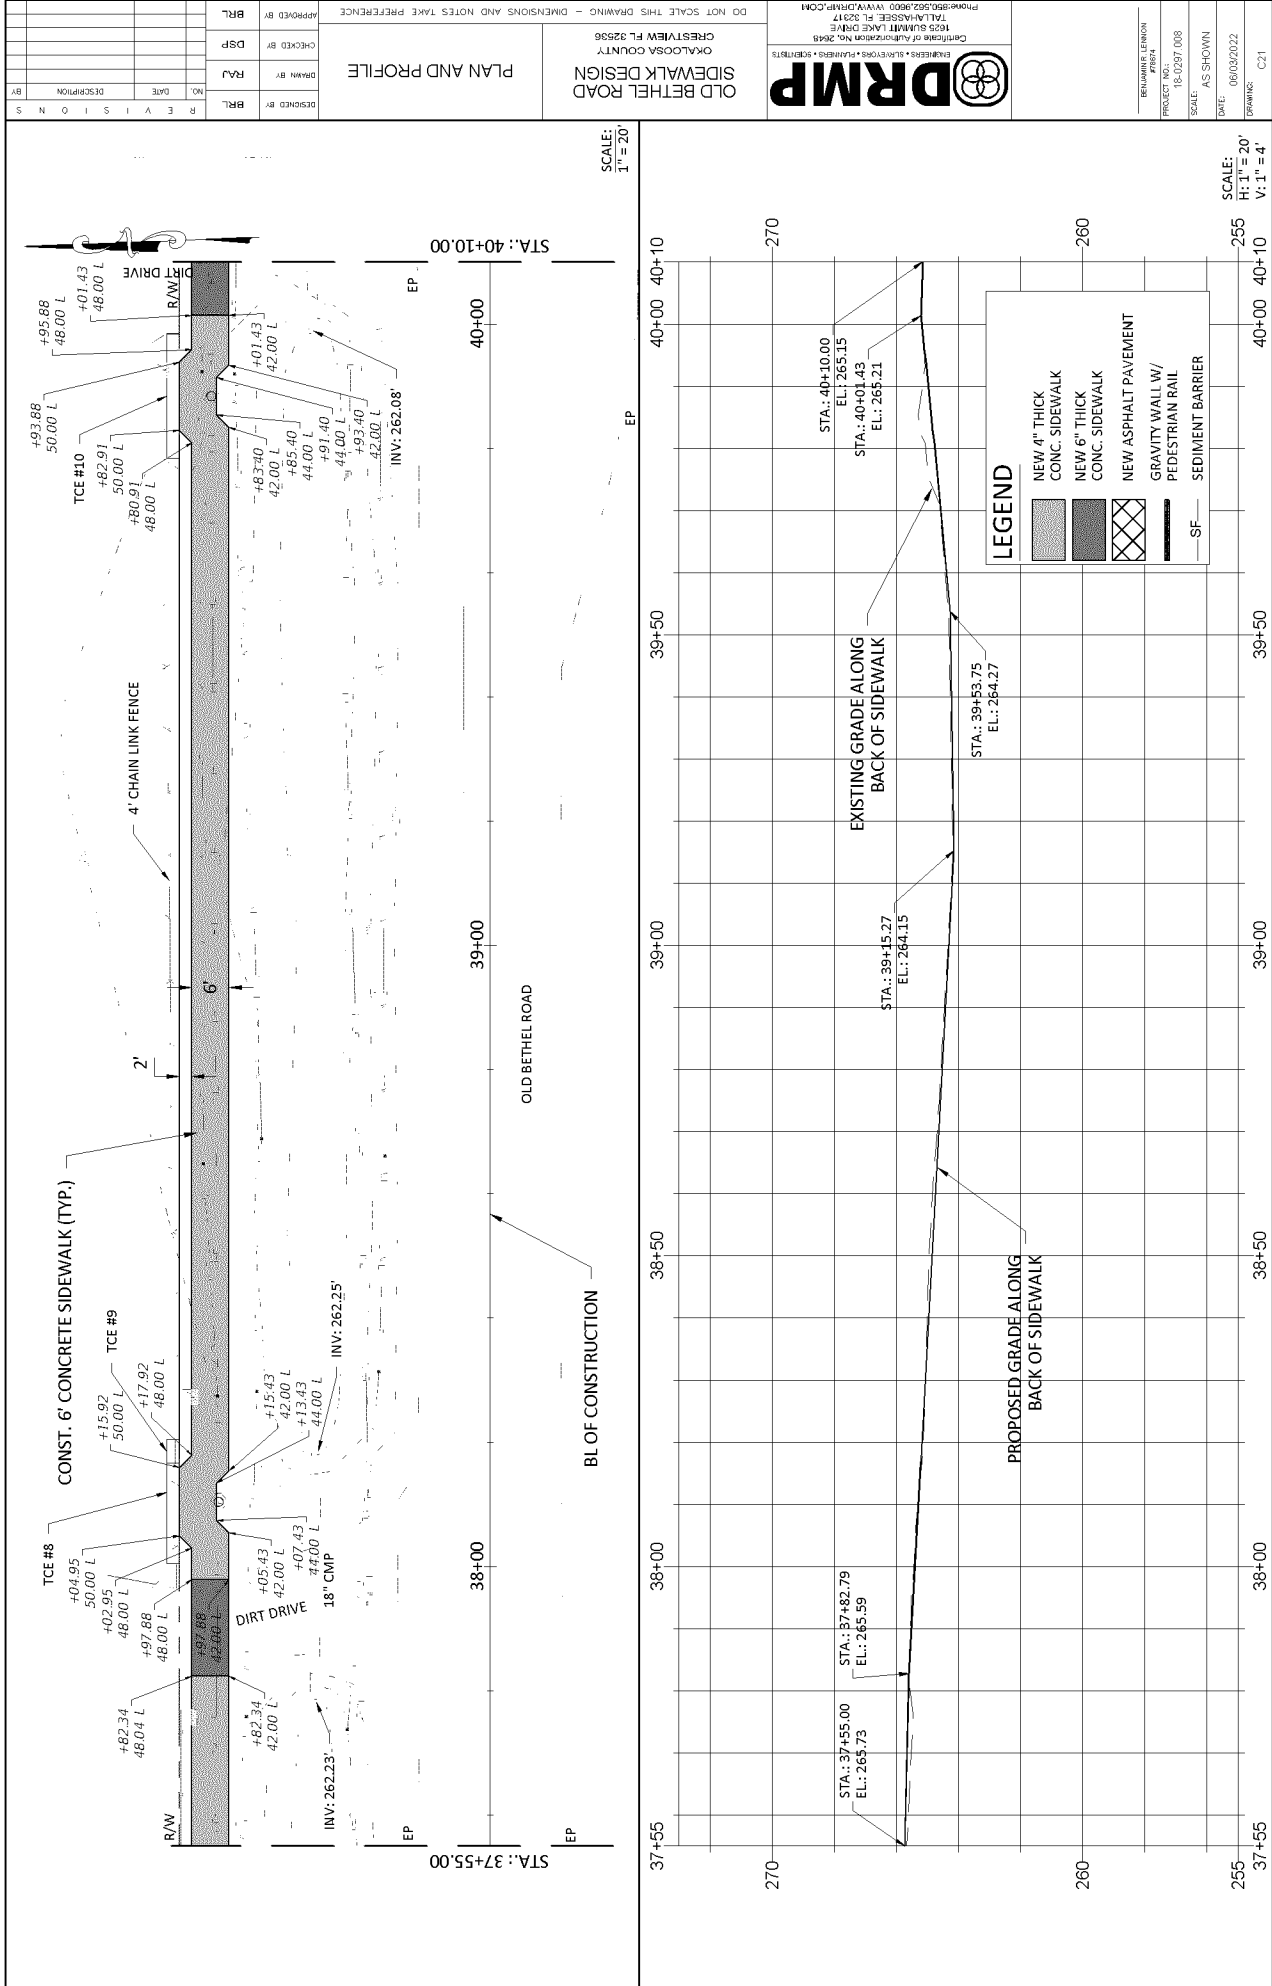

DRMP
CRESTVIEW FL 32836
OKALOOSA COUNTY
1625 SUMMIT LAKE DRIVE
TALLAHASSEE, FL 32317
Phone: 850.502.9800 WWW.DRMP.COM

DESIGNED BY: BRL
CHECKED BY: DDP
APPROVED BY: BRL

NO. DATE DESCRIPTION BY
REVISIONS

DATE: 08/03/2022
DRAWING: C21

PROJECT NO.: 18-0297-008
SCALE: AS SHOWN

ENGINEER: BLANKET DESIGN
PROJECT: 18-0297-008

DESIGNED BY: BRL
CHECKED BY: DDP
APPROVED BY: BRL

NO. DATE DESCRIPTION BY
REVISIONS

DATE: 08/03/2022
DRAWING: C21

PROJECT NO.: 18-0297-008
SCALE: AS SHOWN

ENGINEER: BLANKET DESIGN
PROJECT: 18-0297-008

DESIGNED BY: BRL
CHECKED BY: DDP
APPROVED BY: BRL

NO. DATE DESCRIPTION BY
REVISIONS

DATE: 08/03/2022
DRAWING: C21

PROJECT NO.: 18-0297-008
SCALE: AS SHOWN

ENGINEER: BLANKET DESIGN
PROJECT: 18-0297-008

DESIGNED BY: BRL
CHECKED BY: DDP
APPROVED BY: BRL

NO. DATE DESCRIPTION BY
REVISIONS

DATE: 08/03/2022
DRAWING: C21

PROJECT NO.: 18-0297-008
SCALE: AS SHOWN

ENGINEER: BLANKET DESIGN
PROJECT: 18-0297-008

DESIGNED BY: BRL
CHECKED BY: DDP
APPROVED BY: BRL

NO. DATE DESCRIPTION BY
REVISIONS

DATE: 08/03/2022
DRAWING: C21

PROJECT NO.: 18-0297-008
SCALE: AS SHOWN

ENGINEER: BLANKET DESIGN
PROJECT: 18-0297-008

DESIGNED BY: BRL
CHECKED BY: DDP
APPROVED BY: BRL

NO. DATE DESCRIPTION BY
REVISIONS


DATE: 08/03/2022
DRAWING: C21


PROJECT NO.: 18-0297-008
SCALE: AS SHOWN


ENGINEER: BLANKET DESIGN
PROJECT: 18-0297-008

DESIGNED BY: BRL
CHECKED BY: DDP
APPROVED BY: BRL

NO. DATE DESCRIPTION BY
REVISIONS

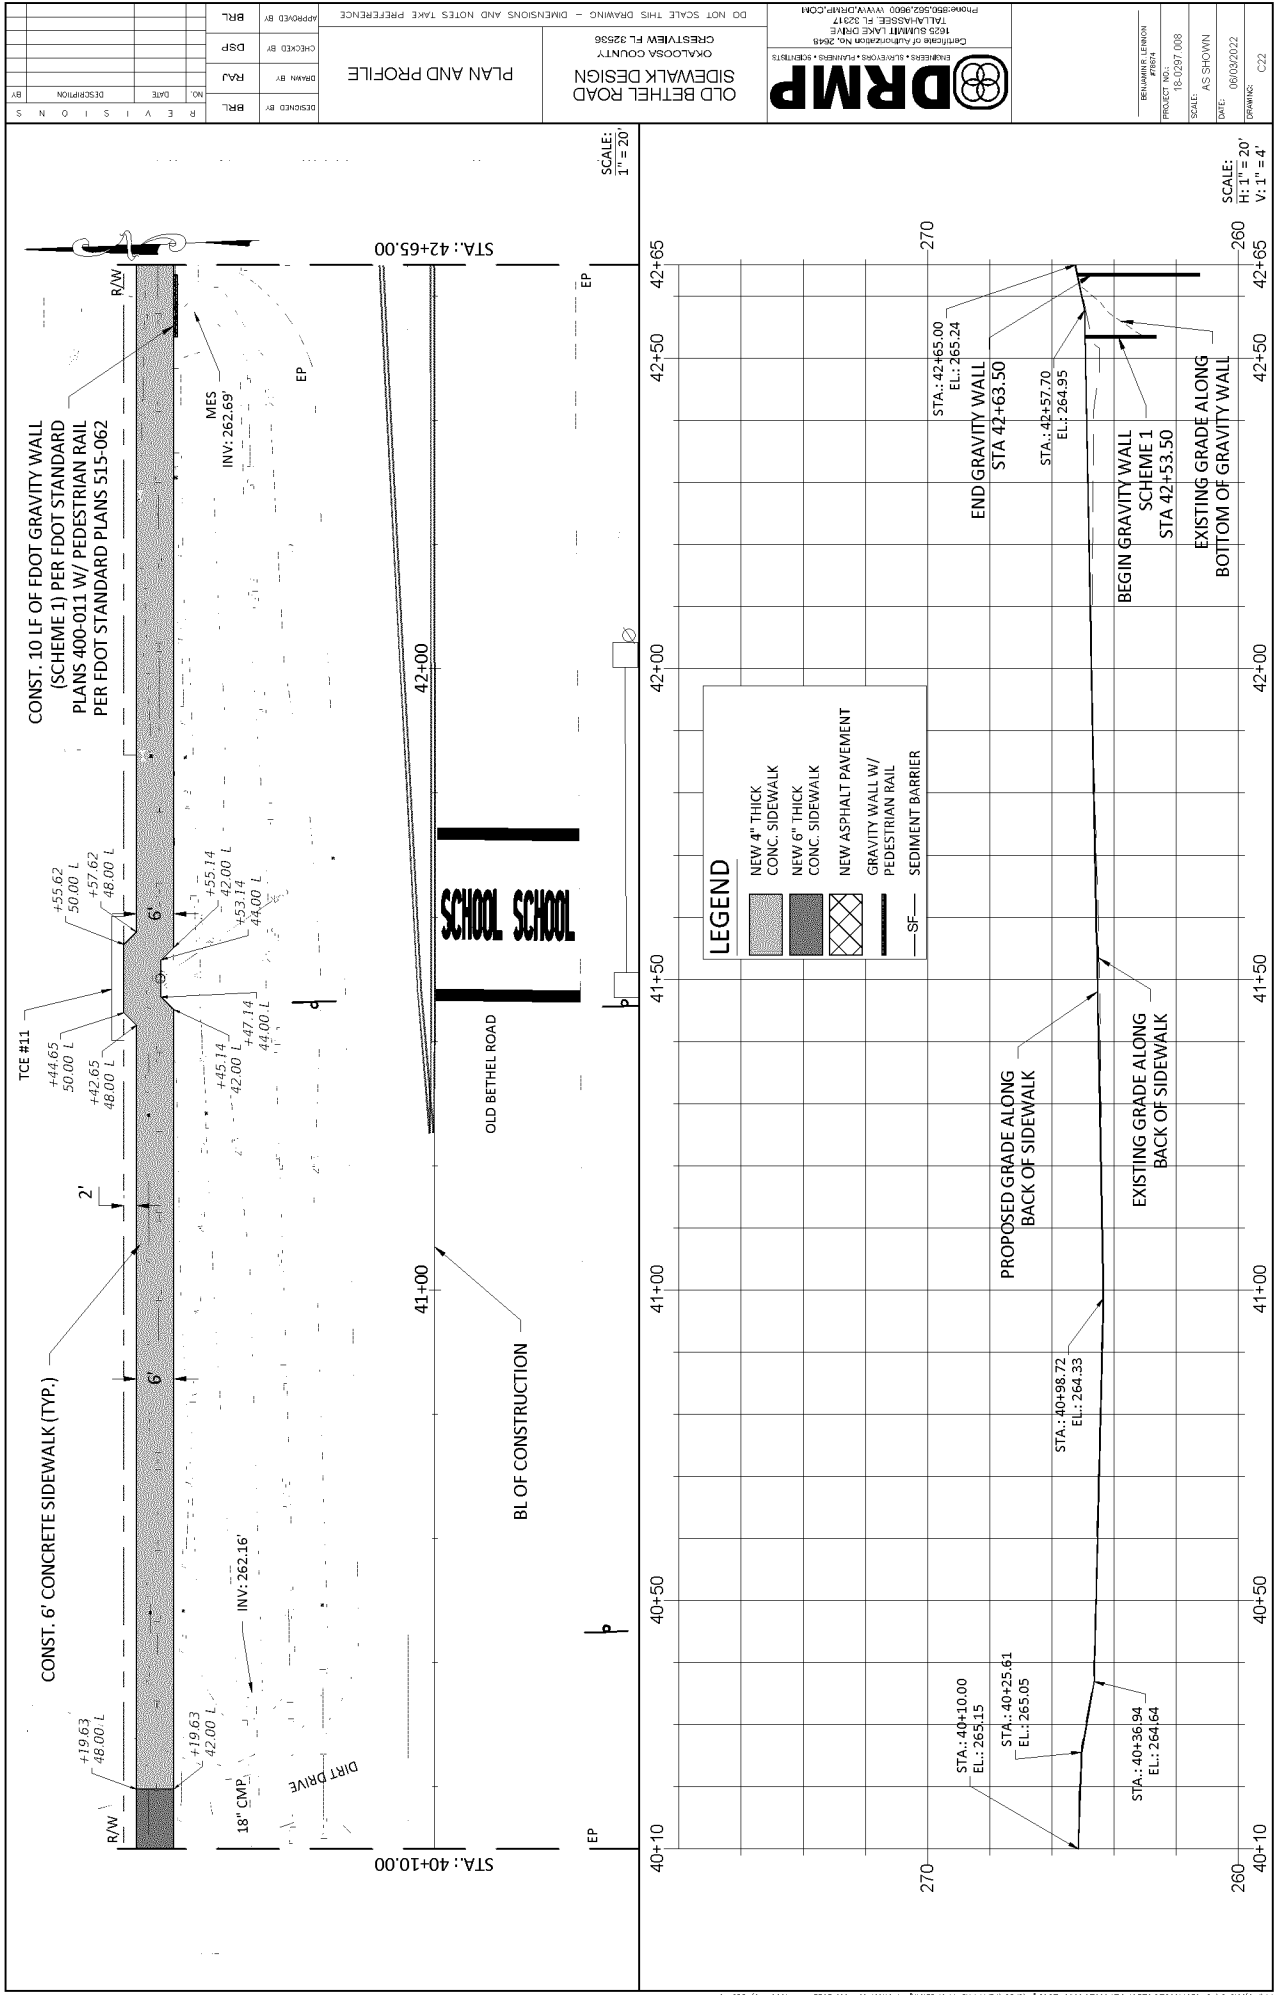

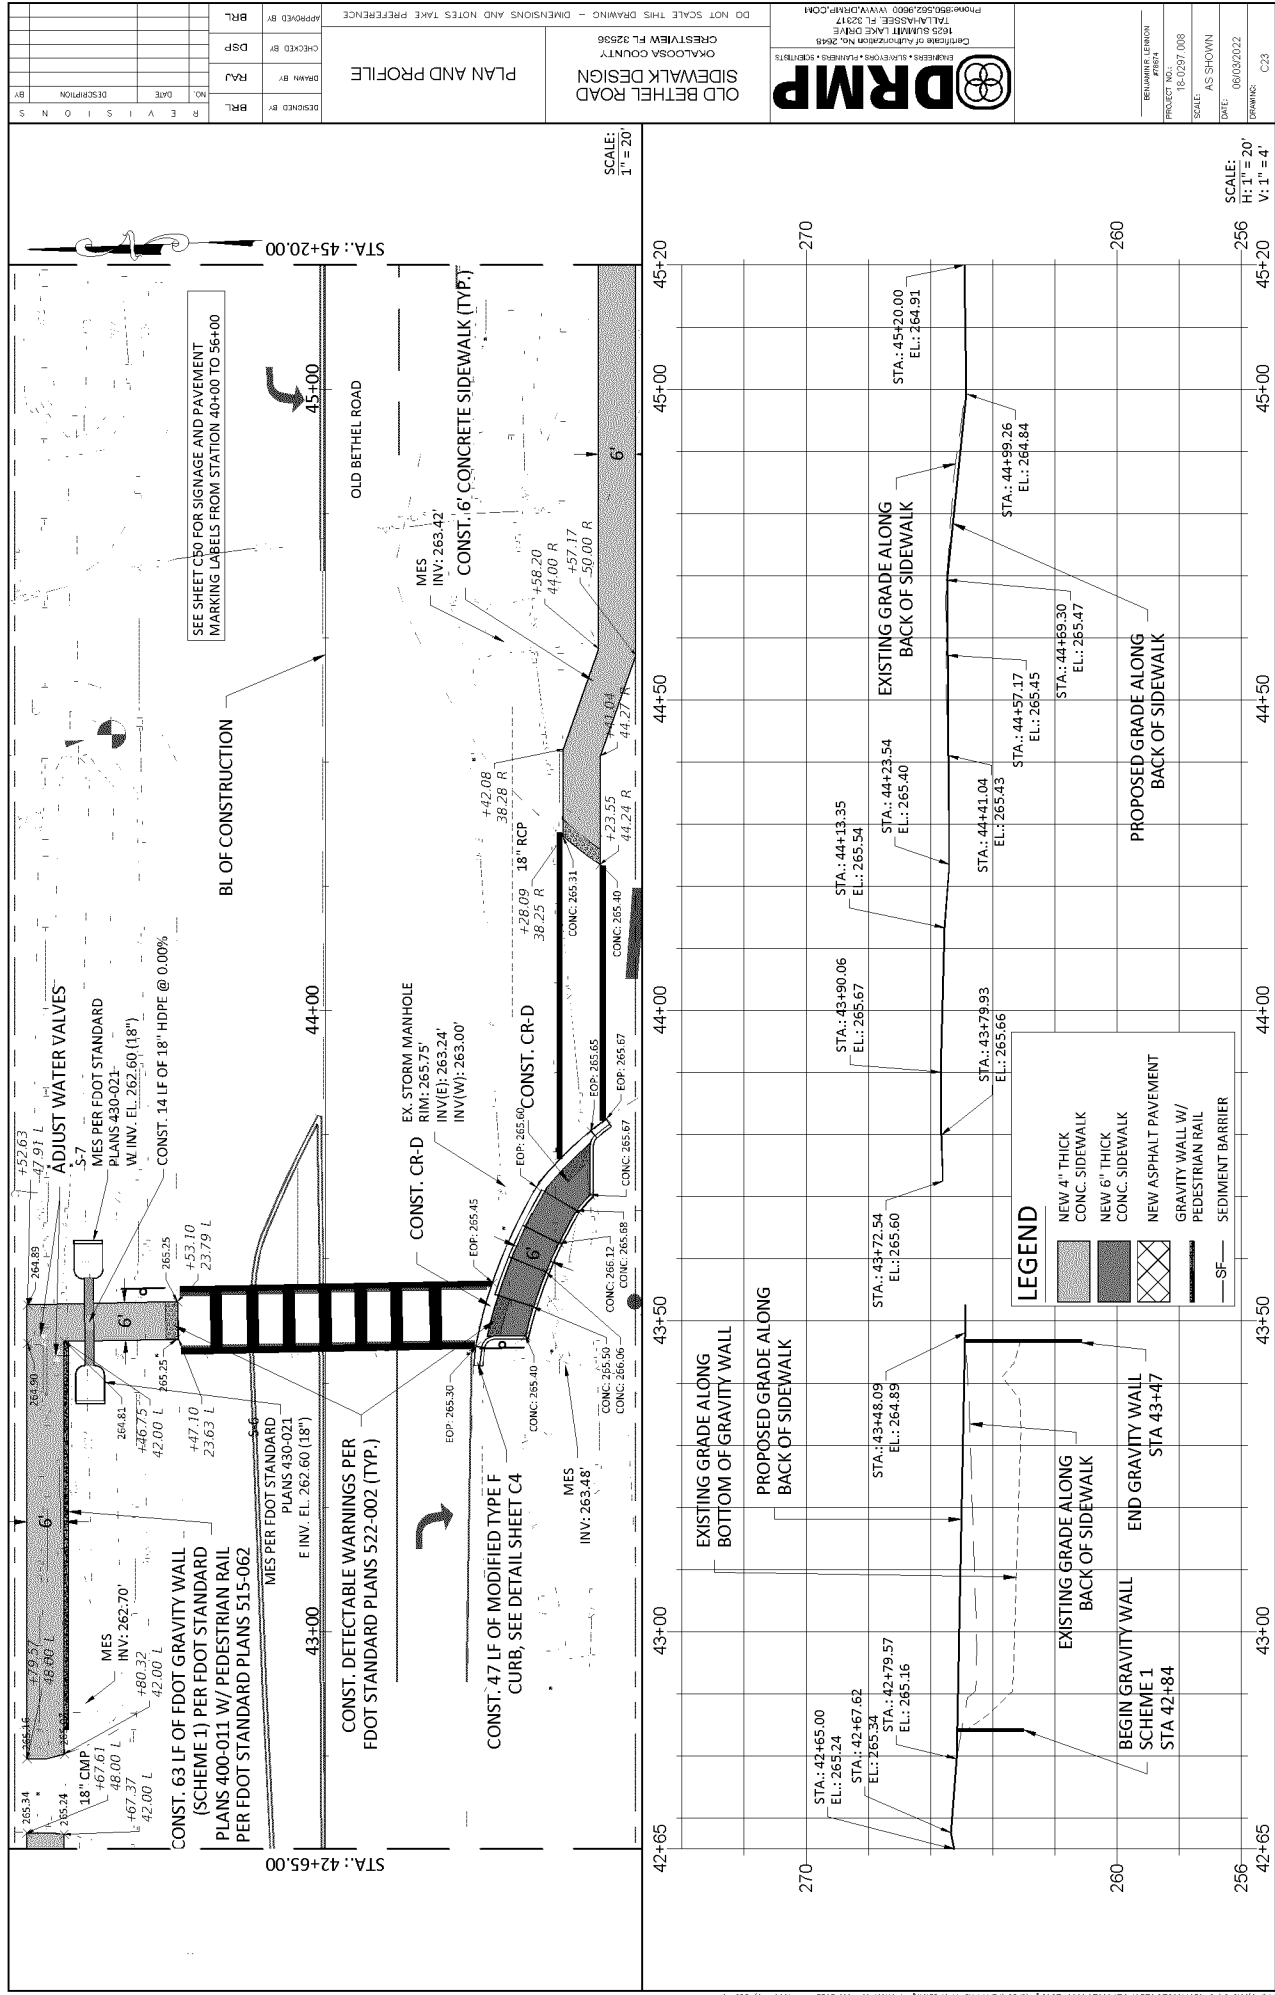





CRESTVIEW FL 32536


PLAN AND PROFILE







DESIGNED BY	BRL
DRAWN BY	RAJ



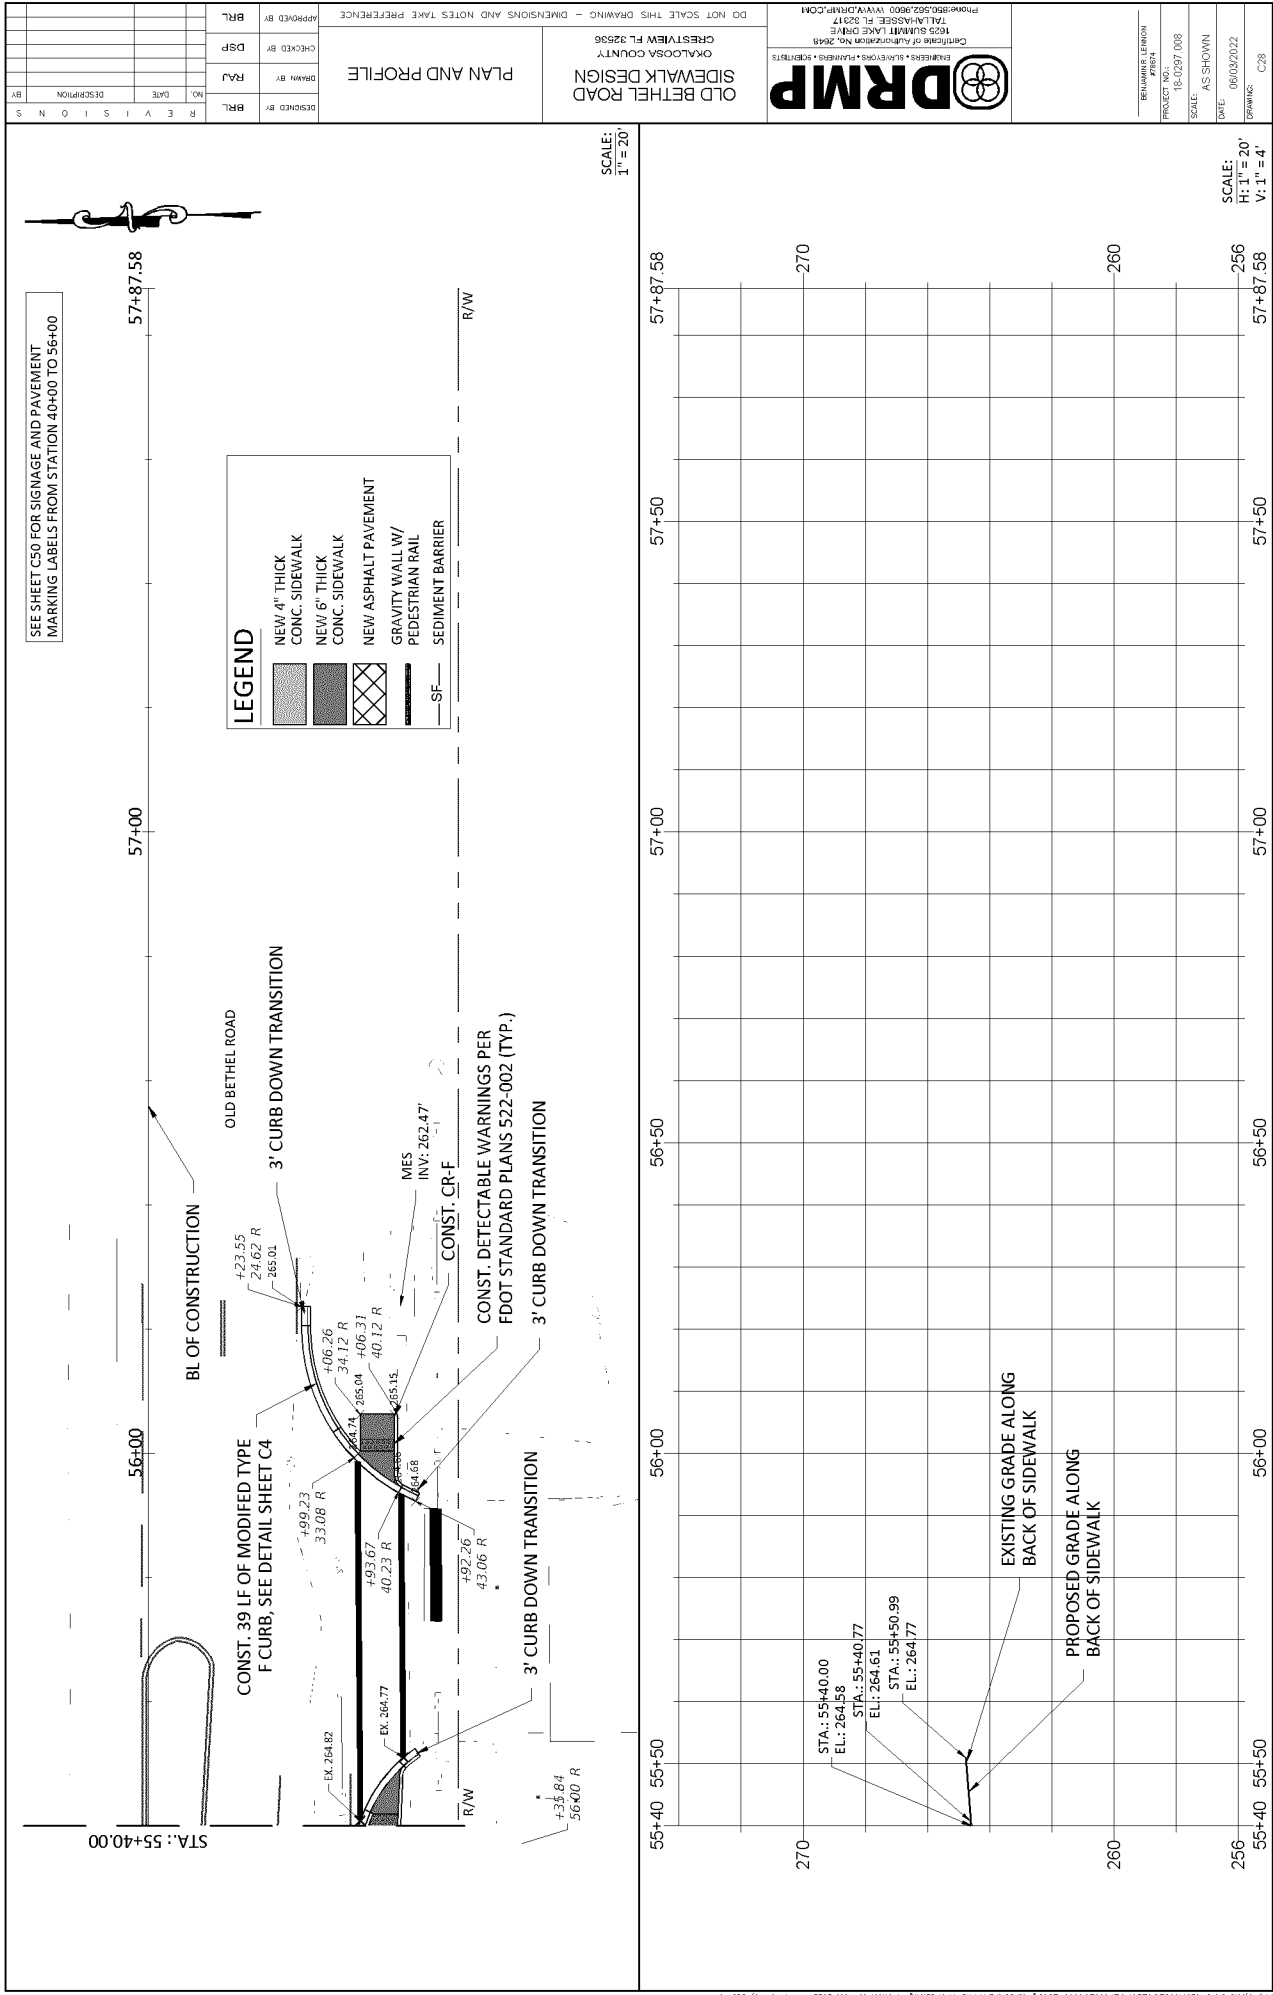

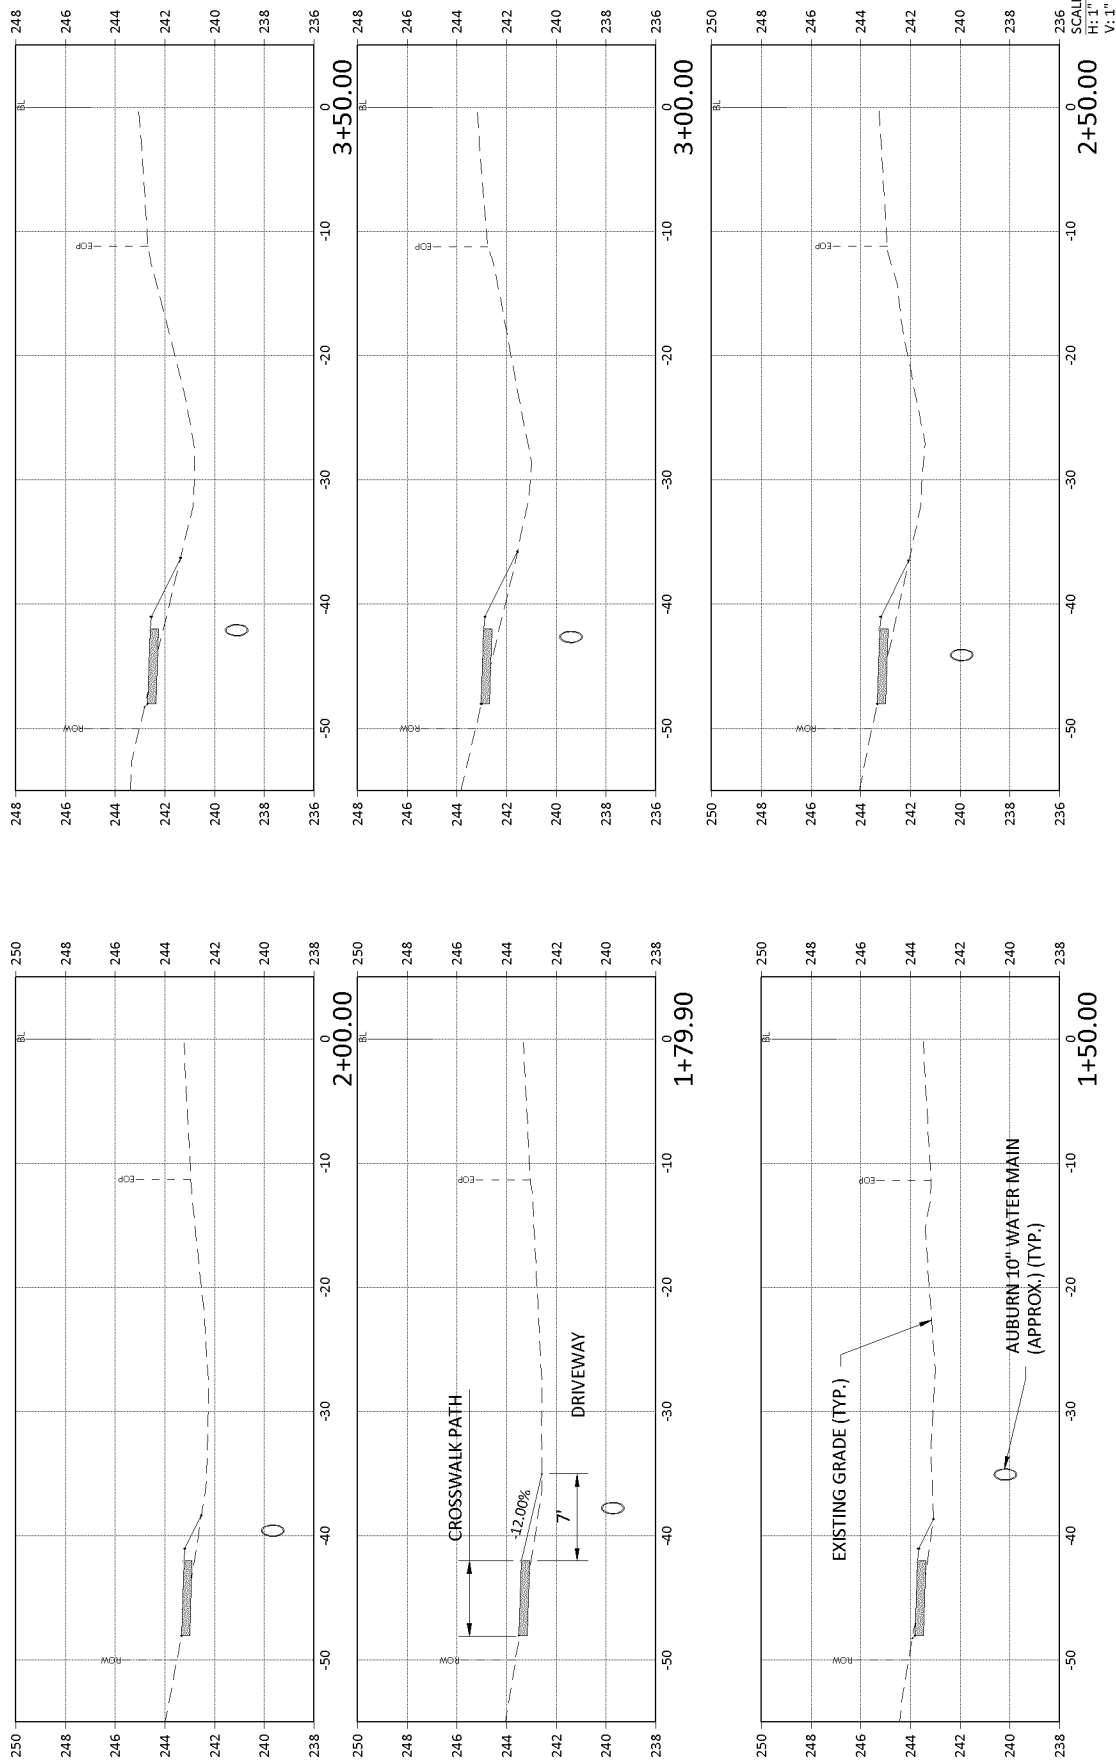
[illegible]

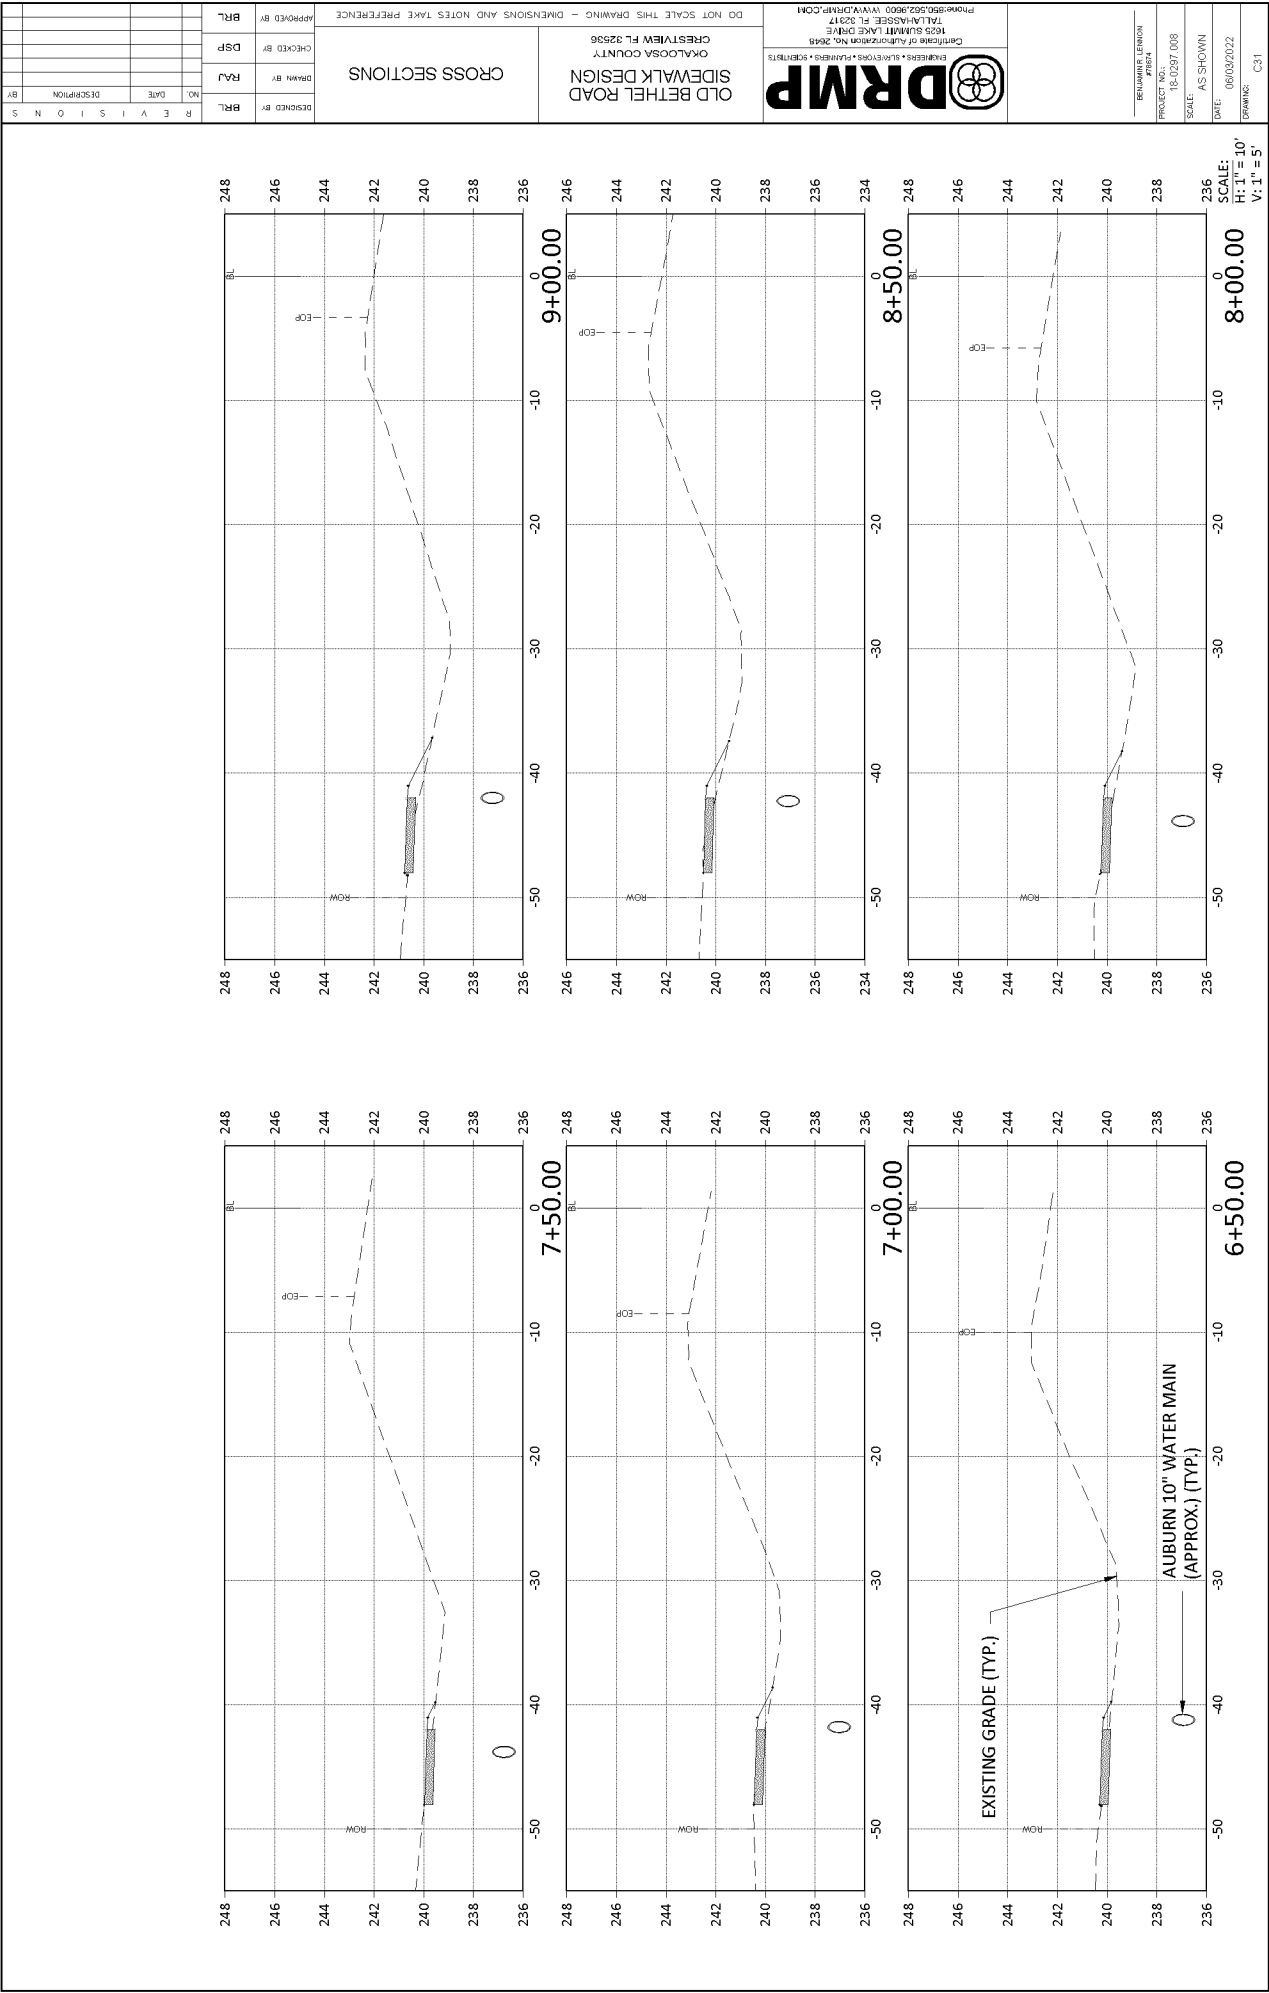


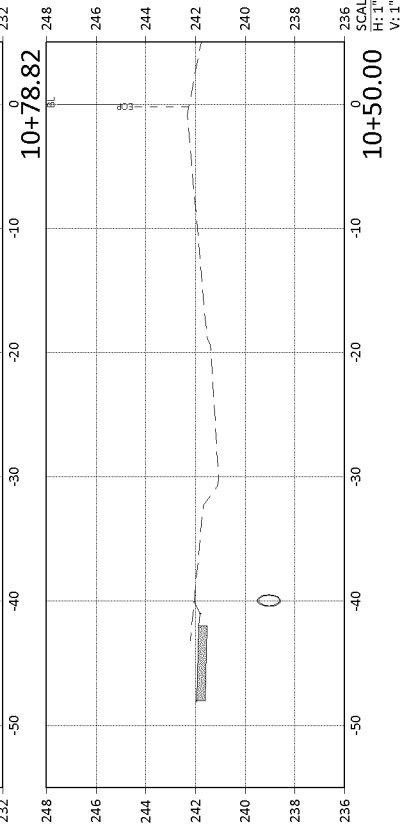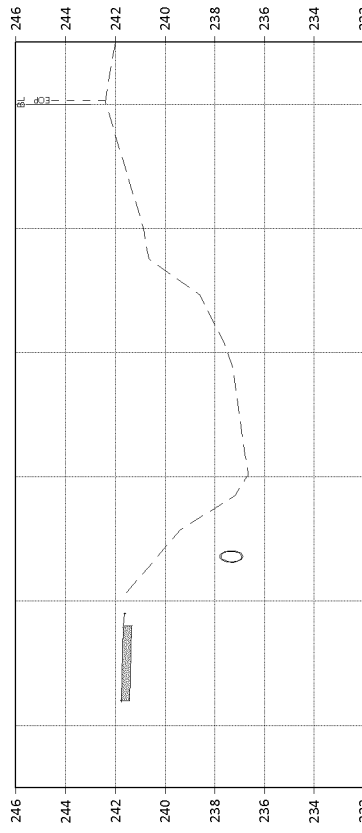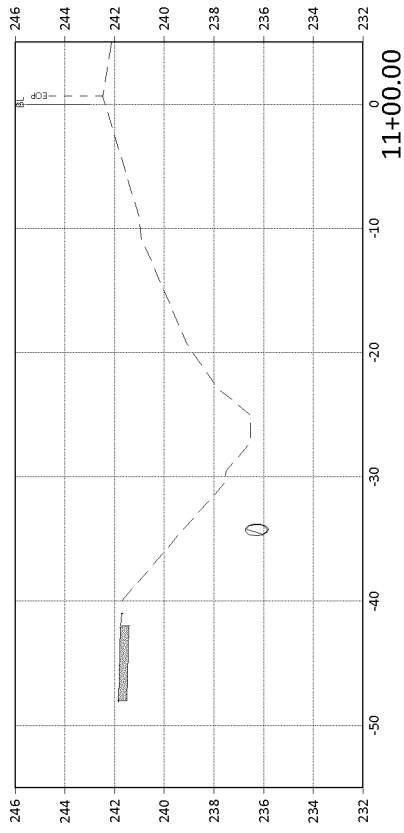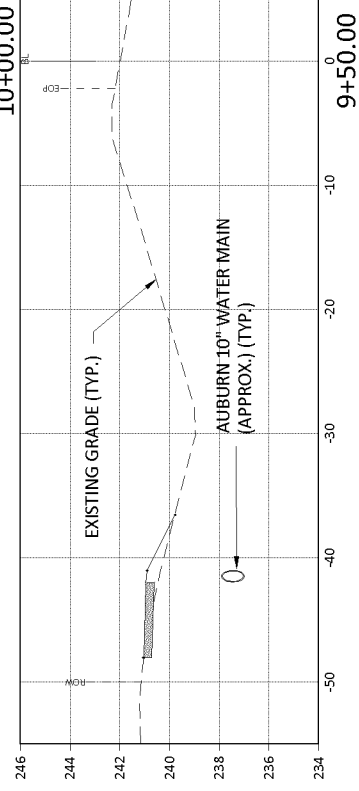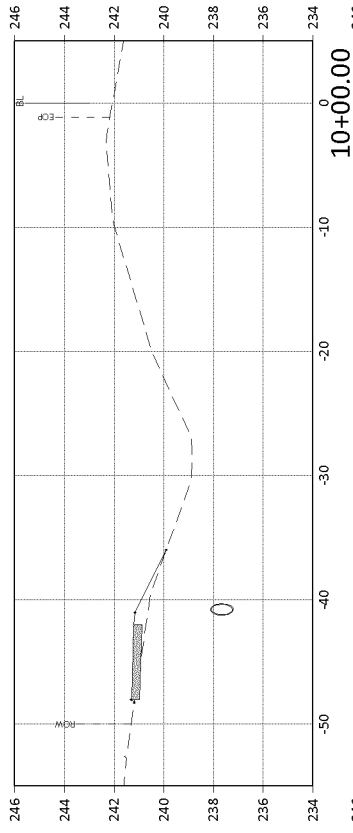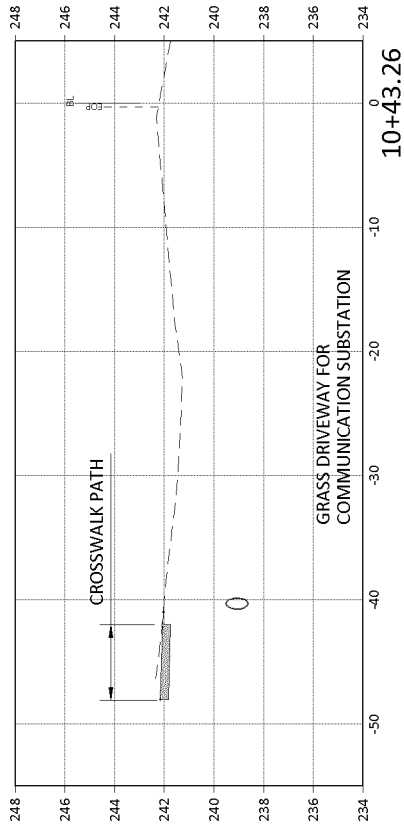






		Certificate of Authorization No. 0048 ENGINEERS • SURVEYORS • PLANNERS • SCIENTISTS 1625 SUNNYSIDE LAKE DRIVE FALLS CHURCH, VA 22041 TEL: (703) 271-1234 FAX: (703) 271-1235 WWW.DRMP.COM Phone: (703) 271-1234		DO NOT SCALE THIS DRAWING - DIMENSIONS AND NOTES TAKE PRECEDENCE APPROVED BY: 									
OLD BETHLE ROAD SIDEWALK DESIGN CRESTVIEW COUNTRY FALLS CHURCH, VA 22041		CROSS SECTIONS		DESIGNED BY: 									
R E V I S I O N S		DRAWN BY: 		CHECKED BY: 									
NO. DATE DESCRIPTION BY		1 08/02/2022 AS SHOWN		SCALE: 15'-0"=1'									
PROJECT NO.: 15-0397-008		SHEET NO.: 15-0397-008		DRAWING: C-32									

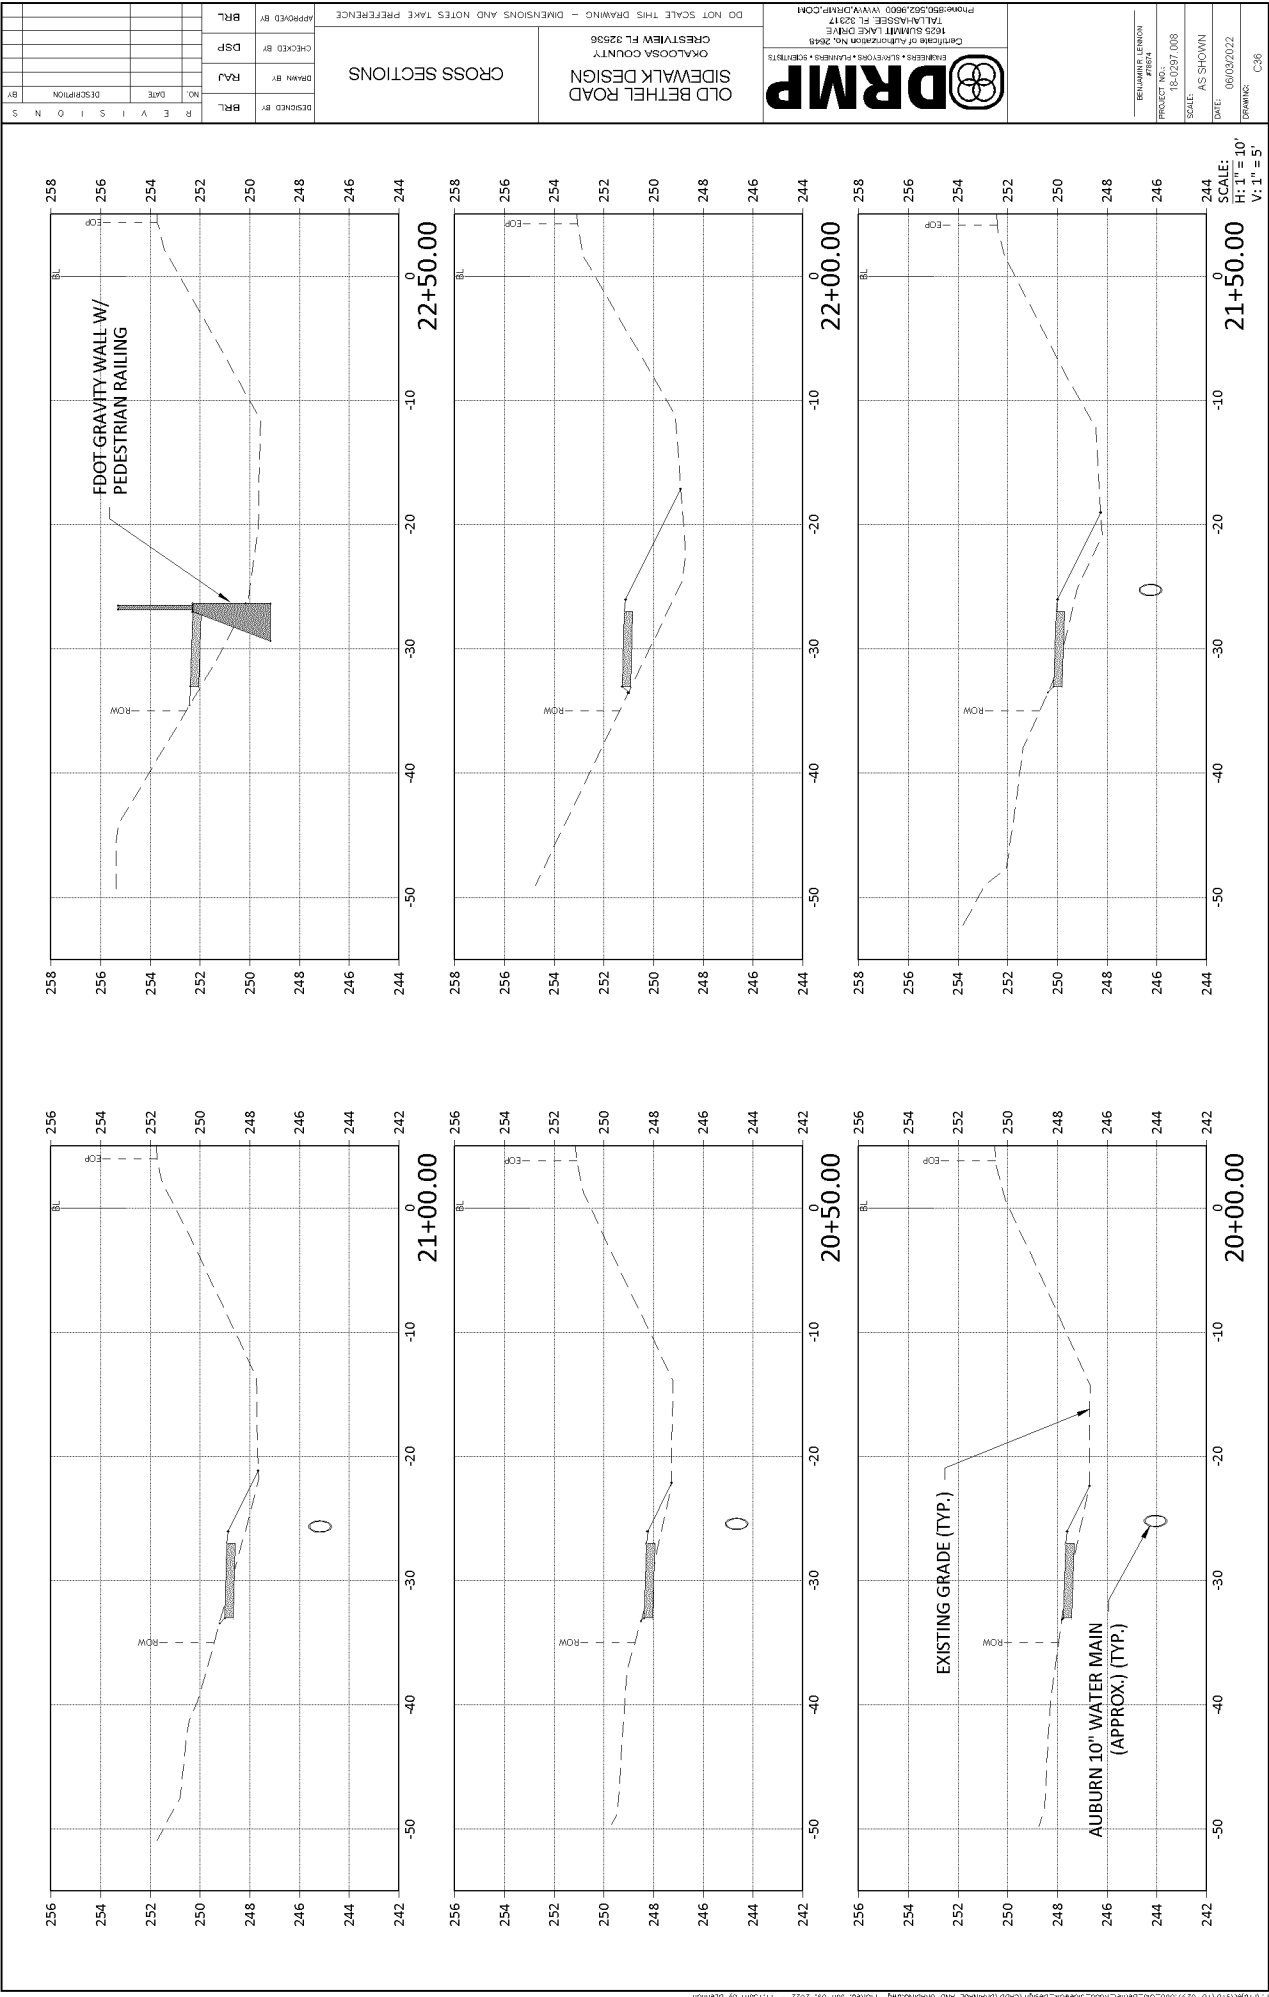



P:\Projects\1811-0297\008_OLD BETHEL ROAD, SHOWB, Design\CD\DWG\DWG AND GRADING.dwg Printed: Jun 09, 2022 - 11:11am by Rikemnon



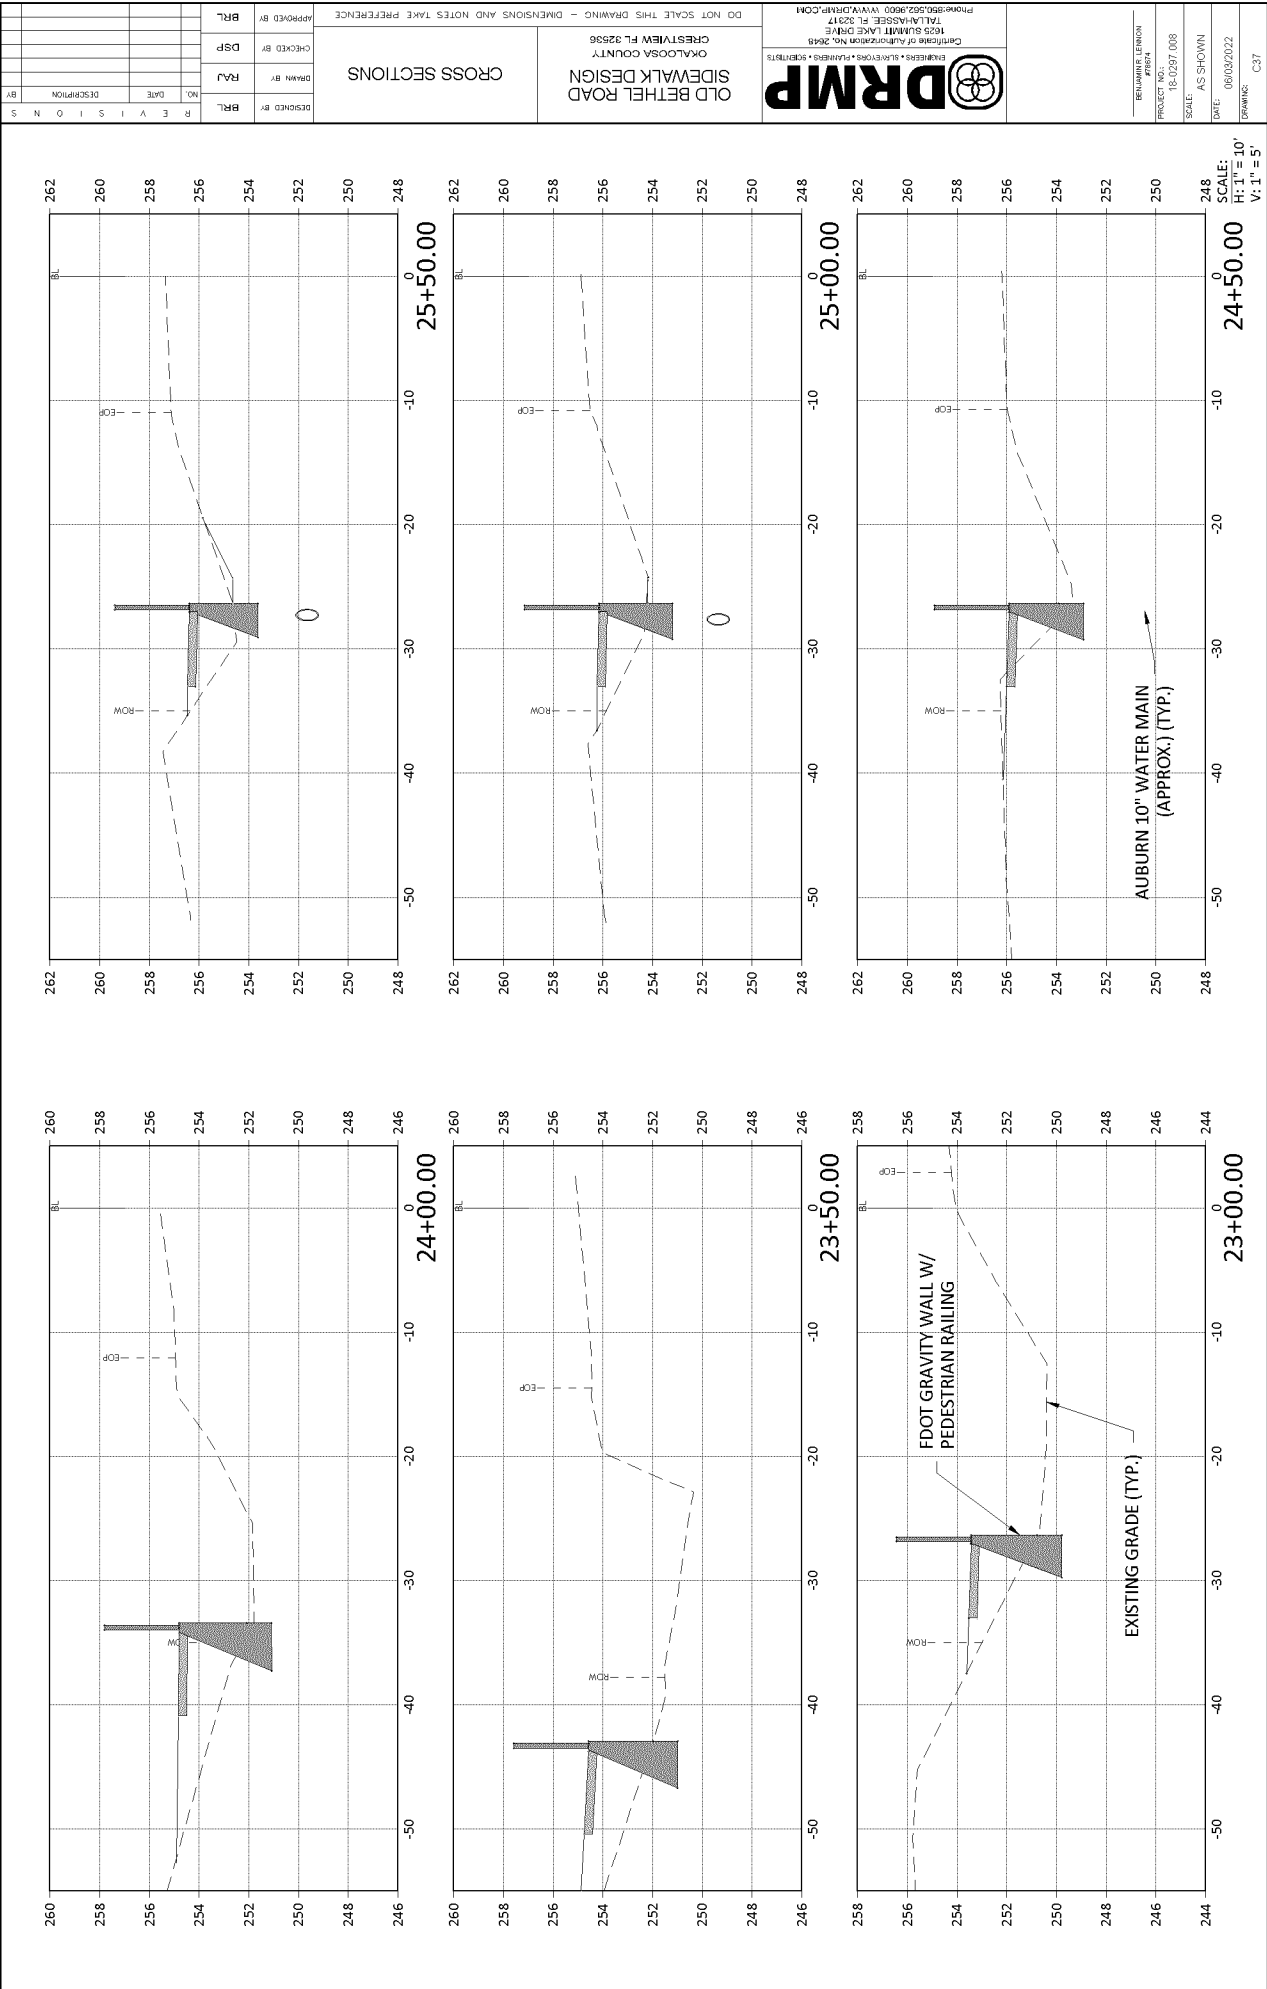




DRMP ENGINEERS, SURVEYORS, PLANNERS, ARCHITECTS 1625 SUMMIT LAKE DRIVE TALLAHASSEE, FL 32317 Phone: 904.502.9800 FAX: 904.502.9801 WWW.DRMP.COM		DO NOT SCALE THIS DRAWING - DIMENSIONS AND NOTES TAKE PRECEDENCE	
OLD BETHEL ROAD SIDEWALK DESIGN CRESTVIEW FL 32836		CROSS SECTIONS	
DESIGNED BY BRL	DRAWN BY RAJ	CHECKED BY DSP	APPROVED BY BRL
NO.	DATE	REVISIONS	
BY DESCRIPTION			


BLANKET LICENSE #7874
PROJECT NO. 1811-0297-008
SCALE: AS SHOWN
DATE: 06/03/2022
DRAWING: C27

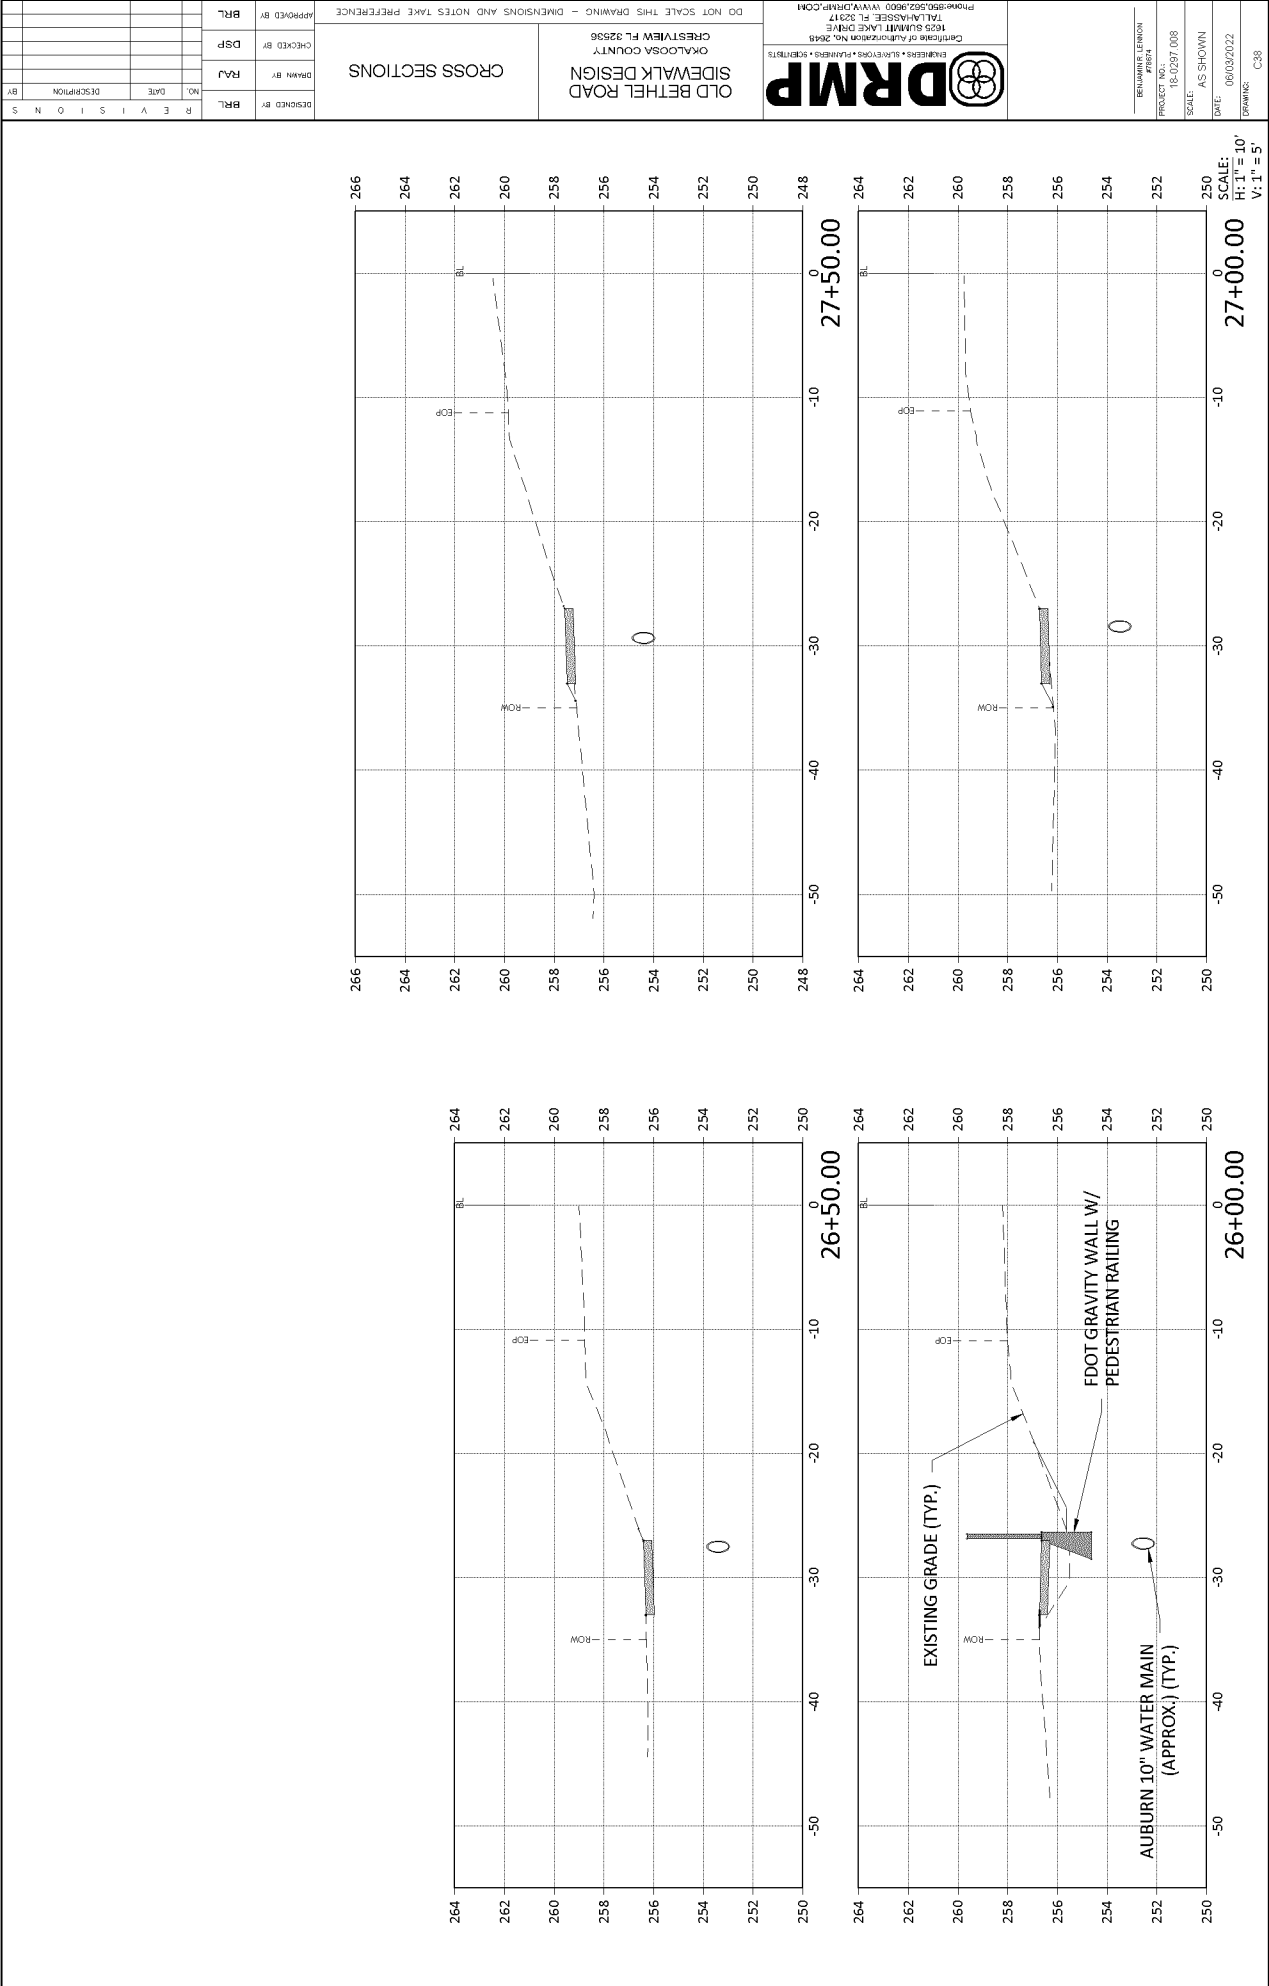


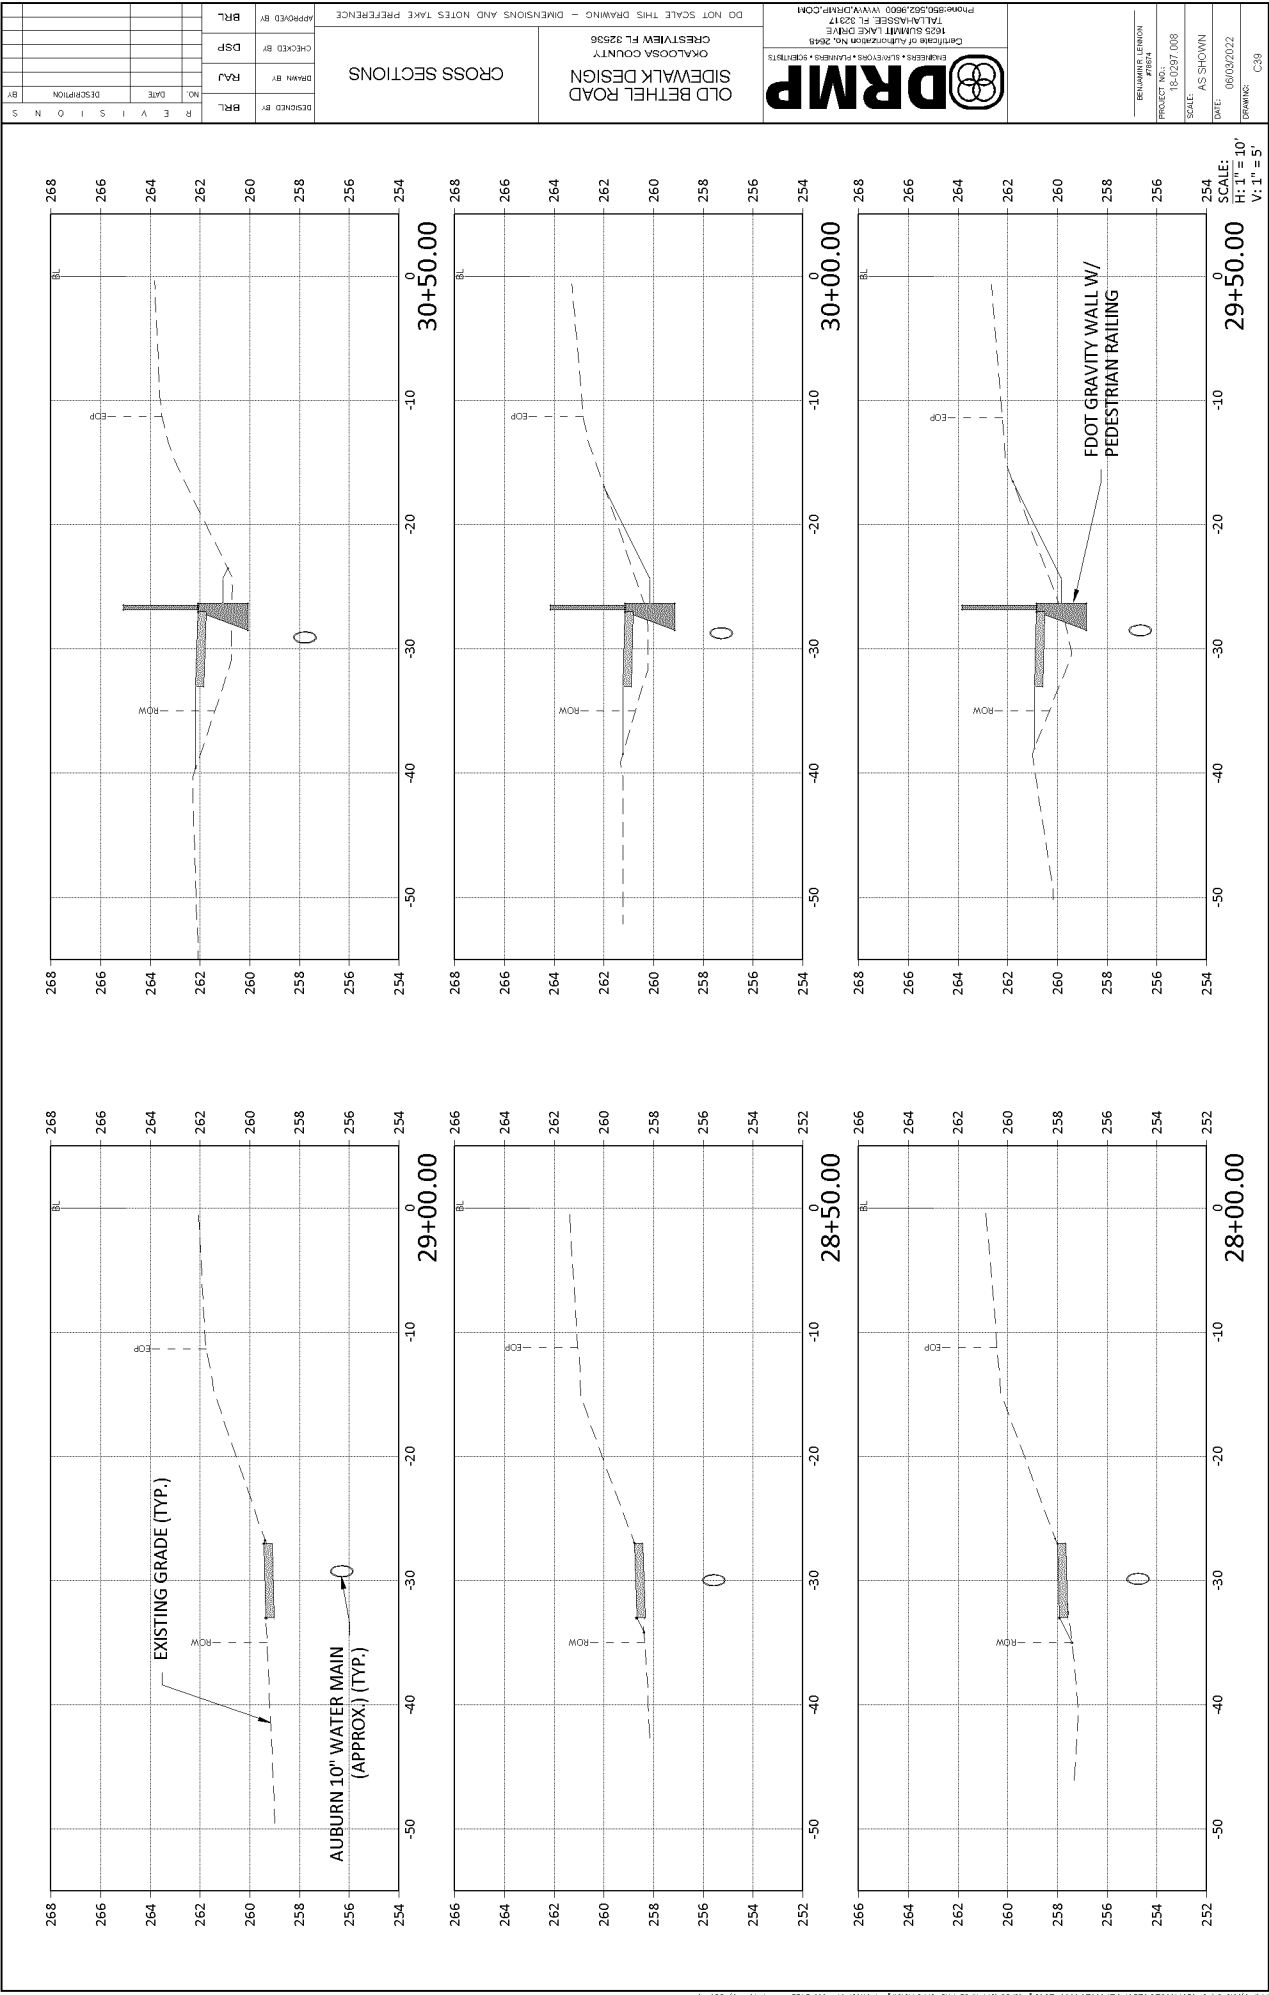


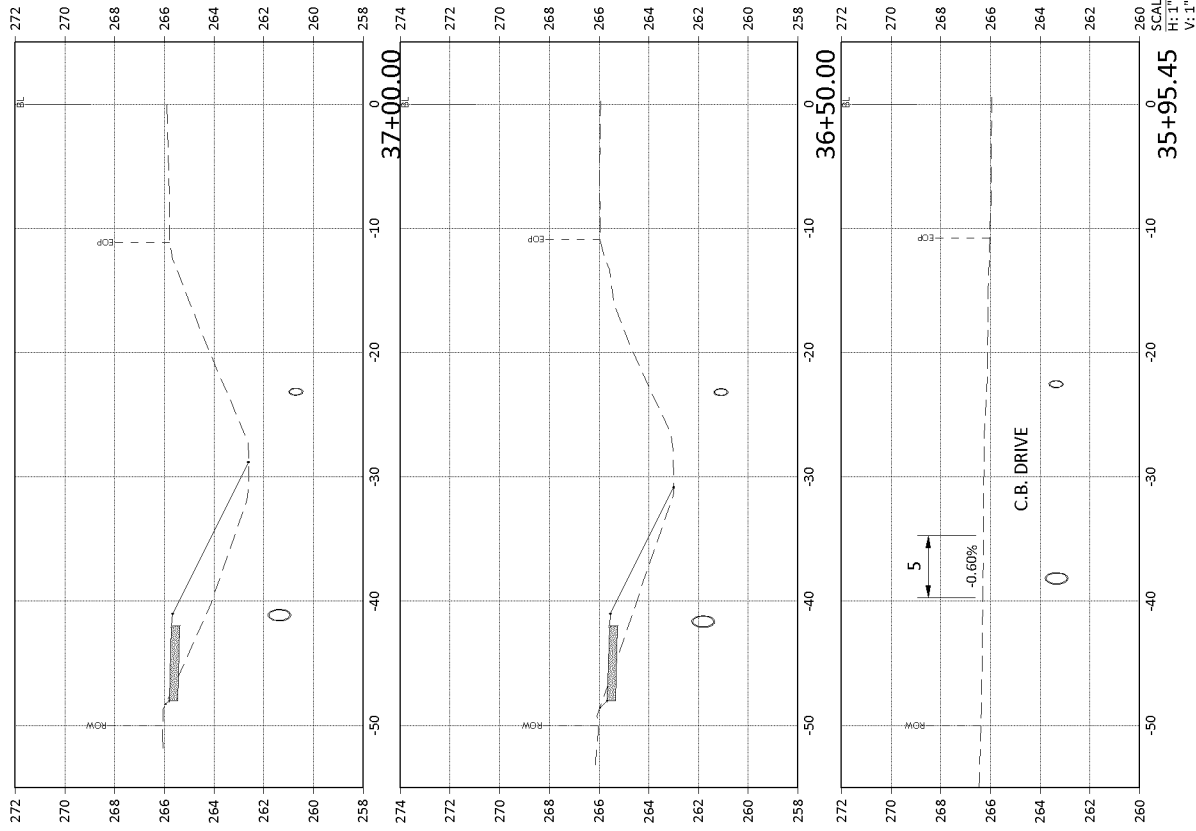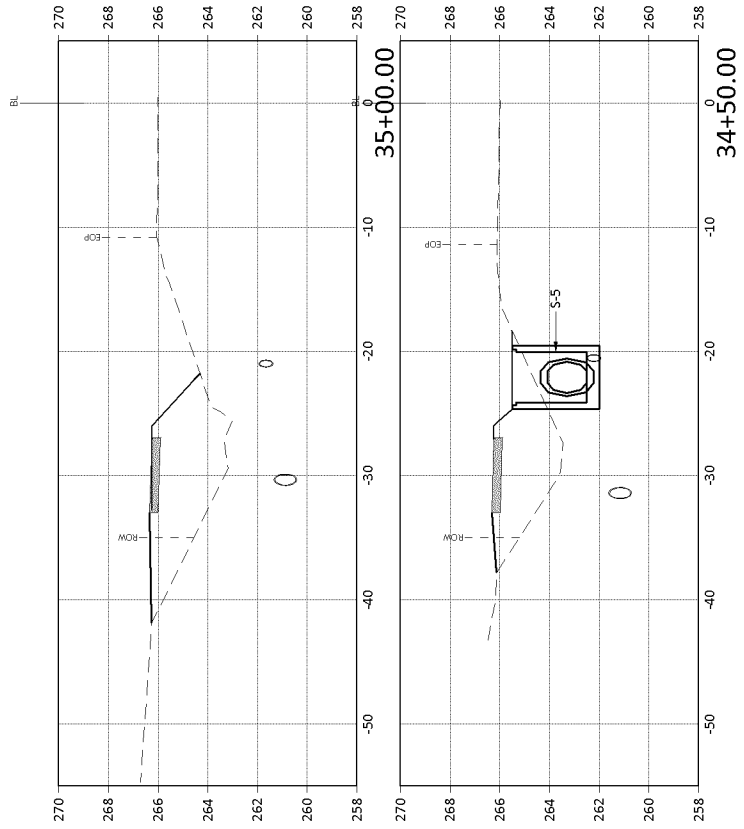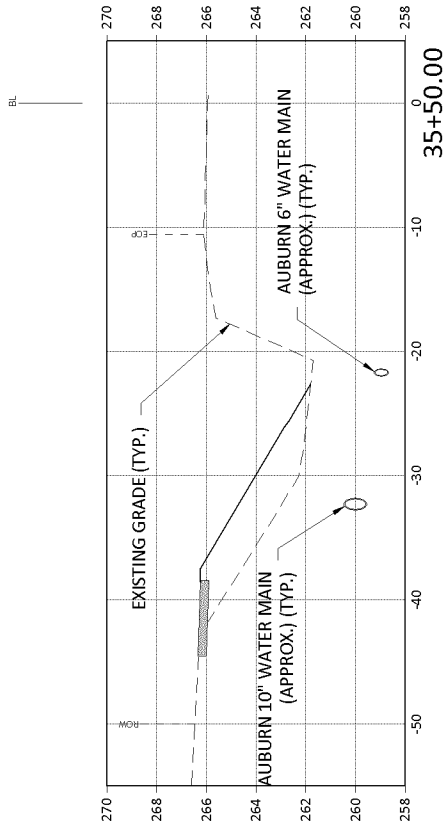


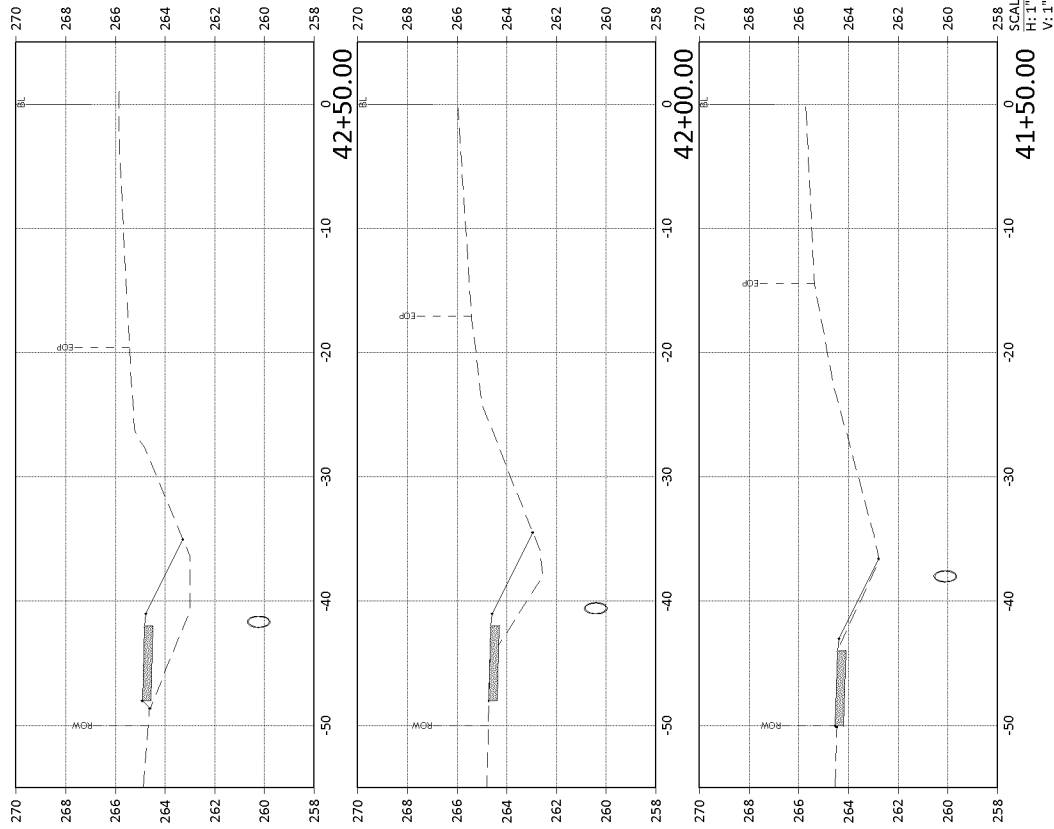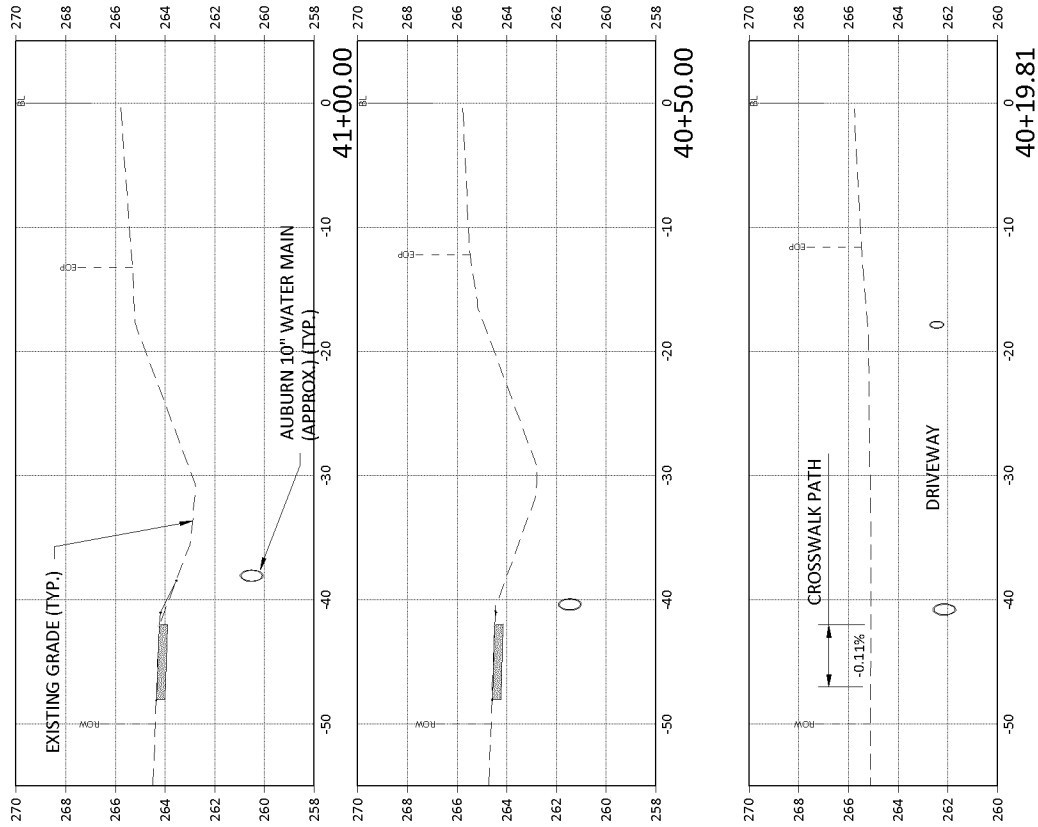


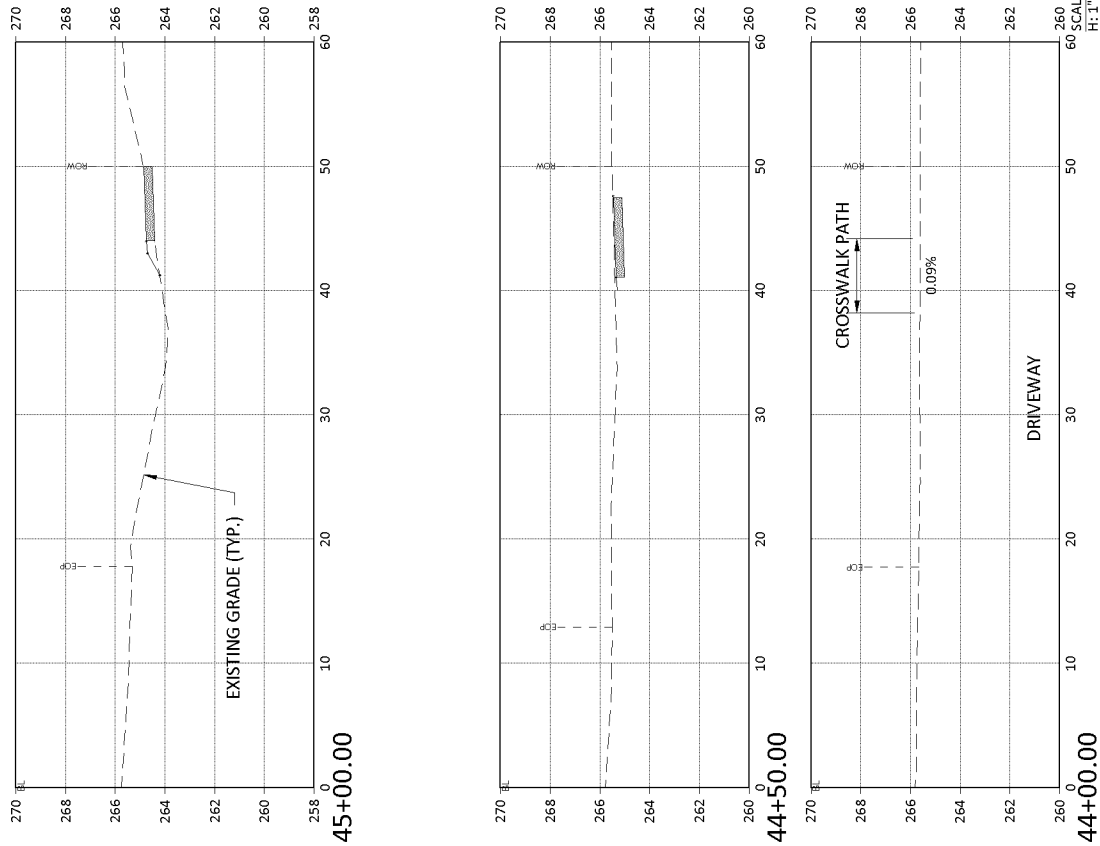

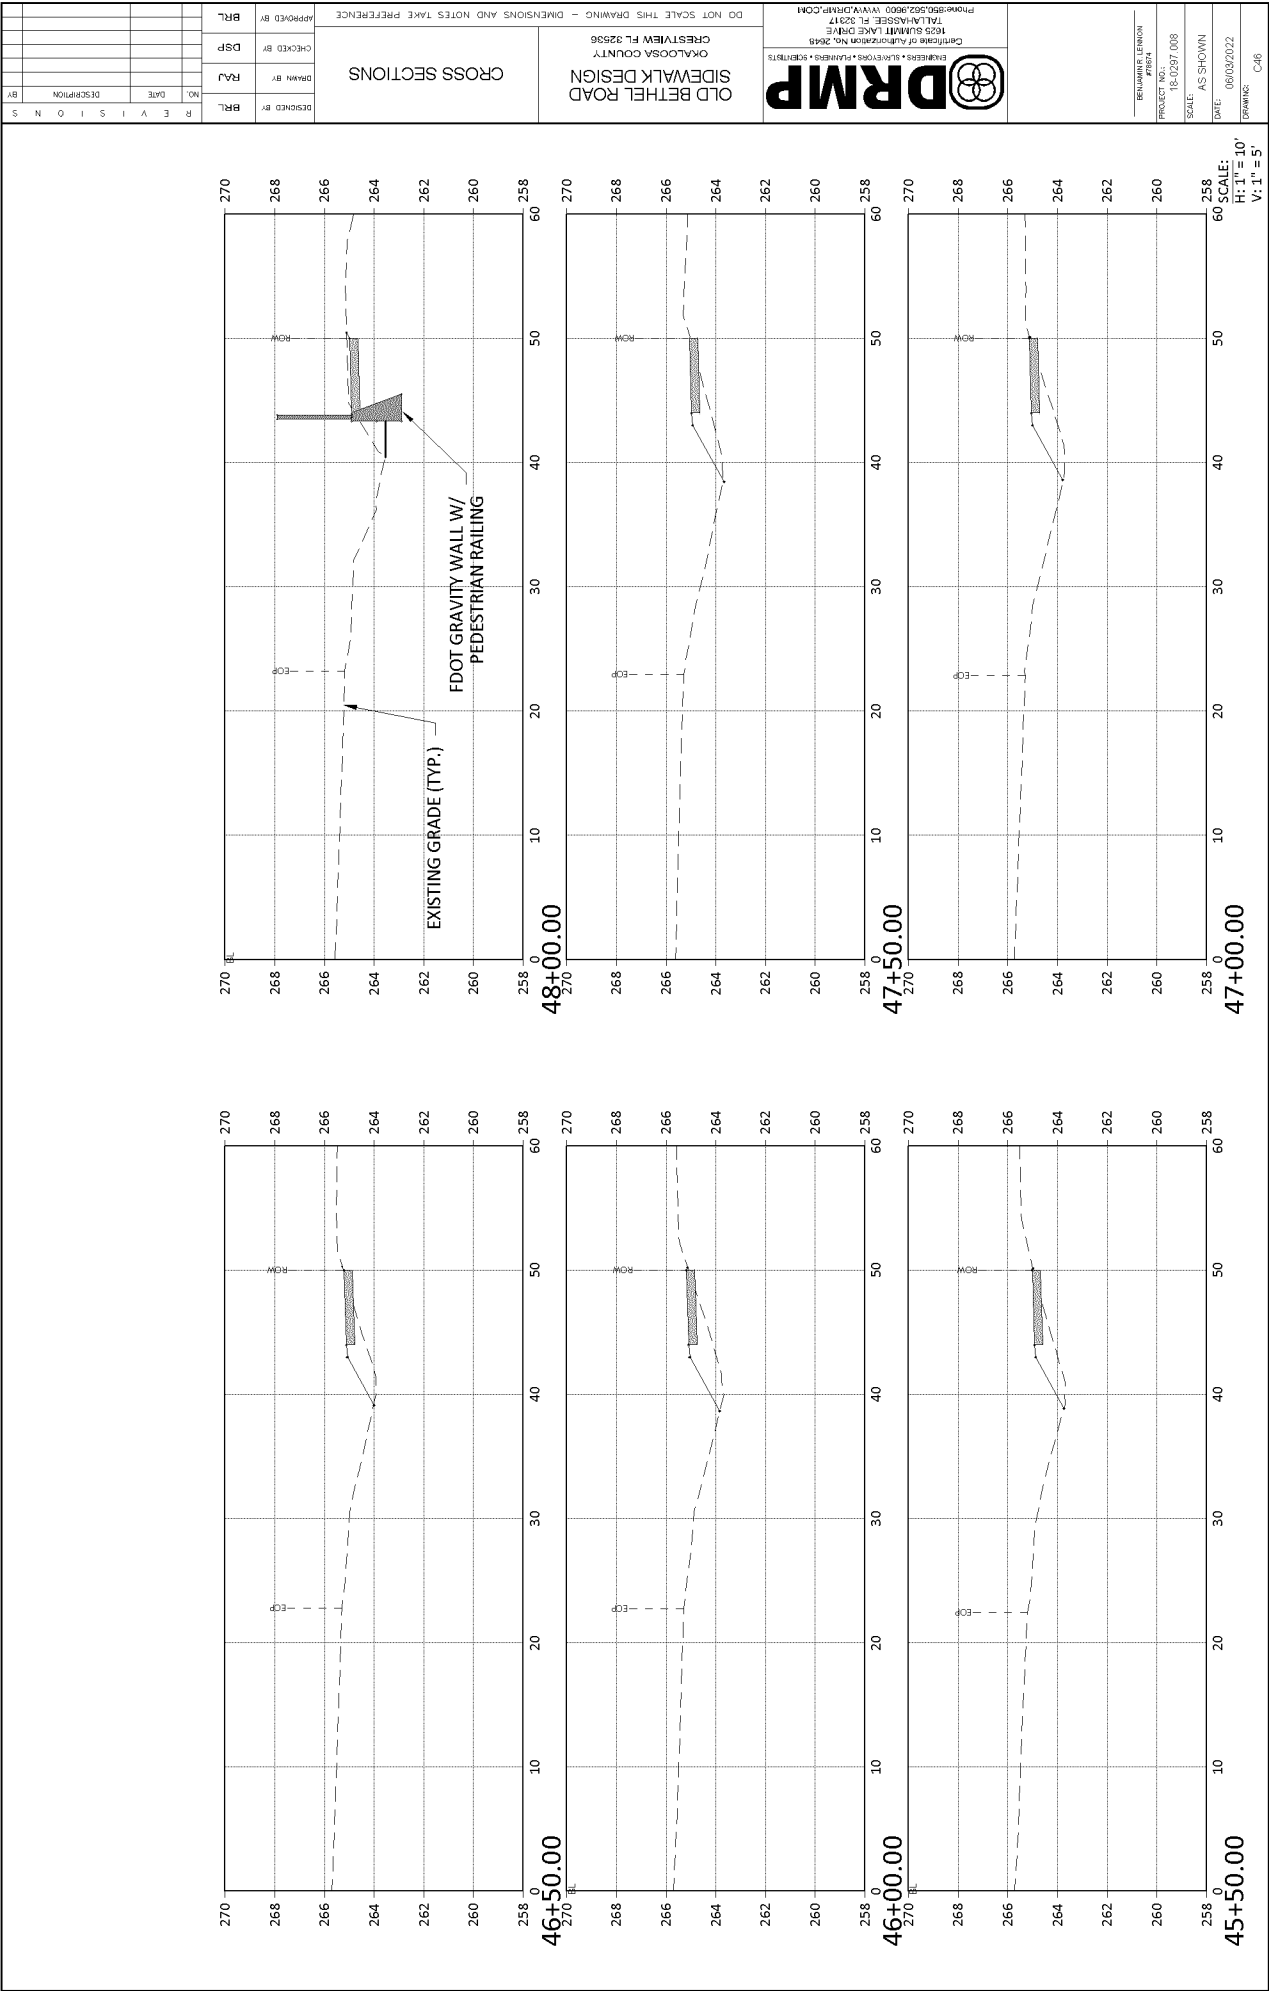

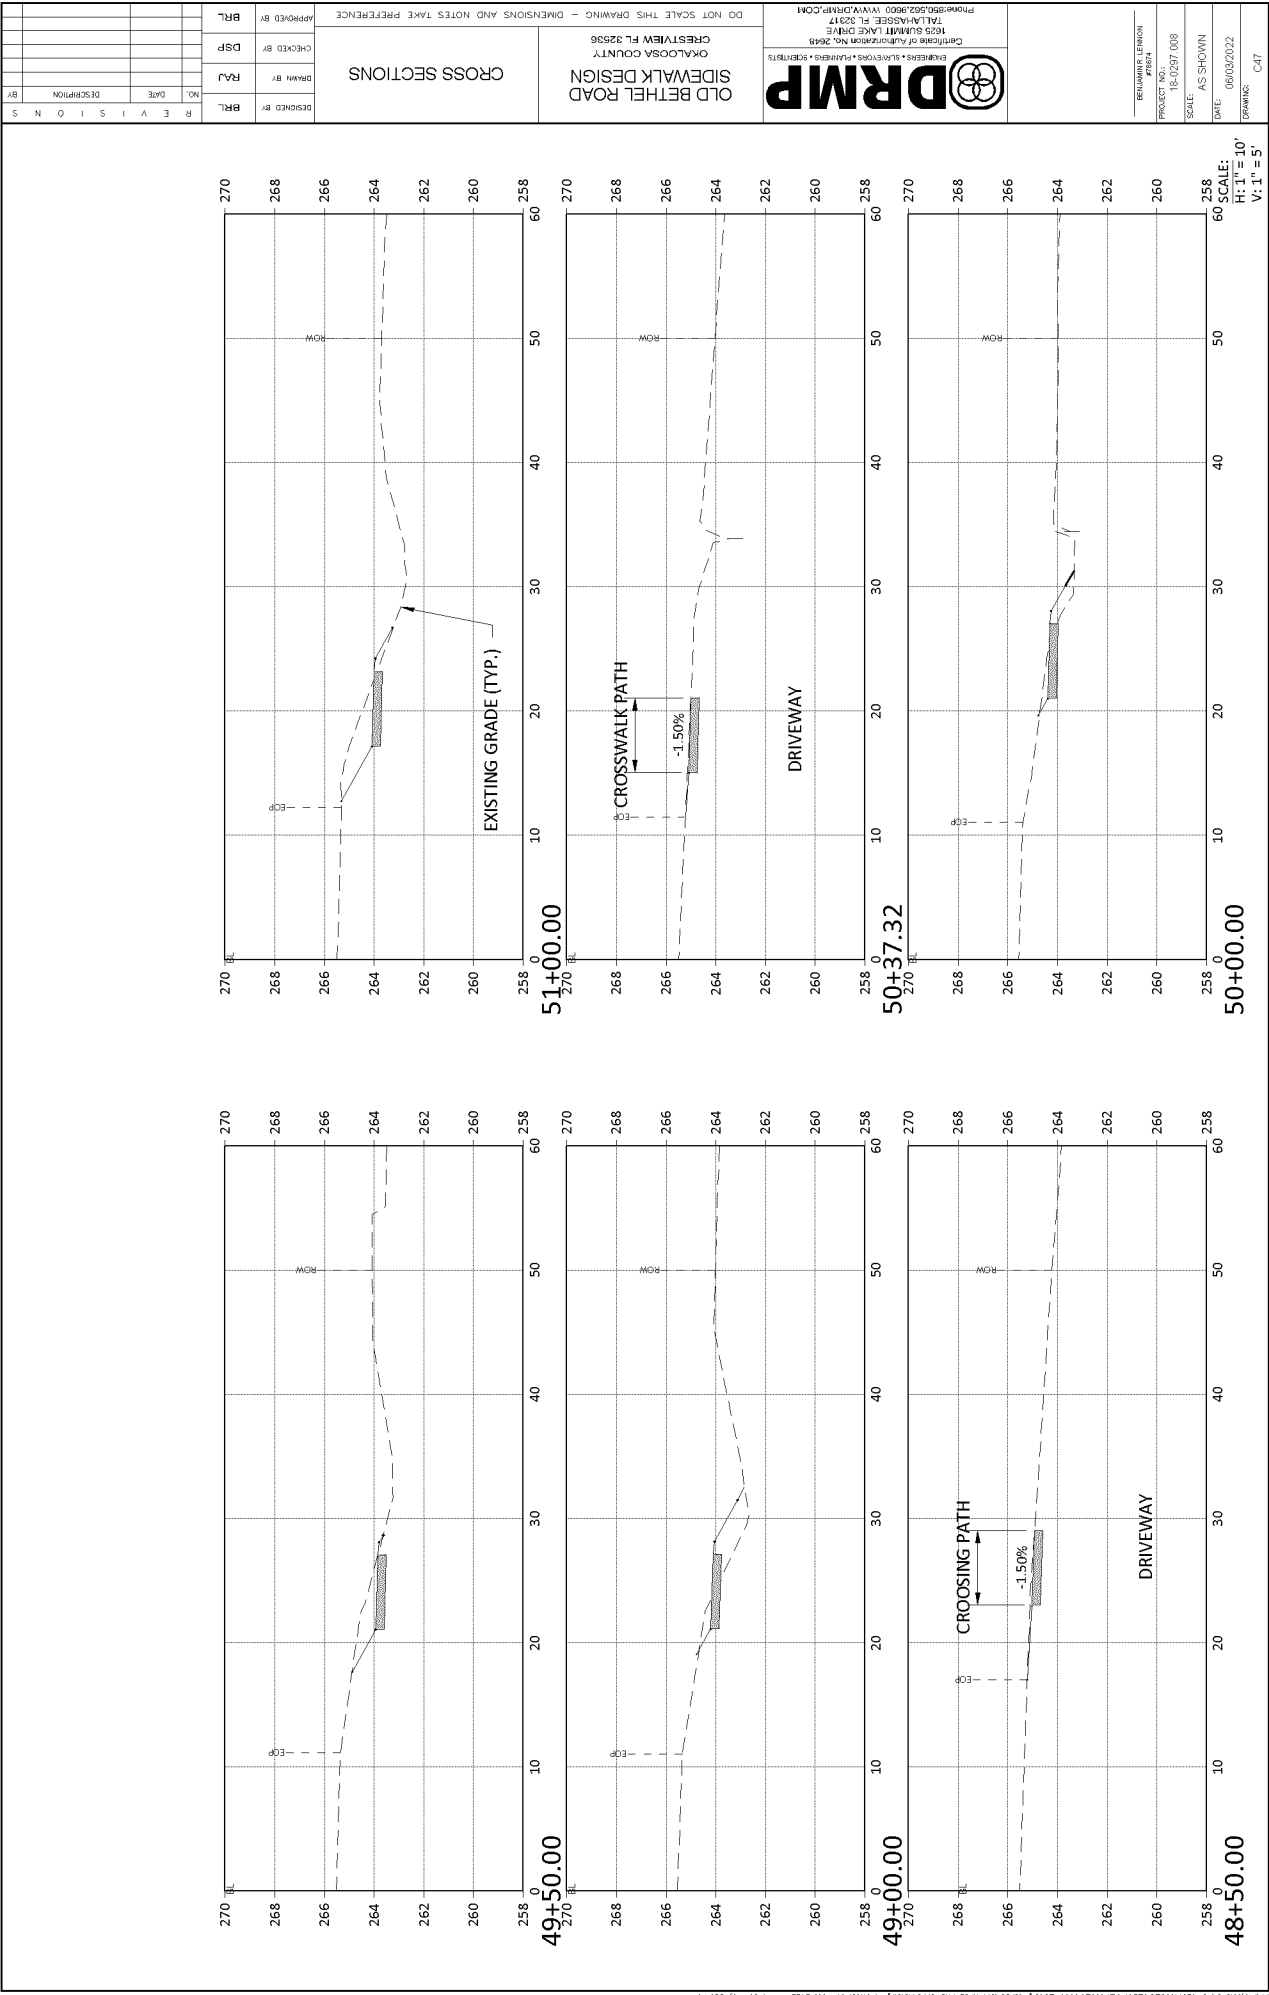


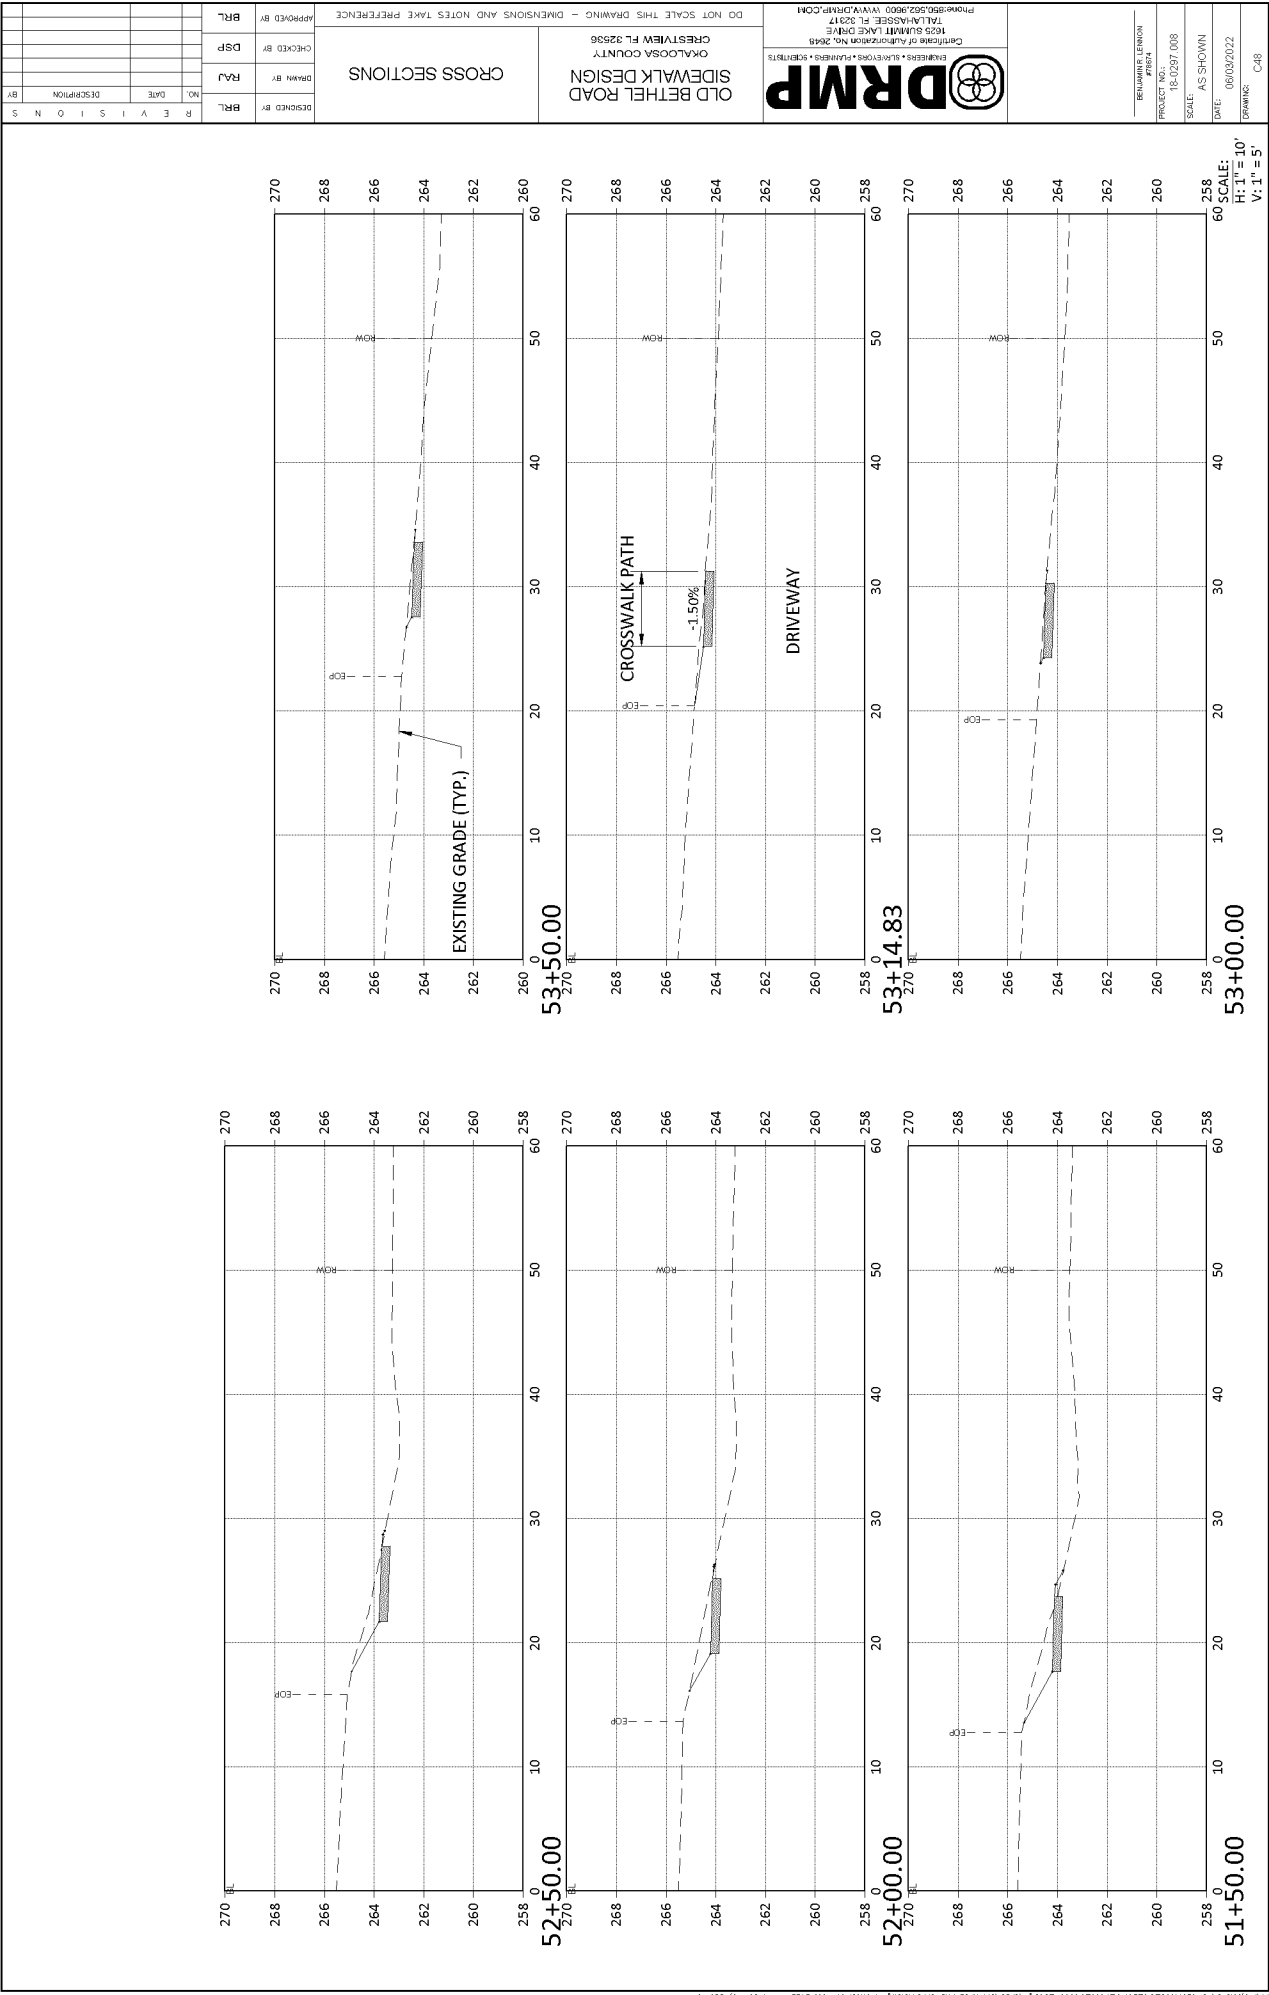


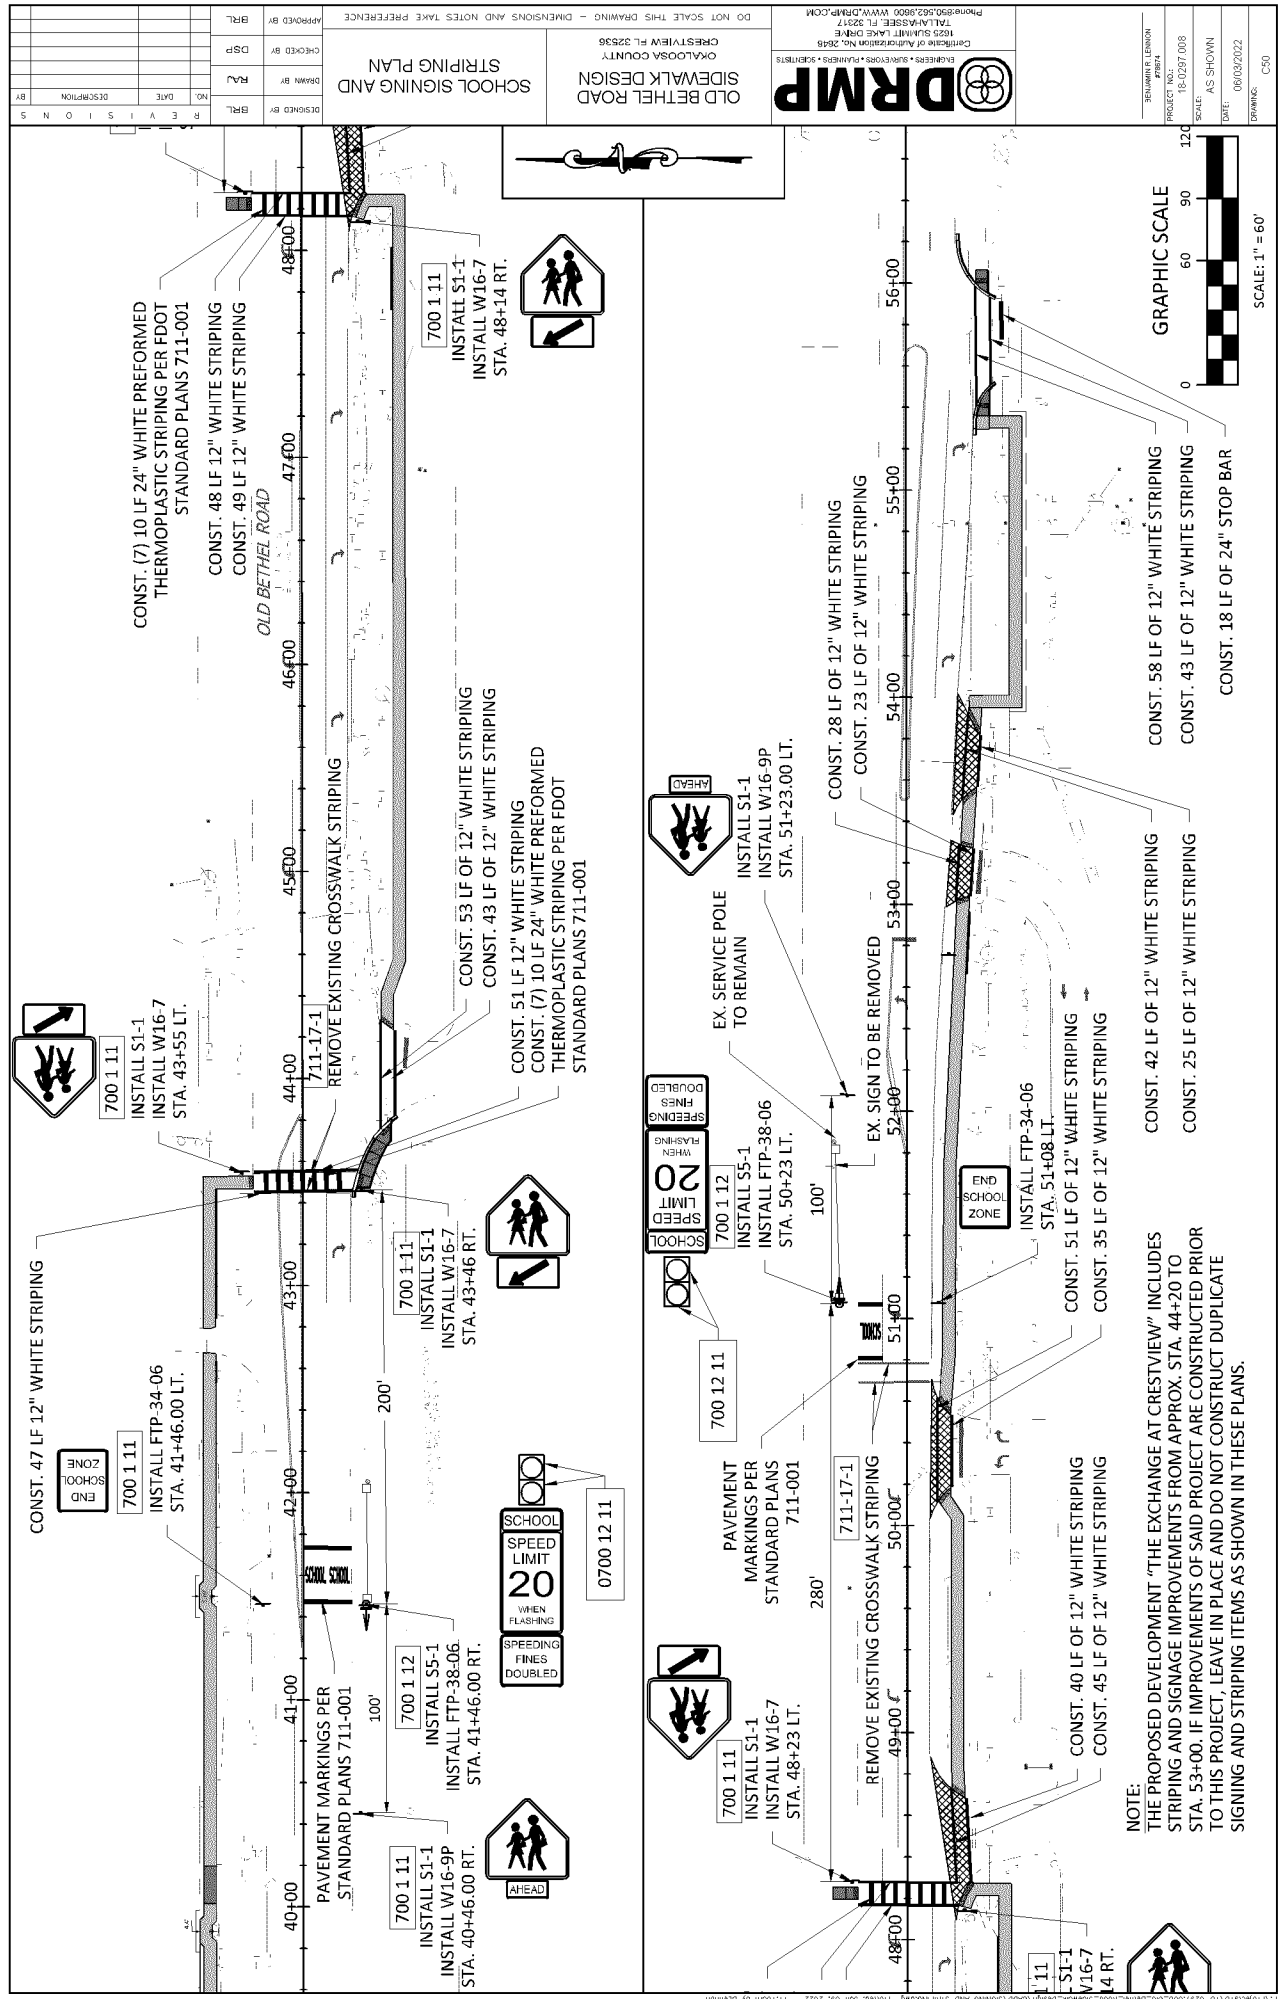

OLD BETHEL ROAD
SIDEWALK DESIGN
OKALOOSA COUNTY
CRESTVIEW FL 32536
DO NOT SCALE THIS DRAWING

SIGNALIZATION PLAN

DESIGNED BY	RAJ	NO.	DATE	DESCRIPTION	BY
APPROVED BY	RAJ				
CHECKED BY					

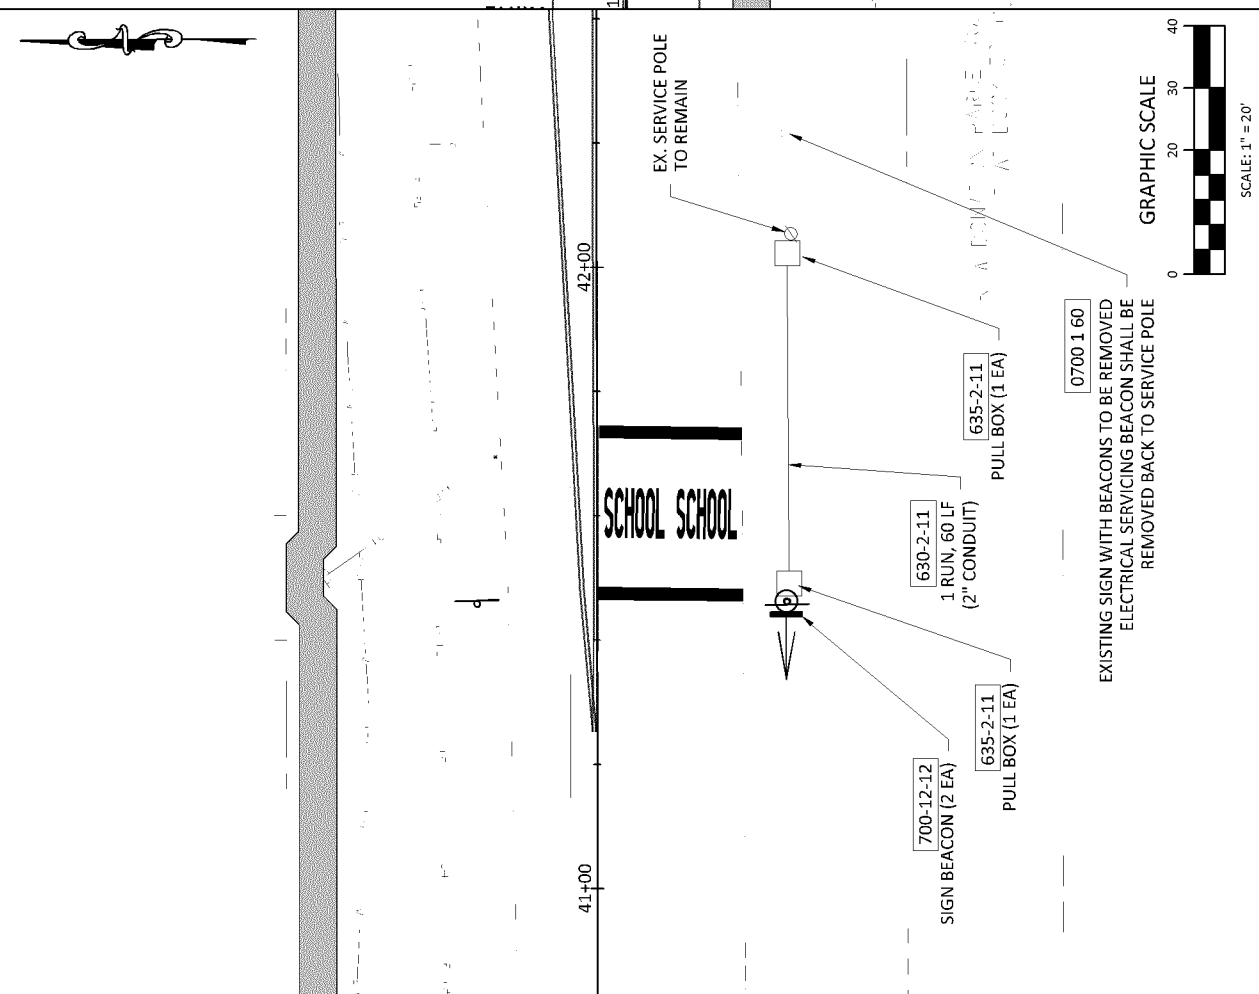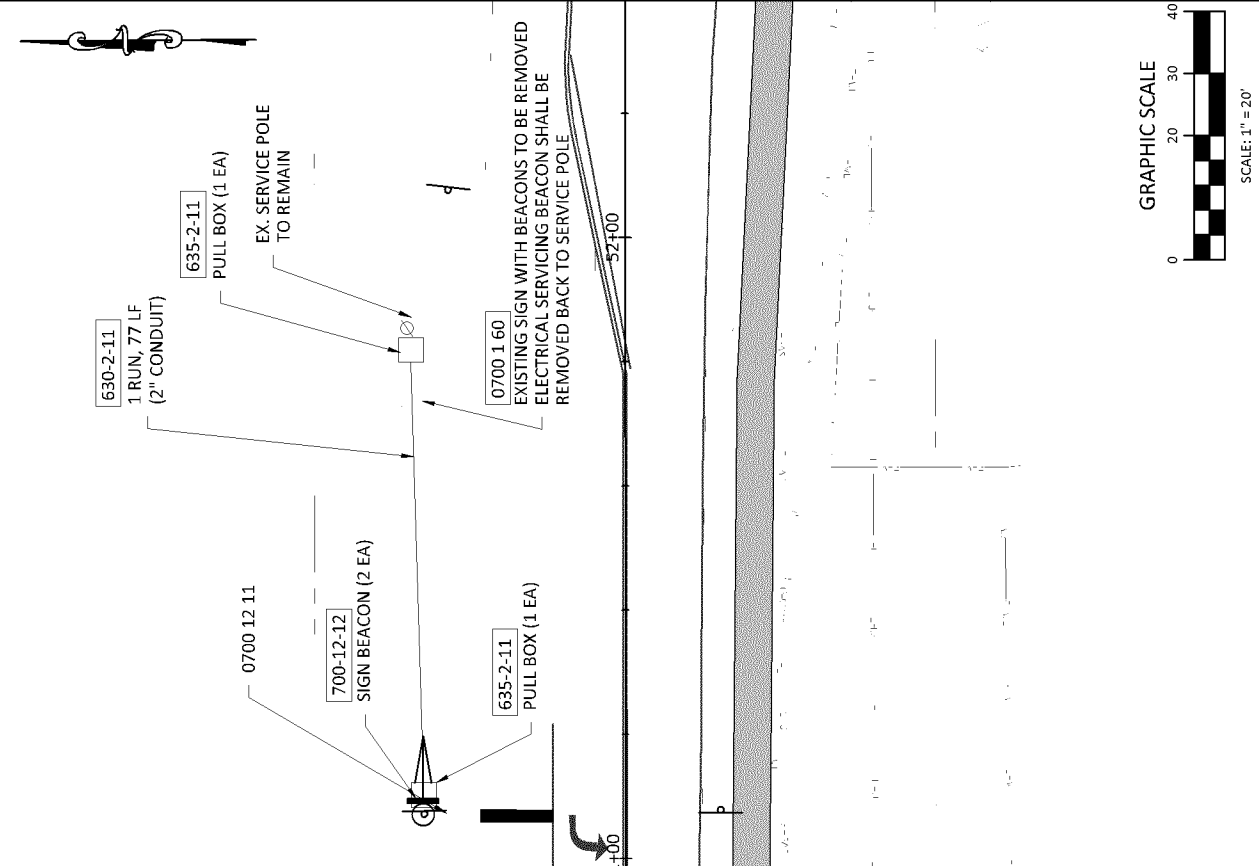

[illegible]

SPECIES	RATES PER ACRE	PLANTING DATES
SEEDING		
RYE GRASS	168 LBS.	15 JULY-30 NOVEMBER
COMMON BUNYARDUE	1/2 BUSH	
COMMON BERNICUDA		1 MARCH-30 JUNE
(PHULLED)	30 LBS.	1 OCTOBER-20 FEBRUARY
COMMON BERNICUDA (UNPHULLED)		
FERTILIZER		
5-10-10	1,800 LBS.	

NOTE: DURING "HIGH FAILURE" MONTHS SEEDING CONTRACTOR TO SPREAD MULCH OR HAY FOR SLOPE STABILIZATION.

The technical drawings illustrate the dimensions and components of the fabric fence backing system:

- Plan View:** Shows the layout of the fabric backing. The total width is 30" min. The fabric backing is 18" min. wide. The distance from the fabric backing to the trench is 6". The distance from the fabric backing to the trench is 20". The distance from the fabric backing to the trench is 20".
- Side View:** Shows the cross-section of the fabric backing. The total width is 4' max. o.c. The fabric backing is 18" min. wide. The distance from the fabric backing to the trench is 6". The distance from the fabric backing to the trench is 20".
- Front View:** Shows the cross-section of the fabric backing. The total width is 30" min. The fabric backing is 18" min. wide. The distance from the fabric backing to the trench is 6". The distance from the fabric backing to the trench is 20".

Labels in the drawings include:

- Flow
- 20"
- 6"
- 18" min.
- 30" min.
- 4' max. o.c.
- 20"
- 30" min.
- 18" min.
- 6"
- Trench
- Fabric Backing
- 20"

NOTE: 30" O.C.T. approved fabric.

NOTE:
Use 36" D.O.T. approved fabric.
Use steel posts - only

PLANTS, PLANTING RATES, AND PLANTING DATES FOR TEMPORARY COVER OR COMPANION CROPS					
SPECIES	BROADCAST Rate per Acre 100 sq ft	Resource <small>(Order details indicate whether you want seed or plants; specify quantity and planting date)</small>	REMARKS		
MILLET, BICOIN (PO) (Parquet festuciformis)					
ALONE	40 lbs.		18,000 SEED PER POUND OF DENSE COVER WILL PROTECT SOO MUCH COMPETITION IN MIXTURES IF SEED AT HIGH RATES		
IN MIXTURES	10 lbs.				
SOULTHERN REDMONT SOUTHERN PLAIN	0.9 lb. 0.2 lb.				
RYE (see grasses)					
ALONE	3 bu. (160 lbs.) (28 bu.)		18,000 SEED PER POUND DENSE COVER VERY TOLERANT AND WINTER-HARDY		
IN MIXTURES	0.6 lb.				
SOULTHERN REDMONT SOUTHERN PLAIN	3.8 lb. 0.6 lb.				
FYEGRASS, ANNUAL (Lolium temeratum)					
ALONE	40 lbs.		27,000 SEED PER POUND DENSE COVER VERY COMPETITIVE AND ADAPTED TO BE USED IN MIXTURES		
IN MIXTURES					
MOUNTAINS SOUTHERN REDMONT SOUTHERN PLAIN	0.9 lb.				

PLANTS, PLANTING RATES, AND PLANTING DATES FOR PERMANENT COVER OR COMPANION CROPS									
SPECIES		BROADCAST		RESOURCE		REMARKS			
		PLANTS (per 100 SQ. YD.)	PLANTING DATE	(Date or dates indicate when seedlings, cuttings, and/or other species become profitable for marginal sites.)					
BAHIA				SOUTHERN REDWOOD		-1,787,000 SEED PER LB. QUICK COVER			
ALONE		10 lbs.	0.2 lb.	SOUTHERN REDWOOD		-COVER, BROWNING AND SOO-FORMING			
WITH OTHER PERENNIALS		6 lbs.	0.1 lb.	SOUTHERN REDWOOD		-FULL SUN			
				SOUTHERN REDWOOD		-GOOD FOR ATHLETIC FIELDS			
BAHIA				SOUTHERN REDWOOD		PLANT WITH WINTER ANNUALS			
WITH TEMPORARY PERENNIALS		10 lbs.	0.2 lb.	SOUTHERN REDWOOD					
WITH OTHER PERENNIALS		6 lbs.	0.1 lb.	SOUTHERN REDWOOD					

LAY SODS IN A STAGGERED PATTERN BUT THE STRIPS TIGHTLY AGAINST EACH OTHER.

DON'T OVERLAP. A SHARPENED MASON'S TROWEL IS A HANDY TOOL TO TRIM THE EDGES.

SOO IMMEDIATELY. WATER TO A DEPTH OF 4" AS NEEDED. WATER WELL AS SOON AS THE SODS ARE Laid.

SHOOTS, OR GRASS BLADES, GRASS SHOULD BE INTERMIXED AND RY, MOVED AT A 2-3" CUTTING HEIGHT.

THATCH, GRASS CLIPPINGS AND DEAD LEAVES, UP TO 1/2" THICK.

ROOT ZONE. SOIL AND ROOTS SHOULD BE 1/2-2" DEEP WITH DENSE ROOTS FOR STRENGTH.

APPEARANCE OF GOOD SOO

SOO IMMEDIATELY. WATER TO A DEPTH OF 4" AS NEEDED. WATER WELL AS SOON AS THE SODS ARE Laid.

SHOOTS, OR GRASS BLADES, GRASS SHOULD BE INTERMIXED AND RY, MOVED AT A 2-3" CUTTING HEIGHT.

THATCH, GRASS CLIPPINGS AND DEAD LEAVES, UP TO 1/2" THICK.

ROOT ZONE. SOIL AND ROOTS SHOULD BE 1/2-2" DEEP WITH DENSE ROOTS FOR STRENGTH.

APPEARANCE OF GOOD SOO

[illegible]

TIMING

- APPLY PERMANENT SEEDING ON AREAS LEFT DORMANT FOR 1 YEAR OR MORE. APPLY PERMANENT SEEDING WHEN NO FURTHER DISTURBANCES ARE PLANNED TO DETERMINE OPTIMUM SEEDING SCHEDULE. CONSULT A LOCAL AGRONOMIST OR EROSION CONTROL SPECIALIST.
- APPLY PERMANENT SEEDING BEFORE SEASONAL RAINS OR FREEZING WEATHER IS ANTICIPATED. USE DORMANT SEEDING FOR LATE FALL OR WINTER SEEDING SCHEDULES.

- USE SEEDS APPROPRIATE TO THE SEASON AND SITE CONDITIONS
- CONSULT LOCAL AGRONOMIST OR EROSION CONTROL SPECIALISTS FOR SEED MIX.
- USE A SEED BLEND TO INCLUDE ANNUALS, PERENNIALS AND LEGUMES.
- USE SEED RATES BASED ON PURE LIVE SEED (PLS) OF 80%. WHEN PLS IS BELOW 80% ADJUST RATES ACCORDINGLY.

- BRING THE PLANTING AREA TO FINAL GRADE AND INSTALL THE NECESSARY EROSION CONTROL PRACTICES DRYING CONCENTRATED FLOWS AWAY FROM THE SEED AREA
- CONDUCT SOIL TEST TO DETERMINE PH AND NUTRIENT CONTENT. ROUGHEN THE SOIL BY HARROWING, TRACKING, GROOVING OR FURROWING. APPLY AMENDMENTS AS NEEDED TO ADJUST PH TO 6.0-7.0. INCORPORATE THESE AMENDMENTS INTO THE SOIL. PREPARE A SEED BED TO THE DEPTH OF 1-2 INCHES. THE SEED BED SHOULD BE FIRM BUT NOT COMPACT. THE TOP THREE INCHES OF SOIL SHOULD BE LOOSE, MOIST AND FREE OF LARGE CLODS AND STONES.
- THE TOP SOIL SURFACE SHOULD BE IN REASONABLY CLOSE CONFORMITY TO THE LINES, GRACES AND CROSS SECTIONS SHOWN ON THE GRADING PLANS.

- SEED TO SOIL CONTACT IS THE KEY TO GOOD GERMINATION
- SEED SHOULD BE APPLIED IMMEDIATELY AFTER SEEDING PREPARATION WHILE THE SOIL IS LOOSE AND MOIST. IF THE SEEDED HAS DRIED, IT SHOULD BE REAPPLIED IMMEDIATELY WITH A DISK, SPRING TOOTH OR HARROW.
- HARROWING, TRACKING OR FLOWROWING SHOULD BE DONE HORIZONTALLY ACROSS THE FACE OF THE SLOPE. SEED TO SOIL CONTACT IS THE KEY TO GOOD GERMINATION
- THE KEY TO GOOD GERMINATION IS A GOOD SEEDING MACH
- APPLY SEED AT THE RATES SPECIFIED USING CALIBRATED SEED SPREADERS, CYCLONE SEEDERS, MECHANICAL DRILLS, OR HYDROSEEDER SO THE SEED IS APPLIED UNIFORMLY ON THE SITE
- BROADCAST SEED SHOULD BE INCORPORATED INTO THE SOIL BY RAKING OR CHAIN DRAGGING, AND THEN LIGHTLY COMPACTED TO PREVENT WIND EROSION
- APPLY FERTILIZER AS SPECIFIED
- APPLY MULCH OR EROSION CONTROL BLANKET, AS SPECIFIED, OVER THE SEEDED AREAS

- NEWLY SEEDER AREAS NEED TO BE INSPECTED FREQUENTLY TO ENSURE THE GRASS IS GROWING
- IF THE SEEDER AREA IS DAMAGED DUE TO RUNOFF, ADDITIONAL STORMWATER MEASURES MAY BE NEEDED.
- SPOT SEEDING CAN BE DONE ON SMALL AREAS TO FILL IN BARE SPOTS WHERE GRASS DID NOT GROW PROPERLY.
